

PFP Project Managers Meeting
Fédéral Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

0071776

Distribution:

J. M. Ayres	Ecology	HO-57
F. W. Bond	Ecology	HO-57
S. L. Charboneau	RL	A5-11
D. A. Faulk	EPA	B1-46
B. J. Gray	FH	T4-34
R. E. Heineman	FH	T1-40
A. M. Hopkins	FH	H8-25
J. E. Hyatt	FH	H8-40
D. E. Jackson	RL	A4-52
G. A. Johnston	FH	T5-30
D. B. Klos	FH	T4-35
E. M. LaRock	FH	T4-33
E. M. Mattlin	RL	A5-15
R. E. Piippo	FH	H8-12
R. W. Oldham	FH	T3-10
C. S. Sutter	FH	T4-32

ADMINISTRATIVE RECORD - Debbi Isom (two copies): H6-08

Please send comments on distribution list to Rob Piippo, H8-12 (373-3285).

RECEIVED
DEC 16 2006
EDMIC

PFP Project Managers Meeting
Federal Building
Richland, Washington
~~August 17, 2006~~
October 12, 2006
3:30 p.m. - 4:30 p.m.
Meeting Minutes Transmittal

The undersigned indicate by their signatures that these meeting minutes reflect the actual occurrences of the above dated Project Managers Meeting.



S. L. Charboneau, PFP Project Manager, DOE-RL

Date: 11/16/06

for 

F. W. Bond, Project Manager,
Washington State Department of Ecology

Date: 11/16/06

PFP, FH Concurrence:



A. M. Hopkins, Contractor Representative, FH

Date: 11/16/06

Purpose: Project Managers Meeting

Attachment 1: Agenda, Action Tracking List and Summary of Discussions

Attachment 2: Presentation Materials

Attachment 3: Attendee List

PFP Project Managers Meeting
Federal Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 1: Agenda, Action Tracking List, and Summary of Discussions

1.0 Administrative Issues

- The meeting minutes from the September 19, 2006 PMM were approved.
- No new actions were established.

2.0 PFP Project Item Status

Ellen Mattlin provided a brief synopsis of the projects status. The project worked very hard to accomplish Performance Incentives that came due at the end of the fiscal year. A tremendous amount of work was accomplished and it was performed safely. Rick Bond inquired as to the status of shipping materials off site. Ellen stated that very little had changed from the last PMM. The project is still on its path to perform D & D over the next two years and then ship materials off site. Three actions that are potentially impacting Hanfords ability to perform shipments this spring are 1) it is an election year so decisions are sometimes delayed until after the election, 2) funding needs to be approved for the MOX facility and it needs to be built and brought on line, 3) regulatory coverage needs to be established and lawsuits avoided. It was agreed that status would be brief as the project is scheduled the following week to provide another status at the quarterly milestone review.

3.0 Milestone Status

- **M83-22** Submit to Ecology an Engineering Evaluation/Cost Analysis(es) (EE/CA(s) for approval and provide an action memorandum(a) as a primary document(s) for the decommissioning of the PFP facility **DUE 9/30/08**

Submit sub-surface EE/CA to Ecology 11/30/06

Andrea Hopkins stated that the EE/CA was at RL going through review and Ellen Mattlin stated that the document would go to the regulators by the 11/30/06 PMM commitment which is well ahead of the 08 due date.

- **M83-41** Complete transition and dismantlement of the 216-Z-9 crib **DUE 9/30/10**

Status: Andrea Hopkins stated the project has been provided funding for fiscal year 07 and 08 which is good news. Staff is coordinating with the central plateau organization and has kicked off the planning effort.

- **M83-32** Complete closure of the PFP 241-Z unit **DUE 9/30/11**

Status: See Attachment 2, Item 1.

PFP Project Managers Meeting
Federal Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

- **M83-42** Complete transition and dismantlement of the 241-Z waste treatment facility
DUE 9/30/11

Status: See Attachment 2, Item 1.

4.0 New Topics

No new topics

5.0 Next Meeting

November 16, 2006

2006 ACTION TRACKING LIST

Action	Assignee	Date Established/ Due Date	Status

PFP Project Managers Meeting
Federal Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 2: Presentation Materials
Item 1

PFP October 12, 2006 PMM
M83-32
M83-42
Jerry Johnston
FH PM for 241-Z Transition

M83-32 Scope - Complete closure of the PFP 241-Z TSD Unit - Due 9/30/11
M83-42 Scope - Complete transition and dismantlement of the 241-Z Facility - Due 9/30/11

Status M83-32

- Cell D4 Status:
 - D4 Cell painting completed on 9/20/06
 - Final D4 inspection video and radiological survey taken on 9/24/06
 - The 60th and final D4 cell entry was completed on 9/25/06 to remove the access ladder
- Cells D7 Status
 - 74 cell entries completed as of 10/12/06
 - Plasma arc cut on tank made on 9/21/06 to allow access for cleaning
 - D7 Overflow tank size reduced and removed
 - Tank D7 cleaning completed on 9/27/06
 - All D7 RCRA closure related activities completed on 9/27/06
 - CERCLA activities will continue to mid-October to complete NDA, equipment removal, and painting the cell
- By 9/29/06 all planned RCRA closure activities were completed and the documentation submitted to the PE for certification
- Refer to the last page for a tabular summary of the status of the documentation associated with the RCRA Closure activities and the CERCLA activities

Status M83-42

- The work planning for Cell D6 is ongoing.
- Mobilization for work in Cell D6 will start in October after the completion of Cell D7.
- Design and planning to support the 241-Z complex transition to a cold and dark status has started.
- Current plans are for the 241-Z to be “*clean slab on grade*” by the end of fiscal year 2007.

PFP Project Managers Meeting
Federal Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal



Interior of Tank D7 on 09-06-06 Prior to Cleaning



Cleaning Tank D7 Walls 09-27-06



Tank D7 on 09-27-06 Cleaning Tank Floor




Cleaning Tank D7 Walls 09-27-06

PFP Project Managers Meeting
Federal Building
Richland, Washington
October 12, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal



Taking Final Rad Surveys Inside Tank D4 09-24-06

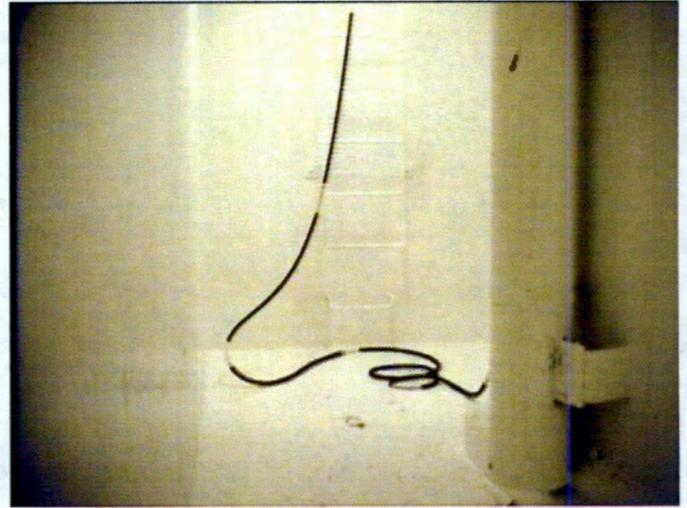

Cell D4 Floor After Painting 09-24-06

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

	241-Z RCRA Closure	D-4	D-5	D-7	D-8		Other	Other Is
	Stainless Steel Tank							
1	Internals	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
2	Void space beneath	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
3	Externals	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
4	Overflow tank (D-7 only, 700 L)			HNF-31198				
5	Concrete containment vault cell	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
6	Ancillary & sample piping in cell	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
7	Soil beneath containment vault	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
8	Piping from 234-5Z	H HNF-31197	HNF-30206	HNF-31198	HNF-30205		HNF-31199	Trench
9	Glovebox GB-2-241-ZA						HNF-31199	241-ZA
	241-Z CERCLA Actions	D-4	D-5	D-7	D-8	D-6	Other	Other Is
	TRU Waste Removal							
1	Process Piping	Note 1	Note 1	Note 1	Note 1			
2	Clean Floor	Note 2	Note 2	Note 2	Note 2			
3	Clean Tank	Note 3	Note 3	Note 3	Note 3			
4	Isolate/seal piping and vent penetrations at building boundaries	Note 4	Note 4	Note 4	Note 4			
5	Characterization data for items remaining after transition	Note 5	Note 5		Note 5			
6	Stabilize below grade spaces (housekeep, remove loose equipment, remove chemicals, fix contamination),	Note 5	Note 5		Note 5			
7	Remove 241-ZG Structure						Note 6	241-ZG
8	Remove 241-Z Structure							241-Z
9	Remove 241-ZA Structure							241-ZA
10	Stabilize site							Complex

NOTES	
1	Process piping removed and documented in accordance with a cell specific work package.
	Cell floor and sump cleaned and documented in accordance with a cell specific work package.
3	Tank cleaned and documented in accordance with a cell specific work package.
4	Lines capped at exterior walls, the 15" vitrified clay cell ventilation lines are considered "cell-to-cell" pipes remain open. Note - The vent from Cell D5 to TK-D9 will be capped during 241-ZA transition
5	Task completed and documented in accordance with a cell specific PFP work package
6	241-ZG structure removed and end point completion document completed and approved by FH Central Plateau Organization.

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

--	--

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Attachment 3: Attendee List

J. Ayres, Ecology
R. Bond, Ecology
R. Bloom, FH
A. M. Hopkins, FH
J. Johnston, FH
E. Mattlin, RL
R. Oldham, FH
R. Piippo, FH
