

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

0071926

Distribution:

J. M. Ayres	Ecology	HO-57
F. W. Bond	Ecology	HO-57
S. L. Charboneau	RL	A5-11
R. H. Engelmann	FH	H8-12
D. A. Faulk	EPA	B1-46
B. J. Gray	FH	T4-34
R. E. Heineman	FH	T1-40
A. M. Hopkins	FH	H8-12
J. E. Hyatt	FH	H8-40
D. E. Jackson	RL	A4-52
G. A. Johnston	FH	T5-30
D. B. Klos	FH	T4-35
E. M. LaRock	FH	T4-33
E. M. Mattlin	RL	A5-15
R. E. Piippo	FH	H8-12
R. W. Oldham	FH	T3-10
C. S. Sutter	FH	T4-32


ADMINISTRATIVE RECORD – Silvia Cook (two copies): H6-08

Please send comments on distribution list to Rob Piippo, H8-12 (373-3285).

RECEIVED
JAN 09 2007
EDMC

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

The undersigned indicate by their signatures that these meeting minutes reflect the actual occurrences of the above dated Project Managers Meeting.



S. L. Charboneau, PFP Project Manager, DOE-RL


Date: 12/21/06



F. W. Bond, Project Manager,
Washington State Department of Ecology

Date: 12/21/06

PFP, FH Concurrence:



A. M. Hopkins, Contractor Representative, FH

Date: 12/21/06

Purpose: Project Managers Meeting

Attachment 1: Agenda, Action Tracking List and Summary of Discussions

Attachment 2: Presentation Materials

Attachment 3: Attendee List

Attachment 1: Agenda, Action Tracking List, and Summary of Discussions

1.0 Administrative Issues

- The meeting minutes from the October 12, 2006 PMM were approved.
- No new actions were established.

2.0 PFP Project Item Status

Stacy Charboneau provided a brief synopsis of the projects status and deferred D&D discussion to the review of individual milestones. For de-inventory, Stacy reported that the Consolidation Implementation Plan should be signed by EM-2 by the end of the month, recommending the start of shipments by FY07.

3.0 Milestone Status

- **M83-22** Submit to Ecology an Engineering Evaluation/Cost Analysis(es) (EE/CA(s) for approval and provide an action memorandum(a) as a primary document(s) for the decommissioning of the PFP facility **DUE 9/30/08**

Submit sub-surface EE/CA to Ecology 11/30/06

Andrea Hopkins provided a preliminary advance copy of the below-grade structures EE/CA to the regulators for review and comment. The EE/CA is being routed thru RL staff for approval and will be formally provided to the regulators once completed.

- **M83-41** Complete transition and dismantlement of the 216-Z-9 crib **DUE 9/30/10**

Status: Andrea Hopkins stated the project is on schedule and a contract has been initiated for development of the SAP and RAWP.

- **M83-32** Complete closure of the PFP 241-Z unit **DUE 9/30/11**

Status: See Attachment 2, Item 1. Jerry Johnston pointed out that a typo was discovered in the closure plan during the PE certification process. The closure plan incorrectly swapped the identity of the two small gloveboxes inside 241-ZA. Since both of the gloveboxes were removed in accordance with provisions of the TSD unit closure plan, the PE concluded that no discrepancy exists.

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

- **M83-42** Complete transition and dismantlement of the 241-Z waste treatment facility
DUE 9/30/11

Status: See Attachment 2, Item 1. A draft TPA change notice was presented by R. Bloom to modify a removal action work plan. Stacy Charboneau stated that 241-Z cell cover blocks will not be removed and that this is documented in the CN. Jeff Ayres stated he would like to discuss the change notice with Rick Bond who was not in attendance and then get with RL to go over the change notice.

4.0 New Topics

No new topics

5.0 Next Meeting

December 14, 2006

2006 ACTION TRACKING LIST

Action	Assignee	Date Established/ Due Date	Status

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 2: Presentation Materials
Item 1

PFP November 16, 2006 PMM

M83-32

M83-42

Jerry Johnston

FH PM for 241-Z Transition

M83-32 Scope - Complete closure of the PFP 241-Z TSD Unit - Due 9/30/11

M83-42 Scope - Complete transition and dismantlement of the 241-Z Facility - Due 9/30/11

Status M83-32

- PE Certification for 241-Z RCRA Closure was received by FH on 11/07/06.
 - The certification noted that the closure plan incorrectly identified the sample glovebox in 241-ZA that operated as a portion of the TSD as GB-2-241-ZA instead of GB-1-241-ZA. Because both gloveboxes were removed in accordance with provisions of the TSD unit closure plan, no discrepancy exists.
- The preparation of the Owner-Operator Certification for the 241-Z RCRA Closure has been initiated.
- Jeff Ayres toured the 241-Z Facility on 11/06/06 to view the five below grade cells through the transparent lexan port covers.
- Refer to the last page for a tabular summary of the status of the documentation associated with the RCRA Closure activities and the CERCLA activities.

Status M83-42

- The last entry into Cell D7 was 10/26/06. There were a total of 85 cell entries made into D7.
- Based on concurrence from RL and Ecology, on 10/25/06 the applicable PFP operating procedures were issued to allow the intermittent operation of the 241-Z ventilation system. This requires the 241-Z exhaust system to be operational only when the below grade cells are being accessed to perform work.
- Weekly meetings with the FH Central Plateau D&D organization were started on 10/24/06 to coordinate the planning for the demolition of the 241-Z structures.
- Performed 296-Z-3 (241-Z stack) annual regulatory inspection on 11/09/06.
- The work planning and mobilization for Cell D6 was completed 11/10/06.
- The initial entry into Cell D6 was 11/13/06.
- Current plans are for the 241-Z to be "clean slab on grade" by the end of fiscal year 2007.

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal






PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal



November 6, 2006 – Job walk with Jeff Ayres to inspect 241-Z Cells through the lexan access port cover.

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

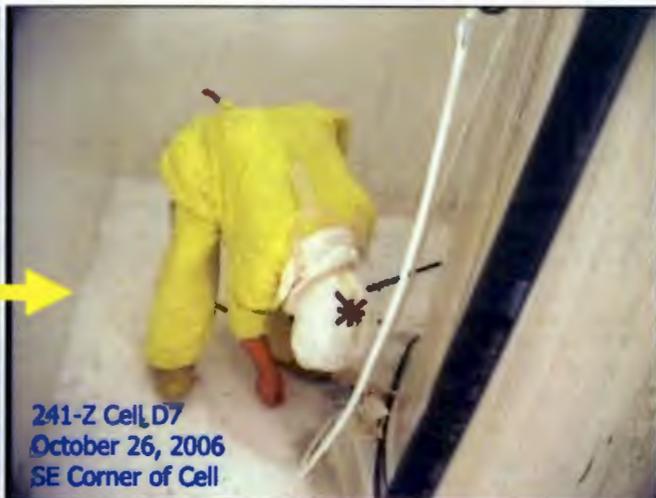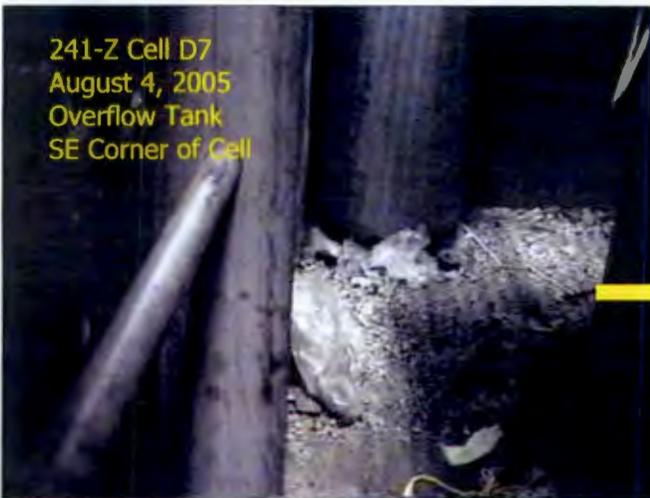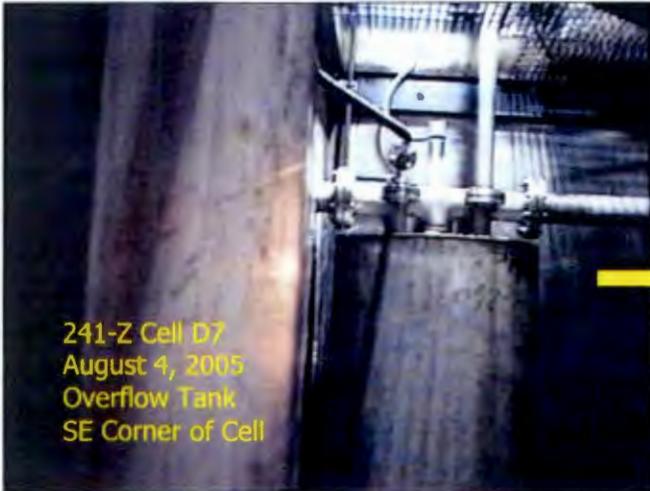

PFP Project Managers Meeting
Federal Building
Richland, Washington
November 16, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal



11-10-06 East and West Entrances to the Cell D6 Containment Tent



11-10-06 Interior of D6 Containment Tent
(above) and Looking West Along the 241-Z
North Wall (right)



PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

241-Z RCRA Closure		D-4	D-5	D-7	D-8		Other	Other Is
	Stainless Steel Tank							
1	Internals	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
2	Void space beneath	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
3	Externals	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
4	Overflow tank (D-7 only, 700 L)			HNF-31198				
5	Concrete containment vault cell	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
6	Ancillary & sample piping in cell	HNF-31197	HNF-30206	HNF-311985	HNF-30205			
7	Soil beneath containment vault	HNF-31197	HNF-30206	HNF-31198	HNF-30205			
8	Piping from 234-5Z	H HNF-31197	HNF-30206	HNF-31198	HNF-30205		HNF-31199	Trench
9	Glovebox GB-2-241-ZA						HNF-31199	241-ZA
241-Z CERCLA Actions		D-4	D-5	D-7	D-8	D-6	Other	Other Is
	TRU Waste Removal							
1	Process Piping	Note 1	Note 1	Note 1	Note 1			
2	Clean Floor	Note 2	Note 2	Note 2	Note 2			
3	Clean Tank	Note 3	Note 3	Note 3	Note 3			
4	Isolate/seal piping and vent penetrations at building boundaries	Note 4	Note 4	Note 4	Note 4			
5	Characterization data for items remaining after transition	Note 5	Note 5	Note 5	Note 5			
6	Stabilize below grade spaces (housekeep, remove loose equipment, remove chemicals, fix contamination),	Note 5	Note 5	Note 5	Note 5			
7	Remove 241-ZG Structure						Note 6	241-ZG
8	Remove 241-Z Structure							241-Z
9	Remove 241-ZA Structure							241-ZA
10	Stabilize site							Complex

NOTES	
1	Process piping removed and documented in accordance with a cell specific work package.
2	Cell floor and sump cleaned and documented in accordance with a cell specific work package.
3	Tank cleaned and documented in accordance with a cell specific work package.
4	Lines capped at exterior walls, the 15" vitrified clay cell ventilation lines are considered "cell-to-cell" pipes remain open. Note - The vent from Cell D5 to TK-D9 will be capped during 241-ZA transition
5	Task completed and documented in accordance with a cell specific PFP work package
6	241-ZG structure removed and end point completion document completed and approved by FH Central Plateau Organization.

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

--	--

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Attachment 3: Attendee List

J. Ayres, Ecology
R. Bloom, FH
S. Charboneau, RL
S. Clarke, RL
B. Cox, FH
A. Hopkins, FH
J. Johnston, FH
G. Laws, WDOH
E. Mattlin, RL
R. Oldham, FH
R. Piippo, FH
