


FINAL

Office of River Protection
Tri-Party Agreement
Monthly Summary Report
March 2013



**Office of River Protection
Tri-Party Agreement Milestone Review
March 2013 (Project EVMS reflects January 2013)**

Page	Topic	Leads
1	Administrative Items / Milestone Status	James Lynch / Dan McDonald / Jeff Lyon
2	System Plan; M-62-40	Dabrisha Smith / Jeff Lyon / Dan McDonald
3	Acquisition of New Facilities; M-90-00; M-47-00	Janet Diediker / Jeff Lyon / Dan McDonald
4	Supplemental Treatment and Part B Permit Applications; M-62-00, -20, -30, -45	Steve Pfaff / Jeff Lyon / Dan McDonald
5	242-A Evaporator Status	Ron Koll / Jeff Lyon
6	SST Integrity Assurance; M-45-91	Jeremy Johnson/ Michelle Hendrickson
7	In Tank Characterization and Summary	Billie Mauss / Michael Barnes
9	Tank Operations Contract (TOC) Overview	Dan Knight / Jeff Lyon
14	Single-Shell Tank Corrective Action; M-45, -50, -60	Chris Kemp / Jeff Lyon
16	Single-Shell Retrieval and Closure Program TPA Milestones Status; M-45-00 series	Chris Kemp / Jeff Lyon
17	Tank Waste Retrieval Work Plan Status	Chris Kemp / Jeff Lyon
17	Tank in TPA Appendix H Status Tank Retrievals with Individual Milestones	Chris Kemp / Jeff Lyon
18	WTP Overall TPA Summary and Milestone Status; M-62-01	Delmar Noyes / Dan McDonald

Milestone	Title	Due Date	Completion Date	Status
Fiscal Year 2013				
M-045-20	Submit Interim Measures Investigation Work Plan and TPA Chg Pckgs for M-045-22 Target Dates	12/31/2012	12/06/2012	Completed
M-090-11	Comp. Neg's No More Than 2 Canister Storage Fac. Const. Int. M/S	12/31/2012	11/19/2012	Completed
M-062-01Z	Submit Semi-Annual Project Compliance Report	1/31/2013	1/31/2013	Completed
M-045-91F-T01	Provide Report of the Liquid Leak Rate Assessments	1/31/2013		Missed
M-045-21	Submit Sampling and Analysis Plan for 241-TX Tank Farm	3/31/2013	3/11/2013	Completed
M-045-91D-T01	Provide Report on the Concrete Dome Samples from Tank C-107 Plug	5/31/2013		On Schedule
M-045-91F-T03	Provide Report on Testing for Ionic Conductivity of SSTs	5/31/2013	5/02/2012	Completed
M-045-91F-T02	Provide Report of Liner Failures for SSTs	7/31/2013		To Be Missed
M-062-01AA	Submit Semi-Annual TPA Project Compliance Report	7/31/2013		On Schedule
M-045-91F-T04	Provide Report on 100-Series SSTs as having Leaked in RPP-32681	7/31/2013		To Be Missed
M-045-91E	Provide SST Farms Dome Deflection Surveys Every Two Years	9/30/2013		On Schedule
M-045-91G-T03	Provide AOR Final Doc. for SSTs on 1,000,000 Gallon Tanks	9/30/2013		To Be Missed
Fiscal Year 2014				
M-045-91G-T04	Provide AOR Final Doc. for SSTs on 55,000 Gallon Tanks	10/31/2013		To Be Missed
M-062-40C	Select a Minimum of Three Scenario's for the System Plan	10/31/2013		On Schedule
M-045-91F	Provide Summary Conclusions Report on Leak Integrity	12/31/2013		To Be Missed
M-045-91G	Provide Summary Conclusions Report of AOR for SSTs	04/30/2014		To Be Missed
M-045-56J	Ecology And DOE Agree, At A Minimum, To Meet Yearly (By July)	07/31/2014		On Schedule
M-045-91B-T01	Provide Ecology report on the Concrete Core from TankA-106 or alt	09/30/2014		On Schedule
M-047-07	CD-1 for Secondary Liquid Waste Treatment and CR for CD-2 to Ecology	09/30/2014		On Schedule
M-090-13	CD-1 for Interim Hanford Storage Project and CR for CD-2 to ECY	09/30/2014		On Schedule

System Plan

M-062-40B, Submit a system plan describing the disposition of all tank waste managed by ORP, Due: 10/31/2011, Status: Completed 10/24/2011 via DOE-ORP/ECY joint signature letter 11-TPD-087.

M-062-40C, Select a minimum of three scenarios that will be analyzed in the system plan, Due: 10/31/2013, Status: On Schedule

M-062-40D, Submit a system plan describing the disposition of all tank waste managed by ORP, Due: 10/31/2014, Status: On Schedule

M-062-45-T01, Every six years, within six-months after last revision of the System Plan, negotiate tank waste retrieval sequencing, Due: 4/30/2015, Status: On Schedule

Significant Past Accomplishments:

DOE/ORP submitted the River Protection Project System Plan, Revision 6, with a joint Ecology signature to EPA on October 24, 2011.

Significant Planned Actions in the Next Six Months:

ORP and WRPS plan to meet with Ecology in April 2013 to provide the status on various recommendations made in regards to several model planning tools in the 2009 "External Technical Review for Evaluation of System Level Modeling and Simulation Tools in Support of Hanford Site Liquid Waste Process." Please see issues below.

Various circumstances have occurred in which no new scenarios have been selected for System Plan 6 Addendum.

ORP and Ecology will jointly begin defining the System Plan 7 scenarios in the July-August 2013 time frame. The defined scenarios milestone (M-062-40C) is due October 31, 2013.

Issues:

In the October 23, 2012 TPA Project Managers meeting Dan Mc Donald, Ecology, informed ORP that system plan development for FY 14 could not move forward until ORP had read and responded to the comments in the headquarters document, "External Technical Review for Evaluation of System Level Modeling and Simulation Tools in Support of Hanford Site Liquid Waste Process." Ecology has asked for a meeting with ORP and WRPS as soon as they have read the document and are able to brief on where they think they are going with comment response development.

Acquisition of New Facilities

M-090-13, Submit CD-1 for Interim Hanford Storage Project and TPA Change Request for CD-2 to Ecology, Due: 09/30/14, Status: On Schedule. Created by TPA Change Control Form M-90-12-02, signed by ORP and Ecology on 11/19/12, to "Submit to Ecology, a Conceptual Design Report Package (Critical Decision-1) for the Interim Hanford Storage Project (storage of the first two years of Hanford Site Immobilized High-Level Waste from WTP operations) and a TPA Change Request (in accordance with TPA Action Plan Section 12.0) to submit to Ecology, a Preliminary Design Report package (Critical Decision-2)."

M-090-00, Acquire/modify facilities for storage of IHLW, Due: 12/31/2019, Status: On Schedule

M-047-07, Submit CD-1 for Secondary Liquid Waste Treatment and CR for CD-2 to Ecology, Due 09/30/14, Status: On Schedule. Created by TPA Change Control Form M-47-12-02, signed by ORP and Ecology on 11/19/12, to "Submit to Ecology, a Conceptual Design Report package (Critical Decision-1) for the Secondary Liquid Waste Treatment Project and a TPA Change Request (in accordance with TPA Action Plan Section 12.0) to submit to Ecology, a Preliminary Design Report package (Critical Decision-2).

M-047-00, Complete Work Necessary to provide facilities for management of secondary waste from the WTP, Due: 12/31/2022, Status: On Schedule

Significant Past Accomplishments:

On November 19, 2012, Ecology and ORP signed TPA Change Control Forms M-47-12-02 and M-90-12-02 establishing M-047-07 and M-090-13, respectively. ORP letter 12-ECD-0225 notified Ecology of completion of milestones M-047-06 and M-090-11.

Significant Planned Actions in the Next Six Months:

None.

Issues:

None.

Supplemental Treatment and Part B Permit Applications

M-062-40ZZ, Submit a one-time Tank Waste Supplemental Treatment Technologies report if a supplemental treatment technology is proposed other than a 2nd LAW, Due: 10/31/2014, Status: On Schedule.

M-062-45ZZ, Negotiate a one-time supplemental treatment selection, Due: 4/30/2015, Status: On schedule. Negotiations are not yet underway.

M-062-45ZZ-A, Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones, Due: 4/30/2015, Status: On Schedule.

M-062-31-T01, Complete final design and submit RCRA Part B permit mod request, Due: 4/30/2016, Status: On schedule

M-062-32-T01, Start construction of supplemental vitrification treatment facility and/or WTP enhancements, Due: 4/30/2018, Status: On schedule

M-062-33-T01, Complete construction of supplemental vitrification treatment facility and/or WTP enhancements, Due: 4/30/2021, Status: On schedule

M-062-45XX, No later than 12/31/2021, the DOE and Ecology shall complete negotiations to establish a mechanism that will apply to resolve future disputes regarding the determinations in M-062-45, paragraphs 4 and 5, due: 12/31/2021, Status: On Schedule

M-062-34-T01, Complete hot commissioning of supplemental vitrification treatment facility and/or WTP enhancements, Due: 12/30/2022, Status: On schedule

M-062-21, Annually, submit data that demonstrates operation of the WTP, Due: 2/28/2023, Status: On Schedule

M-062-00, Complete Pretreatment Processing and Vitrification of HLW and LAW Tank Wastes, Due: 12/31/2047, Status: On Schedule

Significant Past Accomplishments:

None

Significant Planned Actions in the Next Six Months:

None

Issues:

At the January 2013 TPA PMM meeting, ORP stated DOE and Ecology are currently in discussions to move out the due dates for M-062-40ZZ and M-062-45ZZ (current due dates 10/31/2014 and 4/30/2015, respectively).

242-A Evaporator Status (previously reported under Milestone M-48, which has been closed out)

242-A Campaign strategy:

The 242-A Campaign Strategy for FY2010 through FY2015 depicted below has been updated based on ORP-11242, River Protection Project Plan, Revision 6, and ongoing schedule integration efforts.

Fiscal Year	Campaign No.	Feed Source	Slurry Tank	Comments
FY10	10-01	AW-106	AW-106	Campaigns 10-01/10-02 were performed back-to back starting in late August and completing in early October 2010.
FY10	10-02	AW-106	AW-106	Campaign 10-02 was an acceleration of previously planned Campaign 11-01.
FY11	NA	NA	NA	No campaign conducted in FY11 due to ongoing 242-A and Tank Farm facility life extension and ARRA funded upgrades.
FY12	NA	NA	NA	No campaign conducted in FY12 due to ongoing 242-A and Tank Farm facility upgrades and revision to the 242-A Documented Safety Analysis (DSA).
FY13	13-01	AP-107	AP-107	Estimated start early August 2013. May require two (2) passes to achieve waste volume reduction.
FY13	13-02	AW-106	AW-106	Estimated start late August 2013.
FY14	14-01	AN-106 AZ-102 AW-106	AP-107	Estimated start March 2014. Two (2) passes required.
FY15	15-01	AY-101 AZ-102	AP-107	Estimated start March 2015. Three (3) passes required.
FY15	15-02	AY-101	AP-107	Estimated start August 2015. Four (4) passes required.

SST Integrity Assurance

M-045-91F-T01, Provide to Ecology as a HFFACO secondary document a report evaluating the applicability to Hanford SSTs of the liquid leak rate assessments of sludge and salt-cake from the Savannah River Site, Due: 1/31/2013, Status: Missed. See issues below.

M-045-91D-T01, Provide Ecology a report containing the results and interpretation of testing, and analysis performed on the concrete dome samples obtained from the Tank C-107 plug, Due: 5/31/2013, Status: On schedule.

M-045-91F-T03, Provide to Ecology, as a HFFACO secondary document a report assessing the feasibility of testing for ionic conductivity between the inside and outside of SSTs, Due: 5/31/2013, Status: Complete 05/02/2012. (ORP letter 12-TF-0009)

M-045-91F-T02, Provide to Ecology as a HFFACO secondary document a report evaluating the common factors of liner failures for SSTs that have leaked and will provide recommendations as appropriate, such as enhanced Leak Detection, Monitoring, and Mitigation, Due: 7/31/2013, Status: To Be Missed. See issues below.

M-045-91F-T04, provide to Ecology, as a HFFACO secondary document, a report on the 100-series single-shell tanks which have been or will be identified as having leaked in RPP-32681, Rev 0, Due: 7/31/2013, Status: To Be Missed. See issues below.

M-045-91G-T03, Provide to Ecology the Structural Analyses of Record final documentation for SSTs for 1,000,000 gallon tanks (A, AX and SX Farms), Due: 9/30/2013, Status: To Be Missed. See issues below.

M-045-91E, Provide to Ecology a compilation of the Single-Shell Tank farms dome deflection surveys every two years, beginning 9/30/2013, Due: 9/30/2013, Status: On schedule.

M-045-91G-T04, provide to Ecology the Structural Analyses of Record final documentation for SSTs for 55,000 gallon tanks (B, C, T and U Farms), Due: 10/31/2013, Status: To Be Missed. See issues below.

M-045-91F, Provide to Ecology a report (Summary Conclusions Report on Leak Integrity) summarizing and evaluating the information submitted under M-045-91F-T01 through -T04, Due: 12/31/2013, Status: To Be Missed. See issues below.

M-045-91G, Provide a Summary Conclusions Report of Structural Analysis of Record (AOR) for SSTs, Due: 4/30/2014, Status: To Be Missed. See issues below.

M-045-91B-T01, Provide Ecology a report containing the results and interpretation of testing, and analysis, performed on the concrete core obtained from Tank A- 106 or alternate tank, Due: 9/30/2014, Status: On schedule.

M-045-91H, Submit a change package (if deemed necessary by DOE and Ecology) to establish additional milestones based on information obtained from the actions in the preceding M-045-91 series milestones to date, Due: 7/31/2015, Status: On schedule.

M-045-91I, Provide to Ecology an IQRPE certification of SSTs structural integrity for the remainder of the mission, or for such time as the IQRPE believes he/she can reasonably certify, Due: 9/30/2018, Status: On schedule.

Significant Past Accomplishments:

- Work has resumed in the areas of SST structural analysis, sidewall coring, analysis of rebar from C-107, and SST leak cause and location analysis.

Significant Planned Actions in the Next Six Months:

- Conclude discussion with Ecology regarding “To Be Missed” target dates and interim milestone impacts and submit the agreed-upon TPA Change Package for approval.
- Complete analysis of rebar from C-107 and complete M-045-91D-T01.

Issues:

- FY2012 and FY2013 funding constraints have impacted M-045-91 scheduled work. ORP has met with Ecology to discuss impacts on individual milestones and targets dates for FY2013 and beyond per the TPA Section 12.0 Change Process. Ecology’s initial comments on a draft TPA Change Request have been incorporated, and ORP has provided this updated draft to Ecology for review. After Ecology completes this review, ORP will then submit a final, signed TPA Change Request.

In Tank Characterization and Summary

For the period from February 1 – February 28, 2013:

Accomplishments:

- Completed RPP-PLAN-54455, Rev. 0, Tank 241-SY-102 Grab Sampling and Analysis Plan in Support of Corrosion Mitigation after Caustic Addition.
- Completed RPP-PLAN-54233, Rev. 1, Tank 241-AN-101 Grab Sampling and Analysis Plan at Tank 241-C-101 Mid-Retrieval.
- Completed Off-Riser Sampling System (ORSS) sampling of Tank 241-C-104 for closure on February 8, 2013.
- Completed Grab Sampling of Tank 241-SY-102 on February 20, 2013.
- RPP-RPT-54251, Rev. 0, Final Report for Tank 241-AY-102A Annulus Leak-Detection Pit Liquid Grab Samples, December 2012 was released on February 6, 2013.
- RPP-RPT-54251, Rev. 0, Final Report for Tank 241-AW-106 Grab Samples in Support of Evaporator Campaign for Fiscal Year 2013 was released on February 14, 2013.

Planned Action within the next Six Months:

- Tank Sampling
 - Tank 241-AN-101 grab sampling for chemistry control (C-101 mid-retrieval) is currently scheduled for March 2013.
 - Tank 241-C-109 ORSS sampling for closure is currently scheduled for April 2013.
 - Tank 241-AZ-102 grab sampling for the evaporator is currently scheduled for April 2013.
 - Tank 241-C-107 Mobile Arm Retrieval System (MARS) Drag Sampling for closure is currently scheduled for April 2013.
 - Tank 241-C-112 process sampling during hard heel retrieval is scheduled for May, 2013.
 - Tank 241-AY-101 grab sampling for chemistry control is currently scheduled for May 2013.
 - Tank 241-AN-102 grab sampling for chemistry control is currently scheduled for June 2013.

- BBI Updates: The following tanks have been identified for updates in FY13 Quarter 2. The BBI updates will be released in April 2013.
 - 241-AN-101
 - 241-AN-106
 - 241-AP-104
 - 241-AW-105
 - 241-AY-101
 - 241-AY-102
 - 241-AZ-101
 - 241-C-101
 - 241-C-108
 - 241-SY-102

- Data Quality Objectives (DQO)
 - A DQO on a Solubility Model is due to be released in April 2013.
 - A DQO for Tank C-112 Hard Heel Dissolution is due to be released in April, 2013.

Issues:

None.

TANK OPERATIONS CONTRACT (TOC) OVERVIEW


Project Performance

The earned value performance reporting reflects the format, Work Breakdown Structure (WBS) reporting levels, and variance thresholds as agreed to with the Tank Farms Operations Contractor (TOC) for monthly performance reporting. The earned value analysis is not intended to be a measurement of performance against existing Tri-Party Agreement Milestones.

As of January 31, 2012, Washington River Protection Solutions LLC (WRPS) worked 6,354,716 hours (661 days) without a Lost Time Workday Injury and 28,404 hours (3 days) without a Recordable case. There were no Days Away, Restricted, or Transferred (DART) cases and one Recordable case in January.


WRPS Project Performance - (\$k)										
	BCWS	BCWP	ACWP	SV	CV	SPI	CPI	BAC	EAC	VAC
CM	38,179.6	29,766.1	32,202.8	(8,413.5)	(2,436.7)	0.78	0.92			
FYTD	129,236.4	116,042.0	119,300.9	(13,194.4)	(3,258.9)	0.90	0.97	420,089.8	381,782.3	38,307.5
CTD	1,733,336.4	1,714,918.2	1,644,446.6	(18,418.2)	70,471.6	0.99	1.04	6,997,482.1	6,906,839.2	90,642.9

Red shaded cells indicates a SPI/CPI less than .90;
 Green shaded cells indicate a SPI/CPI between .90 and .99; and
 Blue shaded indicates a SPI/CPI greater than or equal to 1.0

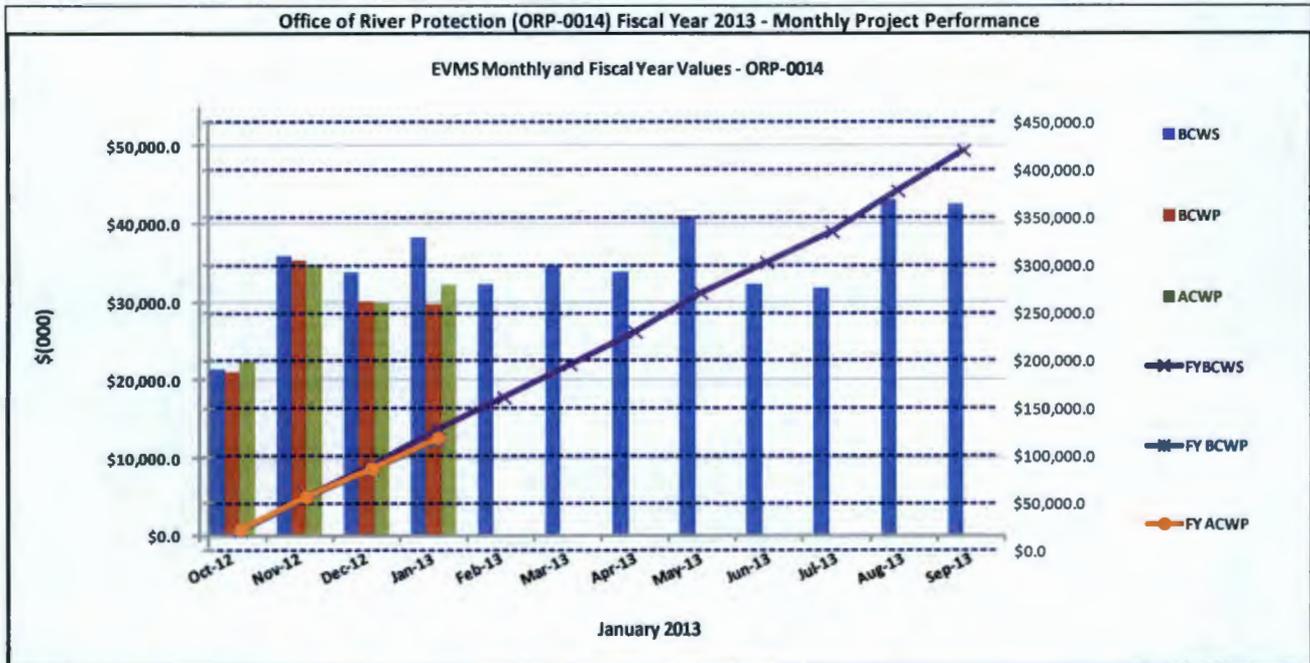

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct-12	\$21,350.5	\$20,911.7	\$22,382.9	0.98	0.93	\$21,350.5	\$20,911.7	\$22,382.9	0.98	0.93
Nov-12	\$35,910.8	\$35,319.2	\$34,775.1	0.98	1.02	\$57,261.3	\$56,230.9	\$57,158.0	0.98	0.98
Dec-12	\$33,795.4	\$30,044.9	\$29,940.1	0.89	1.00	\$91,056.7	\$86,275.8	\$87,098.1	0.95	0.99
Jan-13	\$38,179.6	\$29,766.1	\$32,202.8	0.78	0.92	\$129,236.3	\$116,041.9	\$119,300.9	0.90	0.97
Feb-13	\$32,248.7			0.00		\$161,485.0			0.00	
Mar-13	\$34,599.7			0.00		\$196,084.7			0.00	
Apr-13	\$33,773.8			0.00		\$229,858.5			0.00	
May-13	\$40,892.1			0.00		\$270,750.6			0.00	
Jun-13	\$32,288.5			0.00		\$303,039.1			0.00	
Jul-13	\$31,800.4			0.00		\$334,839.5			0.00	
Aug-13	\$42,997.4			0.00		\$377,836.9			0.00	
Sep-13	\$42,434.3			0.00		\$420,271.2			0.00	
CTD	\$1,733,336.4	\$1,714,918.2	\$1,644,446.6	0.99	1.04					

Office of River Protection (ORP-0014) Fiscal Year 2013 - Monthly Project Performance

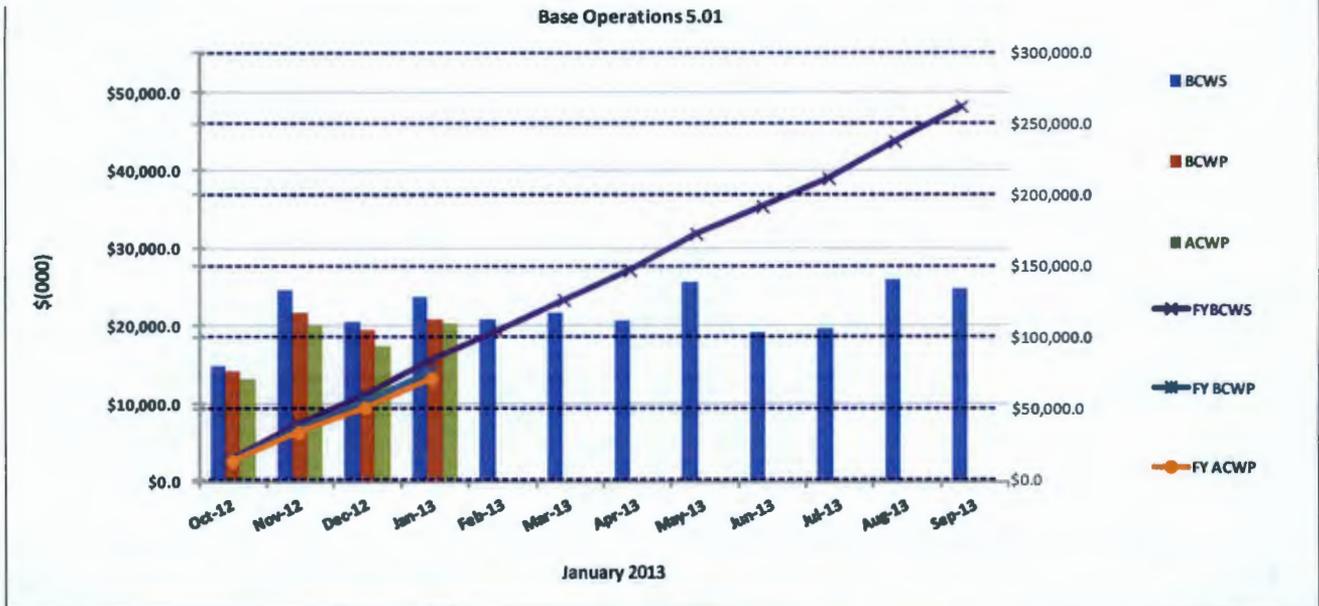

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FYBCWP	FYACWP	FY SPI	FY CPI
Oct-12	\$14,882.7	\$14,170.4	\$13,207.0	0.95	1.07	\$14,882.7	\$14,170.4	\$13,207.0	0.95	1.07
Nov-12	\$24,586.3	\$21,630.8	\$20,130.8	0.88	1.07	\$39,469.0	\$35,801.2	\$33,337.8	0.91	1.07
Dec-12	\$20,440.9	\$19,491.2	\$17,422.8	0.95	1.12	\$59,909.9	\$55,292.4	\$50,760.6	0.92	1.09
Jan-13	\$23,738.1	\$20,753.9	\$20,334.3	0.87	1.02	\$83,648.0	\$76,046.3	\$71,094.9	0.91	1.07
Feb-13	\$20,902.8			0.00		\$104,550.8			0.00	
Mar-13	\$21,758.8			0.00		\$126,309.6			0.00	
Apr-13	\$20,728.3			0.00		\$147,037.9			0.00	
May-13	\$25,607.5			0.00		\$172,645.4			0.00	
Jun-13	\$19,077.3			0.00		\$191,722.7			0.00	
Jul-13	\$19,634.2			0.00		\$211,356.9			0.00	
Aug-13	\$25,939.3			0.00		\$237,296.2			0.00	
Sep-13	\$24,820.9			0.00		\$262,117.1			0.00	
CTD	\$1,118,991.9	\$1,108,910.4	\$1,071,785.6	0.99	1.03					

Base Operations

Schedule Variance (\$2,984K):


The unfavorable schedule variance is primarily due to:

- DST Infrastructure Upgrades; 1) Three month delay in the release of design media and finalized locations for the electrical and thermocouple installation due to resource availability and increased checking requirements identified in the newly issued engineering procedures 2) delays in stimulant valve testing materials procurement due to limited quantity ordered, equipment failure during production and complexity of producing the material.
- AY/AZ Farm Infrastructure; Suspension of the Waste Feed Delivery Systems projects as a result of the leak in AY-102
- One System Engineering; Delays in the completion of the software development of the SmartPlant Foundation (SPF).

Cost Variance \$419K:

The favorable cost variance is primarily due to:

- Base Operations Farms A/AX/AY/AZ: Labor resources charging out to Tank Farm Projects in support of the 241-AY-102 biweekly annulus video and preparation and field work for AY-101, AZ-101 and AZ-102 annulus videos.
- Extent of Conditions Field Execution: Efficiencies experienced in the 100% annulus video inspections.

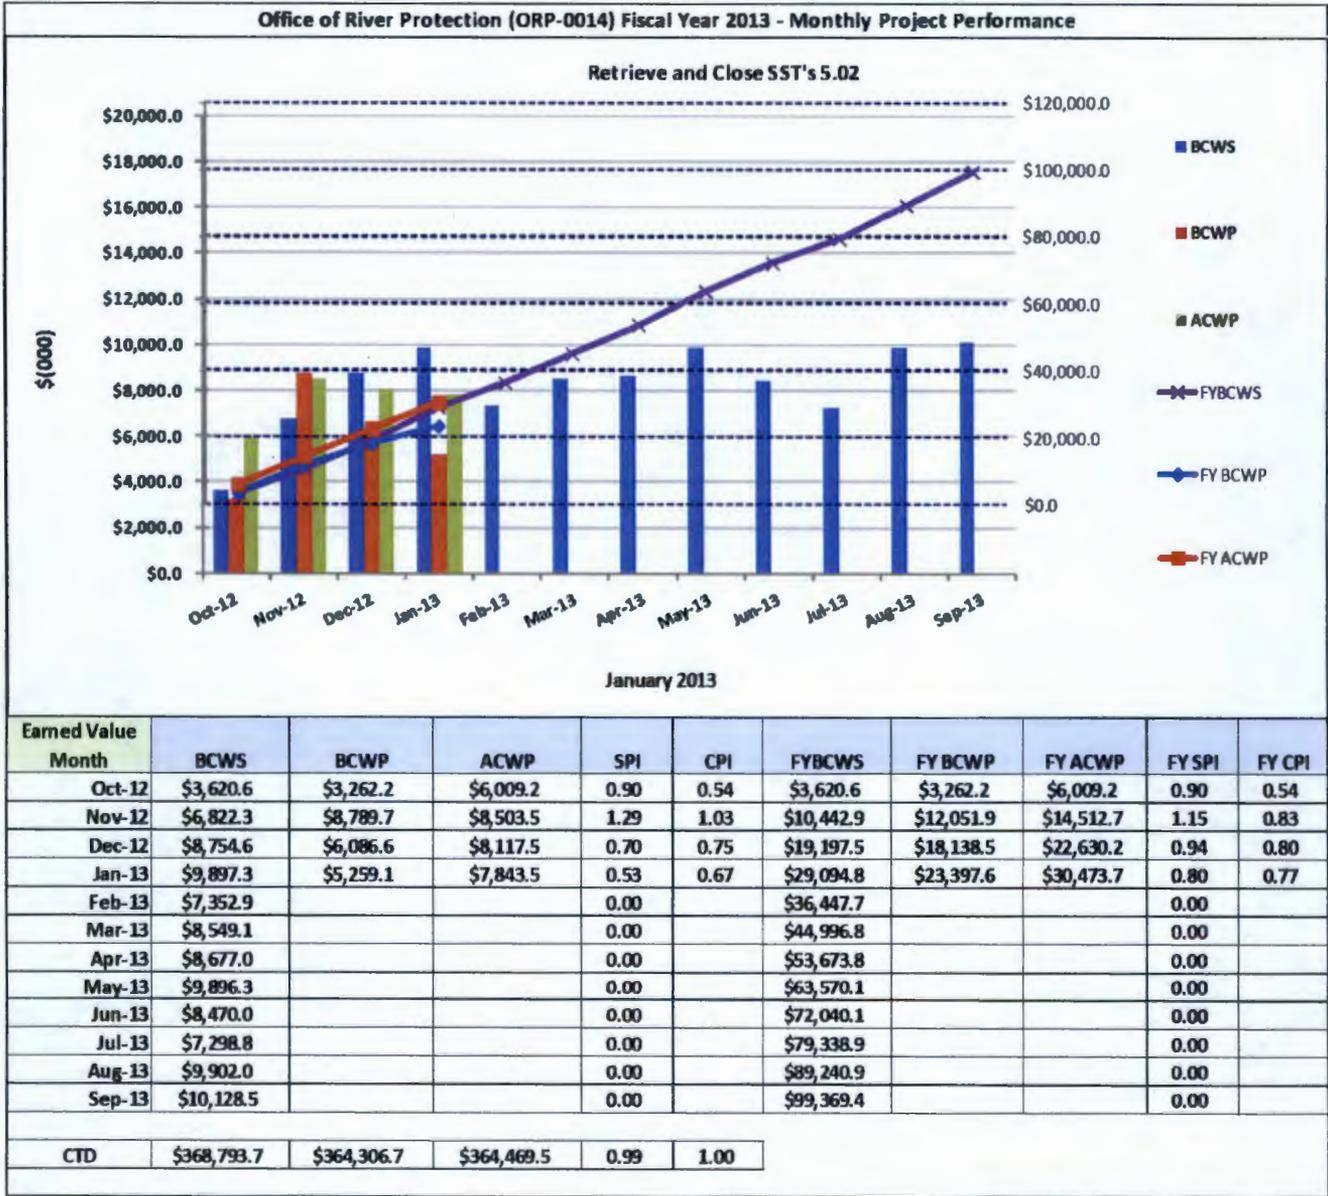

Single-Shell Tanks

Schedule Variance (\$4,638K):


The unfavorable schedule variance is primarily due to:

- Delays in retrieval of single-shell tank C-102
- Increased testing of the MARS Eductor to resolve cross filter plugging issues
- C-107 End Effector Repairs not anticipated
- Delayed replacement of the AN-106 supernate pump.
- Delay to the dome cut progress caused by a deferring profession opinion submitted and appealed.
- C-110 Hot Water Skid Procurement delay

Cost Variance (\$2,584K):

The unfavorable cost variance is primarily due to:

- Additional construction preparation and labor required at SST C-110
- Additional resources, material and subcontract due to hydraulic oil found in the AN-106 pump
- Increased testing of the MARS Educator
- Additional cost for SST C-105 dome cut preparations
- C-107 plugged fan nozzle and end effector repairs not anticipated
- C-112 additional Engineering for Caustic Addition
- Additional required C Farm Maintenance

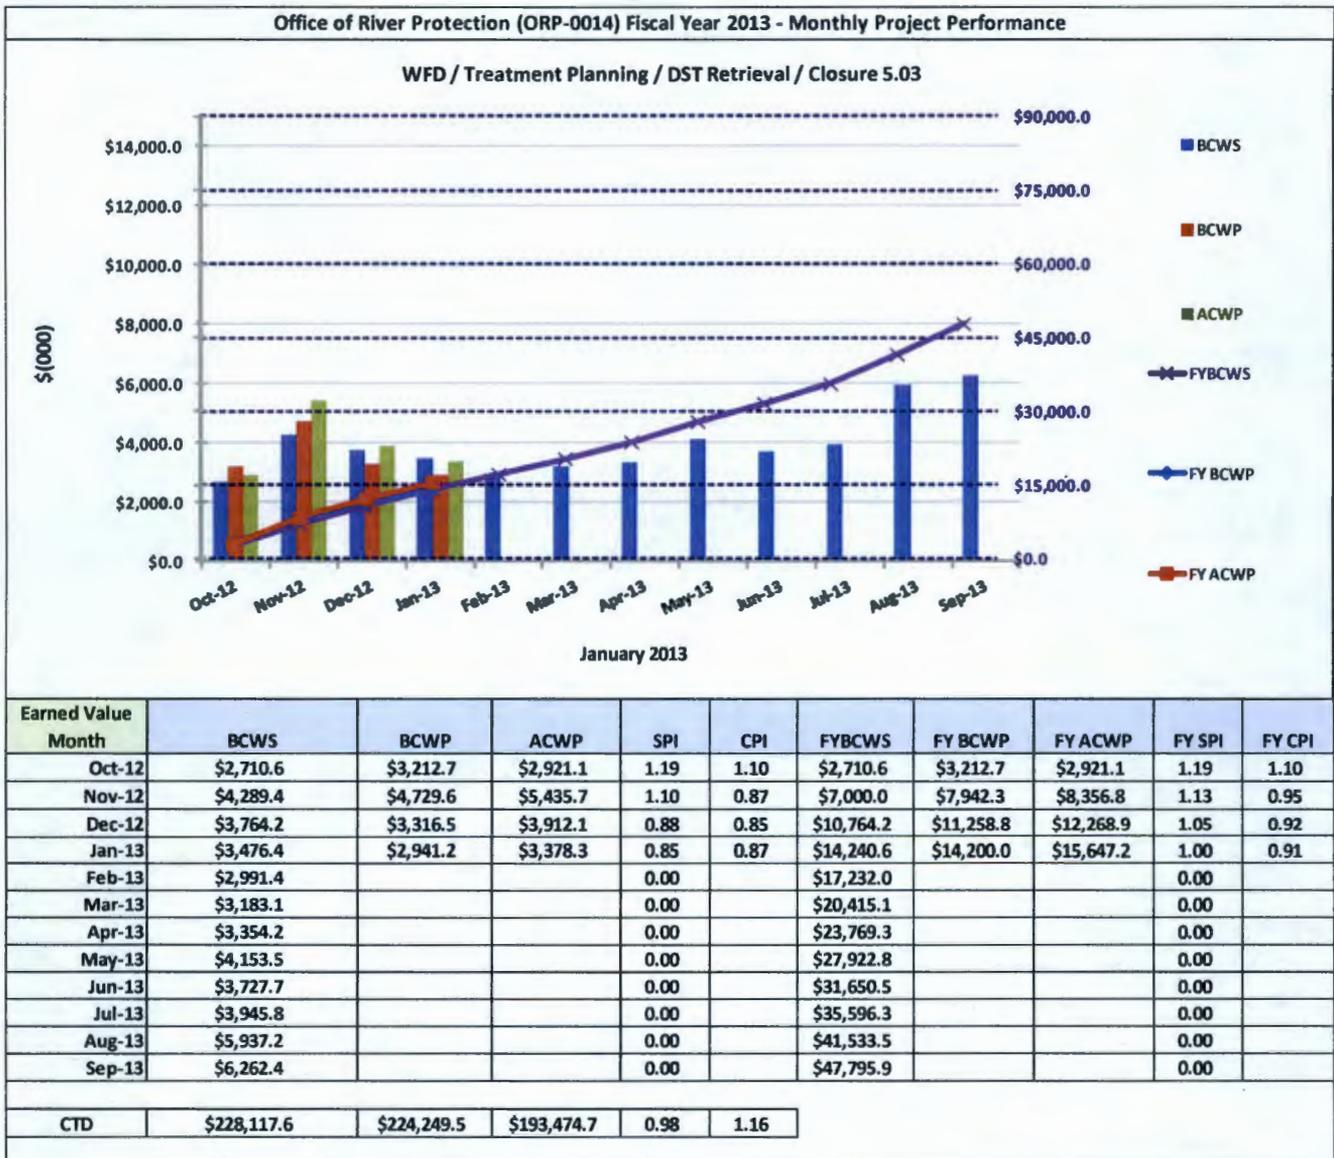

Waste Feed Delivery/Treatment/DST Retrieval Closure

Schedule Variance (\$535K):


The unfavorable schedule variance is primarily due to:

- RPP System Plan; Delays in identifying the scenarios that needs to be included in the update to System Plan 6 Addendum (SP6A).

Cost Variance (\$437K):

The unfavorable cost variance is primarily due to:

- WFD System Performance; Additional contract labor cost associated with the full-scale transfer pump limits-of performance testing and project support.

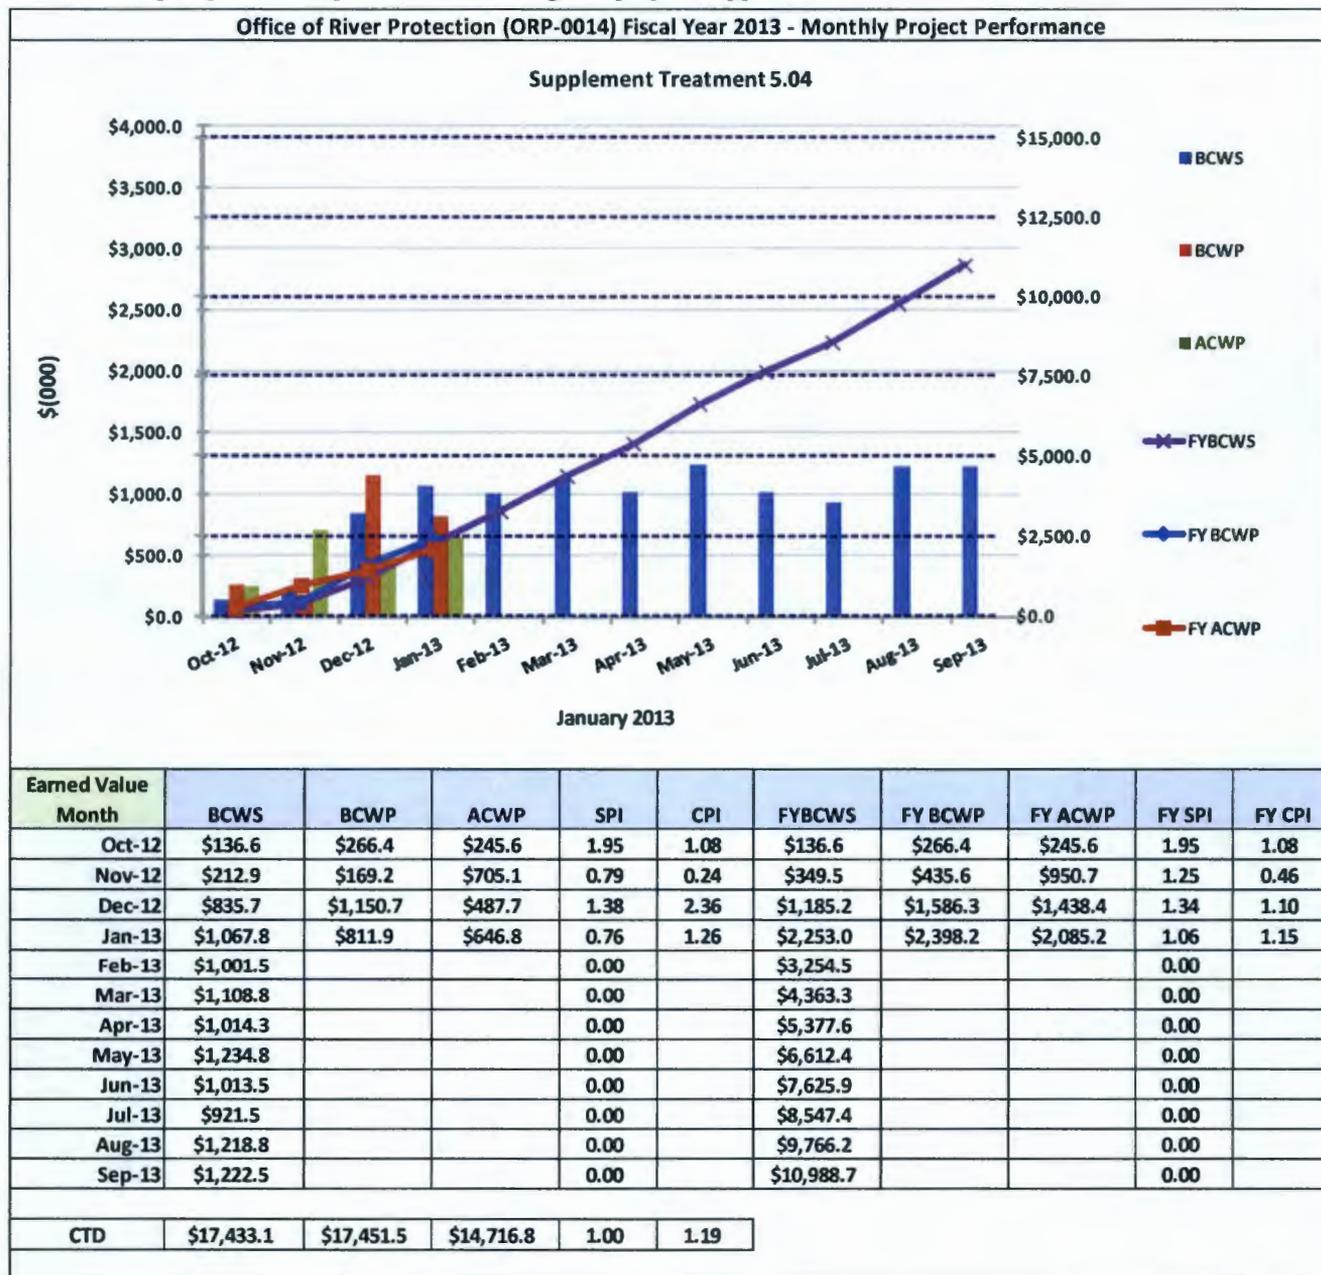

Supplemental Treatment

WBS 5.2 Retrieve and Close Single Shell Tanks

M-045-20, Submit Interim Measure Investigation Work Plan to Ecology, Due: 12/31/12, Status: Completed on 12/06/12. ORP will submit to Ecology for review and approval an interim measures investigation work plan for to vadose zone characterization at 241-TX Farm and 241-U Farm, and soil desiccation/contaminant removal proof-of-principal test at 241-SX Farm. The work plan will also be submitted with a TPA Change Package to establish milestone due date for M-045-22 and target dates for submittal of three secondary documents, see M-045-22-T01, -T02, and -T03. Added per TPA change package M-45-12-04. ORP submitted this work plan and a draft TPA change package for dates for M-045-22 and its targets on 12/06/12 via letter 12-TF-0054. Ecology responded via 12-NWP-190 authorizing ORP to begin field work while Ecology completed their review of the Work Plan. Ecology provided comments on the Work Plan in the January 2013 TPA Project Managers' meeting. Comments have been resolved and the Work Plan revised. The revised Work Plan and final TPA change package are being transmitted to Ecology.

M-045-21, Submit for Review and Approval a Sampling and Analysis Plan to Ecology for Soil Samples for 241-TX Tank Farm Investigation, Due: 03/31/13, Status: Completed on 03/11/13. Added per TPA change package M-45-12-04. The Sample Analysis Plan was finalized and was transmitted to Ecology via ORP letter 13-TF-0013 on 03/11/13.

M-045-22, Review M-045-22-T03 Report and Determine Path Forward, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule. This ORP/Ecology decision point will determine whether to continue with soil desiccation/contaminant removal testing and other interim measures, and if remaining work in Milestone M-045-92 should be modified. Added per TPA change package M-45-12-04. ORP submitted a draft TPA change package for dates for M-045-22 and its targets on 12/06/12 via letter 12-TF-0054.

M-045-22-T01, Submit Results of Vadose Zone Characterization of 241-TX to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-22-T02, Submit Results of Vadose Zone Characterization of 241-U to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-22-T03, Submit SX Soil Desiccation/Contaminate Removal Tech Results to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-56I, Complete Implementation of Agreed to Interim Measures, Due: 07/31/13, Status: On Schedule

M-045-59, Control surface water infiltration pathways as needed to control or significantly reduce the likelihood of migration of subsurface contamination to groundwater at the SST WMAS (pending the CMS report, milestone M-45-58, and implementation of other interim corrective measures), Due: TBD, Status: On Schedule

M-045-61, Submit to Ecology for review and approval as an Agreement primary document a Phase 2 RFI/CMS Report for WMA C, Due: 12/31/2014, Status: To Be Missed. Please see Issues.

M-045-62, Submit to Ecology for review and approval as an Agreement primary document a Phase 2 Corrective Measures Study Implementation Plan for WMA C, Due: 06/30/2015, Status: To Be Missed. Please see Issues.

M-045-92, DOE and Ecology will establish selection criteria for installation of additional interim barriers at additional WMAs (beyond the T-106 and TY barriers), Due: 09/30/2017, Status: On Schedule. This milestone date has been modified according to M-45-12-04 and the decision to move forward with construction/design of additional barriers dependent on discussions per M-045-22.

M-045-92N, Construct Barriers 1 and 2 in 241-SX Farm Due: 10/31/15, Status: On Schedule. The decision to move forward with construction/design of additional barriers is dependent on discussions per M-045-22.

M-045-92O, Submit a Final Design and Monitoring Plan for Interim Barrier 3 Due: 06/30/15, Status: On Schedule. The decision to move forward with construction/design of additional barriers is dependent on discussions per M-045-22.

Significant Past Accomplishments:

- Provided the interim measures investigation Work Plan for M-045-20 and draft TPA change package for M-045-22 and its targets via ORP letter 12-TF-0054 on 12/06/12.
- Automated data collection systems for T-Farm and TY Farm interim barrier monitoring continue gathering data.
- Ground penetrating radar was performed in C farm near the C-200s to support direct push work.
- Ground penetrating radar was performed in U farm, TX farm, and south of SX farm to support interim measures investigation described in the M-045-20 work plan.
- Direct push field work continues south of SX farm under the M-045-20 work plan.
- The Sample Analysis Plan for 241-TX Farm was finalized for transmittal to Ecology.

Significant Planned Actions in the Next Six Months:

- Revise the TY Interim Surface Barrier Monitoring Plan, per approved TPA Change Notice 2012-09.
- Transmit the Sample Analysis Plan for 241-TX Farm for M-045-21.
- Initiate direct push field work in TX farm under the M-045-20 work plan.
- Initiate electrical resistivity field work in U farm under the M-045-20 work plan.
- Perform direct push/electrical resistivity field work near the C-200 tanks per the WMA C Phase 2 RFI/CMS Work Plan.

SST Retrieval and Closure Program

M-045-82, Submit complete permit mod requests for Tiers 1, 2, & 3 of the SST, Due: 9/30/2015 Status: To Be Missed. Please see Issues.

M-045-84, Complete negotiations of TPA interim MS for closure of second WMA, Due: 1/31/2017, Status: On Schedule

M-045-83, Complete the closure of WMA C, Due: 6/30/2019, Status: On Schedule

M-045-85, Complete negotiations of TPA interim MS for closure of remaining WMAs, Due: 1/31/2022, Status: On Schedule

M-045-70, Complete waste retrieval from all remaining SSTs, Due: 12/31/2040, Status: On Schedule

M-045-00, Complete Closure of all Single Shell Tank Farms, Due: 1/31/2043, Status: On Schedule

M-045-86, Submit retrieval data report to Ecology for 19 tanks retrieved, Due: TBD (12 months after retrieval certification), Status: On Schedule. The CD Retrieval Completion Certification for SST Tank C-104 was sent to Ecology on 03/21/13 via ORP letter 13-TF-0018.

Significant Past Accomplishments:

- Completed post-retrieval sampling, analysis and reporting of results for tank C-108 in support of the M-045-86 retrieval data report.
- Completed post-retrieval sampling of tank C-104 in support of the M-045-86 retrieval data report.
- See discussions above and related discussions in Consent Decree report.

Significant Planned Activities in the Next Six Months:

- Perform post-retrieval logging of drywells near C-108 in support of the M-045-86 retrieval data report.
- Continue analysis of the post-retrieval samples from tank C-104.
- See discussions above and related discussions in Consent Decree report.

Issues:

The WMA-C performance assessment (PA) is not currently funded in fiscal year 2013. ORP has reported previously that the WMA-C PA would need to be funded by March 31, 2013 in order to maintain milestone schedule. As a result of the continued non-funding of the WMA-C PA, TPA Milestones M-045-61, M-045-62, and M-045-82 are now To Be Missed.

ORP began discussions with Ecology about a TPA project manager-level agreement to determine an alternative path forward for M-045-61 and M-045-62 on 03/14/13. ORP has provided a draft TPA project manager agreement for discussion at the next ORP/Ecology M-045-61/-62 meeting.

ORP and Ecology will meet separately to discuss TPA milestone M-045-82 for the Tier 1, 2, and 3 WMA C SST closure submittal. ORP and Ecology will discuss impacts to this work scope and the potential for a Tier 1 submittal.

Tank Waste Retrieval Work Plan (TWRWP) Status

Tank	TWRWP	Expected Revisions	Retrieval Technology	Second Technology	Third Technology
C-101	RPP-22520, Rev. 7	Complete	MRS (per 10/7/10 agreement, to be Modified Sluicing)	High-Pressure Water with ERSS	-
C-102	RPP-22393, Rev. 6A	In Process	Modified Sluicing	High-Pressure Water with ERSS	-
C-104	RPP-22393, Rev. 6A	Complete	Modified Sluicing	Chemical Dissolution	-
C-105	RPP-22520, Rev. 7	Complete	MARS-V	MARS-High Pressure Water	-
C-107	RPP-22393, Rev. 6A	Complete	MARS-S	MARS-High Pressure Water	-
C-108	RPP-22393, Rev. 6A	Complete	Modified Sluicing	Chemical Dissolution	-
C-109	RPP-21895, Rev. 5	Complete	Modified Sluicing	Chemical Dissolution	-
C-110	RPP-33116, Rev. 2	Complete	Modified Sluicing	Mechanical Waste Conditioning	High Pressure Water
C-111	RPP-37739, Rev. 1	In process	Modified Sluicing	None	-
C-112	RPP-22393, Rev. 6A	In process	Modified Sluicing	Chemical Dissolution	-

Significant Accomplishments:

None.

Significant Planned Activities in the Next 6 Months:

Work with Ecology on updates to, RPP-22520 and RPP-37739 for tanks C-105 and C-111.

Issues:

None.

Tank in Appendix H. Status - Single Shell Waste Retrieval Criteria

Tank 241-C-106

Significant Past Accomplishments:

None

Significant Planned Activities in the Next Six Months:

Continue U.S. Nuclear Regulatory Commission (NRC) review of the C-106 exception request. A Request for Additional Information (RAI) was received from the NRC in February 2009.

Issues:

It has been discussed with the NRC that much of the additional information requested is dependent upon development of C-Farm residual waste PA and, therefore, cannot be provided until the PA is published.

Tank Retrievals with Individual Milestones

Tank 241-A-103

M-045-15, Completion of Tank A-103 SST Waste Retrieval, Due: 9/30/22 Status: On schedule. Change package M-45-11-04 replaced tank S-102 with tank A-103 and changed to milestone completion date for M-045-15 to 09/30/2022.

M-045-15A, Embedded Milestone, Submit a Retrieval Data Report Pursuant to Agreement Appendix I, Due: 9/30/22, Status: On schedule. Updated with tank A-103 and due date of 9/30/22 per M-45-11-04 Change Package.

M-045-15D, Embedded Milestone, if appropriate, DOE will request an exception to waste retrieval criteria pursuant to Agreement Appendix H, Due: 9/30/22, Status: On Schedule. Updated with A-103 tank and due date of 9/30/22 per M-45-11-04 Change Package.

Significant Past Accomplishments:

Change Package M-45-11-04 was signed by ORP and Ecology on 04/19/11.

Significant Planned Activities in the Next Six Months and Issues:

None

Tank 241-S-112

M-045-13, Interim Completion of Tank S-112 SST Waste Retrieval and Closure Demonstration Project, Due: TBD (in accordance with M-045-84 or M-045-85), Status: On Schedule

M-045-13E, Complete Negotiations for Interim Milestones for Closure of S-112, Due: TBD Status: On Schedule as part of M-045-84 or M-045-85.

Significant Past Accomplishments:

Ecology letter of January 7, 2008, concurred with ORP that retrieval of Tank S-112 is complete.

Significant Planned Activities in the Next Six Months or Issues:

None.

WASTE TREATMENT AND IMMOBILIZATION PLANT (WTP) PROJECT

Number	Title	Due Date	Status
M-062-01Z	Submit Semi-Annual TPA Project Compliance Report	01/31/2013	Complete
M-062-01AA	Submit Semi-Annual TPA Project Compliance Report	7/31/2013	On Schedule

***SEE THE MARCH 2013 ORP CONSENT DECREE 08-5085-FVS
MONTHLY SUMMARY REPORT FOR WTP FACILITY-SPECIFIC
INFORMATION**
