

Office of River Protection



Monthly Reporting Period

December 1–December 31, 2020¹

¹ The narrative descriptions of progress in this report cover the reporting period. Information outside the reporting period may also be included for purposes of providing continuity or useful context. Information may be repeated in multiple sections of this report for continuity and clarity. Earned Value Management System data and descriptions cover the period through November 2020.

Topic	Page
Acronyms and Abbreviations	2
Administrative Items/Milestone Status.....	3
System Plan.....	7
Acquisition of New Facilities	9
Supplemental Treatment and Resource Conservation and Recovery Act Part B Permit Applications	11
Low-Activity Waste Pretreatment System.....	13
Tank-Side Cesium Removal System	14
242-A Evaporator Status.....	16
Liquid Effluent Retention Facility and 200 Area Effluent Treatment Facility.....	18
Tank System Update	21
Independent Qualified Registered Professional Engineer Activities.....	25
In-Tank Characterization and Summary	26
Single-Shell Tank Closure Program	29
Single-Shell Tank Retrieval Program	35
Tank Operations Contract Overview	36
Table 1 Administrative Record Metadata.....	46

Acronyms and Abbreviations

CD	critical decision
CERCLA	<i>Comprehensive Environmental Response, Compensation, and Liability Act</i>
COVID-19	coronavirus disease 2019
CMIP	corrective measures implementation work plan
CV	cost variance
DFLAW	direct-feed low-activity waste
DOE	U.S. Department of Energy
DSA	Documented Safety Analysis
DST	double-shell tank
Ecology	Washington State Department of Ecology
EPA	U.S. Environmental Protection Agency
ETF	Effluent Treatment Facility
FAT	factory acceptance testing
FY	fiscal year
HFFACO	<i>Hanford Federal Facility Agreement and Consent Order</i> (HFFACO and TPA are used interchangeably throughout this report)
IQRPE	independent, qualified, registered, professional engineer
LERF	Liquid Effluent Retention Facility
ORP	U.S. Department of Energy, Office of River Protection
PMR	Permit Modification Request
RCRA	<i>Resource Conservation and Recovery Act</i>
SST	single-shell tank
SV	schedule variance
TPA	Tri-Party Agreement
TSCR	Tank-Side Cesium Removal
WMA	waste management area
WTP	Waste Treatment and Immobilization Plant

Administrative Items/Milestone Status

Milestone	Title	Due Date	DOE PM	Status
Prior Years				
M-062-45-T01	Complete Negotiations 6-Months After Last Issuance of System Plan	04/30/2015	B. Harkins	In Dispute
M-062-45-ZZ	Negotiate a One-Time Supplemental Treatment Selection	04/30/2015	B. Harkins	In Dispute
M-062-45-ZZ-A	Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones	04/30/2015	B. Harkins	In Dispute
M-062-31-T01	Complete Final Design & Submit RCRA Part B Permit Mod Request for Enhanced WTP & Supplemental Treatment	04/30/2016	B. Harkins	In Dispute
M-062-32-T01	Start Construction of Supplemental Vitrification Facility and/or WTP Enhancements	04/30/2018	B. Harkins	In Dispute
M-045-59	Control Surface Water Infiltration Pathways as Needed	TBD ^a	B. Harkins	On Schedule
M-045-62	Submit the Draft Tier 3 Closure Plan with Corrective Measures in Phase 2 CMIP for WMA-C	TBD ^a	B. Harkins	On Schedule
M-045-83	Complete the Closure of WMA-C by Completing Closure Activities Specified in the Tier 2 Closure Plan	TBD ^a	B. Harkins	On Schedule
Fiscal Year 2021 (October 1, 2020 – September 30, 2021)				
M-045-92AD	Submit Yearly Reports Summarizing the Results of Maintenance and Performance Monitoring Activities	10/31/2020	B. Harkins	Complete
M-062-40H	Submit System Plan to Ecology	11/13/2020 ^b	M. Irwin	Complete
M-062-50	Submit to Ecology as a Secondary Document, a Mass Balance Flow	01/30/2021	B. Harkins	Complete

Milestone	Title	Due Date	DOE PM	Status
M-062-01AP	Submit Semi-Annual Project Compliance Report to Ecology	01/31/2021	G. Trenchard	On Schedule
M-090-14	Submit CD-1 for Facility to Store Spent Ion Exchange Columns Prior to DFLAW	3/31/2021	B. Harkins	Complete
M-062-45-A	Complete Negotiations 6-Months After Last Issuance of System Plan	4/30/2021	B. Harkins	On Schedule
M-062-33-T01	Complete Construction of Supplemental Treatment Vitrification Facility and/or WTP Enhancements	4/30/2021	B. Harkins	In Dispute
M-062-01AQ	Submit Semi-Annual Project Compliance Report to Ecology	07/31/2021	G. Trenchard	On Schedule
M-045-56Q	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)	07/31/2021	B. Harkins	On Schedule
M-045-91E4	Provide SST Farms Dome Deflection Surveys Every 2 Years to Ecology	09/30/2021	B. Harkins	On Schedule
M-045-97	Submit to Ecology a WMA Integration Study for WMA A/AX as a Primary Document	09/30/2021	B. Harkins	On Schedule
Fiscal Year 2022 (October 1, 2021 – September 30, 2022)				
M-045-92Y	Complete Construction of Barrier 3 in 241-TX Farm	10/31/2021	B. Harkins	On Schedule
M-045-92Z	Submit to Ecology Design for Barrier 4 in 241-U Farm	10/31/2021	B. Harkins	On Schedule
M-045-92AE	Submit Yearly Reports Summarizing the Results of Maintenance and Performance Monitoring Activities	10/31/2021	B. Harkins	On Schedule
M-062-45-XX	Complete Negotiations to Resolve Future Disputes M-062-45 Paragraphs 4 & 5	12/31/2021	B. Harkins	On Schedule
M-062-51-T01	Submit to Ecology, as a Primary Document, a Secondary Liquid Waste Disposition Work Plan	12/31/2021	B. Harkins	On Schedule

Milestone	Title	Due Date	DOE PM	Status
M-062-52-T01	Submit to Ecology, as a Primary Document, a Secondary Solid Waste Disposition Work Plan	12/31/2021	B. Harkins	On Schedule
M-045-85	Initiate Negotiations of HFFACO Interim Milestones for Closure of Remaining WMAs	1/31/2022	B. Harkins	On Schedule
M-045-92AA	Barrier 4 Design Approved by Ecology	1/31/2022	B. Harkins	On Schedule
M-062-01AR	Submit Semi-Annual Project Compliance Report to Ecology	1/31/2022	B. Trimberger	On Schedule
M-062-53A	Achieve Substantial Completion of EMF Construction	4/30/2022	W. Abdul	On Schedule
M-062-51-T02	Submit to Ecology, PMR for Redesign Upgrades and Ops to Support Volumes of Waste Types	5/15/2022	B. Harkins	On Schedule
M-062-52-T02	Submit to Ecology, PMR for Ancillary Facilities/Capabilities to Support Treatment of Secondary Waste	5/15/2022	B. Harkins	On Schedule
M-045-56R	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)	7/31/2022	B. Harkins	On Schedule
M-062-01AS	Submit Semi-Annual Project Compliance Report to Ecology	7/31/2022	B. Trimberger	On Schedule
M-045-15	Completion of Tank A-103 SST Waste Retrieval	9/30/2022	B. Harkins	On Schedule
M-045-98	Submit to Ecology a RFI/CMS Work Plan for WMA A/AX as a Primary Document	9/30/2022	B. Harkins	On Schedule
M-045-102	Submit to Ecology a Performance Assessment Maintenance Plan for the WMA A/AX PA	9/30/2022	B. Harkins	On Schedule
M-045-15A	Submit a Retrieval Data Report Pursuant to Agreement Appendix I	9/30/2022	B. Harkins	On Schedule

Milestone	Title	Due Date	DOE PM	Status
M-045-15D	Submit, if appropriate, an exception to Waste Retrieval Criteria Pursuant to Agreement Appendix H	9/30/2022	B. Harkins	On Schedule

^a To be established in accordance with the date identified in the M-045-82 Tier 2 closure plan.

^b DOE and Ecology agreed to an extension until November 13, 2020, for submission of System Plan Rev. 9.

CD	=	critical decision	PM	=	project manager
CMIP	=	corrective measures implementation work plan	RCRA	=	<i>Resource Conservation and Recovery Act</i>
DFLAW	=	direct-feed low-activity waste	SST	=	single-shell tank
DOE	=	U.S. Department of Energy	TBD	=	to be determined
Ecology	=	Washington State Department of Ecology	TSCR	=	Tank-Side Cesium Removal
HFFACO	=	<i>Hanford Federal Facility Agreement and Consent Order</i>	WMA-C	=	C Tank Farm waste management area
Mod	=	modification	WTP	=	Waste Treatment and Immobilization Plant

System Plan

Responsible Assistant Manager: Mat Irwin
Technical Lead: Kaylin Burnett
Ecology Project Manager: Dan McDonald, Jeff Lyon

M-062-40H Submit System Plan to Ecology

Due: November 13, 2020²

Status: Complete

M-062-45-A Complete Negotiations 6-Months after Last Issuance of System Plan

Due: April 30, 2021

Status: On schedule

Significant Past Accomplishments

- The U.S. Environmental Protection Agency (EPA), U.S. Department of Energy (DOE), and Washington State Department of Ecology (Ecology) met in the first mediated session of the “Holistic Negotiations” on June 25, 2020. There was one negotiation session held in December.
- On November 13, 2020, DOE transmitted the final *River Protection Project System Plan*, Rev. 9, to Ecology per letter 20-ORP-0016, “Transmittal of the River Protection Project System Plan, Revision 9.”

Significant Planned Actions in the Next Six Months

- Discuss disputes with regard to Milestone M-062-45 and its associated milestones during “Holistic Negotiations.”

Issues

- Ecology and DOE Office of River Protection (ORP) have ended negotiations related to the M-062-45 Milestone and have initiated dispute. “Holistic Negotiation” mediated sessions began in June 2020 to resolve these disputes.
- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing Coronavirus Disease 2019 (COVID-19) concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as

² DOE and Ecology agreed to an extension until November 13, 2020, for submission of System Plan, Rev. 9.

implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.

- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the Tri-Party Agreement (TPA), and if other actions may be necessary.

Acquisition of New Facilities

Tank Farms Assistant Manager: Brian Harkins (Acting)
Technical Lead: Janet Diediker
Ecology Project Manager: Dan McDonald, Jeff Lyon

M-090-13	CD-1³ for Interim Hanford Storage Project and CR for CD-2 to ECY⁴
Due:	September 30, 2025
Status:	On schedule
M-090-00	Acquire/Modify Facilities for Storage of First Two Years of IHLW⁵ from the WTP⁶ Operations
Due:	December 31, 2036
Status:	On schedule
M-047-00	Completion of Work for Management of Secondary Waste from the WTP
Due:	To be determined
Status:	On schedule

Significant Past Accomplishments

- Completed M-090-14 Milestone, “Submit CD-1 for Facility to Store Spent Ion Exchange Columns Prior to DFLAW⁷.” ORP transmitted letter 20-ECD-0050, “Submittal of CD-1 for Facility to Store Spent Ion Exchange Columns Prior to Direct Feed Low-Activity Waster Tri-Party Agreement Milestone M-090-14,” on October 23, 2020, to Ecology.

Significant Planned Actions in the Next Six Months

- None.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as

³ CD denotes critical decision.

⁴ ECY denotes Washington State Department of Ecology.

⁵ IHLW denotes immobilized high-level waste.

⁶ WTP denotes Waste Treatment and Immobilization Plant.

⁷ DFLAW denotes direct-feed low-activity waste.

implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.

- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Supplemental Treatment and Resource Conservation and Recovery Act Part B Permit Applications

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Ricky Bang

Ecology Project Manager: Dan McDonald

The current status for each of the projects listed below, unless noted differently, is:

In Dispute. Ecology and ORP have ended negotiations related to the M-062-45 Milestone and have initiated dispute. Therefore, the status of the milestones below has changed to “In Dispute.”

M-062-45-T01 Complete Negotiations 6-Months after Last Issuance of System Plan
Due: April 30, 2015

M-062-45-ZZ Negotiate a One-Time Supplemental Treatment Selection
Due: April 30, 2015

M-062-45-ZZ-A Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones
Due: April 30, 2015

**M-062-31-T01 Complete Final Design and Submit RCRA⁸ Part B Permit
Modification Request for Enhanced WTP & Supplemental Treatment**
Due: April 30, 2016

**M-062-32-T01 Start Construction of Supplemental Vitrification Facility and/or WTP
Enhancements**
Due: April 30, 2018

**M-062-33-T01 Complete Construction of Supplemental Treatment Vitrification
Facility and/or WTP Enhancements**
Due: April 30, 2021

**M-062-45-XX Complete Negotiations to Resolve Future Disputes M-062-45,
Paragraphs 4 and 5**
Due: December 31, 2021
Status: On schedule

**M-062-34-T01 Complete Hot Commissioning of Supplemental Treatment
Vitrification Facility and/or WTP Enhancements**
Due: December 30, 2022

**M-062-21 Annually Submit Data Which Demonstrates Operation of the WTP at
a Rate Sufficient to Meet M-062-00**
Due: February 28, 2023
Status: At risk

⁸ RCRA denotes *Resource Conservation and Recovery Act*.

M-062-00 Complete Pretreatment Processing and Vitrification of HLW⁹ and LAW¹⁰ Tank Wastes

Due: December 31, 2047

Status: At risk

Significant Past Accomplishments

- None.

Significant Planned Actions in the Next Six Months

- See the “System Plan” section, above, for updates related to the M-062-45 Milestone negotiations.

Issues

- Ecology and ORP have ended negotiations related to the M-062-45 Milestone and have initiated dispute. “Holistic Negotiation” mediated sessions began in June 2020 to resolve these disputes.
- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

⁹ HLW denotes high-level waste.

¹⁰ LAW denotes low-activity waste.

Low-Activity Waste Pretreatment System

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Janet Diediker

Ecology Project Manager: Dan McDonald

Significant Past Accomplishments

- Completed M-062-50 Milestone, “Submit as a Secondary Document, a Mass Balance Flow.” ORP transmitted letter 20-ECD-0057, “Completion of Tri-Party Agreement Milestone M-062-50,” on December 4, 2020, to Ecology.

Significant Planned Actions in the Next Six Months

- None.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Tank-Side Cesium Removal System

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Janet Diediker

Ecology Project Manager: Dan McDonald

This section only covers the Tank Farms Project scope of the DFLAW mission. Please refer to the Consent Decree monthly report for the WTP project scope pertaining to DFLAW.

Significant Past Accomplishments

- Completed Tank AP-107 conduit run.
- Completed Tank-Side Cesium Removal (TSCR) wiring tie-ins and piping insulation to prepare for power-up.
- Completed ultrasonic testing of primary piping welds for SN-637 and SN-700 routing between W-211 portions of piping and ICD-30/31.
- Placed the first six SN-637 transfer line spools into the trench at AP Tank Farm, routing between the AP-06A pit to outside the tank farm fence.

Significant Planned Actions in the Next Six Months

- ORP will review the Documented Safety Analysis (DSA) addendum, Technical Safety Requirements, and TSCR Readiness Plan of Action for approval.
- Receive the *Resource Conservation and Recovery Act* (RCRA) Permit from Ecology.
- Complete TSCR construction activities and commence readiness activities.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.

- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

242-A Evaporator Status

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Paul Hernandez

Ecology Project Manager: Jeff Lyon

The 242-A Evaporator campaign strategy is identified in the following table:

Fiscal Year	Campaign No.	Feed Source	Slurry Tank	Comments
TBD	EC-11	N/A	N/A	Per DOE direction, cold runs will not be used to maintain 242-A Evaporator readiness, staff proficiency, and cycle idle equipment while transfer lines are being replaced.

DOE = U.S. Department of Energy

TBD = to be determined

N/A = not applicable

Significant Past Accomplishments

- Completed replacement of the 242-A Failed Sock Filter assembly.
- Completed 100 percent design for the 242-A Evaporator transfer line replacement.
- Continued wall nozzle fabrication for the 242-A Evaporator slurry and feed transfer line replacement.
- Completed actuator fabrication and functional testing.
- Completed work on the resolution of the universal joint potential inadequacy in the safety analysis. Universal joint testing was completed, and the vendor has incorporated the new universal joints into the calculations, engineering change notices, and drawings.
- Completed work on the resolution of the buried pipe potential inadequacy in the safety analysis. The calculations for Nuclear Safety to perform the safety basis amendment were completed.
- Completed development of the 100 percent engineering design for the 242-A Evaporator DSA upgrades.
- 242-A Evaporator DSA upgrades hardware and software procurement initiated.
- Completed AW-B pit work and excavation for wall nozzle installation in support of 242-A Evaporator transfer line replacement.
- Installed new wall nozzle in the AW-B pit in support of the new 242-A Evaporator slurry line and feed transfer lines.
- Completed 242-A K1 Ventilation Continuous Air Monitor calibration and functional test.
- Completed 242-A overhead crane preventive maintenance to support slurry line replacement.

- Completed replacement of the third, and final, set of pre-filters on the building exhaust plenums.

Significant Planned Actions in the Next Six Months

- Procure new PB-1 and PB-2 replacement pumps
- Initiate DSA safety system upgrades construction phase
- Complete wall nozzle fabrication for the 242-A Evaporator slurry and feed transfer line replacement
- Initiate 242-A Ventilation Control System upgrades
- Install new wall nozzles in the AW-02E, and AW-02A pits in support of the new 242-A Evaporator slurry line and feed transfer lines.

Issues

- Initial testing revealed an issue with the original universal joints on the actuators used to drive the tank farm double isolation valves. A potential inadequacy in the safety analysis was written. Testing of different universal joints was completed, and the vendor has incorporated the new universal joints into the calculations, engineering change notices, and drawings.
- Following universal joint determination, 92 universal joints/actuators will need to be replaced. Project team and facility operations personnel are initiating phased planning of replacement to support tank transfer operations.
- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Liquid Effluent Retention Facility and 200 Area Effluent Treatment Facility

Tank Farms Assistant Manager: Brian Harkins (Acting)
Technical Lead: Richard Valle
Ecology Project Manager: John Temple, Dan McDonald (for milestones)

M-062-51-T01 Submit to Ecology, as a Primary Document for Approval a Secondary Liquid Waste Disposition Work Plan

Due: December 31, 2021
 Status: On schedule

M-062-51-T02 Submit Permit Modification Request for Redesign Upgrades And Operations to Support Volumes of Waste Types Expected

Due: May 15, 2022
 Status: On schedule

M-062-51 Achieve Substantial Completion of LERF¹¹/ETF¹² Construction Upgrades Necessary for LAW Hot Commissioning

Due: April 15, 2023
 Status: On schedule

Significant Past Accomplishments

- Total fiscal year (FY) 2021 processing volume: approximately 1.63 million gallons
- Began final design for the ETF supplemental organic treatment system (i.e., acetonitrile treatment)
- Began conceptual design of the ETF modular grout system
- Began conceptual design of the ETF brine storage tanks
- Completed conceptual design of the ETF carbon dioxide membrane contactors
- Began conceptual design of the ETF motor control center upgrade
- Completed conceptual design of the ETF freeze protection upgrade.

Significant Planned Actions in the Next Six Months

- Complete waste processing operations to reduce LERF Basin 42 to minimum liquid level
- Complete design of the ETF supplemental organic treatment system (i.e., steam stripper) to provide the capability to treat the WTP DFLAW effluent
- Complete design of the ETF modular grout system to provide the onsite capability to stabilize the WTP DFLAW effluent

¹¹ LERF denotes Liquid Effluent Retention Facility.

¹² ETF denotes Effluent Treatment Facility.

- Complete design of the ETF brine storage tanks to provide the capacity to manage the WTP DFLAW effluent
- Complete design of the ETF carbon dioxide membrane contactors to provide the capability to treat the WTP DFLAW effluent
- Complete design of the ETF motor control center upgrade to address the deficient condition and provide additional capability for ongoing upgrade projects
- Complete design of the ETF freeze protection upgrade as systems have become degraded and many replacement parts are considered obsolete
- Receive material procurements for the ETF Monitoring and Control System, Ultraviolet/Oxidation, Redundant Filtration, and Vessel Off-gas system upgrade projects.

Issues

- Work has paused on the LERF Basin 44 cover replacement project while nuclear safety evaluations are performed by Washington River Protection Solutions, LLC and ORP. Evaluations are being performed due to visual indication of solid material in the basin and sample results from that material. ORP has provided approval to implement the approach that will pump down the remaining volume in LERF Basin 44 to perform a radiological analysis of the solids.
- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Liquid Effluent Retention Facility Volumes

LERF liquid levels, inventory, and received waste are shown in the table below. Volumes in the table are estimated.¹³

Description	242AL-42 (Basin 42)	242AL-43 (Basin 43)	242AL-44 (Basin 44)
AZ-301 Condensate	-	-	-
Mixed Waste Trench 31 and 34	+ 2,000	-	-
Other ^a	-	-	-
Processing Campaign(s)	- 897,000	-	-
Total Volume	1,631,000	6,518,000	768,000

^a 325 retention process sewer.

Data Date: December 31, 2020.

Values shown in gallons.

¹³ The volume in each LERF basin is calculated from liquid level sensor readings. Therefore, based on sensor fluctuations and/or environmental effects (e.g., precipitation, temperature), values for basin volumes may vary slightly from the net inputs and outputs shown for the basin.

Tank System Update

Tank Farms Assistant Manager: Brian Harkins (Acting)
Technical Lead: Dustin Stewart
Ecology Project Manager: Jeff Lyon, Nina Menard

Reports are identified as completed (internal access only) or released (external access).

M-045-91E4 Provide SST¹⁴ Farms Dome Deflection Surveys Every 2 Years to Ecology

Due: September 30, 2021
 Status: On schedule

M-045-91K Complete Initial Baseline Visual Inspections of all SSTs

Due: September 30, 2023
 Status: On schedule

M-045-91K-T01 Submit Report of the Initial Baseline Visual Inspection of all SSTs Remaining to be Inspected

Due: March 31, 2024
 Status: On schedule

M-045-91L Obtain Assessment Reviewed/Certified by an IQRPE¹⁵ Attesting to SST Structural Integrity

Due: September 30, 2034
 Status: On schedule

Double-Shell Tank Integrity

Significant Past Accomplishments

- Released RPP-RPT-34311, *Double-Shell Tank Integrity Inspection Report for 241-AY Tank Farm*, in December 2020
- Completed fieldwork for nine of nine enhanced annulus visual inspections in FY 2021:
 - Tank 241-AP-101
 - Tank 241-AP-102
 - Tank 241-AP-103
 - Tank 241-AP-104
 - Tank 241-AP-105
 - Tank 241-AP-106

¹⁴ SST denotes single-shell tank.

¹⁵ IQRPE denotes Independent Qualified Registered Professional Engineer.

- Tank 241-AP-107
- Tank 241-AP-108
- Tank 241-AY-101.
- Completed ultrasonic testing at 241-AW-105 Double-Shell Tank (DST)
- Completed mobilization for ultrasonic testing at 241-AW-104 DST.

Significant Planned Actions in the Next Six Months

- Draft report for Tank 241-AW-105 ultrasonic testing inspection
- Complete the FY 2021 ultrasonic testing inspections at Tanks 241-AW-104 and 241-AP-103
- Complete report development for the nine DST annulus visual inspections performed in FY 2021
- Complete fabrication/receipt of Southwest Research Institute Guided Wave system.

Ultrasonic Testing Report Status

- Tank 241-AW-106 ultrasonic testing is in release process with projected release in February 2021
- Tank 241-AW-105 ultrasonic testing report is in the drafting phase with release projected in March 2021.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Single-Shell Tank Integrity

Significant Past Accomplishments

- Performed TFC-ENG-CHEM-P-57, *Intrusion Notification and Tank Leak Assessment Process*, on the following tanks in FY 2021:
 - Tank 241-TX-113.
- Visual inspections for CHEM-P-57 tank leak assessment:
 - Tank 241-B-109 (completed September 2020).
- Completed work package planning for visual inspection of five miscellaneous underground storage tanks
- Completed the in-tank laser scan for dome spalling extent of condition, as a result of Tank 241-SX-112 findings in February 2020:
 - Tank 241-SX-112 Leica laser scan (August 2020)
 - Tank 241-SX-111 Leica laser scan (September 2020)
 - Tank 241-SX-109 Leica laser scan (September 2020).
- Visual inspections were completed for the following tanks:
 - Tank 241-B-106 (completed November 2020)
 - Tank 241-B-108 (completed December 2020)
 - Tank 241-BY-112 (completed December 2020).

Significant Planned Actions in the Next Six Months

- Perform TFC-ENG-CHEM-P-57 on Tank 241-B-109 (in progress)
- Perform FY 2021 visual inspections of SSTs: 241-BY-108, 241-BY-104, 241-S-102, 241-S-112, 241-TY-101, 241-U-108, 241-U-110, 241-U-112, 241-U-201, 241-U-202, 241-U-203, and 241-U-204.

Issues

- Tank 241-SX-112 was inspected visually in late February 2020. The concrete dome was inspected fully, and there were three spots of spalled concrete in the dome. While there have been past inspections of the tank, they did not include the full dome; and this was the first inspection to reflect the spalling. There was no evidence of structural issues; however, the dome loading is being limited to current levels until further analysis is complete. The full analysis may take several months to complete, but a structural analysis contract is in place with the Pacific Northwest National Laboratory. Tank 241-SX-112 was inspected visually again in late July. The inspection did not identify any changes in the condition of the spalled locations. Concrete was noted on the waste surface under the spalled locations, suggesting that the spalling took place after 1969 when the tank was

pumped and taken out of service. On August 17, 2020, a laser scan of Tank 241-SX-112 was performed to assist with analysis of dome spalling. Tank 241-SX-112 analysis is ongoing.

- Tank 241-SX-109 was inspected visually in late July 2020. Spalled concrete was identified in the northeast portion of the tank dome next to a rectangular construction manhole. Additional small/shallow spalling locations, similar to those in Tank 241-SX-112, were noted on the tank dome. Concrete was noted on the waste surface and, comparing to past visual inspections, suggests that the spalling occurred post-1996. In September 2020, a laser scan of Tank 241-SX-109 was also performed to assist with analysis of dome spalling. Tank 241-SX-109 analysis is ongoing.
- Tank 241-SX-108 was inspected visually in early August 2020. Minor spalled concrete was identified on the tank dome.
- Tank 241-SX-111 was inspected visually in mid-August 2020. Spalled/Cracked concrete was identified in various locations on the tank dome. Concrete was noted on the waste surface and, when comparing to past visual inspections, suggests that the spalling occurred post-1987. On September 1, 2020, a laser scan of Tank 241-SX-111 was performed. Review of the laser scan results identified a new spalling location since the visual inspection.
- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Independent Qualified Registered Professional Engineer Activities

DST System:

- RPP-RPT-58441, *Double-Shell Tank System Integrity Assessment Report (DSTAR)*, Rev. 1, was completed in 2016
- The IQRPE recommended the next DST system integrity assessment report be completed in 10 years.

SST System:

- Completed M-045-9II Milestone report RPP-IQRPE-50028, *Single-Shell Tank System Structural Integrity Assessment Report*, in 2018
- The IQRPE recommended the next SST structural integrity assessment be completed in 16 years. Ecology transmitted letter 19-NWP-009, “*Single-Shell Tank Structural Integrity Assessment, RPP-IQRPE-50028*,” on January 16, 2019. The letter noted Ecology’s agreement with the IQRPE’s 16-year recommendation.

242-A Evaporator:

- Completed RPP-RPT-60098, *242-A Evaporator System Integrity Assessment Report*, Rev. 0, in 2018
- The IQRPE recommended the next 242-A Evaporator system integrity assessment be completed in 15 years. Ecology transmitted letter 18-NWP-114, “Department of Ecology’s (Ecology’s) Comments on the *242-A Evaporator System Integrity Assessment Report, RPP-RPT-60098, Revision 0*,” on July 19, 2018. The letter noted Ecology’s disagreement with the IQRPE’s 15-year recommendation. The Hanford Sitewide permit, Rev. 8C, currently provides for 242-A Evaporator system integrity assessments at a frequency of 10 years. ORP will continue to comply with the permit condition.

ETF:

- Completed RPP-IQRPE-50043, *Effluent Treatment Facility (ETF) IQRPE Integrity Assessment*, in 2019
- The IQRPE recommended the next ETF integrity assessment be completed in 10 years.

219-S Tank System:

- Completed RPP-IQRPE-50029, *219-S Integrity Assessment Report*, in February 2020
- The IQRPE recommended the next 219-S Tank system integrity assessment be completed in 20 years.

In-Tank Characterization and Summary

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Dustin Stewart

Ecology Project Manager: Jeff Lyon

Reports Completed or Released

For December 2020, the following reports were completed (internal access only) or released (external access):

- Completed:
 - RPP-RPT-60128, *Derivation of Best-Basis Inventory for Tank 241-BX-109 as of November 1, 2020*, Rev. 1
 - RPP-RPT-59883, *Derivation of Best-Basis Inventory for Tank 241-BX-112 as of November 1, 2020*, Rev. 1
 - RPP-RPT-59519, *Derivation of Best-Basis Inventory for Tank 241-T-105 as of November 1, 2020*, Rev. 1
 - RPP-RPT-44752, *Derivation of Best-Basis Inventory for Tank 241-BY-103 as of November 1, 2020*, Rev. 4
 - RPP-RPT-60106, *Derivation of Best-Basis Inventory for Tank 241-B-107 as of November 1, 2020*, Rev. 1
 - RPP-RPT-58699, *Derivation of Best-Basis Inventory for Tank 241-TX-108 as of November 1, 2020*, Rev 3
 - RPP-RPT-58727, *Derivation of Best-Basis Inventory for Tank 241-TX-114 as of October 1, 2020*, Rev. 2
 - RPP-RPT-46772, *Derivation of Best-Basis Inventory for Tank 241-AN-107 as of October 1, 2020*, Rev. 5.
- Released:
 - HNF-EP-0182, *Waste Tank Summary Report for Month Ending October 31, 2020*, Rev. 394.

Tank Sampling

Significant Past Accomplishments

For December 2020, the following tank sampling was conducted:

- Performed Tank 241-AN-106 core sampling segments 18, 19-1, 19-2, 20, and 21-1; and shipped to 222-S Laboratory
- Performed Tank 241-AP-107 second large-volume grab sampling on December 3, 2020. Eighteen liquid grab samples were obtained and shipped to Pacific Northwest National Laboratory for testing.

Significant Planned Actions in the Next Six Months

- Complete Tank 241-AN-106 core sampling January 2021
- Tank 241-AP-107 large-volume liquid grab sampling is planned for February 2021
- Tank 241-AN-106 liquid grab sampling is planned for January 2021
- Catch Tank C-301 grab sampling is planned for March 2021.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Best-Basis Inventory Updates

Significant Past Accomplishments

- Best-basis inventory updates for the following tanks were completed in November 2020:
 - Tank 241-AN-107
 - Tank 241-B-107
 - Tank 241-BX-109
 - Tank 241-BX-112
 - Tank 241-BY-103
 - Tank 241-T-105
 - Tank 241-TX-108
 - Tank 241-TX-114.

Significant Planned Actions in the Next Month

- Best-basis inventory updates for the following tanks are currently planned to be completed in January 2021:
 - None.

Issues

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition, protective of the community, the region, and the environment.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Single-Shell Tank Closure Program

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Rod Lobos

Ecology Project Manager: Jeff Lyon

M-045-59 Control Surface Water Infiltration Pathways as Needed

Due: To be determined. Will be implemented if needed to control or significantly reduce the likelihood of migration of subsurface contamination to groundwater at the SST waste management areas (WMAs) (pending the corrective measures study report, M-45-58 Milestone, and implementation of other interim corrective measures).

Status: On schedule

M-045-62 Submit the Draft Tier 3 Closure Plan with Corrective Measures in Phase 2 Corrective Measures Implementation Work Plan (CMIP) for WMA-C¹⁶

Due: To be determined. To be established in accordance with the date identified in the M-45-82 Milestone Tier 2 closure plan.

Status: On schedule

M-045-83 Complete the Closure of WMA-C by Completing Closure Activities Specified in the Tier 2 Closure Plan

Due: To be determined. To be established in accordance with the date identified in the M-45-82 Milestone Tier 2 closure plan.

Status: On schedule

M-045-92AD Submit Yearly Reports Summarizing the Results of Maintenance and Performance Monitoring Activities

Due: October 31, 2020

Status: Completed October 7, 2020

M-045-97 Submit to Ecology as a Primary Document a Waste Management Area Integration Study for WMA A/AX as described in HFFACO¹⁷ Appendix I.2.1.1

Due: September 30, 2021

Status: On schedule

M-045-92Y Complete Construction of Barrier 3 in 241-TX Farm

Due: October 31, 2021

Status: On schedule

M-045-92Z Submit to Ecology Design for Barrier 4 in 241-U Farm

Due: October 31, 2021

¹⁶ WMA-C denotes C Tank Farm waste management area.

¹⁷ HFFACO denotes *Hanford Federal Facility Agreement and Consent Order*.

Status:	On schedule
M-045-92AA	Barrier 4 in 241-U Farm Design Approved by Ecology
Due:	January 31, 2022
Status:	On schedule
M-045-85	Initiate Negotiations of HFFACO Interim Milestones for Closure of Remaining WMAs
Due:	January 31, 2022
Status:	On schedule
M-045-98	Submit to Ecology as a Primary Document an RFI/CMS¹⁸ work plan for WMA A/AX including an implementation schedule in accordance with HFFACO Action Plan Section 11.6
Due:	September 30, 2022
Status:	On schedule
M-045-102	Submit to Ecology a Performance Assessment (PA) Maintenance Plan for WMA A/AX PA
Due:	September 30, 2022
Status:	On schedule
M-045-92AB	Complete Construction of Barrier 4 in 241-U Farm
Due:	October 31, 2023
Status:	On schedule
M-045-103	Submit to Ecology a PMR¹⁹ with Tier 2 RCRA Closure Plan for WMA A/AX and Schedule for Tier 3 Schedule
Due:	September 30, 2026
Status:	On schedule
M-045-104	Submit to Ecology as a PMR the Post-Closure Plan for WMA A/AX
Due:	September 30, 2028
Status:	On schedule
M-045-00	Complete Closure of All SST Farms
Due:	January 31, 2043
Status:	At risk. Decision document 2016-005 signed August 22, 2016, requires this milestone to be addressed with the negotiations supporting M-062-45 Milestone.

Significant Past Accomplishments

- Submitted RPP-RPT-62684, *FY 2019 Annual Interim Surface Barrier Monitoring Report*, Rev. 0, to Ecology via letter 20-TF-0095, “The U.S. Department of Energy, Office of

¹⁸ RFI/CMS denotes *Resource Conservation and Recovery Act* Facility Investigation/Corrective Measure Study.

¹⁹ PMR denotes Permit Modification Request.

River Protection, Transmittal of RPP-RPT-62684, *Fiscal Year 2019 Annual Interim Surface Barrier Monitoring Report*, Rev. 0, to Meet Hanford Federal Facility Agreement and Consent Order Milestone M-045-92AD” on October 7, 2020. This completed the M-045-92AD Milestone.

- Submitted revisions and comment responses to Ecology for RPP-RPT-59389, *Tier 2 Resource Conservation and Recovery Act (RCRA) Closure Action Plan for Waste Management Area C*; RPP-RPT-59390, *Tier 3 Resource Conservation and Recovery Act (RCRA) Component Closure Activity Plan for 241-C-200 Series Tanks*; and RPP-RPT-58858, *Tier 1 Closure Plan Single-Shell Tank System*.
- Continued permitting workshops with Ecology for the SST closure plans in the Hanford Site-wide permit. The workshops are currently being conducted as teleconferences.
- Submitted RPP-ENV-61497, *Preliminary Performance Assessment of Waste Management Area A-AX*, and RPP-ENV-62206, *Analysis of Post-Closure Groundwater Impacts From Hazardous Chemicals in Residual Wastes in Tanks and Ancillary Equipment at Waste Management Area A-AX*, on September 29, 2020, to meet the M-045-99 Milestone.
- Held a data quality objective meeting for defining the WMA A/AX boundary with Ecology and EPA, September 1, 2020. Held two follow-up meetings for defining the WMA A-AX boundary with Ecology on September 16 and November 3, 2020.
- Held a data quality objective sampling meeting for WMA A/AX with Ecology on September 29, 2020.
- Held a sample depth meeting for D0006 in WMA A/AX with Ecology on October 14, 2020.
- Completed liner installation on the TX Evapotranspiration Basin on August 31, 2020.
- Completed the storm water drainage system and stabilization of the Waste Isolation Division site for the TX evapotranspiration basin on November 17, 2020.
- Completed hydro seed application for the TX evapotranspiration basin on November 18, 2020.
- Issued limited notice to proceed to construction subcontractor for TX Tank Farm Barrier construction.
- Report RPP-RPT-61684, *Maintenance and Performance Monitoring Plan for the Interim Barriers Program*, Rev. 00B, was delivered to Ecology on October 10, 2019, to complete the M-045-92AC Milestone. Submitted RPP-RPT-61684 Rev. 1, to Ecology via letter 20-TF-0069, “The U.S. Department of Energy, Office of River Protection, Transmittal of RPP-RPT-61684, *Maintenance and Performance Monitoring Plan for the Interim Barriers Program*, Rev. 1,” on July 23, 2020. Ecology extended its review of the document until September 18, 2020 (20-NWP-137, “Extension of the Department of Ecology’s [Ecology] Comment Review Period for the *Maintenance and Performance Monitoring Plan*, RPP-RPT-61684, Revision 1, for the Interim Barriers Program”). ORP received Ecology comments on the document on September 18, 2020 (20-NWP-159, “Department of Ecology’s [Ecology] Comments on the United States Department of

Energy – Office of River Protection’s [USDOE-ORP] *Maintenance and Performance Monitoring Plan for the Interim Barriers Program* [RPP-RPT-61684, Rev. 1]”). On October 8, 2020, ORP requested an additional 60 days past October 18, 2020, to provide responses to Ecology’s comments on the primary document (20-TF-0101, “Response to 20-NWP-159 from the Washington State Department of Ecology”). On October 9, 2020, Ecology approved ORP’s request for a 60-day extension (20-NWP-164, “Approval of the United States Department of Energy’s 60-day Extension Request for Comment Response on the *Maintenance and Performance Monitoring Plan for the Interim Barriers Program*, RPP-RPT-61684, Rev.1”). On December 1, 2020, DOE submitted to Ecology the updated document via letter 20-TF-0106, “Reissue – The U.S. Department of Energy, Office of River Protection, Transmittal of RPP-RPT-61684, *Maintenance and Performance Monitoring Plan for the Interim Barriers Program*, Rev. 2.” In the Ecology letter dated December 21, 2020 (20-NWP-202, “Extension of the Department of Ecology’s [Ecology] Comment Review Period for the *Maintenance and Performance Monitoring Plan for the Interim Barriers Program*, Revision 2”), Ecology extended their comment review period to February 15, 2020.

Significant Planned Activities in the Next Six Months

- Resolve Ecology’s comments on RPP-RPT-59389, RPP-RPT-59390, and RPP-RPT-58858
- Respond to Ecology’s comments on RPP-RPT-61684
- Release updated TPA Appendix I Performance Assessment documents, incorporating Ecology comments as appropriate for WMA-C
- Hold additional WMAs A/AX boundary meetings for the purpose of reaching agreement
- Formally award construction subcontract for TX Tank Farm Barrier and commence barrier construction.

Issues

- The boundary of WMA A-AX must be defined in order to complete Milestones M-045-97 and M-045-98. In September 2020, Ecology proposed adding three areas to WMA A-AX: 1) the 244-AR Vault and 241-AR-151 diversion box; 2) the soil in the area around DST AY-102; and 3) an area outside the east of Tank Farm A fence line. Meetings about the boundary for WMA A-AX continued through October 2020, and into November 2020. Work necessary to meet these two milestones has fallen behind schedule as the scope is unresolved and resources are being used to support the evaluation of Ecology’s requests. As discussions continue regarding the boundary, the DOE’s ability to complete these milestones is impacted. Additionally, if discussions yield the need to add additional areas to the WMA A-AX boundary, the milestones’ dates will also be impacted. These impacts will be addressed by DOE proposing new dates for these milestones through a TPA Change Control Form.
- The content of the WMA Integration Study was negotiated and agreed upon by DOE, EPA, and the State of Washington, and is captured in Section 2.1.1 of Appendix I of the

HFFACO Action Plan. This content had been agreed upon prior to establishment of Milestone M-045-97, “Submit to Ecology as a Primary Document, a Waste Management Area Integration Study for WMA A/AX, as described in HFFACO Appendix I.2.1.1.” Following establishment of Milestone M-045-97, Ecology submitted a five page annotated outline to DOE for the WMA A-AX Integration Study via letter on September 10, 2020 (20-NWP-154, “Re: Waste Management Area (WMA) A/AX Integration Study Outline”). Although the transmittal letter says the “...outline provides a detailed description of the elements necessary to meet Hanford Facility Agreement and Consent Order Appendix I requirements,” the outline includes many elements not required under Section 2.1.1 of Appendix I of the HFFACO Action Plan. Some of the elements of Ecology’s annotated outline will not be completed for years. DOE is reviewing Ecology’s annotated outline to determine the schedule impacts that could result if all of the elements were included in the WMA A-AX Integration Study.

- Ecology proposed (via an email from Mr. Jeff Lyon on June 17, 2020) to remove the milestone (i.e., M-045-62, “Submit the Draft Tier 3 Closure Plan with Corrective Measures in Phase 2 CMIP for WMA-C”) for submittal of the CMIP, with the intent to install a final closure cap, rather than implement the planned interim barrier. Ecology’s proposal to install the final closure cap before most of the closure activities would be completed at Tank Farms 241-A, 241-AN, 241-AP, 241-AW, 241-AX, 241-AY, and 241-AZ is an issue for the following reasons:
 - Could impact retrievals and tank structural stability
 - Could cause runoff issues for adjacent tank farms
 - Is not consistent with the approach analyzed in DOE/EIS-0391, *Final Tank Closure and Waste Management Environmental Impact Statement for the Hanford Site, Richland, Washington*; the record of decision (78 FR 75918, “Final Tank Closure and Waste Management Environmental Impact Statement for the Hanford Site, Richland, Washington”); and captured in the approved RPP-RPT-59379, *Waste Management Area C Phase 2 Corrective Measures Study Report*.
- DOE is developing the CMIP to submit to Ecology and has followed this path since RPP-RPT-59379 was approved in June 2018. DOE understands that the CMIP is the vehicle that Ecology will use to meet its TPA/HFFACO obligations in its role as lead agency, as set forth in paragraph 54 of the HFFACO legal agreement. Paragraph 54 of the HFFACO states:

DOE shall develop and submit its proposed remedial action (or corrective action) alternative following completion and approval of a Remedial Investigation and Feasibility Study (or RCRA Facility Investigation and Corrective Measures Study), in accordance with the requirements and schedules set forth in the Action Plan. If Ecology is the lead regulatory agency, it will recommend the CERCLA²⁰ remedial action(s) it deems appropriate to EPA. The EPA Administrator, in consultation with the DOE

²⁰ CERCLA denotes the *Comprehensive Environmental Response, Compensation, and Liability Act*, 42 USC § 9601 *et seq.*

and Ecology, shall make final selection of the CERCLA remedial action(s), which shall not be subject to dispute.

Notwithstanding Ecology's forthcoming recommendations and whether they also indicate Ecology's position that corrective actions are not needed for the dangerous waste constituents, the EPA Administrator has sole authority to make the CERCLA remedial action decisions. DOE has not received a clearly articulated rationale for any Ecology-proposed change or the process Ecology plans to use to recommend any remedial action(s) to the EPA and to obtain the EPA's selection of remedial action(s).

- On March 24, 2020, the Hanford Site moved to an essential mission-critical operations posture in recognition of increasing COVID-19 concerns. During this time, the majority of the Hanford Site workforce transitioned to telework, and a limited number of workers reported to the site to perform activities necessary to maintain the site in a safe condition.
- On May 20, 2020, DOE authorized the Hanford Site to move to Phase 1. Hanford Site operations began Phase 1 on May 26, 2020. During Phase 1, essential mission-critical operations were continued and targeted mobilization and low-risk workscope, such as implementation of COVID-19 protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities were added.
- The Hanford Site transitioned to Phase 2 beginning August 31, 2020. In Phase 2, the workforce that has been performing portable work via telework will generally continue to telework. The majority of the workforce performing nonportable work will return to the site to progress work activities, leveraging established COVID-19 controls.
- DOE and its contractors are engaged in ongoing analysis of work schedule impacts. DOE is continuing to evaluate the information, COVID-19 potential impacts on the TPA, and if other actions may be necessary.

Single-Shell Tank Retrieval Program

Tank Farms Assistant Manager: Brian Harkins (Acting)

Technical Lead: Jeff Rambo

Ecology Project Manager: Jeff Lyon

M-045-86 Submit Retrieval Data Report (RDR) to Ecology for 19 Tanks Retrieved Under Consent Decree

Due: To be determined (12 months after retrieval certification).
Status: No retrieval data reports are currently underway. The next planned retrieval is Tank 241-AX-102.

M-045-70 Complete Waste Retrieval from all Remaining Single Shell Tanks (SSTs)

Due: December 31, 2040
Status: At risk. Decision document 2016-005, signed August 22, 2016, requires this milestone be addressed with the negotiations supporting M-062-45 Milestone.

Significant Past Accomplishments

- Refer to the Consent Decree monthly report.

Significant Planned Activities in the Next Six Months

- Refer to the Consent Decree monthly report.

Issues

- Refer to the Consent Decree monthly report.

Tank Operations Contract Overview

Earned Value Data: Fiscal Year 2021

November-2020

Tank Farms ORP-0014 WBS 5 - River Protection Project (in \$000s)										
	BCWS	BCWP	ACWP	SV	CV	SPI	CPI	BAC	EAC	VAC
CM	\$41,528	\$55,244	\$59,604	\$13,716	(\$4,360)	1.33	0.93			
FYTD	\$76,250	\$102,565	\$102,139	\$26,315	\$426	1.35	1.00	\$679,693		
CTD	\$6,396,065	\$6,309,461	\$6,238,367	(\$86,603)	\$71,095	0.99	1.01	\$6,999,507	\$6,938,467	\$61,040

ACWP	=	actual cost of work performed	CV	=	cost variance
BAC	=	budget at completion	EAC	=	estimate at completion
BCWP	=	budgeted cost of work performed	FYTD	=	fiscal year to date
BCWS	=	budgeted cost of work scheduled	SPI	=	schedule performance index
CM	=	current month	SV	=	schedule variance
CPI	=	cost performance index	VAC	=	variance at completion
CTD	=	contract to date	WBS	=	work breakdown structure

The Earned Value Management System is intended to provide a status of how the contractor is progressing against its monthly planned work (i.e., schedule), and whether it is costing more or less to complete the work than planned. The earned value analysis is not intended to be a measurement of performance against existing TPA milestones.

The project plan is measured by expressing the schedule in terms of dollars spread over the anticipated project duration, and then for each month, determining how much of the planned work was accomplished or “earned,” as measured in equivalent dollars. If more work is accomplished than planned, then the project is ahead of schedule and has a favorable schedule variance (SV). Similarly, if less work is accomplished, the project is behind schedule and has an unfavorable SV. Accomplished work is reported in the month it was completed, which may not be when it was planned. For example, work completed in a month earlier than planned would be reported as a favorable SV for the month in which it was completed, but would be reported as an unfavorable SV in the month it was planned. The end result would be a net zero overall cumulative SV over these months. Likewise, work completed late will recover an earlier reported unfavorable SV.


The cost variance (CV) measures the actual cost of work performed against the earned dollar value of that performed work. As an example, assume \$10,000 of work was planned to-date, \$8,000 was reported as being performed (earned), at an actual cost of \$9,000. This work would be reported as being \$2,000 behind schedule [a negative or unfavorable SV: $\$8,000 - \$10,000 = (\$2,000)$], and has cost \$1,000 more [a negative or unfavorable CV: $\$8,000 - \$9,000 = (\$1,000)$] than was planned for completing that work scope. Likewise, a favorable or positive CV would be reported if it cost less to complete the work than the performed dollar value of the work. The SV and CV are reported for each monthly period, fiscal-year-to-date, as well as for the contract-to-date value. The monthly variances can fluctuate significantly (for reasons noted earlier), so the FY or contract-to-date report provides a better indicator of the overall project completion status and can give a reasonable projection of how the project will finish, based on the progress-to-date.

Earned Value Data: Fiscal Year 2021

November-2020

Tank Farms ORP-0014
WBS 5 - River Protection Project

EVMS Monthly and Fiscal Year Values

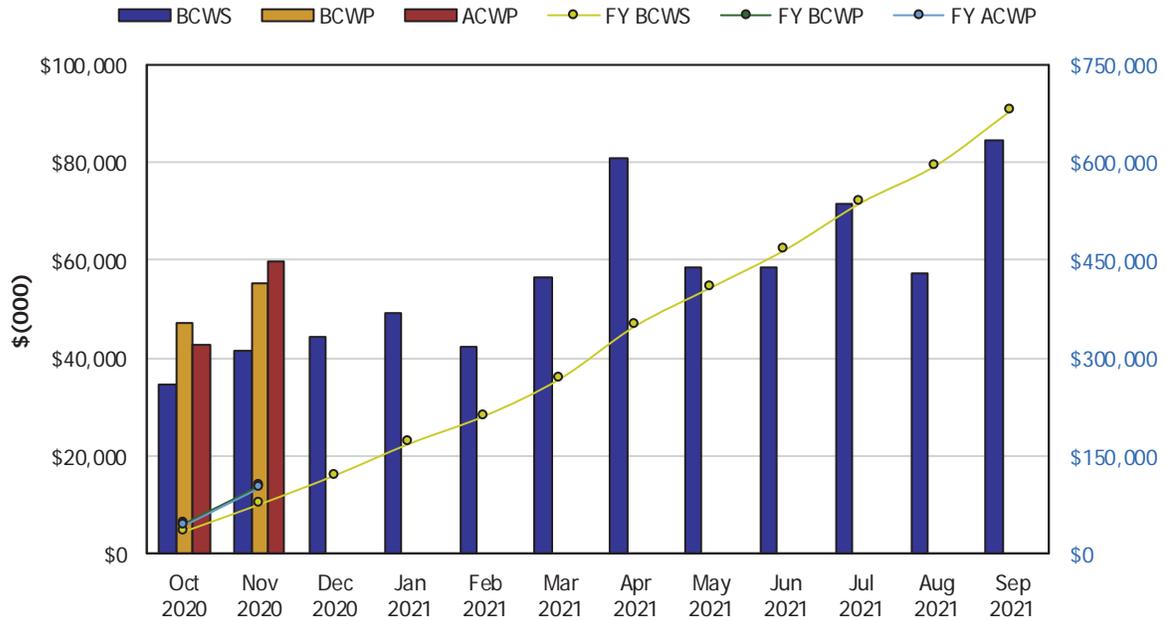

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2020	\$34,722	\$47,321	\$42,535	1.36	1.11	\$34,722	\$47,321	\$42,535	1.36	1.11
Nov 2020	\$41,528	\$55,244	\$59,604	1.33	0.93	\$76,250	\$102,565	\$102,139	1.35	1.00
Dec 2020	\$44,259					\$120,509				
Jan 2021	\$49,008					\$169,517				
Feb 2021	\$42,468					\$211,985				
Mar 2021	\$56,699					\$268,683				
Apr 2021	\$80,737					\$349,420				
May 2021	\$58,522					\$407,942				
Jun 2021	\$58,617					\$466,559				
Jul 2021	\$71,546					\$538,105				
Aug 2021	\$57,239					\$595,344				
Sep 2021	\$84,349					\$679,693				

CTD	\$6,396,065	\$6,309,461	\$6,238,367	0.99	1.01
-----	-------------	-------------	-------------	------	------


- ACWP = actual cost of work performed
- BCWP = budgeted cost of work performed
- BCWS = budgeted cost of work scheduled
- CPI = cost performance index
- CM = current month
- CTD = contract to date
- FY = fiscal year
- SPI = schedule performance index

Earned Value Data: Fiscal Year 2021

November-2020

**Tank Farms ORP-0014
WBS 5.1 - Base Operations**

EVMS Monthly and Fiscal Year Values

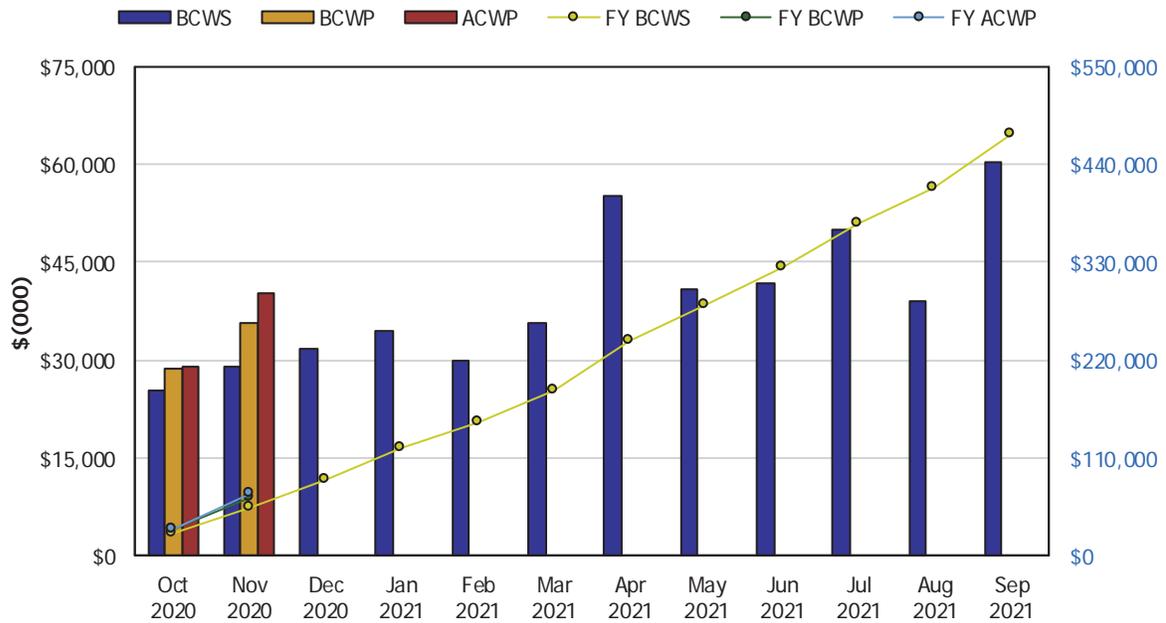

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2020	\$25,298	\$28,696	\$29,098	1.13	0.99	\$25,298	\$28,696	\$29,098	1.13	0.99
Nov 2020	\$28,824	\$35,687	\$40,259	1.24	0.89	\$54,123	\$64,383	\$69,358	1.19	0.93
Dec 2020	\$31,804					\$85,926				
Jan 2021	\$34,390					\$120,316				
Feb 2021	\$29,968					\$150,284				
Mar 2021	\$35,748					\$186,032				
Apr 2021	\$55,087					\$241,119				
May 2021	\$40,797					\$281,916				
Jun 2021	\$41,877					\$323,793				
Jul 2021	\$49,918					\$373,711				
Aug 2021	\$39,021					\$412,731				
Sep 2021	\$60,360					\$473,091				

CTD	\$4,239,901	\$4,200,488	\$4,124,230	0.99	1.02
-----	-------------	-------------	-------------	------	------

- ACWP = actual cost of work performed
- BCWP = budgeted cost of work performed
- BCWS = budgeted cost of work scheduled
- CPI = cost performance index
- CM = current month
- CTD = contract to date
- FY = fiscal year
- SPI = schedule performance index

Tank Farms Assistant Manager: Brian Harkins (Acting)
Technical Lead: Ricky Bang

5.01 – Base Operations

The November 2020 variances below do not impact TPA milestones.

The current month **favorable** SV of \$6,862,248 was primarily due to:

- The implementation of a Baseline Change Request, in support of the new Multi-craft Maintenance Facility, to align the project schedule with the awarded subcontractor's approved schedule. This a realized risk with a one-time point adjustment. The remaining Budgeted Cost for Work Scheduled was re-planned in more detailed schedule activities in alignment with the subcontractor's submitted schedule.
- Current period positive SV for the Encasement Pressure Testing resulting from an early start and accelerated execution of two of the five planned Encasement tests at the AW-B pit, AN-02E pit, and AW-02A pit.
- Current period positive SV for the ultrasonic testing of DST AW-105, which was performed ahead of schedule.
- The favorable SV was partially offset by an unfavorable SV for the 242-A Evaporator Facility Transfer Line Replacement that resulted from fieldwork for the 242-A Evaporator wall penetrations being delayed due to the permit modification not being approved yet. The unfavorable SV for the 242-A Evaporator Facility Transfer Line Replacement will continue to be realized until the permit modification is approved.

The current month **unfavorable** CV of (\$4,572,678) was primarily due to:


- The transfer of actual costs received with a Period of Performance in FY 2020 from a General COVID-19 account to the Retrieval and Closure COVID-19 account. This transfer of costs placed the FY 2020 COVID-19 actuals in the correct account so the funding string for COVID-19 costs can be isolated and tracked consistent with the funding guidance.
- A negative CV for the ETF Brine Stabilization. Additional design, fabrication, installation and testing was experienced during fieldwork. A dimensional error was discovered during fabrication, requiring design modifications of the fill head and drip tray assemblies. Additionally, it was determined that the cooling water system required additional pressure relief valves for the cooling water piping. These changes resulted in an unfavorable cost increase.

Earned Value Data: Fiscal Year 2021

November-2020

Tank Farms ORP-0014
WBS 5.2 - Retrieve and Close SSTs

EVMS Monthly and Fiscal Year Values

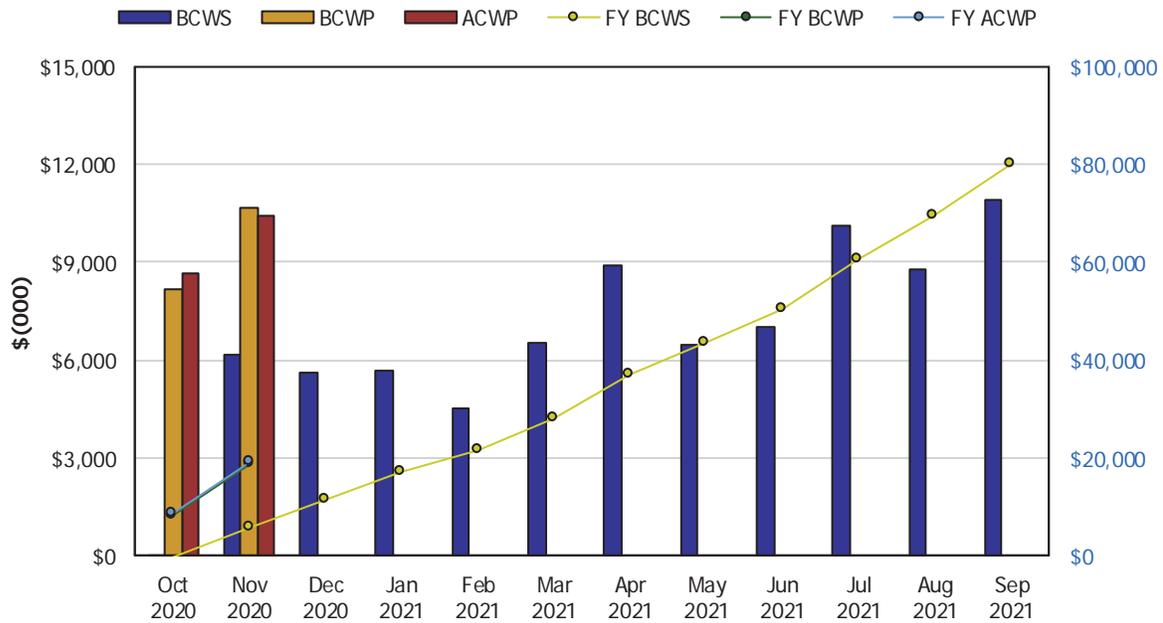

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2020	(\$362)	\$8,176	\$8,653	-22.56	0.94	(\$362)	\$8,176	\$8,653	-22.56	0.94
Nov 2020	\$6,177	\$10,692	\$10,435	1.73	1.02	\$5,815	\$18,867	\$19,088	3.24	0.99
Dec 2020	\$5,605					\$11,419				
Jan 2021	\$5,647					\$17,066				
Feb 2021	\$4,498					\$21,564				
Mar 2021	\$6,531					\$28,095				
Apr 2021	\$8,881					\$36,976				
May 2021	\$6,493					\$43,469				
Jun 2021	\$6,994					\$50,463				
Jul 2021	\$10,115					\$60,578				
Aug 2021	\$8,757					\$69,335				
Sep 2021	\$10,891					\$80,226				

CTD	\$1,223,625	\$1,195,074	\$1,250,350	0.98	0.96
-----	-------------	-------------	-------------	------	------

- ACWP = actual cost of work performed
- BCWP = budgeted cost of work performed
- BCWS = budgeted cost of work scheduled
- CPI = cost performance index
- CM = current month
- CTD = contract to date
- FY = fiscal year
- SPI = schedule performance index

Tank Farms Assistant Manager: Brian Harkins (Acting)
Technical Lead: Jeff Rambo

5.02 – Retrieve and Close Single-Shell Tanks


For the retrieval portion, see the Consent Decree monthly report for cost and schedule status.

Earned Value Data: Fiscal Year 2021

November-2020

Tank Farms ORP-0014
WBS 5.3 - WFD/Treatment Plng/DST Retrieval/Closure

EVMS Monthly and Fiscal Year Values

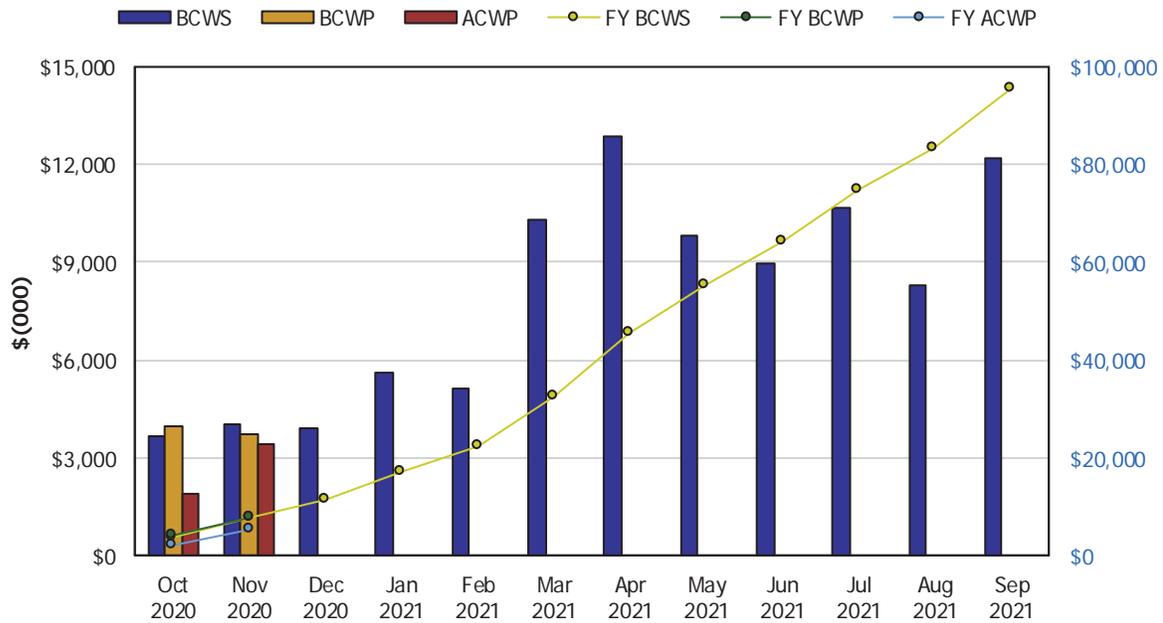

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2020	\$3,681	\$3,941	\$1,894	1.07	2.08	\$3,681	\$3,941	\$1,894	1.07	2.08
Nov 2020	\$4,020	\$3,738	\$3,418	0.93	1.09	\$7,701	\$7,679	\$5,312	1.00	1.45
Dec 2020	\$3,905					\$11,606				
Jan 2021	\$5,597					\$17,202				
Feb 2021	\$5,099					\$22,301				
Mar 2021	\$10,275					\$32,576				
Apr 2021	\$12,891					\$45,467				
May 2021	\$9,790					\$55,257				
Jun 2021	\$8,972					\$64,229				
Jul 2021	\$10,661					\$74,890				
Aug 2021	\$8,303					\$83,194				
Sep 2021	\$12,181					\$95,375				

CTD	\$662,575	\$651,932	\$602,152	0.98	1.08
-----	-----------	-----------	-----------	------	------

- ACWP = actual cost of work performed
- BCWP = budgeted cost of work performed
- BCWS = budgeted cost of work scheduled
- CPI = cost performance index
- CM = current month
- CTD = contract to date
- FY = fiscal year
- SPI = schedule performance index

Tank Farms Assistant Manager: Brian Harkins (Acting)
Federal Program Manager: Brian Harkins

5.03 – Waste Feed Delivery/Treatment

The November 2020 variances below do not impact TPA milestones.

The current month **unfavorable** SV of (\$281,330) was primarily due to:

- The award of the melter assembly facility upgrade contract, related to WTP Transition Support, being issued later than planned, due to the requirement for more in depth cost evaluations of the proposal following the receipt of only one bid for this competitive procurement.

The current month **favorable** CV of \$320,317 was primarily due to:


- The General and Administrative accounting adjustments associated with project support work.

Earned Value Data: Fiscal Year 2021

November-2020

**Tank Farms ORP-0014
WBS 5.5 - Treat Waste**

EVMS Monthly and Fiscal Year Values

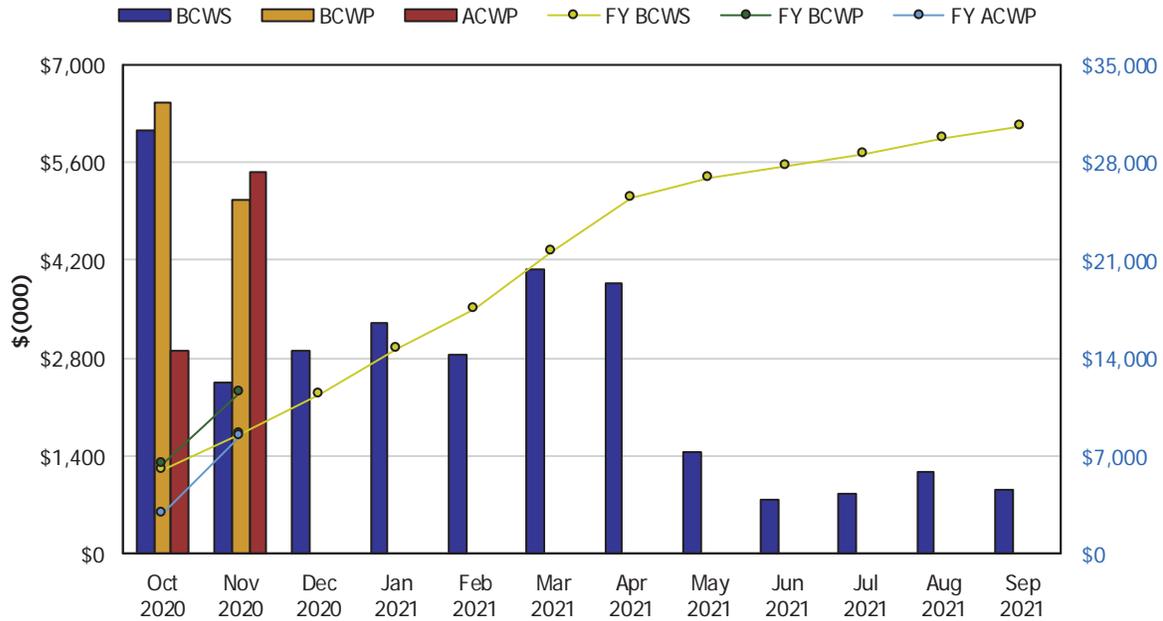

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2020	\$6,053	\$6,465	\$2,900	1.07	2.23	\$6,053	\$6,465	\$2,900	1.07	2.23
Nov 2020	\$2,441	\$5,073	\$5,471	2.08	0.93	\$8,494	\$11,538	\$8,371	1.36	1.38
Dec 2020	\$2,890					\$11,384				
Jan 2021	\$3,313					\$14,697				
Feb 2021	\$2,851					\$17,548				
Mar 2021	\$4,079					\$21,628				
Apr 2021	\$3,875					\$25,503				
May 2021	\$1,443					\$26,945				
Jun 2021	\$774					\$27,720				
Jul 2021	\$852					\$28,572				
Aug 2021	\$1,158					\$29,730				
Sep 2021	\$917					\$30,646				

CTD	\$246,418	\$238,536	\$240,070	0.97	0.99
-----	-----------	-----------	-----------	------	------

- ACWP = actual cost of work performed
- BCWP = budgeted cost of work performed
- BCWS = budgeted cost of work scheduled
- CPI = cost performance index
- CM = current month
- CTD = contract to date
- FY = fiscal year
- SPI = schedule performance index

Tank Farms Assistant Manager: Brian Harkins (Acting)
Federal Program Manager: Brian Harkins

5.05 – Treat Waste

The November 2020 variances below do not impact TPA milestones.

The current month **favorable** SV of \$2,631,900 was primarily due to:

- Schedule recovery on fabrication of AP-07F TSCR feed pumps and TSCR Infrastructure Construction. Fieldwork was previously delayed due to the implementation of COVID-19 site protocols to infrastructure and facilities, required training, medical evaluations, and limited construction activities. Factory acceptance testing (FAT) and system testing of AP-07F TSCR feed pumps was completed and the fabricator is completing final data packages to prepare for delivery. Installation of the primary piping for SN-637 and SN-700 connecting from the existing W-211 piping to ICD-30/31 was completed in the current period. Additionally, progress was made on assembly/hookup of the TSCR system, installation of electrical infrastructure, completion of electrical rack fabrication, progress on Hose-in-Hose Transfer Line shielding fabrication, and receipt of IXC restraints.
- Continued progress made on the development of operation documentation, which was originally planned to complete in September 2020. This work was previously delayed to allow for information from the TSCR FAT and TSCR operation training to be incorporated into the operation documentation. With the completion of both the FAT and the training, significant progress is now being made to complete the operation documentation to support operation acceptance testing and readiness.

The current month **unfavorable** CV of (\$397,800) was primarily due to:

- Modifications to the subcontractor's milestone payment schedule for pipe installation that resulted in misalignment to the budgeted cost of work performance. The subcontractor's sub-tier contract includes milestones for completion of inspections for piping welds, but does not include milestone payments associated with completion of pressure testing. As a result, the subcontractor accrued the full value associated with completion of primary pipe installation. The project baseline includes separate, discrete activities for hydrostatic testing of primary piping. There will be an offsetting favorable variance when they complete the scope without an associated accrual.

Table 1 Administrative Record Metadata

Milestone Number or Facility Identification	Title
M-045-102	Submit to Ecology a Performance Assessment Maintenance Plan for the WMA A/AX PA
M-045-15	Completion of Tank A-103 SST Waste Retrieval
M-045-15A	Submit a Retrieval Data Report Pursuant to Agreement Appendix I
M-045-15D	Exception to Waste Retrieval Criteria Pursuant to Agreement Appendix H
M-045-56Q	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)
M-045-56R	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)
M-045-85	Initiate Negotiations of HFFACO Interim Milestones for Closure of Remaining WMAs
M-045-91E4	Provide SST Farms Dome Deflection Surveys Every 2 Years to Ecology
M-045-92AA	Barrier 4 Design Approved by Ecology
M-045-92AE	Submit Yearly Reports Summarizing the Results of Maintenance and Performance Monitoring Activities
M-045-92Y	Complete Construction of Barrier 3 in 241-TX Farm
M-045-92Z	Submit to Ecology Design for Barrier 4 in 241-U Farm
M-045-97	Submit to Ecology a WMA Integration Study for WMA A/AX as a Primary Document
M-045-98	Submit to Ecology a RFI/CMS Work Plan for WMA A/AX as a Primary Document
M-062-01AP	Submit Semi-Annual Project Compliance Report to Ecology
M-062-01AQ	Submit Semi-Annual Project Compliance Report to Ecology
M-062-31-T01	Comp. Final Design & Submit RCRA Part B Permit Mod Request for Enhanced WTP & Supplemental Treatment
M-062-32-T01	Start Construction of Supplemental Vitrification Facility and/or WTP Enhancements
M-062-33-T01	Complete Construction of Supplemental Treatment Vitrification Facility and/or WTP Enhancements
M-062-45	Complete Negotiations 6-Months After Last Issuance of System Plan
M-062-45-A	Complete Negotiations 6-Months After Last Issuance of System Plan
M-062-45-T01	Complete Negotiations 6-Months After Last Issuance of System Plan
M-062-45-XX	Complete Negotiations to Resolve Future Disputes M-062-45 Paragraphs 4 & 5
M-062-45-ZZ	Negotiate a One-Time Supplemental Treatment Selection

Milestone Number or Facility Identification	Title
M-062-45-ZZ-A	Convert M-062-31-T01 Thru M-062-34-T01 to Interim Milestones
M-062-51-T01	Submit to Ecology, as a Primary Document, a Secondary Liquid Waste Disposition Work Plan
M-062-51-T02	Submit to Ecology, PMR for Redesign Upgrades and Ops to Support Volumes of Waste Types
M-062-52-T01	Submit to Ecology, a Secondary Solid Waste Disposition Work Plan as a Primary Document
M-062-52-T02	Submit to Ecology, PMR for Ancillary Facilities/Capabilities to Support Treatment of Secondary Waste
M-062-53A	Achieve Substantial Completion of EMF Construction
S-2-3	Double-Shell Tank System (DST)
S-2-4	Single-Shell Tank System (SST)
S-2-8	Liquid Effluent Retention Facility (LERF)
T-2-6	242-A Evaporator
T-2-8	Effluent Treatment Facility (ETF)
TS-2-8	Low-Activity Waste Pretreatment System (LAWPS)

CD = critical decision

DFLAW = direct-feed low-activity waste

DOE = U.S. Department of Energy

Ecology = Washington State Department of Ecology

EMF = Effluent Management Facility

HFFACO = *Hanford Federal Facility Agreement and Consent Order*

PMR = Permit Modification Request

RCRA = *Resource Conservation and Recovery Act*

SST = single-shell tank

TSCR = tank-side cesium removal

WMA = waste management area

WTP = Waste Treatment and Immobilization Plant
