


FINAL

**Office of River Protection
Tri-Party Agreement
Monthly Summary Report
February 2013**



**Office of River Protection
Tri-Party Agreement Milestone Review
February 2013 (Project EVMS reflects December 2012)**

Page	Topic	Leads
1	Administrative Items / Milestone Status	James Lynch / Dan McDonald / Jeff Lyon
2	System Plan; M-62-40	Dabrisha Smith / Jeff Lyon / Dan McDonald
3	Acquisition of New Facilities; M-90-00; M-47-00	Janet Diediker / Jeff Lyon / Dan McDonald
4	Supplemental Treatment and Part B Permit Applications; M-62-00, -20, -30, -45	Steve Pfaff / Jeff Lyon / Dan McDonald
5	242-A Evaporator Status	Ron Koll / Jeff Lyon
6	SST Integrity Assurance; M-45-91	Jeremy Johnson/ Michelle Hendrickson
7	In Tank Characterization and Summary	Billie Mauss / Michael Barnes
9	Tank Operations Contract (TOC) Overview	Dan Knight / Jeff Lyon
14	Single-Shell Tank Corrective Action; M-45, -50, -60	Chris Kemp / Jeff Lyon
16	Single-Shell Retrieval and Closure Program TPA Milestones Status; M-45-00 series, - Tank in Appendix H Status - Tank Retrievals with Individual Milestones	Chris Kemp / Jeff Lyon
17	Tank Waste Retrieval Work Plan Status	Chris Kemp / Jeff Lyon
18	Tank in TPA Appendix H Status Tank Retrievals with Individual Milestones	Chris Kemp / Jeff Lyon
19	WTP Overall TPA Summary and Milestone Status; M-62-01	Delmar Noyes / Dan McDonald

Milestone	Title	Due Date	Completion Date	Status
Fiscal Year 2013				
M-045-20	Submit Interim Measures Investigation Work Plan and TPA Chg Pckgs for M-045-22 Target Dates	12/31/2012	12/06/2012	Completed
M-090-11	Comp. Neg's No More Than 2 Canister Storage Fac. Const. Int. M/S	12/31/2012	11/19/2012	Completed
M-062-01Z	Submit Semi-Annual Project Compliance Report	1/31/2013	1/31/2013	Completed
M-045-91F-T01	Provide Report of the Liquid Leak Rate Assessments	1/31/2013		Missed
M-045-21	Submit Sampling and Analysis Plan for 241-TX Tank Farm	3/31/2013		On Schedule
M-045-91D-T01	Provide Report on the Concrete Dome Samples from Tank C-107 Plug	5/31/2013		On Schedule
M-045-91F-T03	Provide Report on Testing for Ionic Conductivity of SSTs	5/31/2013	05/02/2012	Completed
M-045-91F-T02	Provide Report of Liner Failures for SSTs	7/31/2013		To Be Missed
M-062-01AA	Submit Semi-Annual TPA Project Compliance Report	7/31/2013		On Schedule
M-045-91F-T04	Provide Report on 100-Series SSTs as having Leaked in RPP-32681	7/31/2013		To Be Missed
M-045-91E	Provide SST Farms Dome Deflection Surveys Every Two Years	9/30/2013		On Schedule
M-045-91G-T03	Provide AOR Final Doc. for SSTs on 1,000,000 Gallon Tanks	9/30/2013		To Be Missed
Fiscal Year 2014				
M-045-91G-T04	Provide AOR Final Doc. for SSTs on 55,000 Gallon Tanks	10/31/2013		To Be Missed
M-062-40C	Select a Minimum of Three Scenario's for the System Plan	10/31/2013		On Schedule
M-045-91F	Provide Summary Conclusions Report on Leak Integrity	12/31/2013		To Be Missed
M-045-91G	Provide Summary Conclusions Report of AOR for SSTs	04/30/2014		To Be Missed
M-045-56J	Ecology And DOE Agree, At A Minimum, To Meet Yearly (By July)	07/31/2014		On Schedule
M-045-91B-T01	Provide Ecology report on the Concrete Core from TankA-106 or alt	09/30/2014		On Schedule
M-047-07	CD-1 for Secondary Liquid Waste Treatment and CR for CD-2 to Ecology	09/30/2014		On Schedule
M-090-13	CD-1 for Interim Hanford Storage Project and CR for CD-2 to ECY	09/30/2014		On Schedule

System Plan

M-062-40B, Submit a system plan describing the disposition of all tank waste managed by ORP, Due: 10/31/2011, Status: Completed 10/24/2011 via DOE-ORP/ECY joint signature letter 11-TPD-087.

M-062-40C, Select a minimum of three scenarios that will be analyzed in the system plan, Due: 10/31/2013, Status: On Schedule

M-062-40D, Submit a system plan describing the disposition of all tank waste managed by ORP, Due: 10/31/2014, Status: On Schedule

M-062-45-T01, Every six years, within six-months after last revision of the System Plan, negotiate tank waste retrieval sequencing, Due: 4/30/2015, Status: On Schedule

Significant Past Accomplishments:

DOE/ORP submitted the River Protection Project System Plan, Revision 6, with a joint Ecology signature to EPA on October 24, 2011.

Significant Planned Actions in the Next Six Months:

ORP and WRPS plan to meet with Ecology in March 2013 to provide the status on various recommendations made in regards to several model planning tools in the 2009 "External Technical Review for Evaluation of System Level Modeling and Simulation Tools in Support of Hanford Site Liquid Waste Process." Please see issues below.

Various circumstances have occurred in which no new scenarios have been selected for System Plan 6 Addendum.

ORP and Ecology will jointly begin defining the System Plan 7 scenarios in the July-August 2013 time frame. The defined scenarios milestone (M-062-40C) is due October 31, 2013.

Issues:

In the October 23, 2012 TPA Project Managers meeting Dan Mc Donald, Ecology, informed ORP that system plan development for FY 14 could not move forward until ORP had read and responded to the comments in the headquarters document, "External Technical Review for Evaluation of System Level Modeling and Simulation Tools in Support of Hanford Site Liquid Waste Process." Ecology has asked for a meeting with ORP and WRPS as soon as they have read the document and are able to brief on where they think they are going with comment response development.

Acquisition of New Facilities

M-090-11, Complete the Negotiation of No More Than Two Canister Storage Facility Construction Interim Milestones, Due: 12/31/12, Status: Completed on 11/19/12. TPA Change Control Form M-90-12-02, signed by ORP and Ecology on 11/19/12, created new interim milestone, M-090-13, to "Submit to Ecology, a Conceptual Design Report Package (Critical Decision-1) for the Interim Hanford Storage Project (storage of the first two years of Hanford Site Immobilized High-Level Waste from WTP operations) and a TPA Change Request (in accordance with TPA Action Plan Section 12.0) to submit to Ecology, a Preliminary Design Report package (Critical Decision-2)."

M-090-13, Submit CD-1 for Interim Hanford Storage Project and TPA Change Request for CD-2 to Ecology, Due: 09/30/14, Status: On Schedule.

M-090-00, Acquire/modify facilities for storage of IHLW, Due: 12/31/2019, Status: On Schedule

M-047-06, Complete negotiation of no more than two interim milestones governing work necessary to support completion of M-047-00, Due: 06/30/12, Status: Completed on 11/19/12 (note this was initially Missed). Change Control Form M-47- 12-02, that creates a new interim milestone, M-047-07, to "Submit to Ecology, a Conceptual Design Report package (Critical Decision-1) for the Secondary Liquid Waste Treatment Project and a TPA Change Request (in accordance with TPA Action Plan Section 12.0) to submit to Ecology, a Preliminary Design Report package (Critical Decision-2).

M-047-07, Submit CD-1 for Secondary Liquid Waste Treatment and CR for CD-2 to Ecology, Due 09/30/14, Status: On Schedule.

M-047-00, Complete Work Necessary to provide facilities for management of secondary waste from the WTP, Due: 12/31/2022, Status: On Schedule

Significant Past Accomplishments:

On November 15, 2012, Ecology and ORP met and agreed on wording that met the requirements of both M-047-06 and M-090-11. On November 19, 2012, Ecology and ORP signed TPA Change Control Forms M-47-12-02 and M-90-12-02 establishing M-047-07 and M-090-13, respectively. ORP letter 12-ECD-0225 notified Ecology of completion of milestones M-047-06 and M-090-11.

Significant Planned Actions in the Next Six Months:

None.

Issues:

None.

Supplemental Treatment and Part B Permit Applications

M-062-40ZZ, Submit a one-time Tank Waste Supplemental Treatment Technologies report if a supplemental treatment technology is proposed other than a 2nd LAW, Due: 10/31/2014, Status: On Schedule.

M-062-45ZZ, Negotiate a one-time supplemental treatment selection, Due: 4/30/2015, Status: On schedule. Negotiations are not yet underway.

M-062-45ZZ-A, Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones, Due: 4/30/2015, Status: On Schedule.

M-062-31-T01, Complete final design and submit RCRA Part B permit mod request, Due: 4/30/2016, Status: On schedule

M-062-32-T01, Start construction of supplemental vitrification treatment facility and/or WTP enhancements, Due: 4/30/2018, Status: On schedule

M-062-33-T01, Complete construction of supplemental vitrification treatment facility and/or WTP enhancements, Due: 4/30/2021, Status: On schedule

M-062-45XX, No later than 12/31/2021, the DOE and Ecology shall complete negotiations to establish a mechanism that will apply to resolve future disputes regarding the determinations in M-062-45, paragraphs 4 and 5, due: 12/31/2021, Status: On Schedule

M-062-34-T01, Complete hot commissioning of supplemental vitrification treatment facility and/or WTP enhancements, Due: 12/30/2022, Status: On schedule

M-062-21, Annually, submit data that demonstrates operation of the WTP, Due: 2/28/2023, Status: On Schedule

M-062-00, Complete Pretreatment Processing and Vitrification of HLW and LAW Tank Wastes, Due: 12/31/2047, Status: On Schedule

Significant Past Accomplishments:

None

Significant Planned Actions in the Next Six Months:

None

Issues:

At the January TPA PMM meeting, ORP stated DOE and Ecology are currently in discussions to move out the due dates for M-062-40ZZ and M-062-45ZZ (current due dates 10/31/2014 and 4/30/2015, respectively).

242-A Evaporator Status (previously reported under Milestone M-48, which has been closed out)

242-A Campaign strategy:

The 242-A Campaign Strategy for FY2010 through FY2015 depicted below has been updated based on ORP-11242, River Protection Project Plan, Revision 6, and ongoing schedule integration efforts.

Fiscal Year	Campaign No.	Feed Source	Slurry Tank	Comments
FY10	10-01	AW-106	AW-106	Campaigns 10-01/10-02 were performed back-to back starting in late August and completing in early October 2010.
FY10	10-02	AW-106	AW-106	Campaign 10-02 was an acceleration of previously planned Campaign 11-01.
FY11	NA	NA	NA	No campaign conducted in FY11 due to ongoing 242-A and Tank Farm facility life extension and ARRA funded upgrades.
FY12	NA	NA	NA	No campaign conducted in FY12 due to ongoing 242-A and Tank Farm facility upgrades and revision to the 242-A Documented Safety Analysis (DSA).
FY13	13-01	AP-107	AP-107	Estimated start early August 2013. May require two (2) passes to achieve waste volume reduction.
FY13	13-02	AW-106	AW-106	Estimated start late August 2013.
FY14	14-01	AN-106 AZ-102 AW-106	AP-107	Estimated start March 2014. Two (2) passes required.
FY15	15-01	AY-101 AZ-102	AP-107	Estimated start March 2015. Three (3) passes required.
FY15	15-02	AY-101	AP-107	Estimated start August 2015. Four (4) passes required.

SST Integrity Assurance

M-045-91F-T01, Provide to Ecology as a HFFACO secondary document a report evaluating the applicability to Hanford SSTs of the liquid leak rate assessments of sludge and salt-cake from the Savannah River Site, Due: 1/31/2013, Status: Missed. See issues below.

M-045-91D-T01, Provide Ecology a report containing the results and interpretation of testing, and analysis performed on the concrete dome samples obtained from the Tank C-107 plug, Due: 5/31/2013, Status: On schedule.

M-045-91F-T03, Provide to Ecology, as a HFFACO secondary document a report assessing the feasibility of testing for ionic conductivity between the inside and outside of SSTs, Due: 5/31/2013, Status: Complete 05/02/2012. (ORP letter 12-TF-0009)

M-045-91F-T02, Provide to Ecology as a HFFACO secondary document a report evaluating the common factors of liner failures for SSTs that have leaked and will provide recommendations as appropriate, such as enhanced Leak Detection, Monitoring, and Mitigation, Due: 7/31/2013, Status: To Be Missed. See issues below.

M-045-91F-T04, provide to Ecology, as a HFFACO secondary document, a report on the 100-series single-shell tanks which have been or will be identified as having leaked in RPP-32681, Rev 0, Due: 7/31/2013, Status: To Be Missed. See issues below.

M-045-91G-T03, Provide to Ecology the Structural Analyses of Record final documentation for SSTs for 1,000,000 gallon tanks (A, AX and SX Farms), Due: 9/30/2013, Status: To Be Missed. See issues below.

M-045-91E, Provide to Ecology a compilation of the Single-Shell Tank farms dome deflection surveys every two years, beginning 9/30/2013, Due: 9/30/2013, Status: On schedule.

M-045-91G-T04, provide to Ecology the Structural Analyses of Record final documentation for SSTs for 55,000 gallon tanks (B, C, T and U Farms), Due: 10/31/2013, Status: To Be Missed. See issues below.

M-045-91F, Provide to Ecology a report (Summary Conclusions Report on Leak Integrity) summarizing and evaluating the information submitted under M-045-91F-T01 through -T04, Due: 12/31/2013, Status: To Be Missed. See issues below.

M-045-91G, Provide a Summary Conclusions Report of Structural Analysis of Record (AOR) for SSTs, Due: 4/30/2014, Status: To Be Missed. See issues below.

M-045-91B-T01, Provide Ecology a report containing the results and interpretation of testing, and analysis, performed on the concrete core obtained from Tank A- 106 or alternate tank, Due: 9/30/2014, Status: On schedule.

M-045-91H, Submit a change package (if deemed necessary by DOE and Ecology) to establish additional milestones based on information obtained from the actions in the preceding M-045-91 series milestones to date, Due: 7/31/2015, Status: On schedule.

M-045-91I, Provide to Ecology an IQRPE certification of SSTs structural integrity for the remainder of the mission, or for such time as the IQRPE believes he/she can reasonably certify, Due: 9/30/2018, Status: On schedule.

Significant Past Accomplishments:

- Work has resumed in the areas of SST structural analysis, sidewall coring, analysis of rebar from C-107, and SST leak cause and location analysis.

Significant Planned Actions in the Next Six Months:

- Conclude discussion with Ecology regarding “To Be Missed” target dates and interim milestone impacts and submit the agreed-upon TPA Change Package for approval.
- Complete analysis of rebar from C-107 and complete M-045-91D-T01.

Issues:

- FY2012 and FY2013 funding constraints have impacted M-045-91 scheduled work. ORP has met with Ecology to discuss impacts on individual milestones and targets dates for FY2013 and beyond per the TPA Section 12.0 Change Process. Ecology’s initial comments on a draft TPA Change Request have been incorporated, and ORP has provided this updated draft to Ecology for review. After Ecology completes this review, ORP will then submit a final, signed TPA Change Request.

In Tank Characterization and Summary

For the period from January 1 – January 31, 2013:

Accomplishments:

- Completed RPP-PLAN-51499, Rev. 1, Tank 241-SY-102 Grab Sampling and Analysis Plan for Waste Chemistry Control
- Completed RPP-PLAN-53192, Rev. 1, Tank 241-AN-101 Grab Sampling and Analysis Plan after Completion of Tank 241-C-104 Hard Heel Retrieval
- Completed RPP-PLAN-54233, Rev. 0, Tank 241-AN-101 Grab Sampling and Analysis Plan at Tank 241-C-101 Mid-Retrieval
- Completed RPP-PLAN-44844, Rev. 2, Sampling and Analysis Plan for Waste Solids in Tank 241-C-104 To Support Tank Closure
- Completed RPP-RPT-54017, Rev. 0, Derivation of Best-Basis Inventory for Tank 241-AP-102 as of October 1, 2012
- Completed RPP-RPT-50313, Rev. 1, Derivation of Best-Basis Inventory for Tank 241-AP-101 as of October 1, 2012
- Completed RPP-RPT-44049, Rev. 6, Derivation of Best-Basis Inventory for Tank 241-AZ-102 as of October 1, 2012

- Completed RPP-RPT-43498, Rev. 3, Derivation of Best-Basis Inventory for Tank 241-AP-105 as of October 1, 2012
- Completed RPP-RPT-48639, Rev. 5, Derivation of Best-Basis Inventory for Tank 241-AP-104 as of October 1, 2012
- Completed RPP-RPT-46686, Rev. 3, Derivation of Best-Basis Inventory for Tank 241-AW-106 as of October 1, 2012
- Completed RPP-RPT-46616, Rev. 4, Derivation of Best-Basis Inventory for Tank 241-C-104 as of October 1, 2012
- Completed RPP-RPT-48745, Rev. 3, Derivation of Best-Basis Inventory for Tank 241-C-107 as of October 1, 2012
- Completed RPP-RPT-44814, Rev. 9, Derivation of Best-Basis Inventory for Tank 241-AN-101 as of October 1, 2012
- Completed RPP-RPT-43992, Rev. 6, Derivation of Best-Basis Inventory for Tank 241-AN-106 as of October 1, 2012
- Completed RPP-RPT-51343, Rev. 2, Derivation of Best-Basis Inventory for Tank 241-C-109 as of October 1, 2012
- RPP-RPT-54104, Rev. 0, Final Report for Tank 241-AN-106 2012 Grab Samples in support of Chemical Adjustment and Waste Compatibility

Planned Action within the next Six Months:

- Tank Sampling
 - Tank 241-C-104 Off Riser Sampling System (ORSS) sampling for closure is currently scheduled for February 2013.
 - Tank 241-SY-102 grab sampling for chemistry control is currently scheduled for February 2013.
 - Tank 241-AN-101 grab sampling for chemistry control (C-101 mid-retrieval) is currently scheduled for February 2013.
 - Tank 241-AN-106 grab sampling for chemistry control (C-107 100% retrieval) is currently scheduled for March 2013.
 - Tank 241-C-109 ORSS sampling for closure is currently scheduled for March 2013.
 - Tank 241-AN-101 grab sampling for chemistry control (C-101 100% retrieval) is currently scheduled for February 2013.
 - Tank 241-AN-102 grab sampling for chemistry control is currently scheduled for April/May 2013.
- BBI Updates:
 - The tanks identified for updates in FY13 Quarter 2 are still being approved by ORP. The BBI updates will be issued in April 2013.
- Data Quality Objectives (DQO)
 - A DQO on a Solubility Model is due to be released in April 2013.

Issues:

None.

TANK OPERATIONS CONTRACT (TOC) OVERVIEW


Project Performance

The earned value performance reporting reflects the format, Work Breakdown Structure (WBS) reporting levels, and variance thresholds as agreed to with the Tank Farms Operations Contractor (TOC) for monthly performance reporting. The earned value analysis is not intended to be a measurement of performance against existing Tri-Party Agreement Milestones.


As of December 31, 2012, Washington River Protection Solutions LLC (WRPS) worked 6,061,210 hours (630 days) without a Lost Time Workday Injury and 28,081 hours (3 days) without a Recordable case. There were no Days Away, Restricted, or Transferred (DART) cases and one Recordable case in December.

WRPS Project Performance - (\$k)										
	BCWS	BCWP	ACWP	SV	CV	SPI	CPI	BAC	EAC	VAC
CM	33,795.0	30,044.9	29,940.1	(3,750.1)	104.8	0.89	1.00			
FYTD	91,056.8	86,275.9	87,098.1	(4,780.9)	(822.2)	0.95	0.99	420,271.2	397,118.6	23,152.6
CTD	1,695,156.8	1,685,152.1	1,612,243.8	(10,004.7)	72,908.3	0.99	1.05	6,997,663.6	6,907,663.7	89,999.9

Red shaded cells indicates a SPI/CPI less than .90;
 Green shaded cells indicate a SPI/CPI between .90 and .99; and
 Blue shaded indicates a SPI/CPI greater than or equal to 1.0

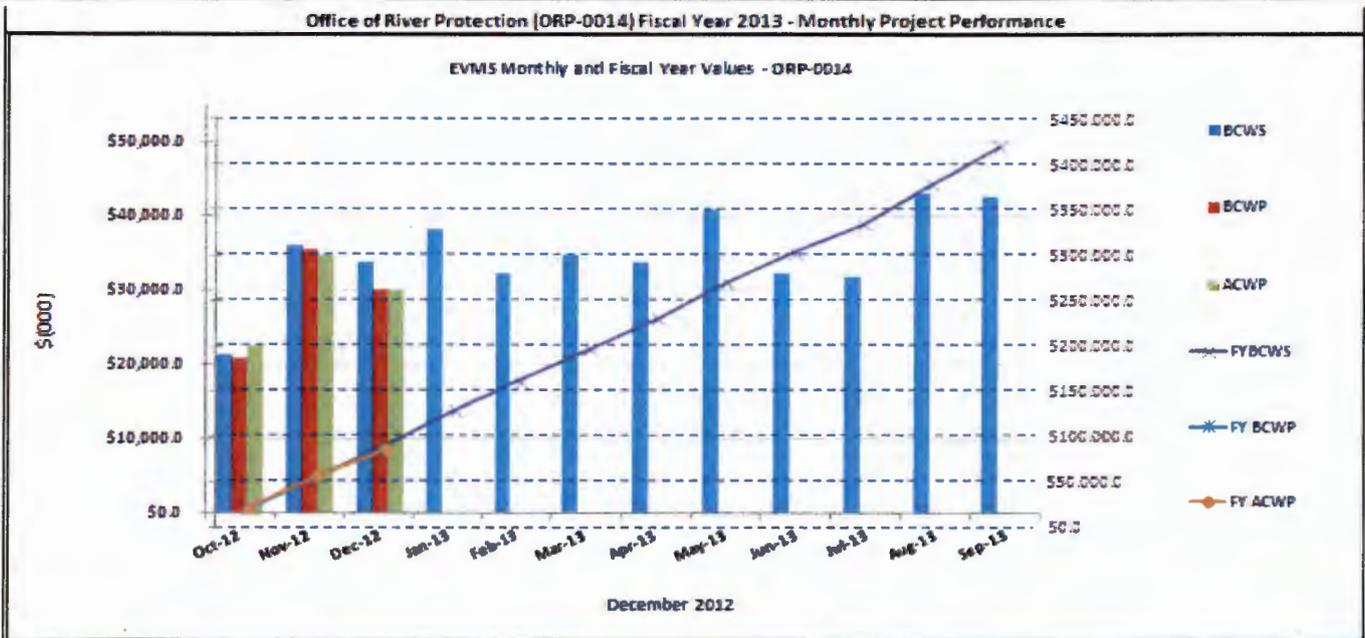

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct-12	\$21,350.5	\$20,911.7	\$22,382.9	0.98	0.93	\$21,350.5	\$20,911.7	\$22,382.9	0.98	0.93
Nov-12	\$35,910.8	\$35,319.2	\$34,775.1	0.98	1.02	\$57,261.3	\$56,230.9	\$57,158.0	0.98	0.98
Dec-12	\$33,795.4	\$30,044.9	\$29,940.1	0.89	1.00	\$91,056.7	\$86,275.8	\$87,098.1	0.95	0.99
Jan-13	\$38,179.6			0.00		\$129,236.3			0.00	
Feb-13	\$32,248.7			0.00		\$161,485.0			0.00	
Mar-13	\$34,599.7			0.00		\$196,084.7			0.00	
Apr-13	\$33,773.8			0.00		\$229,858.5			0.00	
May-13	\$40,892.1			0.00		\$270,750.6			0.00	
Jun-13	\$32,288.5			0.00		\$303,039.1			0.00	
Jul-13	\$31,800.4			0.00		\$334,839.5			0.00	
Aug-13	\$42,997.4			0.00		\$377,836.9			0.00	
Sep-13	\$42,434.3			0.00		\$420,271.2			0.00	
CTD	\$1,695,156.8	\$1,685,152.1	\$1,612,243.8	0.99	1.05					

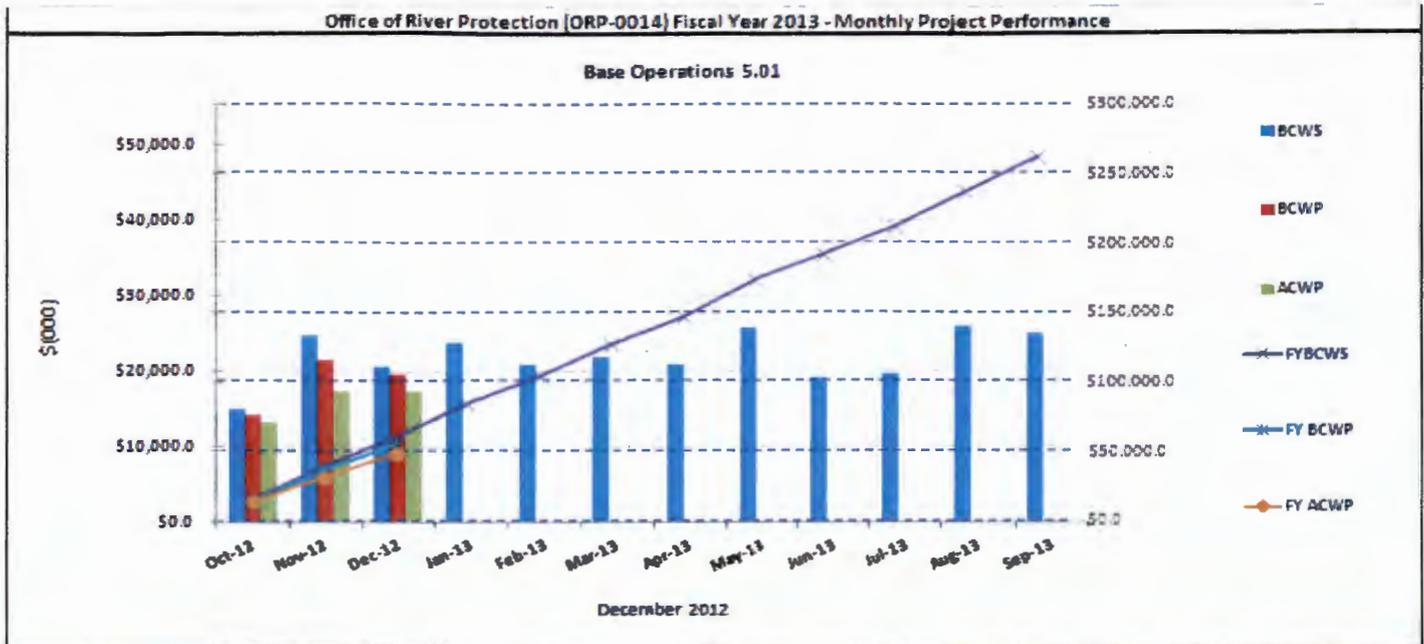

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct-12	\$14,882.7	\$14,170.4	\$13,207.0	0.95	1.07	\$14,882.7	\$14,170.4	\$13,207.0	0.95	1.07
Nov-12	\$24,586.3	\$21,630.8	\$17,422.8	0.88	1.24	\$39,469.0	\$35,801.2	\$30,629.8	0.91	1.17
Dec-12	\$20,440.9	\$19,491.2	\$17,422.8	0.95	1.12	\$59,909.9	\$55,292.4	\$48,052.6	0.92	1.15
Jan-13	\$23,738.1			0.00		\$83,648.0			0.00	
Feb-13	\$20,902.8			0.00		\$104,550.8			0.00	
Mar-13	\$21,758.8			0.00		\$126,309.6			0.00	
Apr-13	\$20,728.3			0.00		\$147,037.9			0.00	
May-13	\$25,607.5			0.00		\$172,645.4			0.00	
Jun-13	\$19,077.3			0.00		\$191,722.7			0.00	
Jul-13	\$19,634.2			0.00		\$211,356.9			0.00	
Aug-13	\$25,939.3			0.00		\$237,296.2			0.00	
Sep-13	\$24,820.9			0.00		\$262,117.1			0.00	
CTD	\$1,095,253.8	\$1,088,156.5	\$1,051,451.3	0.99	1.03					

Base Operations

Schedule Variance (\$3,751K):

The unfavorable schedule variance is primarily due to:


- DST Infrastructure Upgrades; completing installation of the AW, AN, SY, and AY/AZ ventilation flow test ports 2 months early by using an improved strategy to install ductwork saddles and performing a hot tap.
- 242-A Evaporator Operation and Maintenance; late release of design media impacting DSA implementation upgrades construction due to delays in finalizing the design basis safety requirements specifications.

Cost Variance \$105K:

The favorable cost variance is primarily due to:

- Base Operations Farms A/AX/AY/AZ, The CM favorable CV within the level-of-effort accounts is primarily due to labor resources charging out to Tank Farm Projects in support of the DST near-term extent-of-conditions workscope, specifically the 241-AY-102 biweekly annulus video and the work package preparation and fieldwork for 241-AY-101, 241-AZ-101, and 241-AZ-102 annulus videos.

Office of River Protection (ORP-0014) Fiscal Year 2013 - Monthly Project Performance

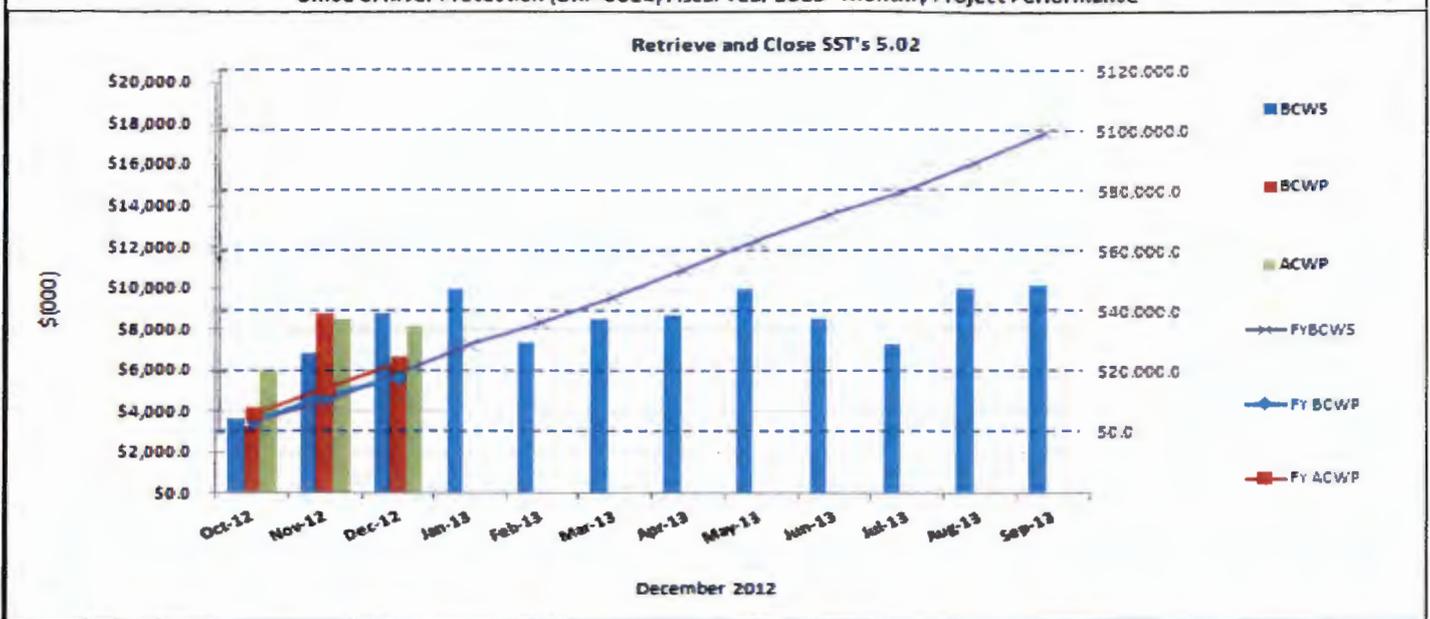

December 2012

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct-12	\$3,620.6	\$3,262.2	\$6,009.2	0.90	0.54	\$3,620.6	\$3,262.2	\$6,009.2	0.90	0.54
Nov-12	\$6,822.3	\$8,789.7	\$8,503.5	1.29	1.03	\$10,442.9	\$12,051.9	\$14,512.7	1.15	0.83
Dec-12	\$8,754.6	\$6,086.6	\$8,117.5	0.70	0.75	\$19,197.5	\$18,138.5	\$22,630.2	0.94	0.80
Jan-13	\$9,897.3			0.00		\$29,094.8			0.00	
Feb-13	\$7,352.9			0.00		\$36,447.7			0.00	
Mar-13	\$8,549.1			0.00		\$44,996.8			0.00	
Apr-13	\$8,677.0			0.00		\$53,673.8			0.00	
May-13	\$9,896.3			0.00		\$63,570.1			0.00	
Jun-13	\$8,470.0			0.00		\$72,040.1			0.00	
Jul-13	\$7,298.8			0.00		\$79,338.9			0.00	
Aug-13	\$9,902.0			0.00		\$89,240.9			0.00	
Sep-13	\$10,128.5			0.00		\$99,369.4			0.00	
CTD	\$358,896.5	\$359,047.6	\$356,626.0	1.00	1.01					

Single-Shell Tanks

Cost Variance (853K):

The unfavorable cost variance is primarily due to:

- Costs incurred for idle operation crews due to delays in declaring startup and readiness and C-101 retrieval operations.
- Installation and startup and readiness activities of the SST C-102 waste retrieval system.

The favorable CV was partially offset by:

- Cost savings by modifying the existing Fold-Track system instead of procuring a new hard heel removal unit for the next technology to be used in SST C-110.


Schedule Variance (\$497K):

The unfavorable schedule variance is primarily due to:

- Weather delays and resource availability issues that prevented the completion of AN-106 pump removal in December.
- One week of schedule delay was incurred because key resources for the pump removal were working on S-Complex HIHTL removals.
- High winds and associated cleanup work in mid-December resulted in another 1-week delay.

Office of River Protection (ORP-0014) Fiscal Year 2013 - Monthly Project Performance

WFD / Treatment Planning / DST Retrieval / Closure 5.03

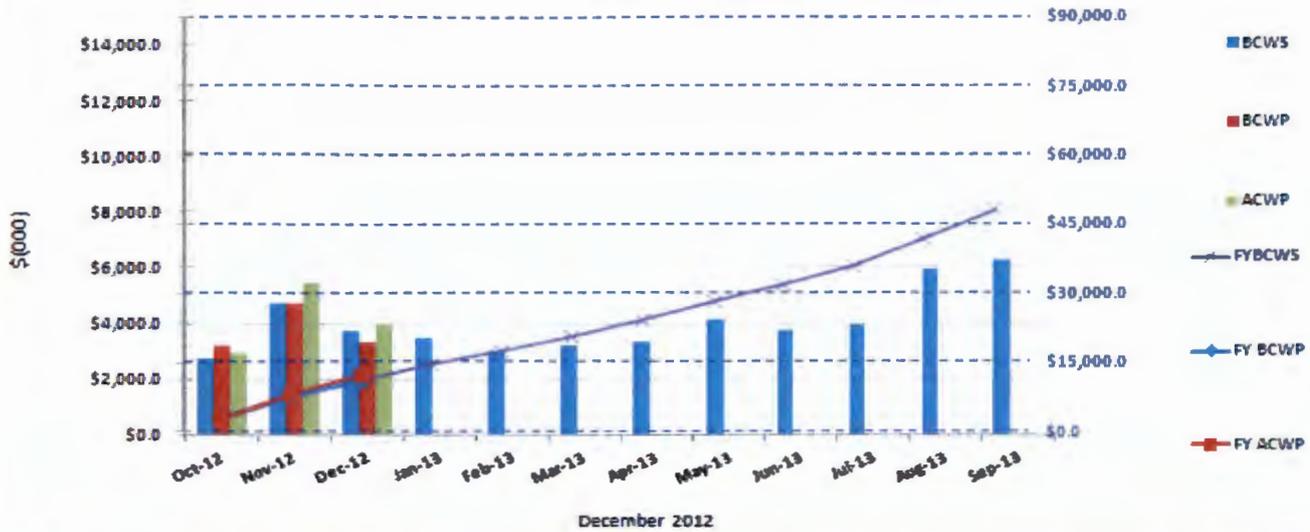


Earned Value Month	BCWS	BCVP	ACVP	SPI	CPI	FYBCWS	FY BCVP	FY ACVP	FY SPI	FY CPI
Oct-12	\$2,710.6	\$3,212.7	\$2,921.1	1.19	1.10	\$2,710.6	\$3,212.7	\$2,921.1	1.19	1.10
Nov-12	\$4,729.6	\$4,729.6	\$5,435.7	1.00	0.87	\$7,440.2	\$7,942.3	\$8,356.8	1.07	0.95
Dec-12	\$3,764.2	\$3,316.5	\$3,912.1	0.88	0.85	\$11,204.4	\$11,258.8	\$12,268.9	1.00	0.92
Jan-13	\$3,476.4			0.00		\$14,680.8			0.00	
Feb-13	\$2,991.4			0.00		\$17,672.2			0.00	
Mar-13	\$3,183.1			0.00		\$20,855.3			0.00	
Apr-13	\$3,354.2			0.00		\$24,209.5			0.00	
May-13	\$4,153.5			0.00		\$28,363.0			0.00	
Jun-13	\$3,727.7			0.00		\$32,090.7			0.00	
Jul-13	\$3,945.8			0.00		\$36,036.5			0.00	
Aug-13	\$5,937.2			0.00		\$41,973.7			0.00	
Sep-13	\$6,262.4			0.00		\$48,236.1			0.00	
CTD	\$224,641.2	\$221,308.3	\$190,096.4	0.99	1.16					

Waste Feed Delivery/Treatment/DST Retrieval Closure

Schedule Variance (\$797K):

The unfavorable schedule variance is primarily due to:

- WFD System Performance due to late completion of the scaled performance testing on the small-scale mixing demonstration platform because of equipment failures and having to repeat testing due to simulant mixing issues. Consequently, the start of the solids accumulation testing was delayed, compounded by the update of the analytic procedures due to changing the testing location to save on costs.
- AY/AZ Farm Infrastructure, The CM unfavorable SV is due to direction from DOE-ORP to suspend Waste Feed Delivery Systems projects as a result of the leak in AY-102. RPP-13-026, "ORP Direction for WFD Project FY13 Workslope," is being prepared to defer the FY 2013 workslope into FY 2014.
- AY-102 Tech Maturation Mixing/Sampling Demonstration, The CM unfavorable SV is due to DOE-ORP letter 12-CPM-0167, "Contract No. DE-AC27-08RV14800 – Direction to Stop Safety Significant (SS) Design Development on Tank AY-102 in Tank Upgrades." RPP-13-026, "ORP Direction for WFD Project FY13 Workslope," will be implemented to defer this scope to FY 2014.

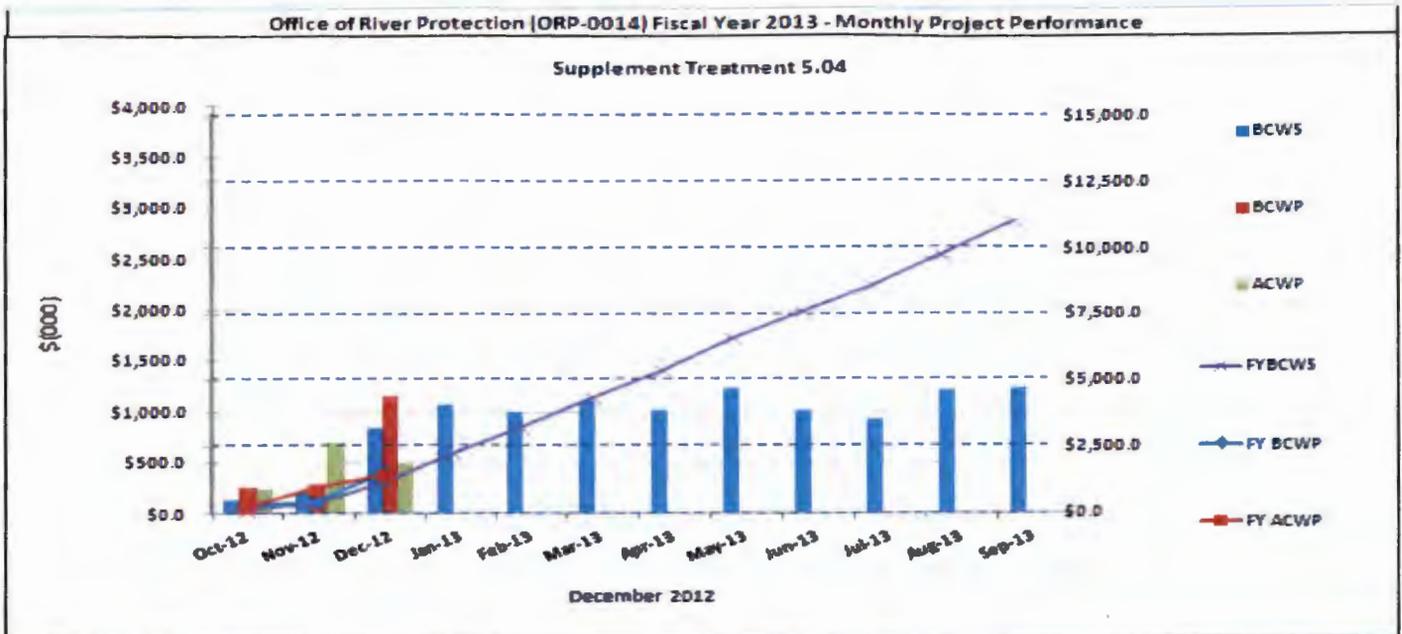

Earned Value Month	BCWS	BCWP	ACWP	SPI	CPI	FYBCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct-12	\$136.6	\$266.4	\$245.6	1.95	1.08	\$136.6	\$266.4	\$245.6	1.95	1.08
Nov-12	\$212.9	\$169.2	\$705.1	0.79	0.24	\$349.5	\$435.6	\$950.7	1.25	0.46
Dec-12	\$835.7	\$1,150.7	\$487.7	1.38	2.36	\$1,185.2	\$1,586.3	\$1,438.4	1.34	1.10
Jan-13	\$1,067.8			0.00		\$2,253.0			0.00	
Feb-13	\$1,001.5			0.00		\$3,254.5			0.00	
Mar-13	\$1,108.8			0.00		\$4,363.3			0.00	
Apr-13	\$1,014.3			0.00		\$5,377.6			0.00	
May-13	\$1,234.8			0.00		\$6,612.4			0.00	
Jun-13	\$1,013.5			0.00		\$7,625.9			0.00	
Jul-13	\$921.5			0.00		\$8,547.4			0.00	
Aug-13	\$1,218.8			0.00		\$9,766.2			0.00	
Sep-13	\$1,222.5			0.00		\$10,988.7			0.00	
CTD	\$16,365.3	\$16,639.6	\$14,070.0	1.02	1.18					

Supplemental Treatment

Schedule Variance \$315K:

The favorable schedule variance is primarily due to:

- Immobilization – Maturation, is due to the ability to correct unclaimed past performance, as BCR RPP-13-019, “Deletions/Modifications from Estimate Reviews,” was implemented this month.

WBS 5.2 Retrieve and Close Single Shell Tanks

M-045-20, Submit Interim Measure Investigation Work Plan to Ecology, Due: 12/31/12, Status: Completed on 12/06/12. ORP will submit to Ecology for review and approval an interim measures investigation work plan for to vadose zone characterization at 241-TX Farm and 241-U Farm, and soil desiccation/contaminant removal proof-of-principal test at 241-SX Farm. The work plan will also be submitted with a TPA Change Package to establish milestone due date for M-045-22 and target dates for submittal of three secondary documents, see M-045-22-T01, -T02, and -T03. Added per TPA change package M-45-12-04. ORP submitted this work plan and a draft TPA change package for dates for M-045-22 and its targets on 12/06/12 via letter 12-TF-0054. Ecology responded via 12-NWP-190 authorizing ORP to begin field work while Ecology completed their review of the Work Plan. Ecology provided comments on the Work Plan in the January 2013 TPA Project Managers' meeting. Comments have been resolved and revision to the Work Plan is underway.

M-045-21, Submit for Review and Approval a Sampling and Analysis Plan to Ecology for Soil Samples for 241-TX Tank Farm Investigation, Due: 03/31/2013, Status: On Schedule. Added per TPA change package M-45-12-04.

M-045-22, Review M-045-22-T03 Report and Determine Path Forward, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule. This ORP/Ecology decision point will determine whether to continue with soil desiccation/contaminant removal testing and other interim measures, and if remaining work in Milestone M-045-92 should be modified. Added per TPA change package M-45-12-04. ORP submitted a draft TPA change package for dates for M-045-22 and its targets on 12/06/12 via letter 12-TF-0054.

M-045-22-T01, Submit Results of Vadose Zone Characterization of 241-TX to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-22-T02, Submit Results of Vadose Zone Characterization of 241-U to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-22-T03, Submit SX Soil Desiccation/Contaminate Removal Tech Results to Ecology, Due: TBD based on M-045-20 TPA Change Package Submittal, Status: On Schedule.

M-045-56I, Complete Implementation of Agreed to Interim Measures, Due: 07/31/13, Status: On Schedule

M-045-59, Control surface water infiltration pathways as needed to control or significantly reduce the likelihood of migration of subsurface contamination to groundwater at the SST WMAS (pending the CMS report, milestone M-45-58, and implementation of other interim corrective measures), Due: TBD, Status: On Schedule

M-045-61, Submit to Ecology for review and approval as an Agreement primary document a Phase 2 RFI/CMS Report for WMA C, Due: 12/31/2014, Status: At Risk. Please see Issues.

M-045-62, Submit to Ecology for review and approval as an Agreement primary document a Phase 2 Corrective Measures Study Implementation Plan for WMA C, Due: 06/30/2015, Status: At Risk. Please see Issues.

M-045-92, DOE and Ecology will establish selection criteria for installation of additional interim barriers at additional WMAs (beyond the T-106 and TY barriers), Due: 09/30/2017, Status: On Schedule. This milestone date has been modified according to M-45-12-04 and the decision to move forward with construction/design of additional barriers dependent on discussions per M-045-22.

M-045-92N, Construct Barriers 1 and 2 in 241-SX Farm Due: 10/31/15, Status: On Schedule. The decision to move forward with construction/design of additional barriers is dependent on discussions per M-045-22.

M-045-92O, Submit a Final Design and Monitoring Plan for Interim Barrier 3 Due: 06/30/15, Status: On Schedule. The decision to move forward with construction/design of additional barriers is dependent on discussions per M-045-22.

Significant Past Accomplishments:

- Provided the interim measures investigation Work Plan for M-045-20 and draft TPA change package for M-045-22 and its targets via ORP letter 12-TF-0054 on 12/06/12.
- Automated data collection systems for T-Farm and TY Farm interim barrier monitoring continue gathering data.
- Ground penetrating radar was performed in C farm near the C-200s to support direct push work.
- Ground penetrating radar was performed in U farm, TX farm, and south of SX farm to support interim measures investigation described in the M-045-20 work plan.
- Direct push field work was initiated south of SX farm under the M-045-20 work plan.

Significant Planned Actions in the Next Six Months:

- Revise the TY Interim Surface Barrier Monitoring Plan, per approved TPA Change Notice 2012-09.
- Provide the Sample Analysis Plan for 241-TX Farm for M-045-21.
- Initiate direct push field work in TX farm under the M-045-20 work plan.
- Initiate electrical resistivity field work in U farm under the M-045-20 work plan.
- Perform direct push/electrical resistivity field work near the C-200 tanks per the WMA C Phase 2 RFI/CMS Work Plan.

SST Retrieval and Closure Program

M-045-82, Submit complete permit mod requests for Tiers 1, 2, & 3 of the SST, Due: 9/30/2015 Status: At Risk. Please see Issues.

M-045-84, Complete negotiations of TPA interim MS for closure of second WMA, Due: 1/31/2017, Status: On Schedule

M-045-83, Complete the closure of WMA C, Due: 6/30/2019, Status: On Schedule

M-045-85, Complete negotiations of TPA interim MS for closure of remaining WMAs, Due: 1/31/2022, Status: On Schedule

M-045-70, Complete waste retrieval from all remaining SSTs, Due: 12/31/2040, Status: On Schedule

M-045-00, Complete Closure of all Single Shell Tank Farms, Due: 1/31/2043, Status: On Schedule

M-045-86, Submit retrieval data report to Ecology for 19 tanks retrieved, Due: TBD (12 months after retrieval certification), Status: On Schedule

Significant Past Accomplishments:

- Completed post-retrieval sampling, analysis and reporting of results for tank C-108 in support of the M-045-86 retrieval data report.
- See discussions above and related discussions in Consent Decree report.

Significant Planned Activities in the Next Six Months:

- Perform post-retrieval logging of drywells near C-108 in support of the M-045-86 retrieval data report.
- See discussions above and related discussions in Consent Decree report.

Issues:

The WMA-C performance assessment is not funded currently in fiscal year 2013. ORP needs to restart the WMA-C performance assessment by March 31, 2013 or milestone M-45-82 will be missed, and will require that other existing data be utilized for M-45-61 and M-45-62 to keep their existing milestone dates. ORP is working to identify funding to restart the WMA-C performance assessment on or before March 31, 2013.

Tank Waste Retrieval Work Plan (TWRWP) Status

Tank	TWRWP	Expected Revisions	Retrieval Technology	Second Technology	Third Technology
C-101	RPP-22520, Rev. 7	Complete	MRS (per 10/7/10 agreement, to be Modified Sluicing)	High-Pressure Water with ERSS	-
C-102	RPP-22393, Rev. 6A	In Process	Modified Sluicing	High-Pressure Water with ERSS	-
C-104	RPP-22393, Rev. 6A	Complete	Modified Sluicing	Chemical Dissolution	-
C-105	RPP-22520, Rev. 7	Complete	MARS-V	MARS-High Pressure Water	-
C-107	RPP-22393, Rev. 6A	Complete	MARS-S	MARS-High Pressure Water	-
C-108	RPP-22393, Rev. 6A	Complete	Modified Sluicing	Chemical Dissolution	-
C-109	RPP-21895, Rev. 5	Complete	Modified Sluicing	Chemical Dissolution	-
C-110	RPP-33116, Rev. 2	Complete	Modified Sluicing	Mechanical Waste Conditioning	High Pressure Water
C-111	RPP-37739, Rev. 1	In process	Modified Sluicing	None	-
C-112	RPP-22393, Rev. 6A	In process	Modified Sluicing	Chemical Dissolution	-

Significant Accomplishments

C-110 TWRWP modification 2012-13 approved.

Significant Planned Activities in the Next 6 Months:

Work with Ecology on updates to TWRWPs RPP-22393, RPP-22520 and RPP-37739 for tanks C-105, C-111, and C-112.

Issues:

None.

Tank in Appendix H. Status - Single Shell Waste Retrieval Criteria

Tank 241-C-106

Significant Past Accomplishments:

None

Significant Planned Activities in the Next Six Months:

Continue U.S. Nuclear Regulatory Commission (NRC) review of the C-106 exception request. A Request for Additional Information (RAI) was received from the NRC in February 2009.

Issues:

It has been discussed with the NRC that much of the additional information requested is dependent upon development of C-Farm residual waste PA and, therefore, cannot be provided until the PA is published.

Tank Retrievals with Individual Milestones

Tank 241-A-103

M-045-15, Completion of Tank A-103 SST Waste Retrieval, Due: 9/30/22 Status: On schedule. Change package M-45-11-04 replaced tank S-102 with tank A-103 and changed to milestone completion date for M-045-15 to 09/30/2022.

M-045-15A, Embedded Milestone, Submit a Retrieval Data Report Pursuant to Agreement Appendix I, Due: 9/30/22, Status: On schedule. Updated with tank A-103 and due date of 9/30/22 per M-45-11-04 Change Package.

M-045-15D, Embedded Milestone, if appropriate, DOE will request an exception to waste retrieval criteria pursuant to Agreement Appendix H, Due: 9/30/22, Status: On Schedule. Updated with A-103 tank and due date of 9/30/22 per M-45-11-04 Change Package.

Significant Past Accomplishments:

Change Package M-45-11-04 was signed by ORP and Ecology on 04/19/11.

Significant Planned Activities in the Next Six Months and Issues:

None

Tank 241-S-112

M-045-13, Interim Completion of Tank S-112 SST Waste Retrieval and Closure Demonstration Project, Due: TBD (in accordance with M-045-84 or M-045-85), Status: On Schedule

M-045-13E, Complete Negotiations for Interim Milestones for Closure of S-112, Due: TBD Status: On Schedule as part of M-045-84 or M-045-85.

Significant Past Accomplishments:

Ecology letter of January 7, 2008, concurred with ORP that retrieval of Tank S-112 is complete.

Significant Planned Activities in the Next Six Months or Issues:

None.

WASTE TREATMENT AND IMMOBILIZATION PLANT (WTP) PROJECT

Number	Title	Due Date	Status
M-062-01Z	Submit Semi-Annual TPA Project Compliance Report	01/31/2013	Complete
M-062-01AA	Submit Semi-Annual TPA Project Compliance Report	7/31/2013	On Schedule

***SEE THE FEBRUARY 2013 ORP CONSENT DECREE 08-5085-FVS
MONTHLY SUMMARY REPORT FOR WTP FACILITY-SPECIFIC
INFORMATION**
