

Office of River Protection



Monthly Reporting Period

March 1–March 31, 2019¹

¹ The narrative descriptions of progress in this report cover the reporting period. Information outside the reporting period may also be included for purposes of providing continuity or useful context. Information may be repeated in multiple sections of this report for continuity and clarity. Earned Value Management System data and descriptions cover the period through February 2019.

Topic	Page
Acronyms and Abbreviations	2
Administrative Items/Milestone Status.....	3
System Plan.....	6
Acquisition of New Facilities	7
Supplemental Treatment and Part B Permit Applications	8
Tank-Side Cesium Removal System	10
242-A Evaporator Status.....	12
Liquid Effluent Retention Facility and 200 Area Effluent Treatment Facility.....	13
Tank System Update	15
In-Tank Characterization and Summary.....	18
Single-Shell Tank Closure Program	21
Single-Shell Tank Retrieval Program	25
Tank Operations Contract Overview	26

Acronyms and Abbreviations

CV	cost variance
DOE	U.S. Department of Energy
Ecology	Washington State Department of Ecology
ETF	Effluent Treatment Facility
FY	fiscal year
HFFACO	<i>Hanford Federal Facility Agreement and Consent Order</i> (HFFACO and TPA are used interchangeably throughout this report)
IQRPE	independent, qualified, registered, professional engineer
ORP	U.S. Department of Energy, Office of River Protection
SST	single-shell tank
SV	schedule variance
TPA	Tri-Party Agreement
TSCR	tank-side cesium removal
WMA	waste management area
WRPS	Washington River Protection Solutions LLC

Administrative Items/Milestone Status

Milestone	Title	Due Date	DOE PM	Status
Prior Years				
M-062-45-T01	Complete Negotiations 6-Months After Last Issuance of System Plan	04/30/2015	R. Bang	In Abeyance
M-062-45-ZZ	Negotiate a One-Time Supplemental Treatment Selection	04/30/2015	R. Bang	In Abeyance
M-062-45-ZZ-A	Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones	04/30/2015	R. Bang	In Abeyance
M-047-07	CD-1 for Secondary Liquid Waste Treatment and CR for CD-2 to Ecology	03/31/2016	J.A. Diediker	In Abeyance
M-090-13	CD-1 for Interim Hanford Storage Project and CR for CD-2 to Ecology	03/31/2016	J.A. Diediker	In Abeyance
M-062-31-T01	Complete Final Design & Submit RCRA Part B Permit Mod Request for Enhanced WTP & Supplemental Treatment	04/30/2016	R. Bang	In Abeyance
M-062-32-T01	Start Construction of Supplemental Vitrification Facility and/or WTP Enhancements	04/30/2018	R. Bang	In Abeyance
Fiscal Year 2019				
M-062-01AL	Submit Semi-Annual Project Compliance Report to Ecology	01/31/2019	B.R. Trimberger	Complete
M-062-01AM	Submit Semi-Annual Project Compliance Report to Ecology	07/31/2019	B.R. Trimberger	On Schedule

Milestone	Title	Due Date	DOE PM	Status
M-045-56O	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)	07/31/2019	R.A. Lobos ¹	On Schedule
M-045-91E3	Provide SST Farms Dome Deflection Surveys Every 2 Years to Ecology	09/30/2019	D.M. Stewart	On Schedule
M-045-59	Control Surface Water Infiltration Pathways as Needed	TBD ²	R.A. Lobos ¹	On Schedule
M-045-62	Submit the Draft Tier 3 Closure Plan with Corrective Measures in Phase 2 CMIP for WMA-C	TBD ²	R.A. Lobos ¹	On Schedule
M-045-83	Complete the Closure of WMA-C by Completing Closure Activities Specified in the Tier 2 Closure Plan	TBD ²	R.A. Lobos ¹	On Schedule
Fiscal Year 2020				
M-062-40G	Select a Minimum of 3 Scenarios	10/31/2019	K.W. Burnett	On Schedule
M-045-92V	Complete Construction of Barriers 1 (North) and 2 (South) and Expansion Barrier in 241-SX Farm	10/31/2019	R.A. Lobos ¹	On Schedule
M-045-92W	Submit to Ecology Design for Barrier 3 in 241-TX Farm	10/31/2019	R.A. Lobos ¹	On Schedule
M-045-92AC	Submit to Ecology for Approval a Maintenance and Performance Monitoring Plan for Interim Barriers	10/31/2019	R.A. Lobos ¹	On Schedule

Milestone	Title	Due Date	DOE PM	Status
M-045-92X	Barrier 3 in 241-TX Farm Design Approved by Ecology	01/31/2020	R.A. Lobos ¹	On Schedule
M-062-01AN	Submit Semi-Annual Project Compliance Report to Ecology	01/31/2020	B.R. Trimberger	On Schedule
M-062-01AO	Submit Semi-Annual Project Compliance Report to Ecology	07/31/2020	B.R. Trimberger	On Schedule
M-045-56P	Ecology and DOE Agree, at a Minimum, to Meet Yearly (by July)	07/31/2020	R.A. Lobos ¹	On Schedule

¹ In March 2019, Rod Lobos replaced Jan Bovier as the project manager.

² To be established in accordance with the date identified in the M-045-82 Tier 2 closure plan.

CD-1/-2 = critical decision-1/-2.

CMIP = corrective measures implementation work plan.

CR = change request.

DOE = U.S. Department of Energy.

Ecology = Washington State Department of Ecology.

Mod = modification.

PM = project manager.

RCRA = *Resource Conservation and Recovery Act*.

SST = single-shell tank.

TBD = to be determined.

WTP = Waste Treatment and Immobilization Plant.

WMA-C = C Tank Farm waste management area.

System Plan

Responsible Assistant Manager: TBD
Federal Program Manager: Kaylin Burnett
Ecology Project Manager: Dan McDonald, Jeff Lyon

Significant Past Accomplishments

- The U.S. Department of Energy (DOE), Office of River Protection (ORP); U.S. Environmental Protection Agency; and Washington State Department of Ecology (Ecology) have been in negotiations related to M-062-45 Milestone since September 2016. The parties have agreed on multiple occasions that it was prudent to extend the completion of the negotiations. DOE and Ecology met on October 30, 2018, to discuss, amongst other things, the M-062-45 Milestone and DOE's mark-up of Ecology's proposal. DOE and Ecology agreed to meet regularly to continue these discussions and have agreed to additional extensions of the negotiations until April 19, 2019.

Significant Planned Actions in the Next Six Months

- Continue negotiations of the M-062-45 Milestone and related milestones using information from the ORP-11242, *River Protection Project System Plan*, Rev. 8.
- Ecology and ORP will continue discussions to develop scenarios for System Plan, Rev. 9, due October 31, 2019.

Issues

- None.

Acquisition of New Facilities

Tank Farms Assistant Manager: Rob Hastings
Deputy Federal Project Director: Janet Diediker
Ecology Project Manager: Dan McDonald, Jeff Lyon

The current status for all projects listed below is:

- In Abeyance. Decision document 2016-005, *Hanford Federal Facility Agreement and Consent Order Interagency Management Integration Team (IAMIT) Decision/Determination/Action Agreement*, signed August 22, 2016, requires addressing this milestone with the negotiations supporting M-062-45 Milestone. Negotiations began on September 8, 2016.

M-047-07 CD-1 for Secondary Liquid Waste Treatment and CR² for CD-2 to Ecology

Due: March 31, 2016.

M-090-13 CD-1 for Interim Hanford Storage Project and CR for CD-2 to ECY³

Due: March 31, 2016.

M-090-00 Acquire/Modify Facilities for Storage of First Two Years of IHLW⁴ from the WTP⁵ Operations

Due: December 31, 2036.

M-047-00 Completion of Work for Management of Secondary Waste from the WTP

Due: To Be Determined.

Significant Past Accomplishments

- See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Significant Planned Actions in the Next Six Months

- See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Issues

- None.

² TPA Change Request.

³ ECY denotes Washington State Department of Ecology.

⁴ IHLW denotes immobilized high-level waste.

⁵ WTP denotes Waste Treatment and Immobilization Plant.

Supplemental Treatment and Part B Permit Applications

Tank Farms Assistant Manager: Rob Hastings
Federal Project Director: Ricky Bang
Ecology Project Manager: Dan McDonald

The current status for each of the projects listed below, unless noted differently, is:

- In Abeyance. Decision document 2016-005, signed August 22, 2016, requires addressing this milestone with the negotiations supporting M-062-45 Milestone. Negotiations began on September 8, 2016.

M-062-45-T01 Complete Negotiations 6-Months after Last Issuance of System Plan

Due: April 30, 2015.

M-062-45-ZZ Negotiate a One-Time Supplemental Treatment Selection

Due: April 30, 2015.

M-062-45-ZZ-A Convert M-062-31-T01 through M-062-34-T01 to Interim Milestones

Due: April 30, 2015.

M-062-31-T01 Complete Final Design and Submit RCRA⁶ Part B Permit Modification Request for Enhanced WTP & Supplemental Treatment

Due: April 30, 2016.

M-062-32-T01 Start Construction of Supplemental Vitrification Facility and/or WTP Enhancements

Due: April 30, 2018.

M-062-33-T01 Complete Construction of Supplemental Treatment Vitrification Facility and/or WTP Enhancements

Due: April 30, 2021.

M-062-45-XX Complete Negotiations to Resolve Future Disputes M-062-45, Paragraphs 4 and 5

Due: December 31, 2021.

Status: On Schedule.

⁶ RCRA denotes *Resource Conservation and Recovery Act*.

M-062-34-T01 Complete Hot Commissioning of Supplemental Treatment Vitrification Facility and/or WTP Enhancements

Due: December 30, 2022.

M-062-21 Annually Submit Data Which Demonstrates Operation of the WTP at a Rate Sufficient to Meet M-062-00

Due: February 28, 2023.

Status: At risk.

M-062-00 Complete Pretreatment Processing and Vitrification of HLW⁷ and LAW⁸ Tank Wastes

Due: December 31, 2047.

Status: At risk.

Significant Past Accomplishments

- See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Significant Planned Actions in the Next Six Months

- See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Issues

- None.

⁷ HLW denotes high-level waste.

⁸ LAW denotes low-activity waste.

Tank-Side Cesium Removal System

Tank Farms Assistant Manager: Rob Hastings
Federal Project Manager: Sahid Smith
Ecology Project Manager: Dan McDonald

This section only covers the Tank Farms Project scope of the direct-feed low-activity waste mission. Please refer to the Consent Decree monthly report for the Waste Treatment and Immobilization Plant Project scope pertaining to direct-feed low-activity waste.

Significant Past Accomplishments

- The tank-side cesium removal (TSCR) system 60 percent design review was completed in January 2019.
- The waste feed delivery system 60 percent design review was initiated in January 2019.

Significant Planned Actions in the Next Six Months

- The TSCR spent ion exchange column storage pad 60 percent design review is projected to begin in April 2019.
- The TSCR system 90 percent design review is projected to begin in April 2019.
- The waste feed delivery system 90 percent design review is projected to begin in April 2019.
- The tank farm infrastructure upgrades system 90 percent design review is projected to begin in May 2019.
- The TSCR spent ion exchange column storage pad 90 percent design review is projected to begin in June 2019.

Issues

- Since April 2018, DOE and Ecology have been engaged in discussions on the potential regulatory significance of the TSCR emissions. Ecology has expressed a concern about permitting a system that sends air emissions or ventilation to a double- or single-shell tank. Based on recent discussions, and to address Ecology's concerns, ORP is developing and evaluating potential options for sampling and monitoring TSCR emissions vented to the AP Tank Farm.
- On December 3, 2018, Ecology sent ORP and the DOE Richland Operations Office a letter (18-NWP-177, "Hanford Site Ambient Air Boundary Concerns") regarding the Hanford Site ambient air boundary. Ecology expressed its concern that the ambient air boundary appears to have changed as a result of increased public access to parts of the Hanford Site. DOE, Ecology, and the Washington State Department of Health have met several times to attempt to develop a shared understanding of existing conditions and a path forward.

242-A Evaporator Status

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Paul Hernandez
Ecology Project Manager: Jeff Lyon

The 242-A Evaporator campaign strategy for fiscal year (FY) 2019 is in the following table:

Fiscal Year	Campaign No.	Feed Source	Slurry Tank	Comments
2019	EC-10	102-AW	102-AW	A cold run followed by a short hot run will be performed at 242-A Evaporator while efforts to install new slurry transfer lines from 242-A Evaporator to 241-AW Tank Farm progress. This maintains 242-A Evaporator staff proficiency and allows for new equipment testing. This work effort is scheduled for June 2019.

Significant Past Accomplishments

- Completed rebuild of the spare PB-1 pump, now located in the 242-A Evaporator load-out room
- Received permission from Ecology to perform campaign EC-10.

Significant Planned Actions in the Next Six Months

- Establish future campaign and outage scheduling
- Perform campaign EC-10 prior to June 26, 2019
- Continue design efforts related to installation of new slurry transfer lines from 242-A Evaporator to AW Tank Farm
- Prepare for removal of installed PB-1 pump and installation of rebuilt spare PB-1 pump
- Procure new PB-1 and PB-2 replacement pumps
- Prepare 242-A Evaporator air instrument dryer upgrade design
- Prepare 60 percent design for 242-A Evaporator slurry line replacement.

Issues

- Ecology provided a second set of comments on the 2016 independent, qualified, registered, professional engineer (IQRPE) Integrity Assessment Report for 242-A Evaporator. DOE expects to provide the second set of responses to Ecology in April 2019.

Liquid Effluent Retention Facility and 200 Area Effluent Treatment Facility

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Richard Valle
Ecology Project Manager: Stephanie Schleif

The Liquid Effluent Retention Facility liquid levels, inventory, and received waste are shown in the table below. Volumes in the table are estimated. Tanker shipment volumes are estimated by multiplying the number of shipments by the capacity of the tanker being used.

	242AL-42 (Basin 42)	242AL-43 (Basin 43)	242AL-44 (Basin 44)
Total Volume (as of Mar 31, 2019)	~ 7.17 Mgal	~ 6.23 Mgal	~ 0.70 Mgal

Waste Received			
AZ-301 Condensate	-	~ 2,500 gal	-
MWT-31 and 34 Leachate	-	~ 168,000 gal	-
Other (325 RPS)	-	1,200 gal	-

gal = gallon.

Mgal = million gallons.

MWT = mixed waste trench.

RPS = radioactive process sewer (process wastewater generated from laboratory research, steam condensate, air conditioner condensate, compressed air system blowdown, and fire suppression system water).

Significant Past Accomplishments

- Total FY 2019 volume processed (as of March 31, 2019): approximately 0 gallons
- Continued installation of the three replacement surge pumps and their associated equipment
- Completed construction and commissioning of Effluent Treatment Facility (ETF) air compressor upgrade
- Completed visual inspections of the pH adjust tank and evaporator vapor body in support of the ETF integrity assessment.

Significant Planned Actions in the Next Six Months

- Complete plant cleanout and corrective maintenance outage
- Complete remaining fieldwork (i.e., visual inspections and leak test) for the ETF integrity assessment

- Initiate waste processing of Liquid Effluent Retention Facility Basin 42 effluent through ETF.

Issues

- None.

Tank System Update

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Dustin Stewart
Ecology Project Manager: Jeff Lyon, Cheryl Whalen

Reports are identified as completed (internal access only) or released (external access).

Double-Shell Tank Integrity

Significant Past Accomplishments

- The annual comprehensive inspection of Tank AY-101 annulus was completed in January 2019. Engineering is reviewing the inspections. The previous annulus visual inspection was completed in January 2018.
- Ultrasonic testing inspections were completed for the following tanks in FY 2019:
 - 241-AP-107
 - 241-AP-108
 - 241-AP-108 air slots inspection
- Completed enhanced annulus visual inspection in FY 2019:
 - 241-AN-107.

Significant Planned Actions in the Next Six Months

- Ultrasonic testing inspections is planned for the following tanks in FY 2019:
 - 241-AP-102 (annulus floor only)
 - 241-AN-102 (ultrasonic testing; air slots inspection)
 - 241-AP-106 (annulus floor only; air slots inspection).
- Enhanced annulus visual inspections is planned for the following tanks in FY 2019:
 - 241-AN-101
 - 241-AN-102
 - 241-AN-103
 - 241-AN-104
 - 241-AN-105
 - 241-AN-106
 - 241-AZ-101 (ongoing)
 - 241-AZ-102.
- Procure/Design annulus floor cleaning technology in FY 2019 to clean the annulus floor of Tank AY-101.
- Procure a design of a primary tank bottom volumetric inspection system to be deployed into the annulus of double-shell tanks and used to characterize regions of the primary tank bottom.

Issues

- None.

Single-Shell Tank Integrity**Significant Past Accomplishments**

- Visual inspections were completed for the following tanks in FY 2019:
 - 241-B-102
 - 241-B-103
 - 241-BX-104
 - 241-B-110
 - 241-B-111
 - 241-B-112
 - 241-SX-114.

Significant Planned Actions in the Next Six Months

- Visual inspections are planned for the following tanks in FY 2019:
 - 241-SX-115
 - 241-U-101
 - 241-U-106
 - 241-U-109
 - 241-T-103
 - 241-T-108
 - 241-T-202
 - 241-TY-106.
- Perform the following three miscellaneous underground storage tank visual camera inspections in FY 2019:
 - Catch tank 204-AR-TK-1
 - 241-A-302-A
 - 242-A-302-B.
- Perform TFC-ENG-CHEM-D-42, *Tank Leak Assessment Process*, on the following tanks in FY 2019:
 - 241-T-101 (ongoing)
 - 241-T-103.

Issue

- None.

Independent Qualified Registered Professional Engineer Activities

- Double-shell tank system:
 - RPP-RPT-58441, *Double-Shell Tank System Integrity Assessment Report (DSTAR)*, Rev. 1, was completed in 2016.
 - The IQRPE recommended the next double-shell tank system integrity assessment report be completed in 10 years.
- Single-shell tank (SST) system:
 - Completed M-045-9II Milestone report RPP-IQRPE-50028, *Single-Shell Tank System Structural Integrity Assessment Report*, in 2018.
 - The IQRPE recommended the next SST structural integrity assessment be completed in 16 years.
- 242-A Evaporator:
 - Completed RPP-RPT-60098, *242-A Evaporator System Integrity Assessment Report*, Rev. 0, in 2018.
 - The IQRPE recommended the next 242-A Evaporator system integrity assessment be completed in 15 years.
- ETF:
 - Washington River Protection Solutions LLC (WRPS) provided technical material and support needed to perform the ETF integrity assessment to the IQRPE project team. A meeting was held between WRPS and Meier Architecture Engineering personnel to discuss potential requests for additional testing or inspections to support the integrity assessment.
- 219-S Tank system:
 - WRPS awarded the contract for the 219-S integrity assessment project to Meier Architecture Engineering.
 - As part of the 219-S assessment, the 24-hour static leak test was successfully performed on tanks 101 and 104 on September 13, 2018, and September 5, 2018, respectively. Tank 102 is next to be leak tested (forecasted for April 2019). Work packages for the internal and external visual inspections of the tanks and associated piping have been drafted and are under review.

In-Tank Characterization and Summary

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Dustin Stewart
Ecology Project Manager: Jeff Lyon

Reports Completed or Released

For March 2019, the following reports were completed (internal access only) or released (external access):

- Completed:
 - None
- Released:
 - RPP-RPT-43493, *Derivation of Best-Basis Inventory for Tank 241-AP-106 as of January 1, 2019*, Rev. 7
 - RPP-RPT-54017, *Derivation of Best-Basis Inventory for Tank 241-AP-102 as of January 1, 2019*, Rev. 10
 - RPP-RPT-59510, *Derivation of Best-Basis Inventory for Tank 241-B-201 as of January 1, 2019*, Rev. 1
 - RPP-RPT-44049, *Derivation of Best-Basis Inventory for Tank 241-AZ-102 as of January 1, 2019*, Rev. 12 and Rev. 13
 - RPP-RPT-60009, *Derivation of Best-Basis Inventory for Tank 241-BX-106 as of January 1, 2019*, Rev. 1
 - RPP-RPT-44814, *Derivation of Best-Basis Inventory for Tank 241-AN-101 as of February 1, 2019*, Rev. 26
 - RPP-RPT-56803, *Derivation of Best-Basis Inventory for Tank 241-BX-103 as of January 1, 2019*, Rev. 2
 - RPP-RPT-43992, *Derivation of Best-Basis Inventory for Tank 241-AN-106 as of March 1, 2019*, Rev. 21
 - RPP-RPT-44637, *Derivation of Best-Basis Inventory for Tank 241-AZ-101 as of January 1, 2019*, Rev. 14
 - RPP-RPT-44625, *Derivation of Best-Basis Inventory for Tank 241-AW-105 as of January 1, 2019*, Rev. 6
 - HNF-EP-0182, *Waste Tank Summary Report for Month Ending January 31, 2019*, Rev. 373
 - HNF-EP-0182, *Waste Tank Summary Report for Month Ending February 28, 2019*, Rev. 374.

Tank Sampling

Significant Past Accomplishments

For March 2019, the following tank sampling was conducted:

- Tank 241-SY-102 grab sampling was completed and samples were shipped for laboratory analysis.

Significant Planned Actions in the Next Six Months

Future tank sampling is scheduled to be performed as identified below:

- Tank 241-AW-103 grab sampling is planned for April 2019.
- Tank 241-AN-107 grab sampling is planned for May 2019.
- 241-AY-101 core sampling is planned for June 2019.
- Tank 241-AZ-101 grab sampling is planned for June 2019.
- Catch Tank 241-C-301 closure grab sampling is planned for July 2019.
- Tank 241-AP-106 post-repurposing grab sampling is planned for August 2019.
- 241-A-104 solids grab sampling is planned for September 2019.

Issues

- None.

Best-Basis Inventory Updates

Significant Past Accomplishments

- Best-basis inventory updates for the following tanks were completed in March 2019:
 - 241-AN-101
 - 241-AN-106
 - 241-AP-102
 - 241-AP-106
 - 241-AW-105
 - 241-AZ-101
 - 242-AZ-102
 - 241-B-201
 - 241-BX-103
 - 241-BX-106.

Significant Planned Actions in the Next Month

- Best-basis inventory updates for the following tank are currently planned to be completed in April 2019:
 - 241-SY-101.

Issues

- None.

Single-Shell Tank Closure Program

Tank Farms Assistant Manager: Rob Hastings

Federal Program Manager: Rod Lobos

Ecology Project Manager: Jeff Lyon

M-045-59 Control Surface Water Infiltration Pathways as Needed

Due: To Be Determined. Will be implemented if needed to control or significantly reduce the likelihood of migration of subsurface contamination to groundwater at the SST waste management areas (WMA) (pending the corrective measures study report, M-45-58 Milestone, and implementation of other interim corrective measures).

Status: On Schedule.

M-045-62 Submit the Draft Tier 3 Closure Plan with Corrective Measures in Phase 2 Corrective Measures Implementation Work Plan (CMIP) for WMA-C⁹

Due: To Be Determined. To be established in accordance with the date identified in the M-45-82 Milestone Tier 2 closure plan.

Status: On Schedule.

M-045-83 Complete the Closure of WMA-C by Completing Closure Activities Specified in the Tier 2 Closure Plan

Due: To Be Determined. To be established in accordance with the date identified in the M-45-82 Milestone Tier 2 closure plan.

Status: On Schedule.

M-045-84 Initiate Negotiations to Establish HFFACO¹⁰ Interim Milestones for Closure of 2nd SST WMA

Due: April 3, 2017.

Status: Completed (March 14, 2017). Negotiations initiated on March 14, 2017.

Note: Decision on location of next WMA to be closed needs to be finalized.

⁹ WMA-C denotes C Tank Farm waste management area.

¹⁰ HFFACO denotes *Hanford Federal Facility Agreement and Consent Order* (HFFACO and the Tri-Party Agreement [TPA] are used interchangeably throughout this report).

- M-045-92V Complete Construction of Barriers 1 (South) and 2 (North) and Expansion Barrier in 241-SX Farm**
Due: October 31, 2019.
Status: On Schedule.
Note: This includes the construction of the SX Tank Farm expansion barrier as well.
- M-045-92W Submit to Ecology Design for Barrier 3 in 241-TX Farm**
Due: October 31, 2019.
Status: On Schedule.
- M-045-92AC Submit to Ecology for Approval a Maintenance and Performance Monitoring Plan for Interim Barriers**
Due: October 31, 2019.
Status: On Schedule.
- M-045-92X Barrier 3 in 241-TX Farm Design Approved by Ecology**
Due: January 31, 2020.
Status: On Schedule.
- M-045-92AD Submit Yearly Reports Summarizing the Results of Maintenance and Performance Monitoring Activities**
Due: October 31, 2020.
Status: On Schedule.
- M-045-92Y Complete Construction of Barrier 3 in 241-TX Farm**
Due: October 31, 2021.
Status: On Schedule.
- M-045-92Z Submit to Ecology Design/Maintenance and Performance Monitoring Plan for Barrier 4 in 241-U Farm**
Due: October 31, 2021.
Status: On Schedule.
- M-045-92AA Barrier 4 in 241-U Farm Design Approved by Ecology**
Due: January 31, 2022.
Status: On Schedule.

M-045-85 Initiate Negotiations of HFFACO Interim Milestones for Closure of Remaining WMAs

Due: January 31, 2022.

Status: On Schedule.

M-045-92AB Complete Construction of Barrier 4 in 241-U Farm

Due: October 31, 2023.

Status: On Schedule.

M-045-00 Complete Closure of All SST Farms

Due: January 31, 2043.

Status: At Risk. Decision document 2016-005 signed August 22, 2016, requires this milestone to be addressed with the negotiations supporting M-062-45 Milestone. See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Significant Past Accomplishments

- Completed construction of the SX Tank Farm Barrier 1 (south) and SX Tank Farm Barrier 2 (north).
- Submitted revisions and comment responses to Ecology for RPP-RPT-59389, *Tier 2 Resource Conservation and Recovery Act (RCRA) Closure Action Plan for Waste Management Area C*; RPP-RPT-59390, *Tier 3 Resource Conservation and Recovery Act (RCRA) Component Closure Activity Plan for 241-C-200 Series Tanks*; and RPP-RPT-58858, *Tier 1 Closure Plan Single-Shell Tank System*.
- Began permitting workshops with Ecology for the SST closure plans in the Hanford Site-wide permit.

Significant Planned Activities in the Next Six Months

- Resolve Ecology’s comments on RPP-RPT-59389, RPP-RPT-59390, and RPP-RPT-58858.
- Complete construction of the SX Tank Farm expansion barrier.

Issues

- Report DOE/ORP-2014-02, *Clean Closure Practicality Demonstration for the Single-Shell Tanks*, Rev. 1 dated July 23, 2014. ORP received Ecology letter 15-NWP-149, “Department of Ecology’s Response Comments Regarding Review of the *Clean Closure Practicality Demonstration for the Single-Shell Tanks*, DOE/ORP-2014-02,” dated August 3, 2015. Ecology provided comments on the document and ORP met with Ecology in November 2017 to discuss a path forward. ORP provided an update to DOE/ORP-2014-02 via 18-ECD-0079, “Transmittal of

Supplemental Information to the Clean Closure Practicability Demonstration for the Single-Shell Tanks DOE/ORP-201-4-02-SUPP-1,” dated January 24, 2019. Awaiting Ecology approval.

- ORP formally initiated the Tri-Party Agreement (TPA) Dispute Resolution process with Ecology over Ecology’s “Denial of Request for Waiver for TPA Waste Retrieval Criteria for SST 241-C-106” (C-106). This dispute is at the TPA Inter-agency Management Team-level until May 13, 2019. ORP’s Statement of Dispute suggests that Ecology’s C-106 regulator waiver denial could cause significant time and cost impacts to tank closure schedules.

Single-Shell Tank Retrieval Program

Tank Farms Assistant Manager: Rob Hastings

Federal Program Manager: Jeff Rambo

Ecology Project Manager: Jeff Lyon

M-045-86 Submit Retrieval Data Report (RDR) To Ecology for 19 Tanks Retrieved Under Consent Decree

Due: To Be Determined (12 months after retrieval certification).

Status: On Schedule. Sub-milestone M-045-86D; RPP-RPT-60956, *Retrieval Data Report for Single-Shell Tank 241-C-105*, Rev. 0.

M-045-70 Complete Waste Retrieval from All Remaining Single Shell Tanks (SSTs)

Due: December 31, 2040.

Status: At Risk. Decision document 2016-005 signed August 22, 2016, requires this milestone be addressed with the negotiations supporting M-062-45 Milestone. See the “System Plan” section above for updates related to the M-062-45 Milestone negotiations.

Significant Past Accomplishments

- Refer to the Consent Decree monthly report for retrieval accomplishments.

Significant Planned Activities in the Next Six Months

- Refer to the Consent Decree monthly report for planned activities.

Issues

- Refer to the Consent Decree monthly report for retrieval issues.

Tank Operations Contract Overview

Earned Value Data: Fiscal Year 2019

February-19

Tank Farms ORP-0014 WBS 5 - River Protection Project (in \$000s)										
	BCWS	BCWP	ACWP	SV	CV	SPI	CPI	BAC	EAC	VAC
CM	\$55,780	\$48,760	\$45,820	(\$7,020)	\$2,940	0.87	1.06			
FYTD	\$250,471	\$238,463	\$243,503	(\$12,009)	(\$5,041)	0.95	0.98	\$704,650		
CTD	\$5,034,197	\$4,992,885	\$4,962,786	(\$41,313)	\$30,099	0.99	1.01	\$5,488,376	\$5,459,932	\$28,444

ACWP actual cost of work performed.

BAC budget at completion.

BCWP budgeted cost of work performed.

BCWS budgeted cost of work scheduled.

CM current month.

CPI cost performance index.

CTD contract to date.

CV cost variance.

EAC estimate at completion.

FYTD fiscal year to date.

SPI schedule performance index.

SV schedule variance.

VAC variance at completion.

The Earned Value Management System is intended to provide a status of how the contractor is progressing against its monthly planned work (i.e., schedule), and whether it is costing more or less to complete the work than planned. The earned value analysis is not intended to be a measurement of performance against existing TPA milestones.

The project plan is measured by expressing the schedule in terms of dollars spread over the anticipated project duration, and then for each month, determining how much of the planned work was accomplished or “earned,” as measured in equivalent dollars. If more work is accomplished than planned, then the project is ahead of schedule and has a favorable schedule variance (SV). Similarly, if less work is accomplished, the project is behind schedule and has an unfavorable SV. Accomplished work is reported in the month it was completed, which may not be when it was planned. For example, work completed in a month earlier than planned would be reported as a favorable SV for the month in which it was completed, but would be reported as an unfavorable SV in the month it was planned. The end result would be a net zero overall cumulative SV over these months. Likewise, work completed late will recover an earlier reported unfavorable SV.


The cost variance (CV) measures the actual cost of work performed against the earned dollar value of that performed work. As an example, assume \$10,000 of work was planned to-date, \$8,000 was reported as being performed (earned), at an actual cost of \$9,000. This work would be reported as being \$2,000 behind schedule [a negative or unfavorable SV: $\$8,000 - \$10,000 = (\$2,000)$], and has cost \$1,000 more [a negative or unfavorable CV: $\$8,000 - \$9,000 = (\$1,000)$] than was planned for completing that work scope. Likewise, a favorable or positive CV would be reported if it cost less to complete the work than the performed dollar value of the work. The SV and CV are reported for each monthly period, fiscal-year-to-date, as well as for the contract-to-date value. The monthly variances can fluctuate significantly (for reasons noted earlier), so the fiscal year or contract-to-date report provides a better indicator of the overall project completion status and can give a reasonable projection of how the project will finish, based on the progress-to-date.

Earned Value Data: Fiscal Year 2019

February-19

Tank Farms ORP-0014
WBS 5 - River Protection Project

EVMS Monthly and Fiscal Year Values

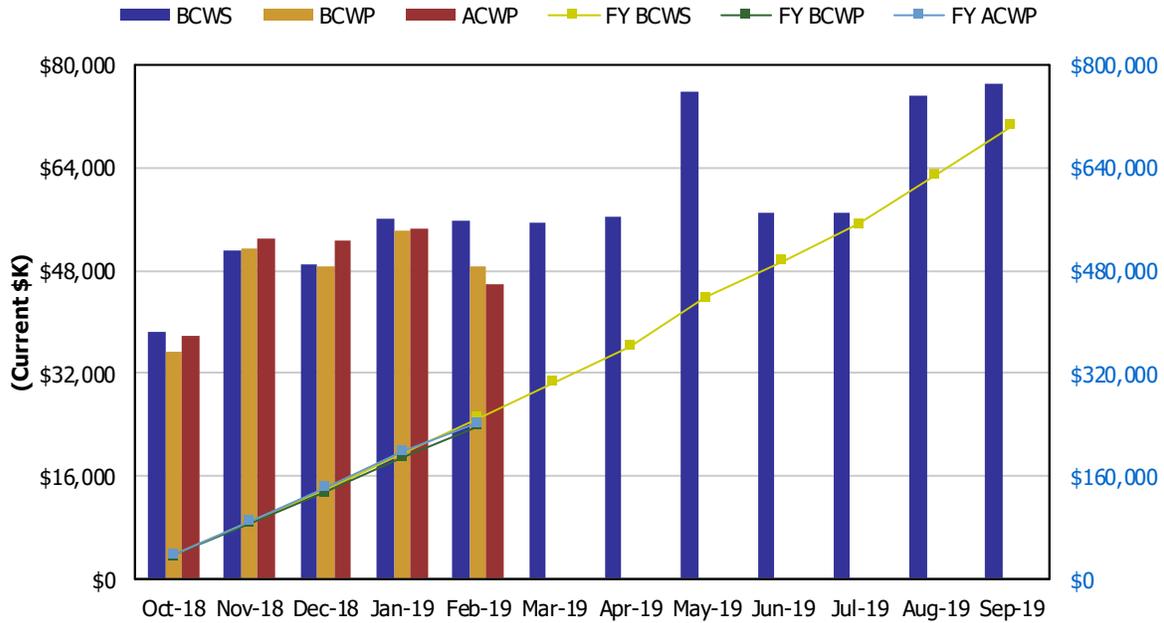

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2018	\$38,412	\$35,485	\$37,730	0.92	0.94	\$38,412	\$35,485	\$37,730	0.92	0.94
Nov 2018	\$51,217	\$51,557	\$52,805	1.01	0.98	\$89,629	\$87,042	\$90,536	0.97	0.96
Dec 2018	\$48,948	\$48,478	\$52,703	0.99	0.92	\$138,577	\$135,520	\$143,239	0.98	0.95
Jan 2019	\$56,114	\$54,183	\$54,445	0.97	1.00	\$194,691	\$189,703	\$197,684	0.97	0.96
Feb 2019	\$55,780	\$48,760	\$45,820	0.87	1.06	\$250,471	\$238,463	\$243,503	0.95	0.98
Mar 2019	\$55,510					\$305,981				
Apr 2019	\$56,496					\$362,477				
May 2019	\$75,821					\$438,297				
Jun 2019	\$56,971					\$495,269				
Jul 2019	\$56,884					\$552,153				
Aug 2019	\$75,306					\$627,459				
Sep 2019	\$77,191					\$704,650				

CTD	\$5,034,197	\$4,992,885	\$4,962,786	0.99	1.01
-----	-------------	-------------	-------------	------	------

ACWP actual cost of work performed.
 BCWP budgeted cost of work performed.
 BCWS budgeted cost of work scheduled.
 CPI cost performance index.


CM current month.
 CTD contract to date.
 FY fiscal year.
 SPI schedule performance index.

Earned Value Data: Fiscal Year 2019

February-19

Tank Farms ORP-0014
WBS 5.1 - Base Operations

EVMS Monthly and Fiscal Year Values

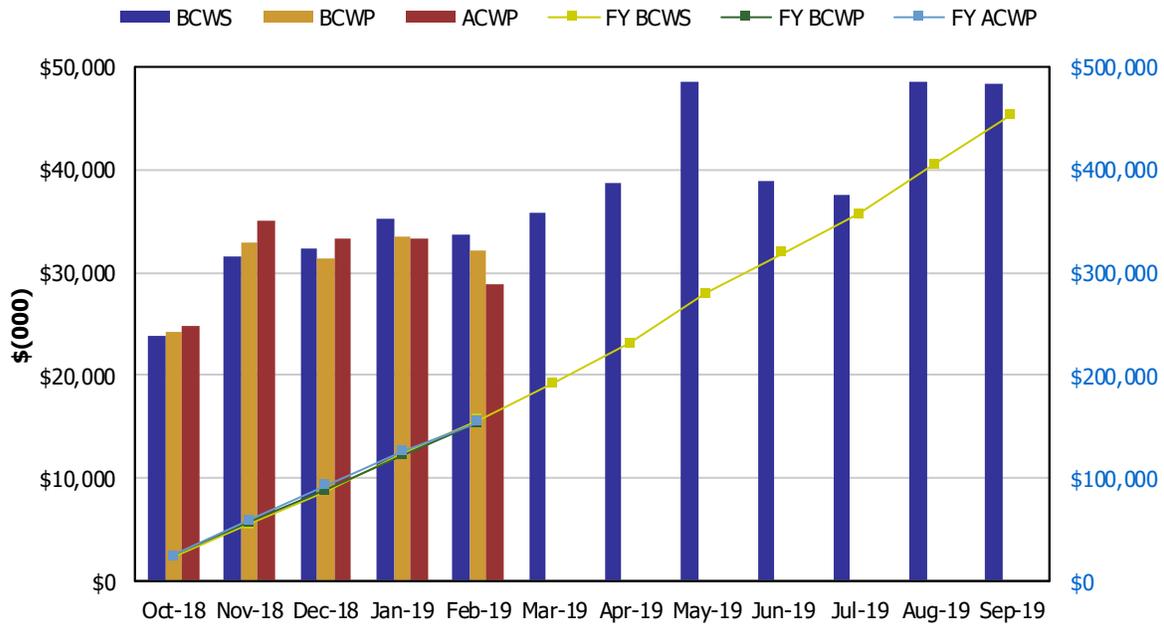

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2018	\$23,815	\$24,288	\$24,807	1.02	0.98	\$23,815	\$24,288	\$24,807	1.02	0.98
Nov 2018	\$31,462	\$32,868	\$34,951	1.04	0.94	\$55,276	\$57,155	\$59,758	1.03	0.96
Dec 2018	\$32,379	\$31,352	\$33,247	0.97	0.94	\$87,655	\$88,507	\$93,005	1.01	0.95
Jan 2019	\$35,182	\$33,427	\$33,218	0.95	1.01	\$122,837	\$121,934	\$126,224	0.99	0.97
Feb 2019	\$33,669	\$32,157	\$28,838	0.96	1.12	\$156,506	\$154,092	\$155,062	0.98	0.99
Mar 2019	\$35,873					\$192,379				
Apr 2019	\$38,668					\$231,047				
May 2019	\$48,601					\$279,648				
Jun 2019	\$38,859					\$318,506				
Jul 2019	\$37,568					\$356,074				
Aug 2019	\$48,497					\$404,571				
Sep 2019	\$48,354					\$452,924				

CTD	\$3,333,159	\$3,316,709	\$3,270,589	1.00	1.01
-----	-------------	-------------	-------------	------	------

- ACWP actual cost of work performed.
- BCWP budgeted cost of work performed.
- BCWS budgeted cost of work scheduled.
- CPI cost performance index.
- CM current month.
- CTD contract to date.
- FY fiscal year.
- SPI schedule performance index.

Tank Farms Assistant Manager: Rob Hastings
Federal Project Director: Brian Harkins

5.01 – Base Operations

The February 2019 variances below do not impact TPA milestones.

The **unfavorable** SV of (\$1,512,000) was primarily due to:

- For ETF processing, was a result of an extended facility outage period in order to prepare for future processing. This was primarily due to significant maintenance deemed critical to prepare the facility for successful processing campaigns in coordination with the Tank Farms Project teams proceeding with the ETF upgrades concurrently. These issues delayed ETF processing.
- Delays in performing double-shell tank annulus visual inspections due to critical resources allocated to perform the SST visual inspections. The predecessor SST visual inspections were delayed due to adverse weather conditions.

The **favorable** CV of \$3,320,000 was primarily due to:


- Adverse weather conditions at the Hanford Site, the level of effort type of accounts did not incur the charges. All the cost incurred during the shutdowns are charged to indirect accounts.

Earned Value Data: Fiscal Year 2019

February-19

Tank Farms ORP-0014
WBS 5.2 - Retrieve and Close SSTs

EVMS Monthly and Fiscal Year Values

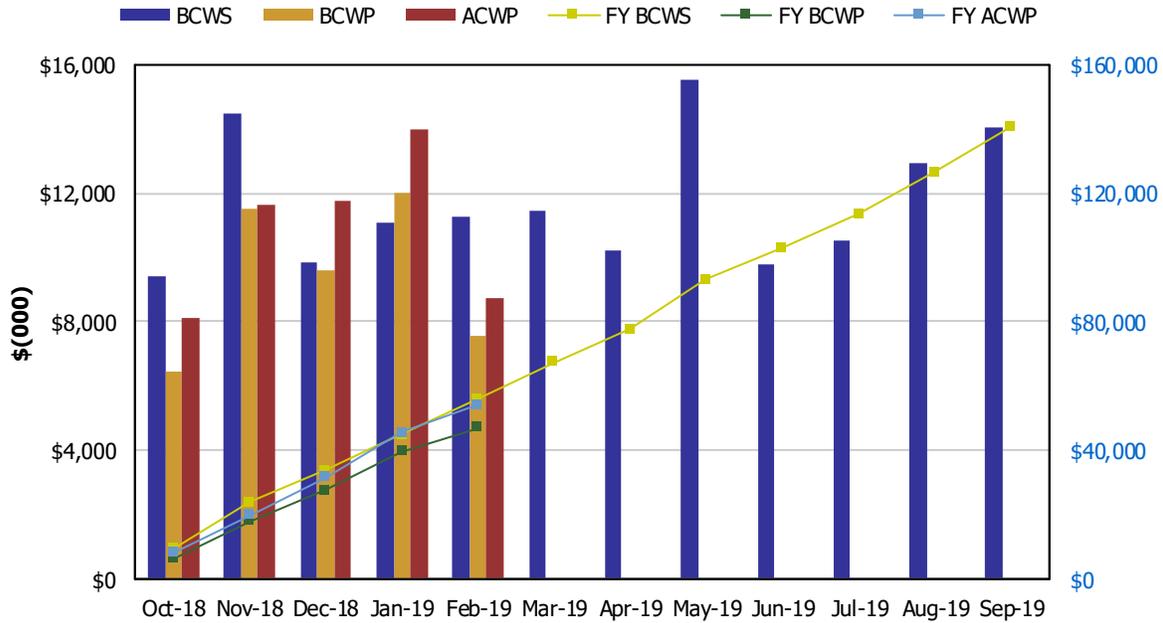

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2018	\$9,402	\$6,448	\$8,124	0.69	0.79	\$9,402	\$6,448	\$8,124	0.69	0.79
Nov 2018	\$14,501	\$11,516	\$11,634	0.79	0.99	\$23,902	\$17,964	\$19,757	0.75	0.91
Dec 2018	\$9,824	\$9,620	\$11,762	0.98	0.82	\$33,726	\$27,585	\$31,519	0.82	0.88
Jan 2019	\$11,060	\$12,034	\$13,959	1.09	0.86	\$44,786	\$39,618	\$45,479	0.88	0.87
Feb 2019	\$11,259	\$7,545	\$8,742	0.67	0.86	\$56,046	\$47,163	\$54,221	0.84	0.87
Mar 2019	\$11,437					\$67,483				
Apr 2019	\$10,243					\$77,726				
May 2019	\$15,506					\$93,232				
Jun 2019	\$9,802					\$103,034				
Jul 2019	\$10,542					\$113,576				
Aug 2019	\$12,947					\$126,523				
Sep 2019	\$14,029					\$140,552				

CTD	\$996,785	\$977,893	\$1,032,719	0.98	0.95
-----	-----------	-----------	-------------	------	------

- ACWP actual cost of work performed.
- BCWP budgeted cost of work performed.
- BCWS budgeted cost of work scheduled.
- CPI cost performance index.
- CM current month.
- CTD contract to date.
- FY fiscal year.
- SPI schedule performance index.

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Jeff Rambo

5.02 – Retrieve and Close Single-Shell Tanks


For the retrieval portion see the Consent Decree monthly report for cost and schedule status.

Earned Value Data: Fiscal Year 2019

February-19

Tank Farms ORP-0014
WBS 5.3 - WFD/Treatment Plng/DST Retrieval/Closure

EVMS Monthly and Fiscal Year Values

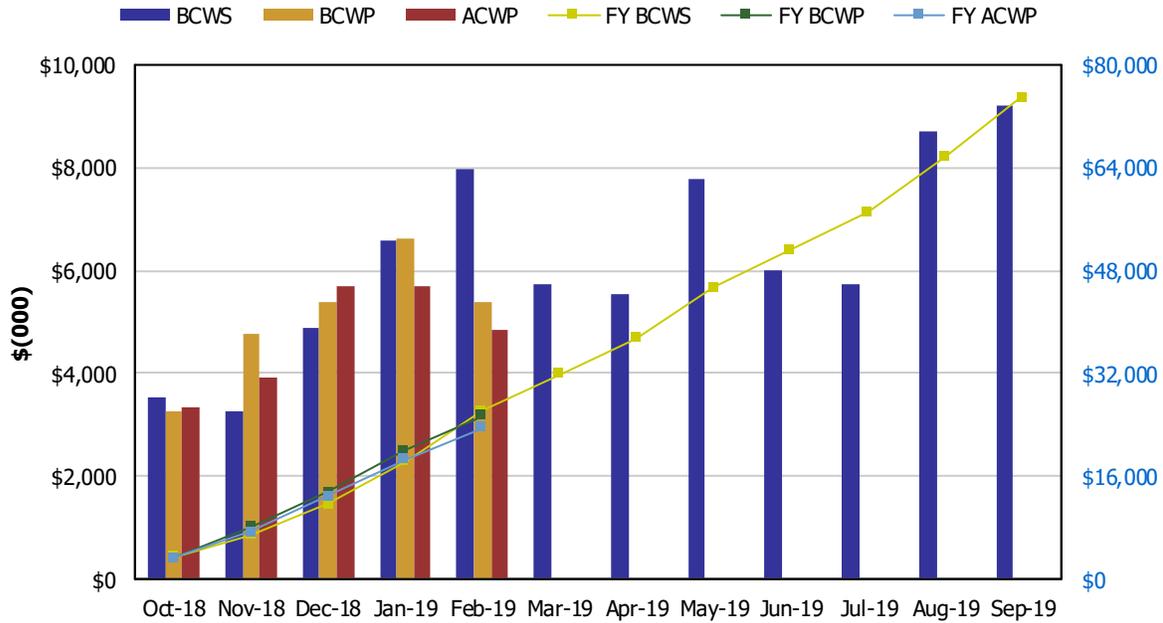

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2018	\$3,529	\$3,267	\$3,336	0.93	0.98	\$3,529	\$3,267	\$3,336	0.93	0.98
Nov 2018	\$3,269	\$4,771	\$3,923	1.46	1.22	\$6,798	\$8,039	\$7,259	1.18	1.11
Dec 2018	\$4,868	\$5,392	\$5,695	1.11	0.95	\$11,666	\$13,431	\$12,954	1.15	1.04
Jan 2019	\$6,572	\$6,604	\$5,699	1.00	1.16	\$18,238	\$20,035	\$18,653	1.10	1.07
Feb 2019	\$7,962	\$5,389	\$4,829	0.68	1.12	\$26,200	\$25,425	\$23,482	0.97	1.08
Mar 2019	\$5,716					\$31,917				
Apr 2019	\$5,548					\$37,464				
May 2019	\$7,790					\$45,254				
Jun 2019	\$5,991					\$51,245				
Jul 2019	\$5,749					\$56,994				
Aug 2019	\$8,702					\$65,696				
Sep 2019	\$9,220					\$74,916				
CTD	\$525,785	\$521,373	\$478,258	0.99	1.09					

ACWP actual cost of work performed.
 BCWP budgeted cost of work performed.
 BCWS budgeted cost of work scheduled.
 CPI cost performance index.

CM current month.
 CTD contract to date.
 FY fiscal year.
 SPI schedule performance index.

Tank Farms Assistant Manager: Rob Hastings
Federal Program Manager: Brian Harkins

5.03 – Waste Feed Delivery/Treatment

The February 2019 variances below do not impact TPA milestones.

The **unfavorable** SV of (\$2,573,000) was due to:

- Adverse weather conditions that prevented crews from performing planned fieldwork.

The **favorable** CV of \$561,000 was due to:


- Fewer subcontractor resources utilized during the immobilized LAW transporter design/testing, preparation of the AP-107 filtration test plan, and package specific safety document development.

Earned Value Data: Fiscal Year 2019

February-19

**Tank Farms ORP-0014
WBS 5.5 - Treat Waste**

EVMS Monthly and Fiscal Year Values

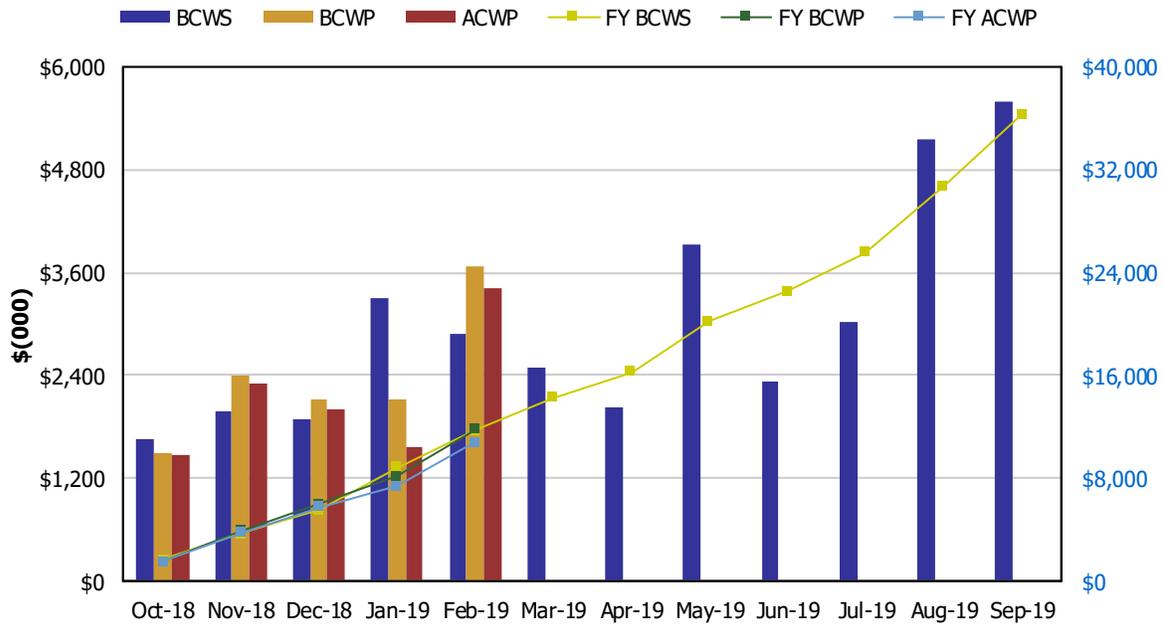

Earned Value Month

Month	BCWS	BCWP	ACWP	SPI	CPI	FY BCWS	FY BCWP	FY ACWP	FY SPI	FY CPI
Oct 2018	\$1,666	\$1,482	\$1,464	0.89	1.01	\$1,666	\$1,482	\$1,464	0.89	1.01
Nov 2018	\$1,986	\$2,402	\$2,297	1.21	1.05	\$3,652	\$3,884	\$3,761	1.06	1.03
Dec 2018	\$1,877	\$2,114	\$2,001	1.13	1.06	\$5,529	\$5,997	\$5,762	1.08	1.04
Jan 2019	\$3,301	\$2,118	\$1,568	0.64	1.35	\$8,830	\$8,115	\$7,330	0.92	1.11
Feb 2019	\$2,890	\$3,668	\$3,411	1.27	1.08	\$11,720	\$11,783	\$10,741	1.01	1.10
Mar 2019	\$2,483					\$14,202				
Apr 2019	\$2,037					\$16,240				
May 2019	\$3,924					\$20,164				
Jun 2019	\$2,320					\$22,483				
Jul 2019	\$3,025					\$25,508				
Aug 2019	\$5,161					\$30,669				
Sep 2019	\$5,588					\$36,257				

CTD	\$158,359	\$156,800	\$162,056	0.99	0.97
-----	-----------	-----------	-----------	------	------

ACWP actual cost of work performed.
 BCWP budgeted cost of work performed.
 BCWS budgeted cost of work scheduled.
 CPI cost performance index.

CM current month.
 CTD contract to date.
 FY fiscal year.
 SPI schedule performance index.

Tank Farms Assistant Manager: Rob Hastings
Deputy Federal Project Director: Sahid Smith

5.05 – Treat Waste

The February 2019 variances below do not impact TPA milestones.

The favorable SV of \$778,000 was due to:

- Recovery in the current period associated with completing the TSCR system 60 percent design review, which was originally planned for completion in the previous reporting period. The initial delay was to allow for the incorporation of comments from the process hazard analysis into the 60 percent design package.

The favorable CV of \$257,000 was due to:

- Efficiencies realized by the A/E in support of the 60 percent design review. This was attributed to fewer project support resources being necessary as compared to planning assumptions due to close coordination between the A/E and WRPS for 60 percent design activities and the use of lessons learned from similar system design efforts.
