


PFP Project Managers Meeting
Federal Building
Richland, Washington
May 24, 2006
3:30 p.m. - 4:30 p.m.
Meeting Minutes Transmittal

0073923

The undersigned indicate by their signatures that these meeting minutes reflect the actual occurrences of the above dated Project Managers Meeting.



E. M. Mattlin, Acting PFP Project Manager, RL

Date: 8/30/07



F. W. Bond, Project Manager,
Washington State Department of Ecology

Date: 8/30/07

PFP, FH Concurrence:



A. M. Hopkins, Contractor Representative, FH

Date: 8/30/07

Purpose: Project Managers Meeting

Attachment 1: Agenda, Action Tracking List and Summary of Discussions

Attachment 2: Presentation Materials

Attachment 3: Attendee List

RECEIVED
SEP 17 2007

EDMC

PFP Project Managers Meeting
Federal Building
Richland, Washington
May 24, 2006
3:30 p.m. - 4:30 p.m.
Meeting Minutes Transmittal

Distribution:

J. M. Ayres	Ecology	HO-57
F. W. Bond	Ecology	HO-57
S. L. Charboneau	RL	A5-11
R. H. Engelmann	FH	H8-12
D. A. Faulk	EPA	B1-46
R. E. Heineman	FH	T1-40
A. M. Hopkins	FH	H8-12
J. E. Hyatt	FH	H8-40
D. E. Jackson	RL	A4-52
G. A. Johnston	FH	T5-30
D. B. Klos	FH	T4-35
E. M. LaRock	FH	T4-33
E. M. Mattlin	RL	A5-15
R. E. Piippo	FH	H8-12
R. W. Oldham	FH	T3-10
D. L. Romine	FH	T4-35
S. A. Seydel	FH	T4-35
C. S. Sutter	FH	T4-32

ADMINISTRATIVE RECORD - Silvia Cook (two copies): H6-08

Please send comments on distribution list to Andrea Hopkins and Debbie Romine.

PFP Project Managers Meeting
Federal Building
Richland, Washington
May 24, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 1: Agenda, Action Tracking List, and Summary of Discussions

1.0 Administrative Issues

- The meeting minutes from the March 15, 2007, PMM were approved.
- No new actions were established.
- Stacy Charboneau provided Rick Bond a ROM estimate (\$25 Million that comes out of RL-20 [SAS]) for Security Cost at PFP, PFP's budget does not include Security costs.

2.0 PFP Project Item Status

Stacy Charboneau on deinventory – FH is in a cold standby mode, they will need authorization 3 months prior to starting shipments. To start shipments this fiscal year, DOE would need to provide that guidance to FH by June 1, 2007. DOE-HQ said we need to be ready to go by August 1, 2007. DOE is sending a letter of direction to FH to start packaging 3013s into the 9975s. FH is starting their preparatory activities to facilitate shipping in the August/September timeframe. The August 1st date depends upon when DOE has the authority to start the construction of MOX. The current plan is for DOE to sign the NEPA ROD for shipment when the construction of the MOX plant is started. Currently, shipments are planned for September.

Negotiations start next week. New FY 08 PIs.

3.0 Milestone Status

- **M83-22** Submit to Ecology an Engineering Evaluation/Cost Analysis(es) (EE/CA(s) for approval and provide an action memorandum(a) as a primary document(s) for the decommissioning of the PFP facility **DUE 9/30/08**

Status: It has been determined that the PFP sub-grade EE/CA will be issued as an engineering evaluation and environmental analysis report. The reason for this change is that an EE/CA is usually followed by an Action Memorandum. It is not prudent to issue an action memorandum for the sub-grade structures at PFP since an action will not be taken at this time. Andrea Hopkins provided the latest updated draft of the Engineering Evaluation and environmental analysis report for review, the final will go out under a FH to RL letter to transmit to the Regulators.

- **M83-41** Complete transition and dismantlement of the 216-Z-9 crib **DUE 9/30/10**

Status: Andrea Hopkins provided an update on the Z-9 Project. Preparations are nearly complete for the deployment of a fixed camera and crawler for inspection of the 216-Z-9 crib slab and equipment. The inspection is required to determine the condition of the slab for the planned D&D activities and to support project planning.

PFP Project Managers Meeting
Federal Building
Richland, Washington
May 24, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

A mock-up of the deployment of the inspection equipment was performed at Hammer. Modifications identified during the mock up have been incorporated. Data from the inspection will be used along with a visual inspection of the above grade structures will be used to evaluate the condition of the slab. For the deployment of the inspection equipment, a field implementation plan for the inspection activity was prepared. Copies of the plan were distributed for review. Ecology and EPA are asked to concur with the plan in order to deploy the inspection equipment.

- **M83-42** Complete transition and dismantlement of the 241-Z waste treatment facility
DUE 9/30/11

Status: See Attachment 2, Item 2.

4.0 New Topics

5.0 Next Meeting

June 21, 2007, 3:30 to 4:30, Federal Building, room 340

2007 ACTION TRACKING LIST

Action	Assignee	Date Established/ Due Date	Status

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Attachment 2: Presentation Materials

PFP May 24, 2007 PMM

M83-32

M83-42

Jerry Johnston

FH PM for 241-Z Transition

M83-32 Scope - Complete closure of the PFP 241-Z TSD Unit - Due 9/30/11

M83-42 Scope - Complete transition and dismantlement of the 241-Z Facility - Due 9/30/11

Status M83-32


- RL made formal notification of completion of this milestone to Ecology via letter number 07-AMCP-0159 dated April 4, 2007. The RCRA Part A, Form 3 was stamped closed with the date of February 22, 2007 which was the date of Ecology's letter accepting RCRA clean closure for the 241-Z TSD unit. This will be the final status report provided for this milestone.

Status M83-42

- Physical work activities supporting deactivation of the 241-Z complex to be "Ready for Demolition" were completed on March 30, 2007.
- The FH internal activity based management review for the 241-Z demolition work scope was approved on April 4, 2007.
- Demolition preparation activities were completed on April 18, 2007.
- Demolition activities started on April 19, 2007 with the piping and structure around 241-ZB Tank D9.
- Tank D9 was moved to the 241-Z CERCLA waste queue area in the Southwest yard area of PFP on April 24, 2007. The tank is awaiting transport to ERDF where it will be grout filled.
- The 241-Z HEPA filter housings and the above grade duct work upstream from the filter housings were loaded into a LLW IP1 container on May 1, 2007. The container will be transported to ERDF for grout fill.
- Jeff Ayres made a site visit on the morning of May 7, 2007 to observe the start of the demolition of the 241-Z structure. The structure was pulled down that afternoon. The size reduction and removal of the remaining structure debris was completed on May 14, 2007. Rick Bond and Jeff Ayres also visited the job site on May 23, 2007.
- On May 17, 2007 approximately 24" of controlled density fill (CDF) were added to the bottom of 241-Z Cell D6 to stabilize the floor area and tank base for end state objectives.
 - Structural analysis of the cell walls indicates that while unlikely, minor collapse of portions of the D6 South wall and near facility subsidence over a 20 year period could not be precluded.
 - The addition of CDF would anchor Tank D6 to inhibit movement should a wall section collapse and also encapsulate any contamination beneath the tank to prevent the spread of contamination. This approach also minimizes any impact to the options available for the decision on final remediation actions.
- The installation of the contamination control cap is ongoing with general site stabilization and posting to be complete by May 31, 2007.
- The project should be complete in early June, 2007.

PFP Project Managers Meeting
 Federal Building
 Richland, Washington
Meeting Minutes Transmittal

Plan view of 241-Z Complex – Contamination Control Cap

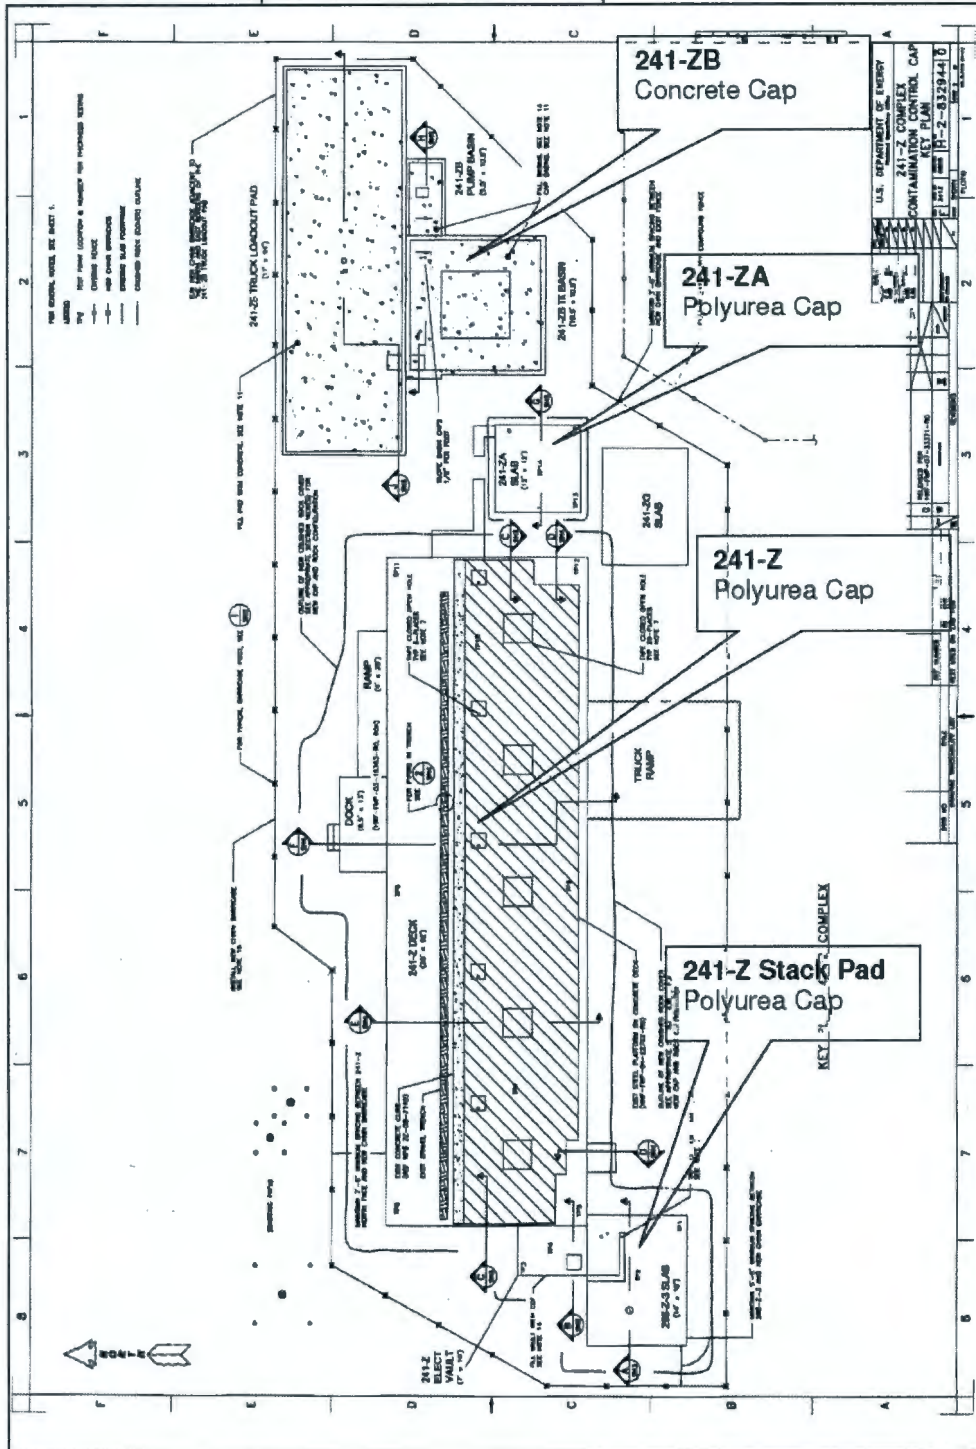

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal



4/19/07 – Demolition of 241-ZB Structure



4/24/07 – Lifting Tank D9



4/26/07 – 241-Z Annex Demolition



4/27/07 – 241-Z Stack Demolition



5/01/07 – Loading Out Upstream HVAC Duct



5/03/07 – Demolish 241-ZA1

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal



5/07/07 – J. Ayres Site Visit



5/07/07 – 241-Z Structure Dropped



5/10/07 – Size Reducing 241-Z Rubble



5/14/07 – 241-Z Slab Clean Up



5/17/07 – Adding CDF to Cell D6 Floor



5/17/07 – Adding CDF to 241-ZB Basins

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Attachment 3: Attendee List

J. Ayres, Ecology
R. Bloom, FH
F. Bond, Ecology
S. Charboneau, RL
S. Clarke, RL
W. Cox, FH
A. Hopkins, FH
G. Johnston, FH
E. Mattlin, RL
R. Piippo, FH
D. Romine, FH
C. Sutter, FH
