



PFP Project Managers Meeting
Federal Building/Room 248
Richland, Washington
August 9, 2005
3:30 p.m. - 4:30 p.m.
Meeting Minutes Transmittal

The undersigned indicate by their signatures that these meeting minutes reflect the actual occurrences of the above dated Project Managers Meeting.



C.R. Richins, Acting PFP Project Manager, DOE-RL

Date: 9-20-05


F. W. Bond, Project Manager,
Washington State Department of Ecology

Date: 9-20-05

PFP, FH Concurrence:


A. M. Hopkins, Contractor Representative, FH

Date: 10/18/05

Purpose: Project Managers Meeting

Attachment 1: Agenda, Action Tracking List and Summary of Discussions

Attachment 2: Presentation Materials

Attachment 3: Attendee List

RECEIVED
NOV 07 2005
EDMC

PFP Project Managers Meeting
Federal Building/Room 248
Richland, Washington
August 9, 2005
3:30 p.m. - 4:30 p.m.
Meeting Minutes Transmittal

Distribution:

J. M. Ayres	Ecology	HO-57
D. Bartus	EPA	HO-57
F. W. Bond	Ecology	HO-57
S. L. Charboneau	RL	A5-11
D. A. Faulk	EPA	B1-46
R. E. Heineman	FH	T1-40
A. M. Hopkins	FH	H8-25
D. E. Jackson	RL	A4-52
G. A. Johnston	FH	T5-30
J. T. Lilly	FFS	T4-32
S. J. Killoy	POLES	T3-10
E. M. LaRock	FH	T4-33
E. M. Mattlin	RL	A5-15
R. E. Piippo	FH	A4-25
R. W. Oldham	FH	T3-10
C. J. Simiele	FH	T4-32
T. C. Synoground	FH	T4-33
P. K. Sato	FH	T4-33
C. S. Sutter	FH	T4-32
W. A. Woolery	RL	A6-33

ADMINISTRATIVE RECORD (two copies): A4-25
Debbi Isom (two copies): H6-08

Please send comments on distribution list to Rob Piippo, A4-25 (373-3285).

PFP Project Managers Meeting
Federal Building/Room 248
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 1: Agenda, Action Tracking List, and Summary of Discussions

1.0 Administrative Issues

- The meeting minutes from the June 14, 2005 PMM were previously approved. The Action Tracking List was reviewed. Action #1 to conduct a workshop on PFP facility based on the Design Basis Threat and long term storage strategy was discussed. It was agreed that this will occur on an as needed basis. Action item #2 to determine if a subgrade EE/CA action memo is needed due date was moved to February 15, 2006.

2.0 PFP Project Item Status

- Ellen Mattlin provided an update on PFP status. PFP is continuing to move forward with cleanup and the 07 budget estimate is being developed. Headquarters is evaluating consolidation cost estimates.

3.0 Milestone Status

- **M83-40** Complete transition and dismantlement of the 232-Z Bldg incinerator to slab-on-grade (pending environmental determination) **DUE 9/30/06.**

Status: See Attachment 2 Item 1

- **M83-14** Complete 100% Of The Legacy Pu Holdup Removal As Defined In The Legacy Pu Holdup Removal Plan For PFP Required By MX-83-12-T01 **DUE 9/30/06.**

Status: Completed

- **M83-32** Complete closure of the PFP 241-Z unit **DUE 9/30/11**

Status: See attachment 2 item 2

- **M83-22** Submit to Ecology an Engineering Evaluation/Cost Analysis(es) (EE/CA(s) for approval and provide an action memorandum(a) as a primary document(s) for the decommissioning of the PFP facility **DUE 9/30/08**

Submit PFP above grade structures EE/CA to Ecology	8/31/04 - Complete
Issue Fact Sheet/perform 30 day public comment	10/11/04 - Complete
Respond to public comments	11/12/04 - Complete
Approve action memo	12/12/04 - Complete
Approve two RAWPs and SAP	4/30/05 - Complete
Submit sub-surface EE/CA to Ecology	9/30/07

PFP Project Managers Meeting
Federal Building/Room 248
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

(The sub-surface scope is being determined thru negotiations with Ecology John Price)

4.0 New Topics

Rick Oldham brought up that building 234-5, room 176 air lock is to be added to the demolition work plan. Rob Piippo stated that this room could be added to the work plan by processing a TPA section 9.3 change notice and took the action to provide a form to the project.

5.0 Next Meeting

September 13, 2005, Fed Bldg, 3:30-4:30

2005 ACTION TRACKING LIST

Action	Assignee	Date Established/ Due Date	Status
1) Conduct a workshop on PFP facility based on the Design Basis Threat and long term storage strategy. A scoping document is in work and when complete will be discussed with the regulators.	Ron Brunke	5-10-2005/as required	
2) Agencies determine whether a subgrade EE/CA action memo is needed.	Andrea Hopkins	5-10-2005/2-14-2006	

PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal


Attachment 2: Presentation Materials
Item 1

PFP August 2005 PMM
Status of M83-40
Paul Sato

M83-40 COMPLETE TRANSITION AND DISMANTLEMENT OF THE 232-Z BLDG INCINERATOR TO SLAB-ON-GRADE (PENDING ENVIRONMENTAL DETERMINATION) DUE 9/30/06

1. Project is currently on schedule to complete transition and dismantlement of 232-Z on or before 9/30/06.
2. D&D Activity Status
 - Removed & packaged the 232-Z glovebox into an IP-2 shipping container and completed shipment to T Plant.
 - The agencies met on July 27, 2005 to discuss the path forward for the completion of the M-83-40 milestone regarding the 232-Z duct removal. It was agreed that a portion of the 232-Z duct that extends in to the 291-Z building would be removed with the demolition of the 232-Z building and that the remaining 232-Z duct located in the 291-Z building would be removed with the demolition of the 291-Z building. It was further agreed that the path forward for the 232-Z duct would be documented as a new topic in the June 14, 2005 PMM meeting minutes. Attendees included Craig Richins, Rick Bond, Ellen Mattlin and Andrea Hopkins
 - Completed isolation of the 291-Z ducting from the underground portion of the 232-Z underground ductwork.
 - Finalizing bid package for contract to grout the underground portion of the 232-Z duct work.
 - Made initial entry into the 232-Z Scrubber Cell on August 2, 2005. Equipment removal tasks on-going.
 - Completed fabrication of the structural supports which will be installed on the south (exterior) wall of the 232-Z facility to support possible removal of concrete block.
 - Initiated walkdowns & design work supporting facility isolation prior to starting demolition.
 - Awarded contract for the shearer which will be used during demolition.
 - Evaluated options for size reduction & disposition of the floor filter boxes and E-4 processing ventilation ducting (SWB/ERDF vs IP-2/T Plant). Implementing detailed planning to support the T Plant option.
3. Upcoming Activities
 - a. Complete equipment removal in the 232-Z Scrubber Cell.
 - b. Initiate decontamination of the 232-Z Scrubber Cell.
 - c. Finalize the 232-Z end point criteria document and start approval process.

PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

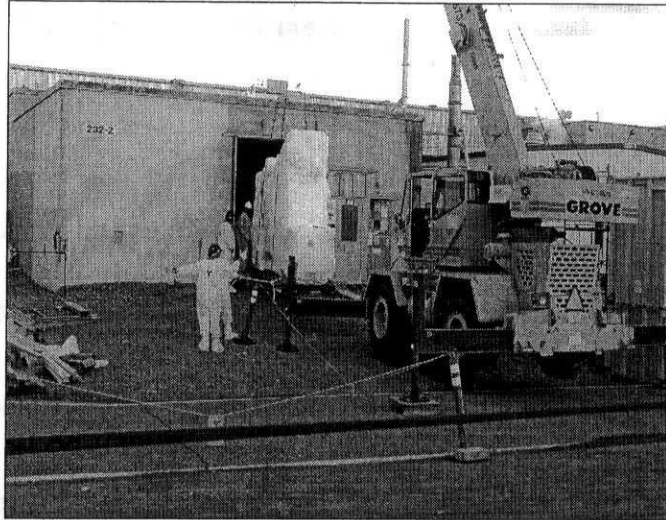

Glovebox Removal from 232-Z



Loading Glovebox into IP-2 Shipping Container

PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 2: Presentation Materials

Item 2

PFP August 9, 2005 PMM

M83-32

Jerry Johnston

FH PM for 241-Z Transition


M83-32

Scope


Complete closure of the PFP 241-Z TSD Unit - Due 9/30/11

Status


- The SAP for sampling Cell D8 piping is approved and issued (HNF-25105 Rev. 0)
- Initial characterization and debris removal is proceeding on Cell D7.
 - First D&D entry into Cell D7 was made on June 23, 2005
 - D7 NDA and Video Inspections completed
 - Physical isolation of all electrical circuits to the 241-Z Cells completed August 7, 2005
 - Waste load out will continue through 8/11/05
 - Aerosol fogging of D6 will occur this week with entries starting week of 8/15/05.
- Would like to arrange a meeting with Rick Bond to provide an overview of changes being planned for 241-Z.

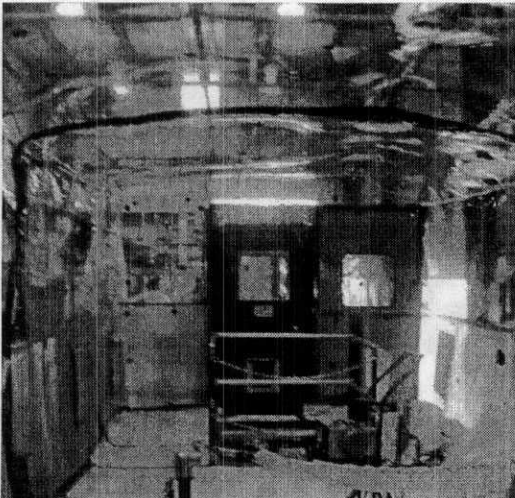


Large Containment Tent
Over 241-Z Cells D6 and D7
(left)

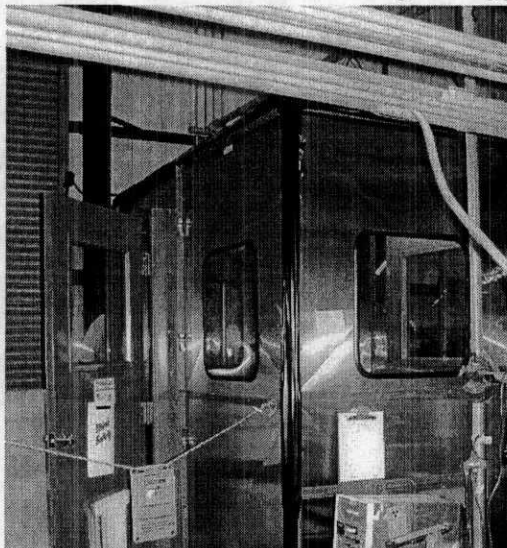


Hard Sided Anteroom for the
D6 / D7 Containment Tent
(right)

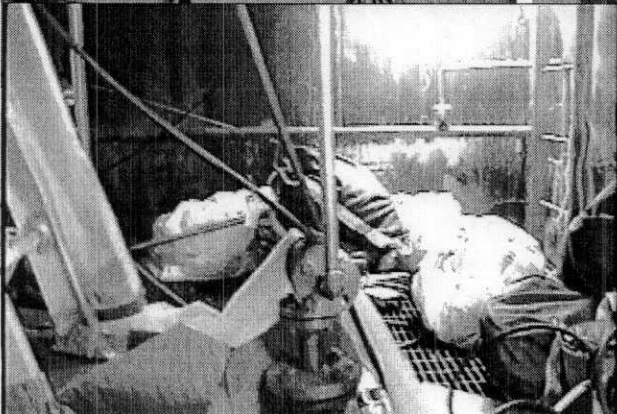

Bags of debris
on grating to
be loaded out.

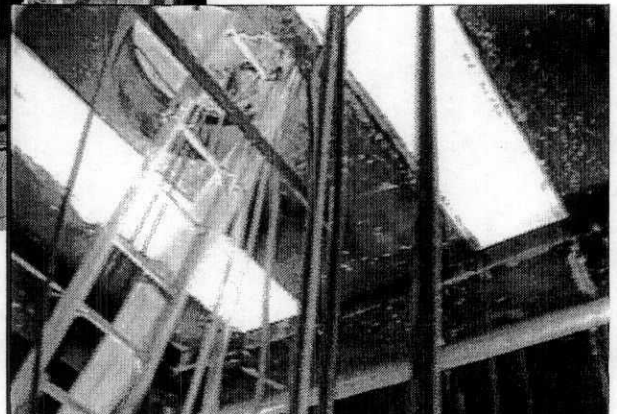

PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

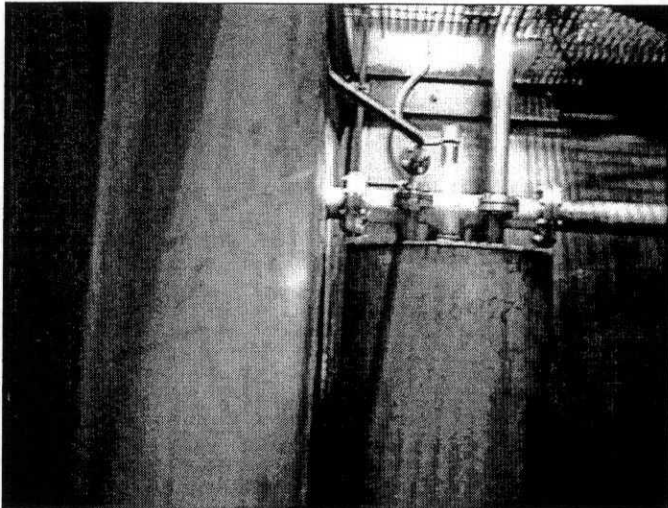


D7 Overflow Tank



Floor of Cell D7




Southeast Corner of Cell D7

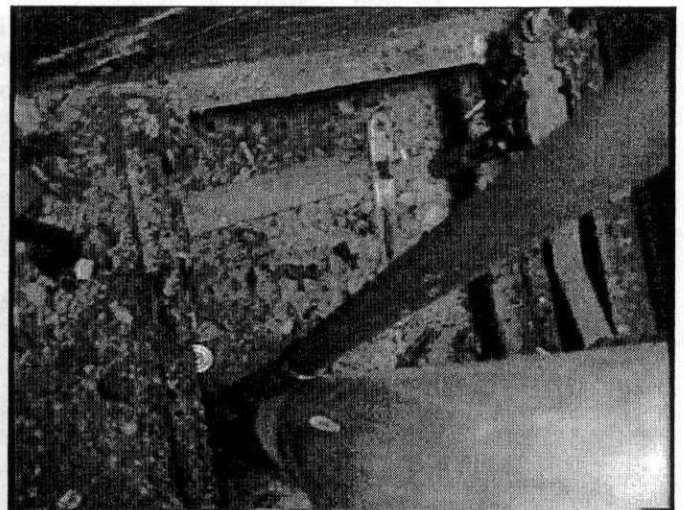


Cell D7 Sump


PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

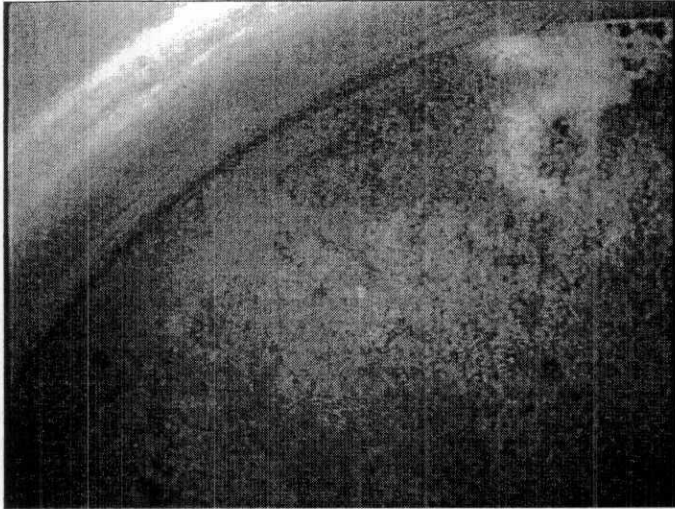

Bottom of Tank D7

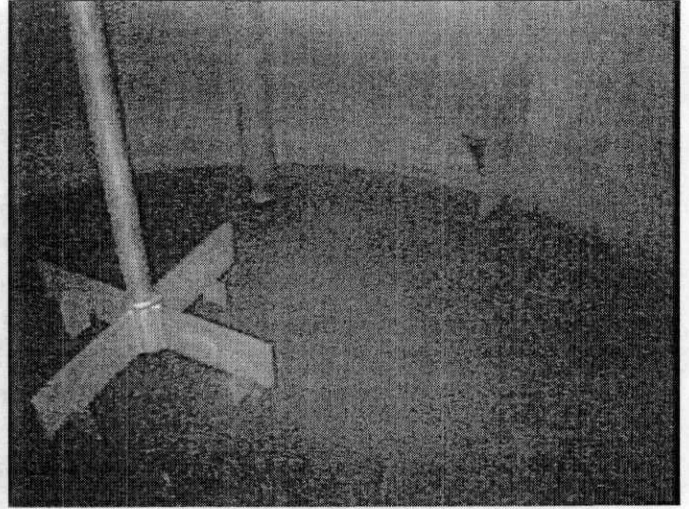

Tank D7 Agitator

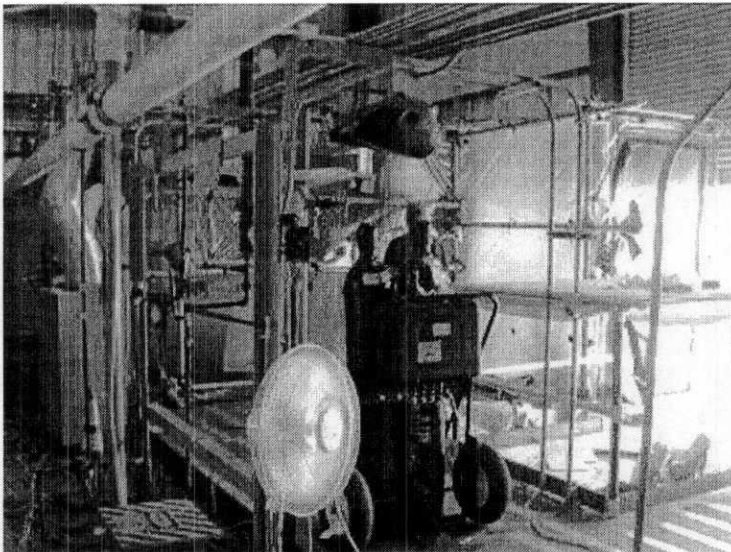

241-Z Containment Over D5



241-Z Typical Debris in Cell D5

PFP Project Managers Meeting
Federal Building
Richland, Washington
August 9, 2005
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 3: Attendee List

J. Ayres, Ecology
R. Bloom, FH
R. Bond, Ecology
R. Brunke, FH
A. Hopkins, FH
J. Johnston, FH
J. Lilly, FGG
E. Lloyd, FGG
E. Mattlin, RL
M. Minette, FH
R. Oldham, FH
R. Piippo, FH
W. Woolery, RL
