

PFP Project Managers Meeting
Federal Building
Richland, Washington
June 21, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal


0073924

The undersigned indicate by their signatures that these meeting minutes reflect the actual occurrences of the above dated Project Managers Meeting.



E. M. Mattlin, Acting PFP Project Manager, RL


Date: 8/30/07



F. W. Bond, Project Manager,
Washington State Department of Ecology

Date: 8/30/07

PFP, FH Concurrence:



A. M. Hopkins, Contractor Representative, FH

Date: 8/30/07

Purpose: Project Managers Meeting

Attachment 1: Agenda, Action Tracking List and Summary of Discussions

Attachment 2: Presentation Materials

Attachment 3: Attendee List

RECEIVED
SEP 17 2007

EDMC

PFP Project Managers Meeting
Federal Building
Richland, Washington
June 21, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Distribution:

J. M. Ayres	Ecology	HO-57
F. W. Bond	Ecology	HO-57
S. L. Charboneau	RL	A5-11
R. H. Engelmann	FH	H8-12
D. A. Faulk	EPA	B1-46
R. E. Heineman	FH	T1-40
A. M. Hopkins	FH	H8-12
J. E. Hyatt	FH	H8-40
D. E. Jackson	RL	A4-52
G. A. Johnston	FH	T5-30
D. B. Klos	FH	T4-35
E. M. LaRock	FH	T4-33
E. M. Mattlin	RL	A5-15
R. E. Piippo	FH	H8-12
R. W. Oldham	FH	T3-10
D. L. Romine	FH	T4-35
S. A. Seydel	FH	T4-35
C. S. Sutter	FH	T4-32

ADMINISTRATIVE RECORD – Silvia Cook (two copies): H6-08

Please send comments on distribution list to Andrea Hopkins and Debbie Romine.

PFP Project Managers Meeting
Federal Building
Richland, Washington
June 21, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

Attachment 1: Agenda, Action Tracking List, and Summary of Discussions

1.0 Administrative Issues

One new action was established.

2.0 PFP Project Item Status

Shipments: RL sent a letter to FH on June 1, 2007, instructing FH to be ready to ship inventory by September 1, 2007. RL has not yet received needed authorization from HQ. DOE/HQ is required to give notice to Congress 30 days in advance of shipment. HQ is operating to the August 1st date, which means RL and FH would have to be ready to ship by September 1st. Supporting the current shipment schedule are the following activities: meetings in Albuquerque NM in July, support from QA to look at the loading of the 9975s, and personnel to do the necessary reviews.

Milestone Status: 234-5Z and PRF Milestones will be added to the status of ongoing projects in the PMM.

234-5Z and PRF: FH has been working on 17 gloveboxes scheduled to be completed in 2007 & 2008. All but one of these will be completed in 2007. Therefore, FH has negotiated some new Performance Incentives with RL which add 11 gloveboxes to be completed in fiscal year 2008.

3.0 Milestone Status

- **M83-22** Submit to Ecology an Engineering Evaluation/Cost Analysis(es) (EE/CA(s) for approval and provide an action memorandum(a) as a primary document(s) for the decommissioning of the PFP facility **DUE 9/30/08**

Status: RL briefed the Hanford Advisory Board and Rick Bond of Ecology June 20, 2007 to state that the *PFP Engineering Evaluation and Environmental Analysis Report* has been placed in the Administrative Record. The report is available for public review and the notice for availability of public review has been sent. Comments from the public will be accepted and placed in the Administrative Record. These activities complete the requirements of the M83-22 milestone. RL will send Ecology the completion letter during July.

- **M83-41** Complete transition and dismantlement of the 216-Z-9 crib **DUE 9/30/10**

Status: See Attachment 2, Item 1.

PFP Project Managers Meeting
Federal Building
Richland, Washington
June 21, 2006
3:30 p.m. – 4:30 p.m.
Meeting Minutes Transmittal

- **M83-42** Complete transition and dismantlement of the 241-Z waste treatment facility
DUE 9/30/11

Status: See Attachment 2, Item 2.

4.0 New Topics

5.0 Next Meeting

August 30, 2007, 3:30 to 4:30, Federal Building, room 340

2007 ACTION TRACKING LIST

Action	Assignee	Date Established/ Due Date	Status
Have a meeting with Dennis Faulk, Rick Bond, Ellen Mattlin, Caroline Sutter, and Virginia Rohay about Z-9 in July	Andrea Hopkins	July	

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal


Attachment 2: Presentation Materials

Item 1

Z-9 Project Status - June 21, 2007

Accomplishments:

- The CERCLA data package for the 216-Z-9 crib inspection equipment was approved by the Department of Energy, (DOE), Department of Ecology (Ecology) and the Environmental Protection Agency (EPA).
- The 216-Z-9 crib inspection equipment was successfully deployed. Equipment checkout was completed and initial inspection completed. Final pictures of the floor are being assembled.
- Inspection of the equipment in 216-Z-9C, *Mining Equipment Enclosure*, was completed. A work package is being prepared to sample the hydraulic oil.
- The revision of the Memorandum of Understanding (MOU) between the Soil and Groundwater Remediation Project and PFP Closure Project to reflect the Z-9 Project activities was issued.
- Arrangements have been made for the structural evaluation of the data from the inspection of the crib. Evaluation is scheduled to start next week.
- The documentation of the evaluation of the hazards associated with the removal of the 216-Z-9 structures has been initiated.
- The development of the Removal Action Work Plan (RAWP) for the removal of the 216-Z-9 structures has been initiated.
- Nondestructive assay of the 216-Z-9 exhaust ventilation for waste disposal has been initiated. While surveying the exhaust filter housing, fixed contamination was found on the pad under one of the filter housing (24,000 dpm/100cm²). Follow up surveys found removable contamination on a section of the pad under the ventilation ducting (1,200 dpm/100cm) and fixed contamination on some dirt next to the pad (24,000 dpm/100cm). All contamination was fixed or removed.

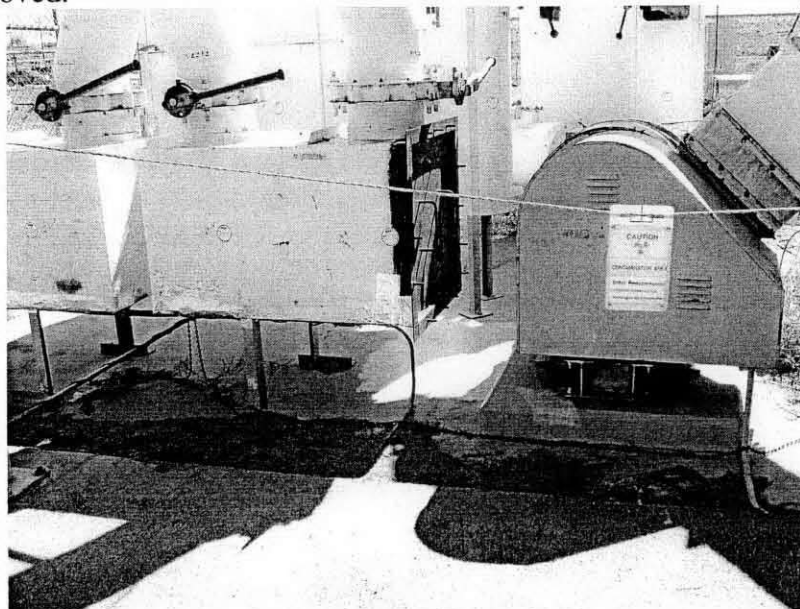

216-Z-9 Ventilation System

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal



PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Item 2

PFP June 21, 2007 PMM

M83-42


Jerry Johnston

FH PM for 241-Z Transition


**M83-42 Scope - Complete transition and dismantlement of the 241-Z Facility -
Due 9/30/11**

Status M83-42

- Physical work activities supporting demolition and stabilization of the 241-Z complex were completed on June 4, 2007. This is four years and four months ahead of the September 30, 2011, due date.
- The demobilization of the Central Plateau D&D crew was completed on June 5, 2007.
- Jeff Ayres visited PFP on June 6, 2007, to inspect the completed 241-Z site.
- The 241-Z Facility End Point Criteria and Completion Checklists document (HNF-30038 Rev 0) was signed complete on June 8, 2007. The purpose of this document is to provide a means to record how the general PFP end point criteria in HNF-22401 is being specifically applied to the 241-Z Facility. This document also provides an agreed upon checklist to record the completion of work to meet these end points.
- A letter from FH to RL providing notification of completion of TPA milestone M83-42 has been drafted and is in the approval process. Upon receipt of the FH letter, RL will transmit a letter to Ecology requesting concurrence that the milestone has been completed.
- FH Nuclear Safety has formally down graded the 241-Z Facility to a less than Hazard Category 3 inactive waste site.
- The update for the 241-Z waste site for the WIDS database has been drafted and is under review.
- Work has started on preparing the 241-Z Removal Action Construction Completion Report.

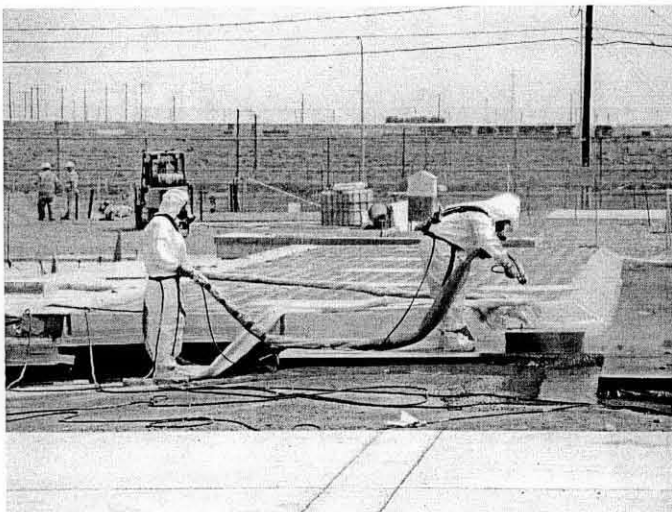


5/26/07 – Spraying Polyurea on Slab

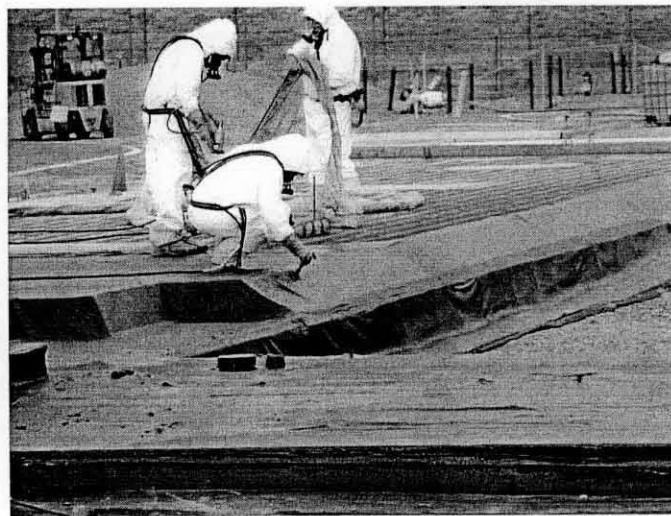


5/26/07 – Testing Mil Thickness on Coating

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

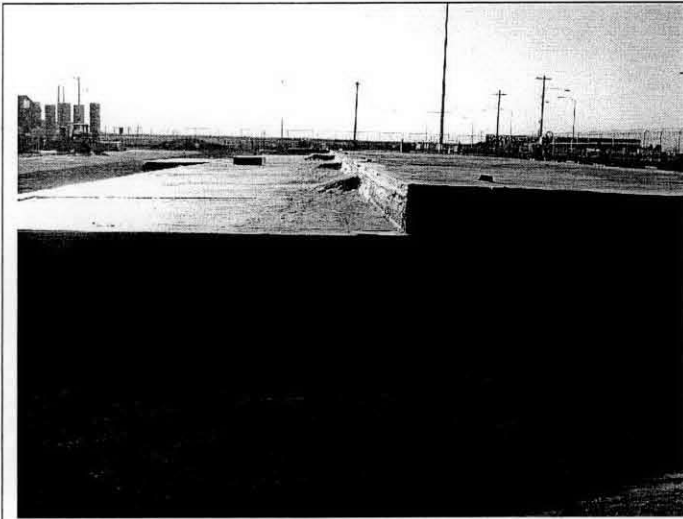

5/29/07 – Polyurea Cap Complete

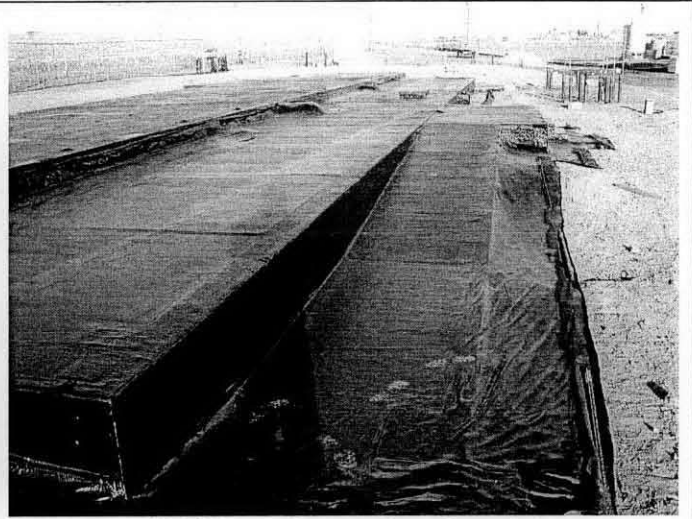

5/29/07 – Polyurea Cap Complete




5/29/07 – Pouring Concrete Cap on 241-ZB



5/30/07 – Spreading Gravel on Slabs



5/31/07 – Site Stabilized and Posted

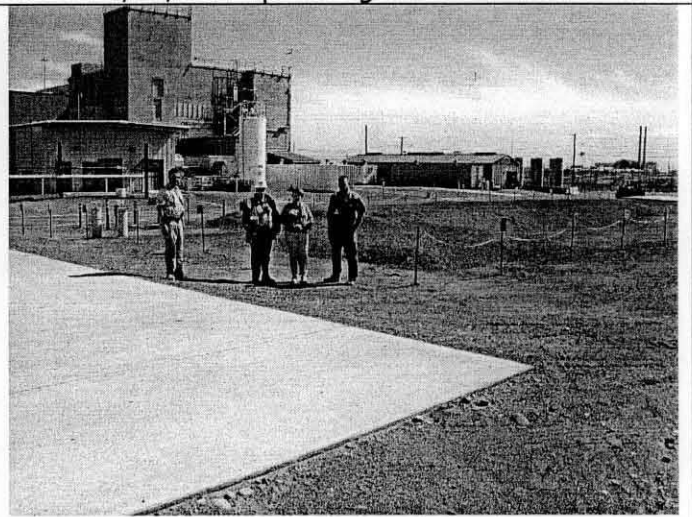

6/06/07 – J. Ayres Site Visit

PFP Project Managers Meeting
Federal Building
Richland, Washington
Meeting Minutes Transmittal

Attachment 3: Attendee List

J. Ayres, Ecology
R. Bloom, FH
F. Bond, Ecology
G. Johnston, FH
E. Mattlin, RL
V. Rohay, FH
D. Romine, FH
C. Schweiger, FH-CI
S. Seydel, FH
C. Sutter, FH
