

START

0030716

WHC-MR-0403-9

UC-600

Tri-Party Agreement Milestone Summary July 1993

Date Published
August 1993

Prepared for the U.S. Department of Energy



**Westinghouse
Hanford Company**

P.O. Box 1970
Richland, Washington 99352

Hanford Operations and Engineering Contractor for the
U.S. Department of Energy under Contract DE-AC06-87RL10930



Approved for Public Release

9 3 1 3 0 2 5 1 6 1 6

This page intentionally left blank.

93130261617

9 3 1 3 2 6 1 6 1 8

LEGAL DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

This report has been reproduced from the best available copy.

Printed in the United States of America

DISCLM-2 CHP (1-91)

**THIS PAGE INTENTIONALLY
LEFT BLANK**

PREFACE

The *Tri-Party Agreement Milestone Summary Report* is issued monthly by the U.S. Department of Energy, Richland Field Office (RL). The report provides a summary progress and financial status for each active *Hanford Federal Facility Agreement and Consent Order* (Tri-Party Agreement) major milestone and its related interim milestones that are active in the current 12-month period. Of the 261 planned interim milestones due by July 31, 1993, 256 were completed. Four other milestones have been completed early.

The following Tri-Party Agreement major milestones have been completed and are not included in this report:

		<u>Completed</u>
M-12-00	Submit remedial investigation/feasibility study (RI/FS) or <i>Resource Conservation and Recovery Act</i> (RCRA) facility investigation/corrective measures study (RFI/CMS) work plan for 15 operable units.	6/30/92
M-21-00	Submit RCRA interim status compliance assessments for all treatment, storage, and disposal units.	4/30/89
M-22-00	Establish enforceable compliance action schedules.	12/29/89
M-23-00	Complete interim status corrective actions.	9/30/91
M-25-00	Provide annual reports of in-progress studies or efforts to identify alternatives to land disposal of radioactive mixed waste	Deleted*
	*M-25-00 was deleted 3/31/92 and requirements combined with revised Tri-Party Agreement milestone M-26-00.	
M-27-00	Submit all aggregate area management study reports (AAMSR) for the 200 areas.	9/29/92
M-28-00	Submit all soils and groundwater background determination documents to U.S. Environmental Protection Agency (EPA) and Washington State Department of Ecology (Ecology).	4/30/92
M-29-00	Submit documentation to EPA and Ecology describing Hanford Site risk assessment methodology.	3/31/92

9 0 1 3 0 2 6 1 5 1 9

**TRI-PARTY AGREEMENT
BUDGET BASELINE SUMMARY
JULY 1993**


(\$ in Millions)

<u>MAJOR MILESTONE</u>	<u>FYTD BUDGET</u>	<u>FYTD COST</u>	<u>SPENDING VARIANCE</u>	<u>ANNUAL BUDGET</u>
M-00 *	15.5	11.5	3.7	19.9
M-01	31.0	31.5	(0.5)	39.1
M-02 *	15.1	12.8	2.3	22.8
M-03 *	91.0	86.2	4.8	125.6
M-04	0.1	0.0	0.1	0.1
M-05	7.2	7.1	0.1	9.8
M-06 *	2.6	2.2	0.4	3.0
M-07	4.2	3.9	0.3	5.0
M-08	1.8	1.5	0.3	2.4
M-09	5.7	5.2	0.5	6.4
M-10	19.6	19.5	0.1	23.3
M-11	11.7	9.5	2.2	13.6
M-12	0.4	0.3	0.1	0.5
M-13	1.0	0.8	0.2	1.2
M-14	8.0	10.0	(2.0)	10.3
M-15 *	63.0	57.8	5.2	93.0
M-16	9.2	8.9	0.3	9.7
M-17 *	43.3	41.0	2.3	59.2
M-18	7.1	7.1	0.0	7.9
M-19	4.6	4.5	0.1	5.9
M-20 *	8.4	5.7	2.7	12.6
M-24	2.3	2.7	(0.4)	3.6
M-26	0.1	0.1	0.0	0.1
M-30	1.6	1.6	0.0	2.1
M-31	9.2	8.3	0.9	12.3
	<u>363.7</u>	<u>340.0</u>	<u>23.7</u>	<u>489.4</u>

* These milestones include costs from other contractors.
All other milestones are WHC only. \$0.0=less than \$100K.


TRI PARTY AGREEMENT ALL MILESTONES FY 1993

\$ Millions

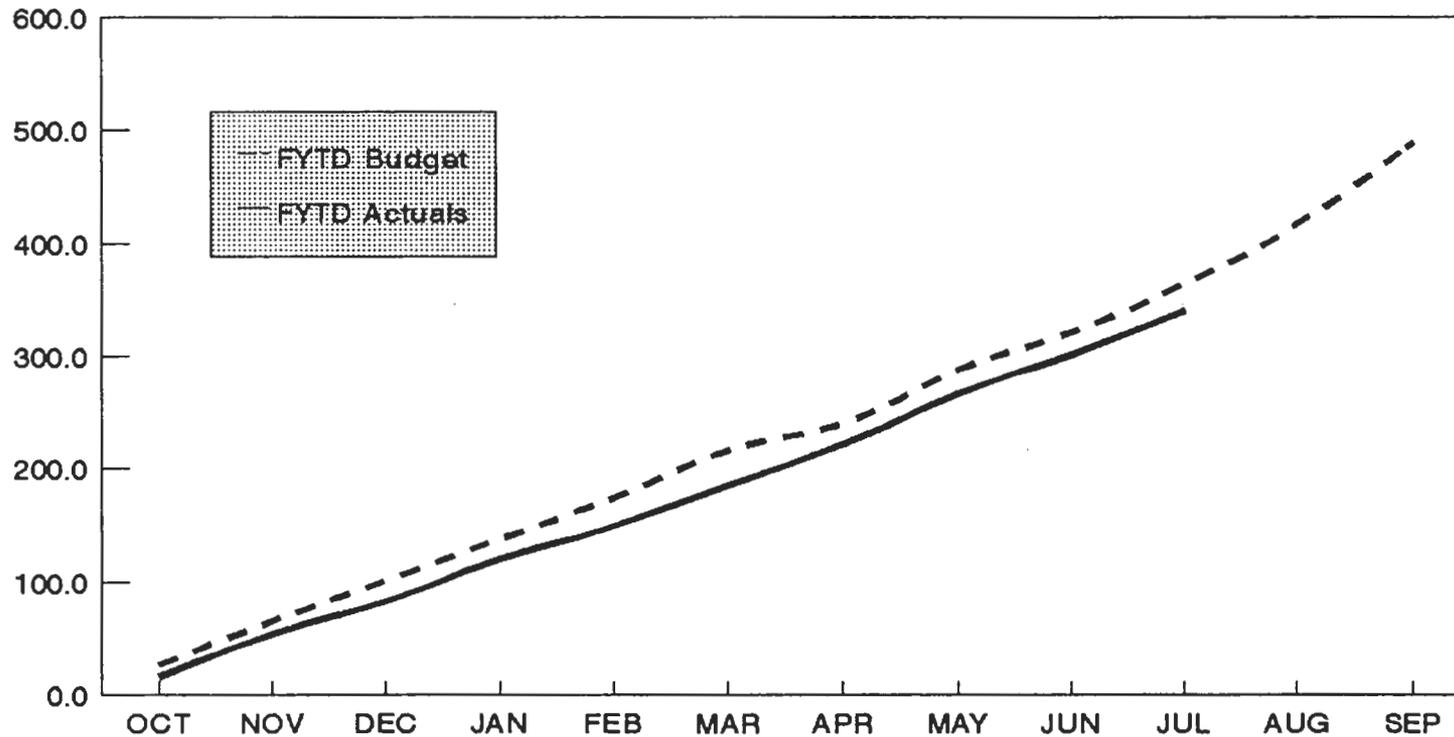

FYTD Budget	27.1	65.2	100.7	138.0	174.2	216.5	240.3	287.7	321.1	363.7	416.7	489.4
FYTD Actuals	16.1	53.8	83.1	120.2	149.6	185.5	221.9	266.6	301.1	340.0		
Spending Var	11.0	11.4	17.6	17.8	24.6	31.0	18.5	21.1	20.0	23.7		

TPA MILESTONES

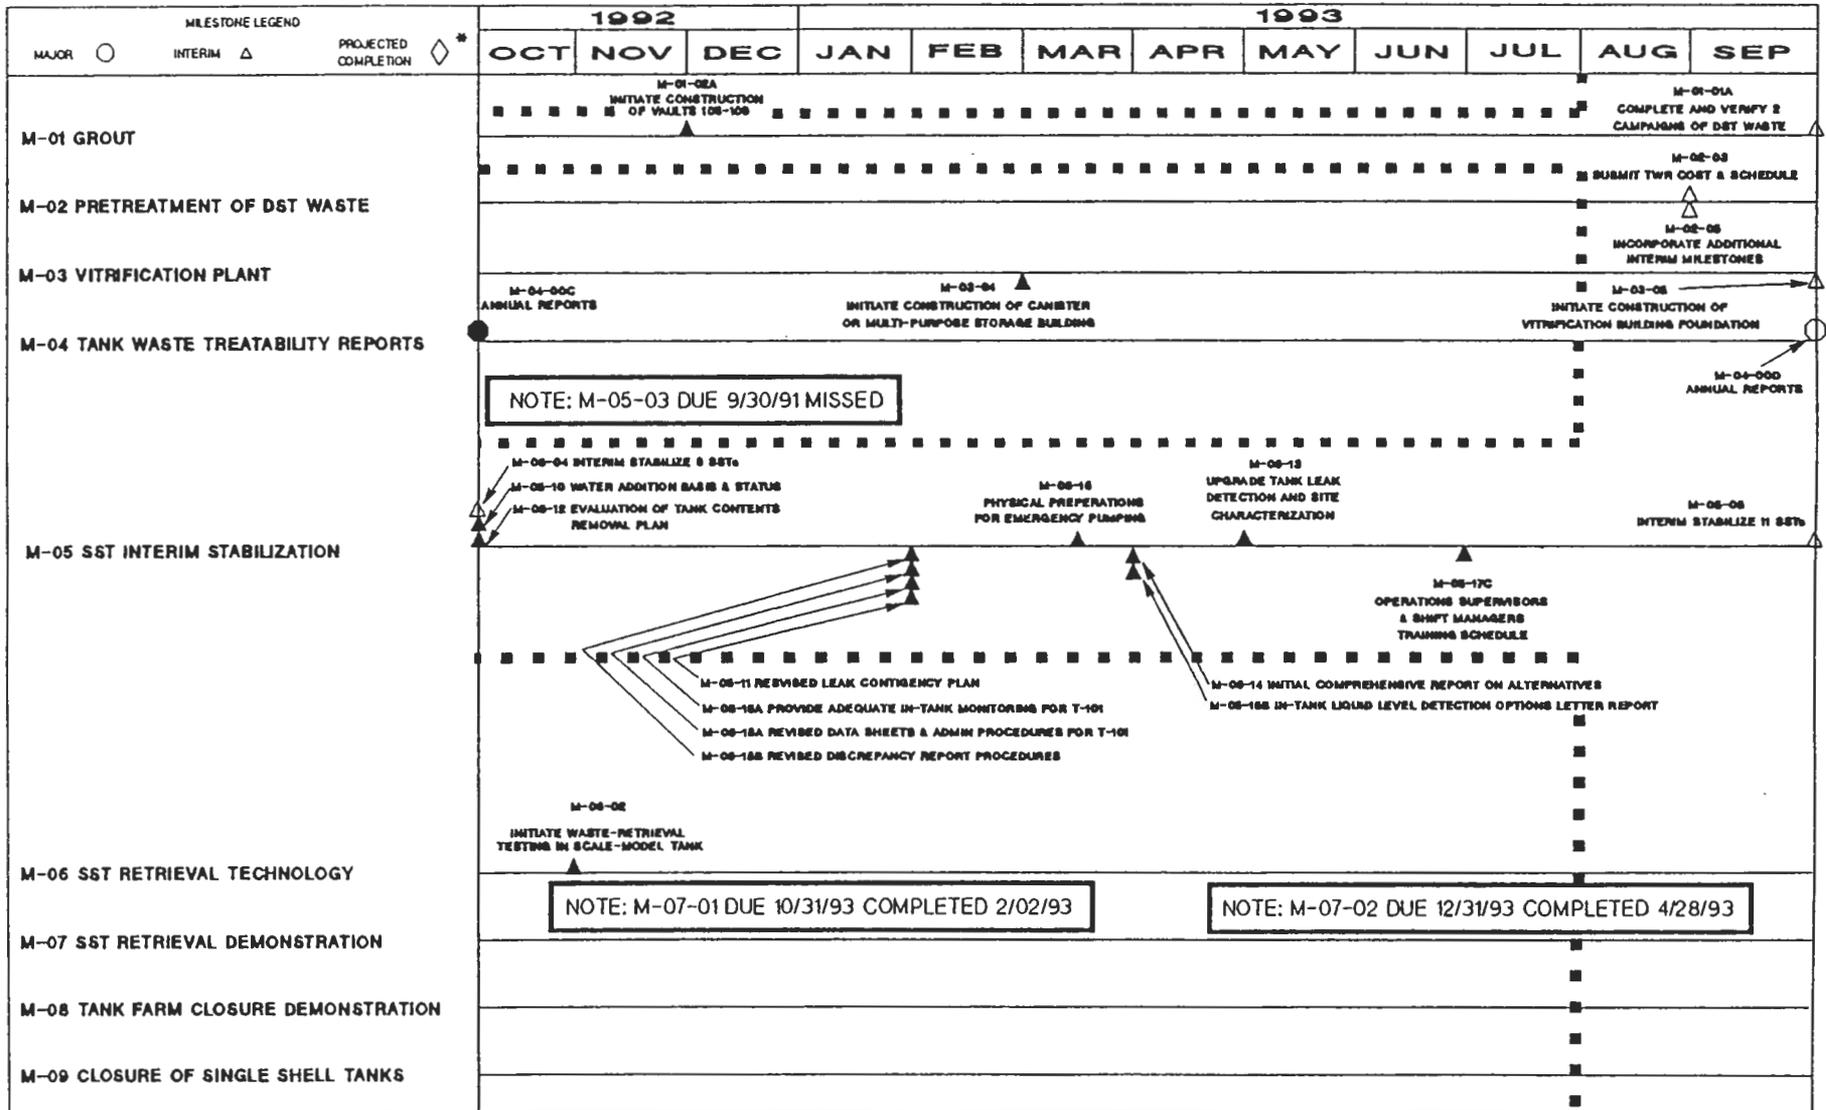


V.I.

WHC-MR-0403-9

STATUS AS OF 8-1-93 →

* PROJECTED MAJOR MILESTONE COMPLETION BASED ON FY 94 PLANNING CASE NOT FY 94 TARGET CASE

TPA MILESTONES

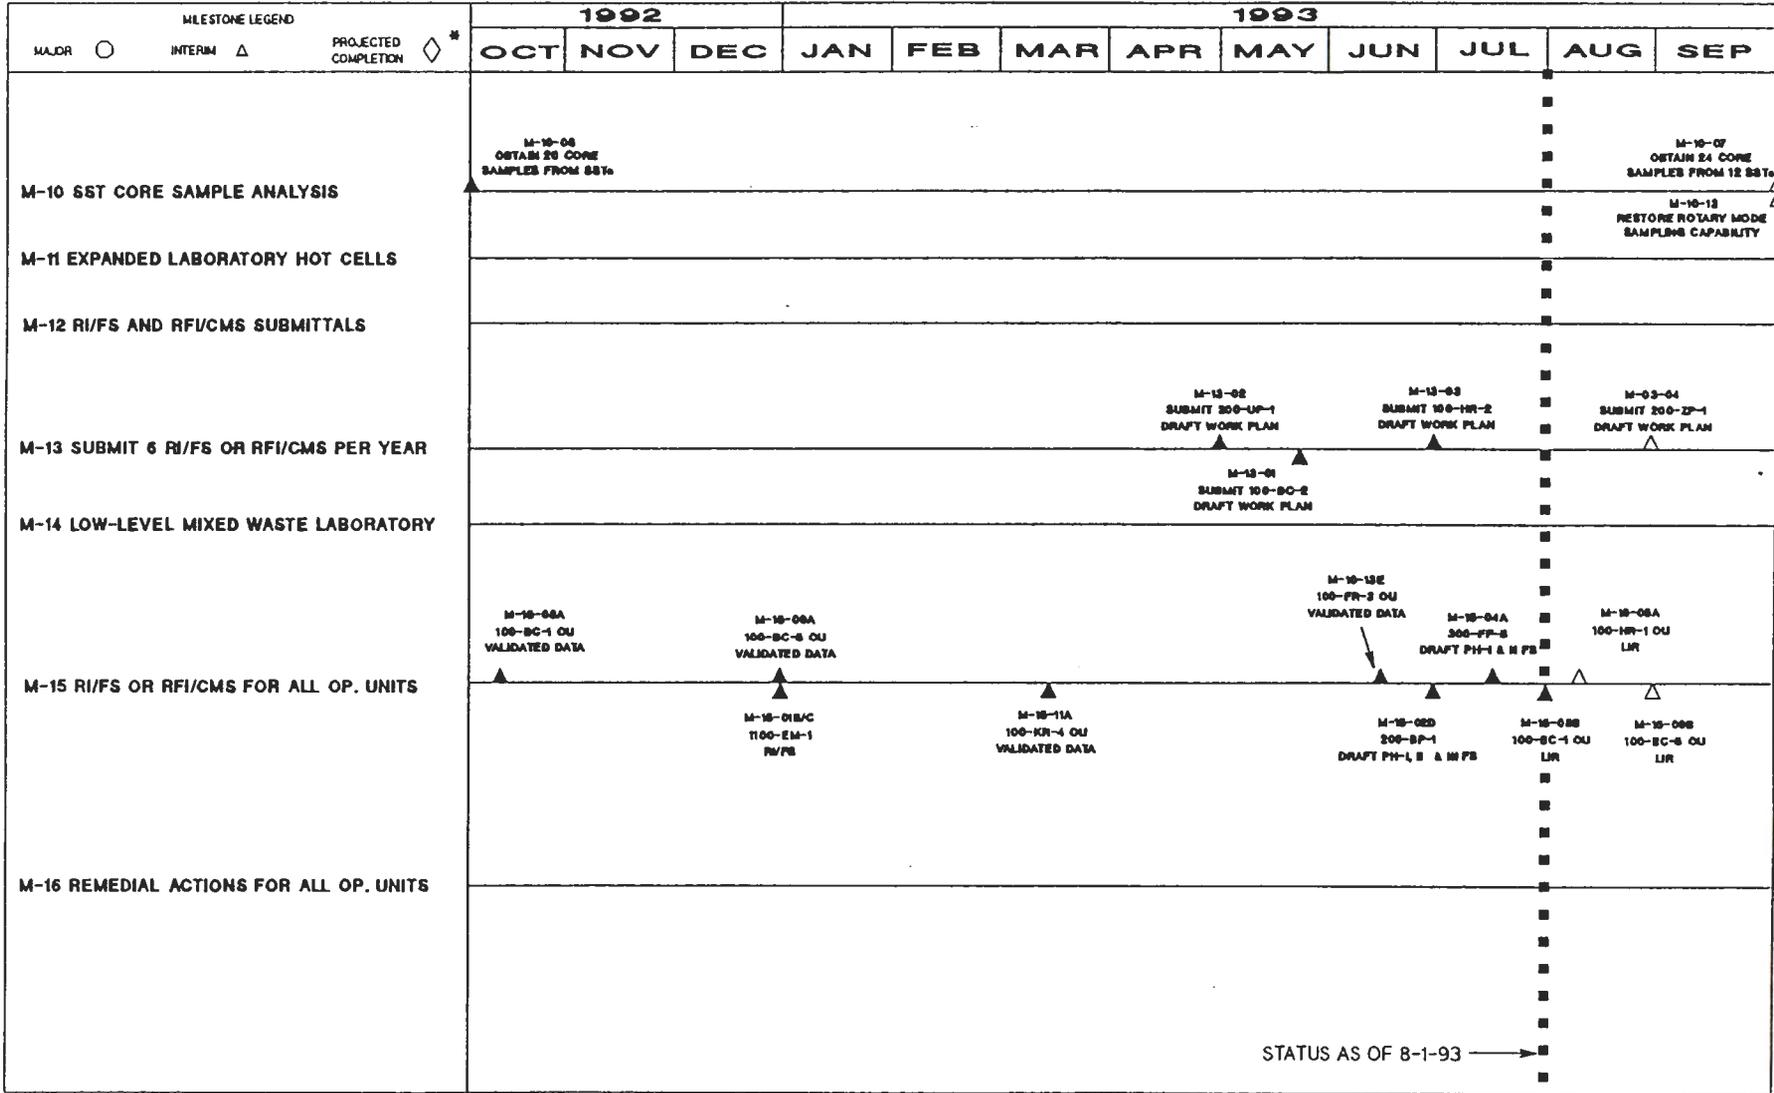


V I I

WHC-MR-0403-9

* PROJECTED MAJOR MILESTONE COMPLETION BASED ON FY 94 PLANNING CASE NOT FY 94 TARGET CASE

TPA MILESTONES

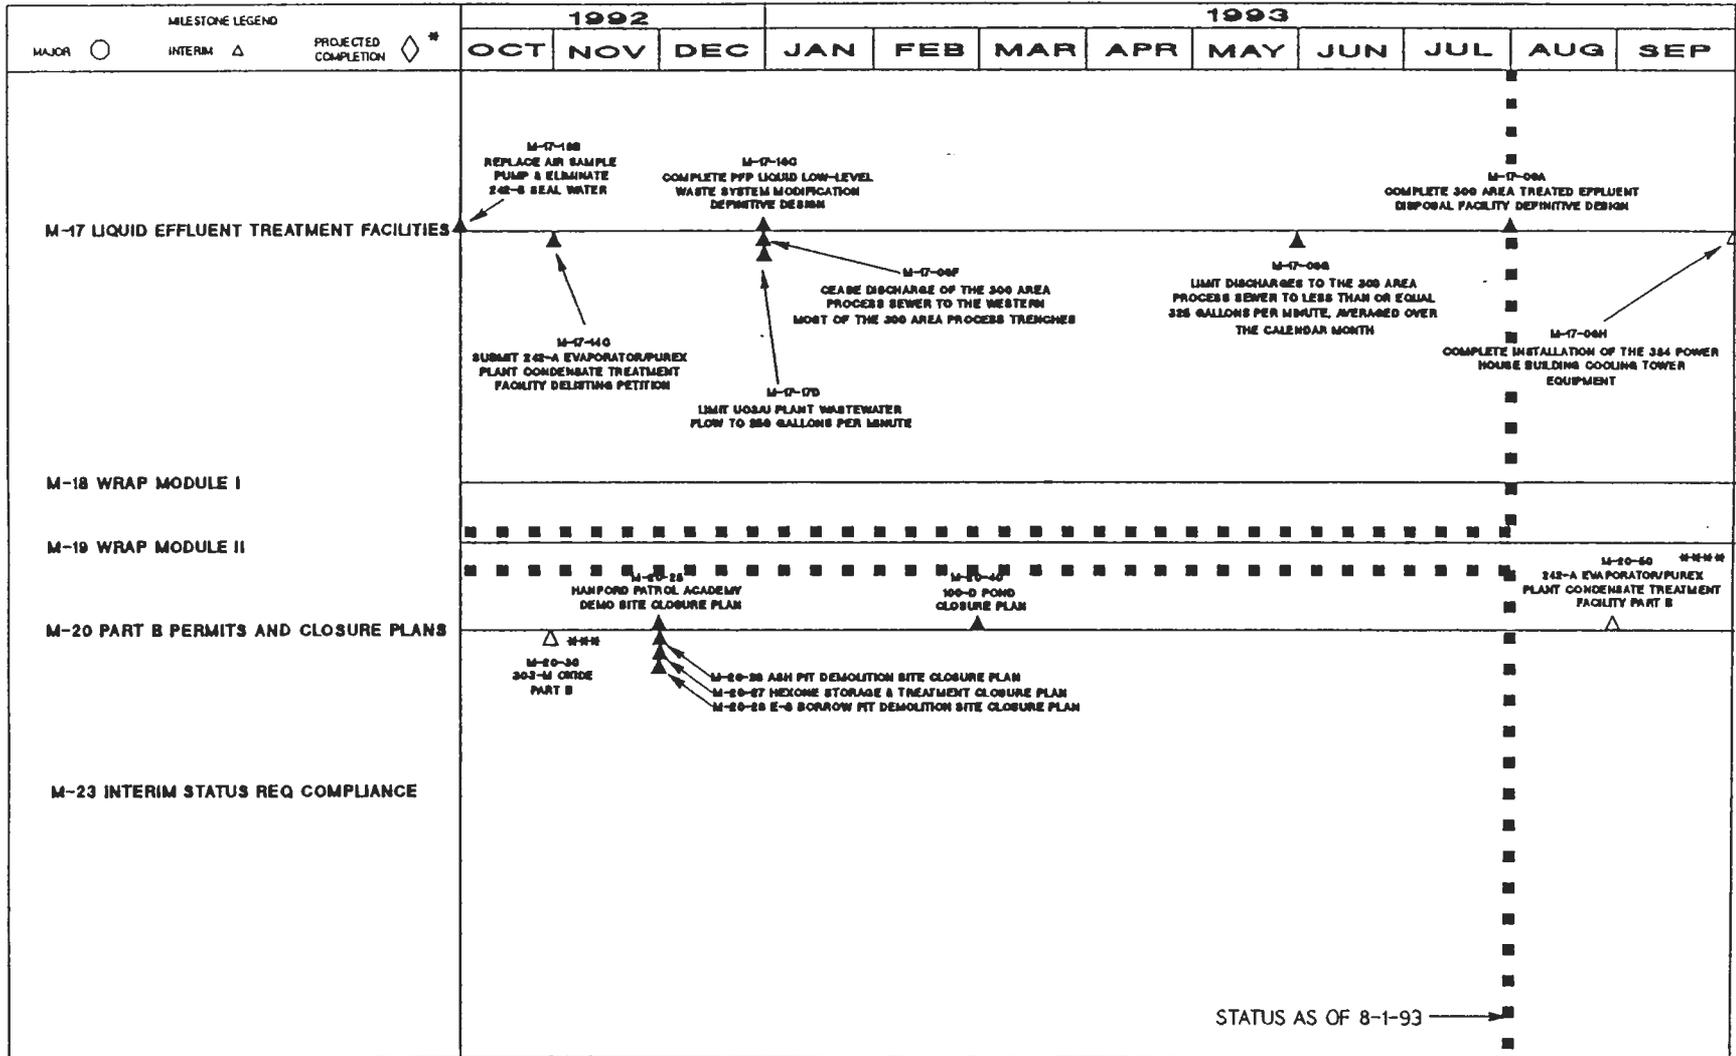

* PROJECTED MAJOR MILESTONE COMPLETION BASED ON FY 94 PLANNING CASE NOT FY 94 TARGET CASE

** WRAP 2B (TRU WASTE) DELAYED - WRAP 2A (LLW/RMW) PROJECTED TO BE COMPLETED AS SCHEDULED ON 9-30-99


*** REQUEST TO WITHDRAW PART A DENIED; DISPUTE RESOLUTION STARTED.

**** FACILITY CURRENTLY TITLED "200 AREA EFFLUENT TREATMENT FACILITY".

VTTT

WHC-MR-0403-9

TPA MILESTONES

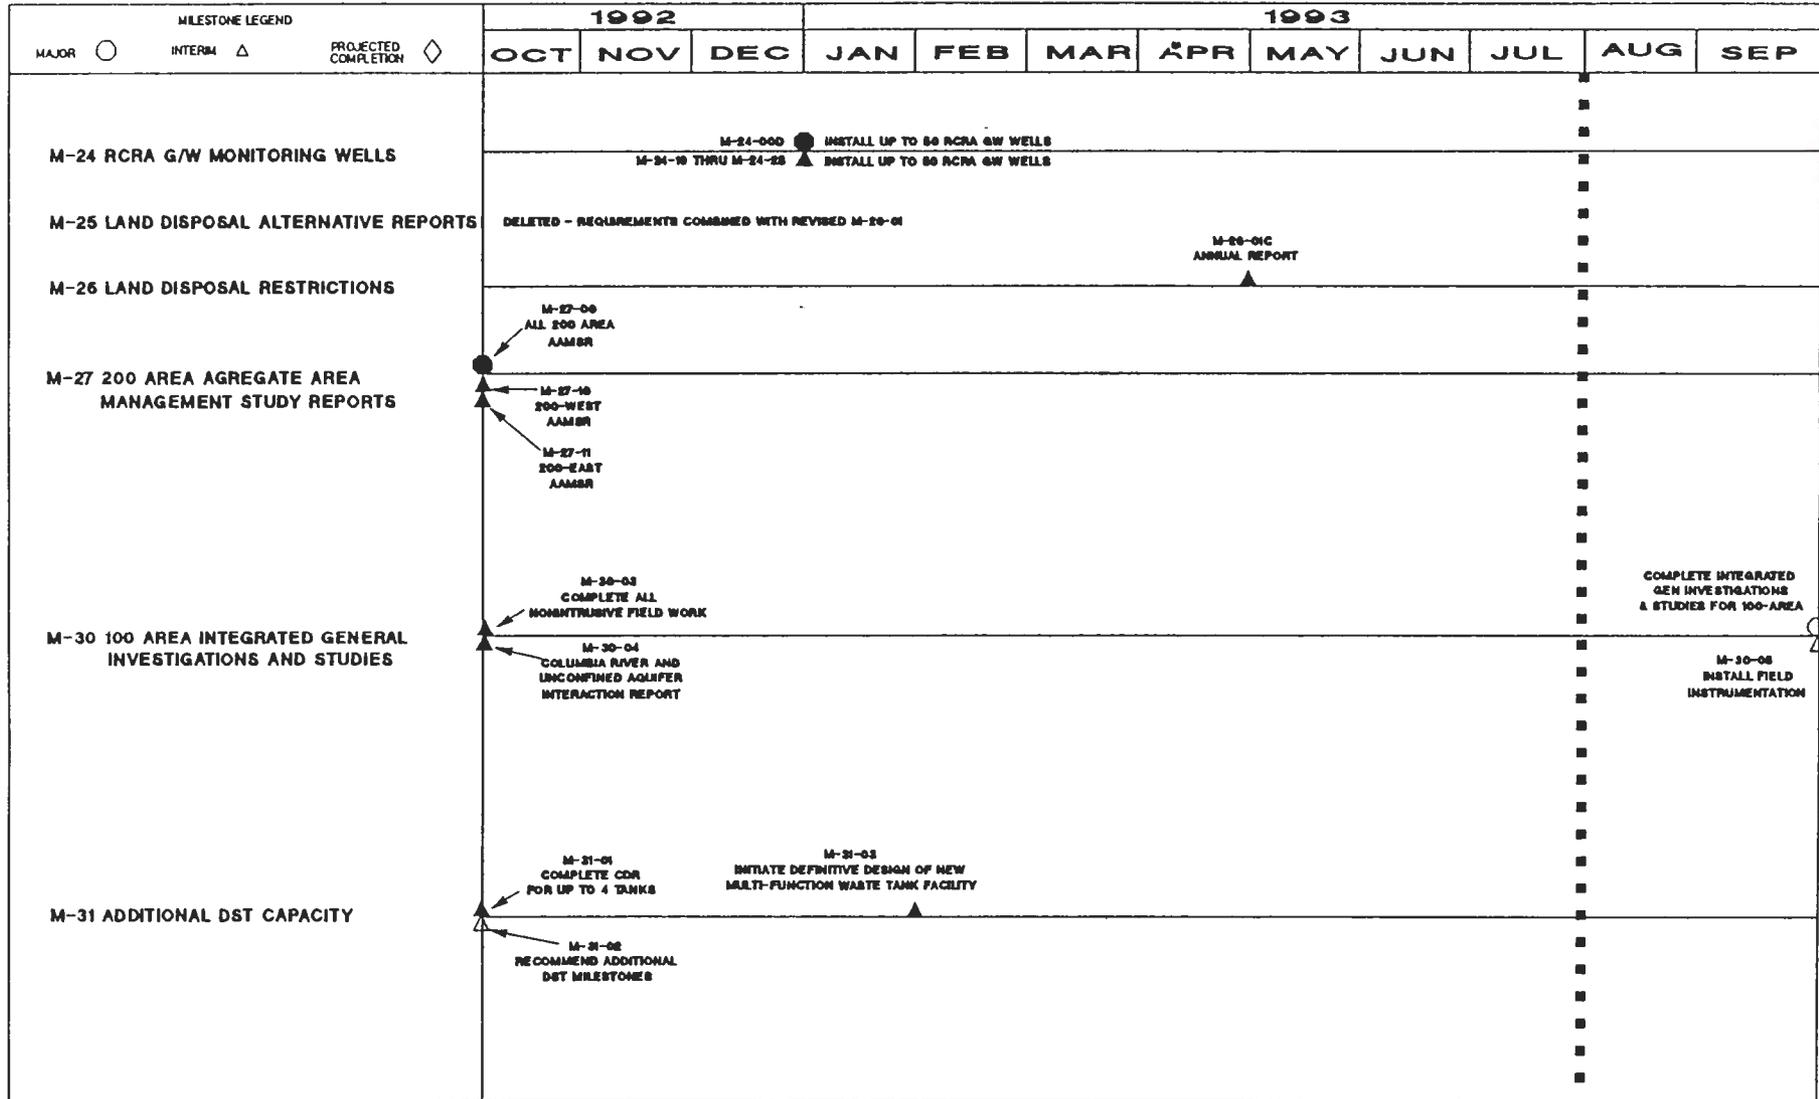

IX

WHC-MR-0403-9

LIST OF TERMS

CERCLA	Comprehensive Environmental Response Compensation and Liability Act
CY	calendar year
DST	double-shell tank
Ecology	Washington State Department of Ecology
EPA	U.S. Environmental Protection Agency
FY	fiscal year
HQ	U.S. Department of Energy, Headquarters
HWVP	Hanford Waste Vitrification Plant
LDR	land disposal restrictions
LFI	limited field investigation
NEPA	<i>National Environmental Policy Act</i>
OU	operable unit
PUREX	Plutonium-Uranium Extraction (Plant)
RCRA	Resource Conservation and Recovery Act
RFI/CMS	RCRA facility investigation/corrective measures study
RI/FS	remedial investigation/feasibility study
RL	U.S. Department of Energy, Richland Operations Office
SST	single-shell tank
TBD	to be determined
Tri-Party Agreement	<i>Hanford Federal Facility Agreement and Consent Order</i>
TWRS	tank waste remediation system
WRAP	Waste Receiving and Processing (Facility)
WSCF	Waste Sampling and Characterization Facility

9 3 1 3 0 6 1 6 0 0

MAJOR MILESTONE: M-01-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: G. H. Sanders **MANAGER:** R. J. Murkowski
BASELINE DATE: December 1996 **PROJECTED DATE:** To be determined (TBD)
DESCRIPTION: Complete 14 grout campaigns.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected*
M-01-01A	Complete and verify two campaigns of double-shell tank (DST) waste (including one campaign of phosphate-sulfate waste).	9/93	TBD
M-01-01B	Complete one additional campaign of DST waste (total is three campaigns including one phosphate-sulfate waste campaign).	12/93	TBD

*Projected date reflects *Hanford Federal Facility Agreement and Consent Order* (Tri-Party Agreement) change request M-01-92-01A.

ACCOMPLISHMENTS

- Received verbal agreement from Washington State Department of Ecology (Ecology) about the vault 103 rehydrotest. Ecology has reviewed and returned the videotapes.
- Completed Grout Treatment Facility capacity study. This study will analyze the logistics on the number of vaults to be filled each year.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Place cold cap material in vault 101.
- Continue characterization activities for DST 241-AP-102 in preparation of a data package to be sent to Ecology.
- Prepare four vault performance assessments for U.S. Department of Energy, Richland Operations Office (RL) review and forward to U.S. Department of Energy, Headquarters (HQ) peer review panel.
- Continue engineering of facility upgrades such as fire protection, Grout Processing Facility computer modifications, ventilation heat trace, lube oil, sanitary water, and fire system water.


9 3 1 3 7 2 5 1 6 2 7

- Complete operational test procedures on vault ventilation system and portable instrument house.
- Continue to resolve and close out comments from Brookhaven National Laboratory on the final safety analysis report. Continue confirmatory testing and validation of gas generation in the vaults.

MILESTONE STATUS/PROBLEMS/ISSUES

- HQ has interpreted a letter from the U.S. Nuclear Regulatory Commission as direction to pretreat waste before grouting. This has been incorporated in the new technical strategy and is the subject of ongoing negotiations.
- Reworking the comments and recommendations from the Performance Assessment HQ Peer Review Panel has had a major impact on resources and meeting of milestones. This rework is the major driver for delaying Grout Treatment Facility Tri-Party Agreement milestones (reference change request M-01-92-01A).
- Starting up the Grout Treatment Facility and initiating grout vault 102 filling to meet milestone M-01-01A is highly unlikely. Late mobilization in fiscal year (FY) 1993, facility readiness activities, and lack of appropriate staff already are causing delays (reference change request M-01-92-01A).

\$ Millions

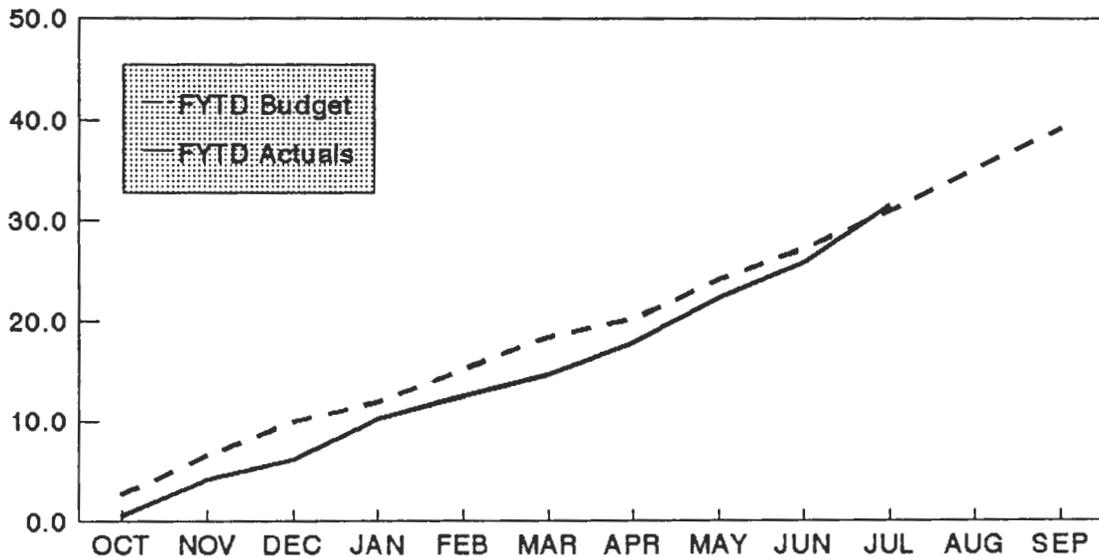

FYTD Budget	2.7	6.6	9.9	11.9	15.2	18.5	20.3	24.2	27.3	31.0	35.2	39.1
FYTD Actuals	0.5	4.2	6.2	10.2	12.5	14.7	17.9	22.4	25.9	31.5		
Spending Var	2.2	2.4	3.7	1.7	2.7	3.8	2.4	1.8	1.4	-0.5		

Variance Explanation: None required.

93130261628

MAJOR MILESTONE: M-02-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: L. Erickson

MANAGER: W. C. Miller

BASELINE DATE: TBD

PROJECTED DATE: TBD

DESCRIPTION: Initiate pretreatment of DST waste.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-02-03	Submit tank waste remediation system (TWRS) baseline scope, cost, and schedule.	8/31/93	1/31/94
M-02-05	Incorporate additional interim milestones to support pretreatment of DST waste.	8/31/93	1/31/94

ACCOMPLISHMENTS

- Continued negotiations with Ecology and U.S. Environmental Protection Agency (EPA) on TWRS rebaselining and revision, including M-02.
- Began Phase I of the DST 241-AZ-101 settling test to evaluate temperature response caused by shutting off airlift circulators (M-02-00-T7).

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Leave airlift circulators off through end of 90-day test period and continue to monitor DST 241-AZ-101 temperatures and sludge level. Issue process test report for Phase I of settling-bump test.
- Continue negotiations on M-02-00-related work. Establish revised milestones to reflect new strategy.


MILESTONE STATUS/PROBLEMS/ISSUES

- Target milestone M-02-00-T07 ("Initiate Settling Tests for Neutralized Current Acid Waste In-Tank Solids Washing") may be satisfied through initiation of Phase I of the DST 241-AZ-101 settling-bump test. Formal documentation is being prepared to obtain agreement on what constitutes completion of this milestone.

9 3 1 3 0 2 6 1 6 2 9

- The TWRS rebaselining study was completed and released in March. A 6-month public participation period has begun to allow public review and comment before agreements are reached with the regulators. The process includes public meetings, workshops, and the formation of a task force of representatives from potentially affected groups. The task force will review the study and provide comments to the three parties.
- Milestones M-02-03 and M-02-05 were established before the Evaluation of Hanford Tank Waste Remediation Alternatives Agreement in Principle was reached. The scope of these two milestones is an integral part of the evaluation and negotiation authorized by the agreement. Draft change requests to delay completion to January 31, 1994, following completion of ongoing negotiations, were prepared and discussed with Ecology and EPA at the Project Managers' meeting on August 3, 1993. Ecology and EPA agreed to approve the change requests.

\$ Millions

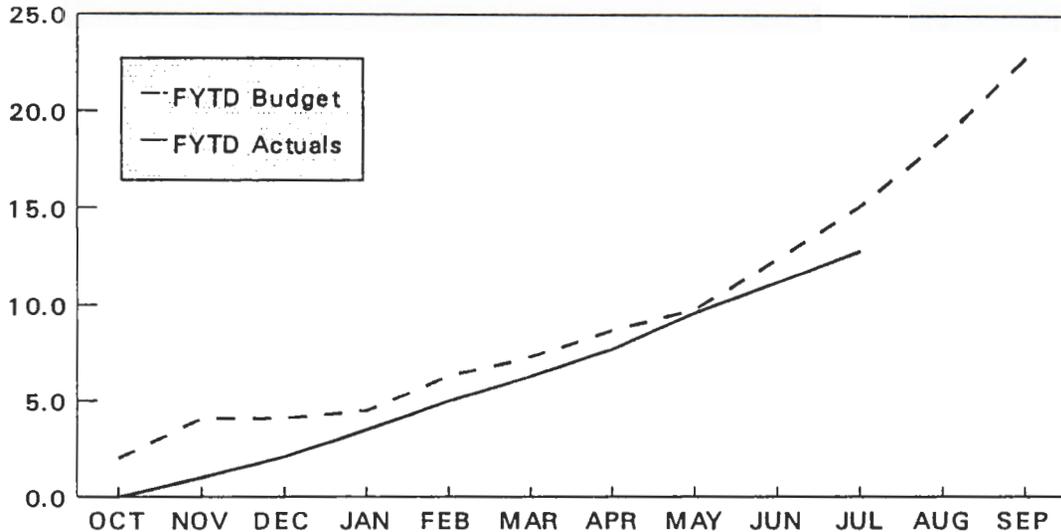

FYTD Budget	2.0	4.1	4.1	4.5	6.3	7.3	8.7	9.8	12.4	15.1	18.6	22.8
FYTD Actuals	0.0	1.0	2.1	3.5	5.0	6.3	7.7	9.6	11.2	12.8		
Spending Var	2.0	3.1	2.0	1.0	1.3	1.0	1.0	0.2	1.2	2.3		

Variance Explanation: The underrun results from five principal causes: subcontractors have delayed billing, manpower is not available to start work in some areas, and long-lead procurement times cause some delay. The baseline budgets in pretreatment has not been reduced to reflect work scope transferred to Pacific Northwest Laboratory, and work stopped in the Initial Pretreatment Module for less promising organic destruction technology development.

Change from June budget: Capital budget for the B Plant Process Condensate Treatment Facility (Project W-007H) was reduced again as a result of B Plant's change in mission.

MAJOR MILESTONE: M-03-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. W. Brown

MANAGER: R. A. Smith

BASELINE DATE: December 1999

PROJECTED DATE: December 1999

DESCRIPTION: Initiate Hanford Waste Vitrification Plant (HWVP) Operations.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-03-05	Initiate construction of the Vitrification Building foundation.	3/93	9/93

ACCOMPLISHMENTS

- Placed 80% of the base slab and started structural steel erection of the Operations Administration Building/TWRS Building.
- Completed aggregate crushing operations for calendar year (CY) 1993.
- Awarded the subcontract for construction of Mechanical Site Utilities.
- Completed 55% of detailed design.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Initiate installation of Mechanical Site Utilities.
- Complete Phase II of the HWVP TOE evaluation, verifying Phase I.
- Continue study to increase the throughput capacity of the HWVP.
- Begin formal safety evaluation activities for the increased plant capacity (4X) concept.
- Complete construction of the temporary warehouse.
- Begin construction of underground utilities.

9 3 1 3 7 2 6 1 6 3 1

MILESTONE STATUS/PROBLEMS/ISSUES

- Start of construction of the Vitrification Building foundation, milestone M-03-05, has been suspended for 6 months. The 6-month period will be used for public review of the proposed TWRS rebaselining and for negotiating of potential changes to the milestones in the agreement.

\$ Millions

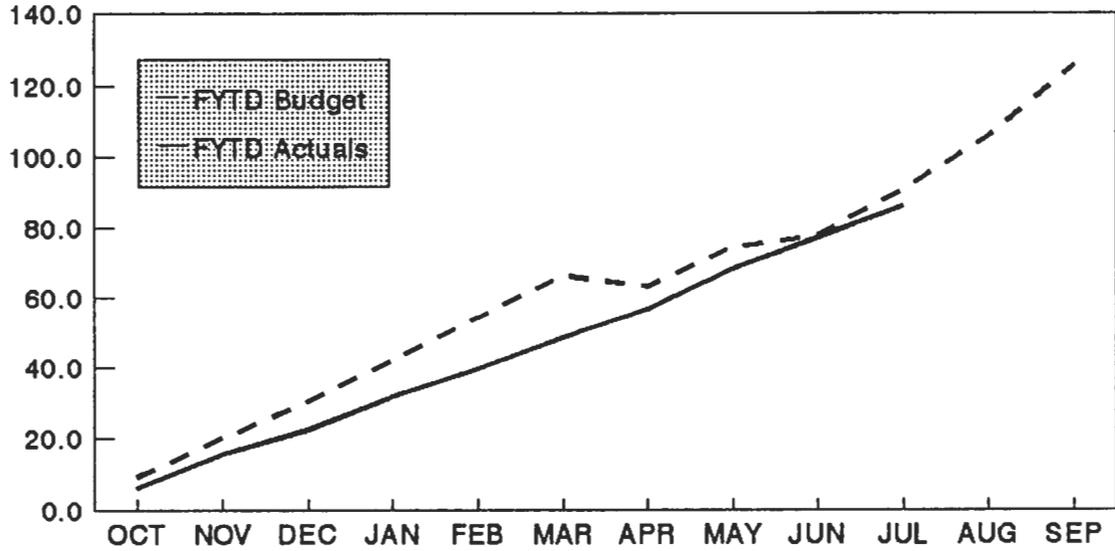

FYTD Budget	9.3	20.2	30.5	42.2	54.4	66.4	63.2	74.4	77.9	91.0	106.0	125.6
FYTD Actuals	6.2	15.8	22.5	32.0	39.5	48.4	56.9	68.3	77.2	86.2		
Spending Var	3.1	4.4	8.0	10.2	14.9	18.0	6.3	6.1	0.7	4.8		

Variance Explanation: None required.

9 3 1 3 7 2 6 1 5 3 2

MAJOR MILESTONE: M-04-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: L. Erickson

MANAGER: W. C. Miller

BASELINE DATE: September 30, 1993

PROJECTED DATE: September 30, 1993

DESCRIPTION: Provide annual reports of tank waste treatability studies.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-04-00D	Provide annual report of tank waste treatability studies.	09/93	09/93

ACCOMPLISHMENTS

- Received all draft sections from contributors.
- Completed draft report and began its review within Westinghouse Hanford Company.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Prepare and issue annual report.

MILESTONE STATUS/PROBLEMS/ISSUES

- Nothing significant to report.

9 5 1 3 0 2 6 1 6 3 3

\$ Thousands

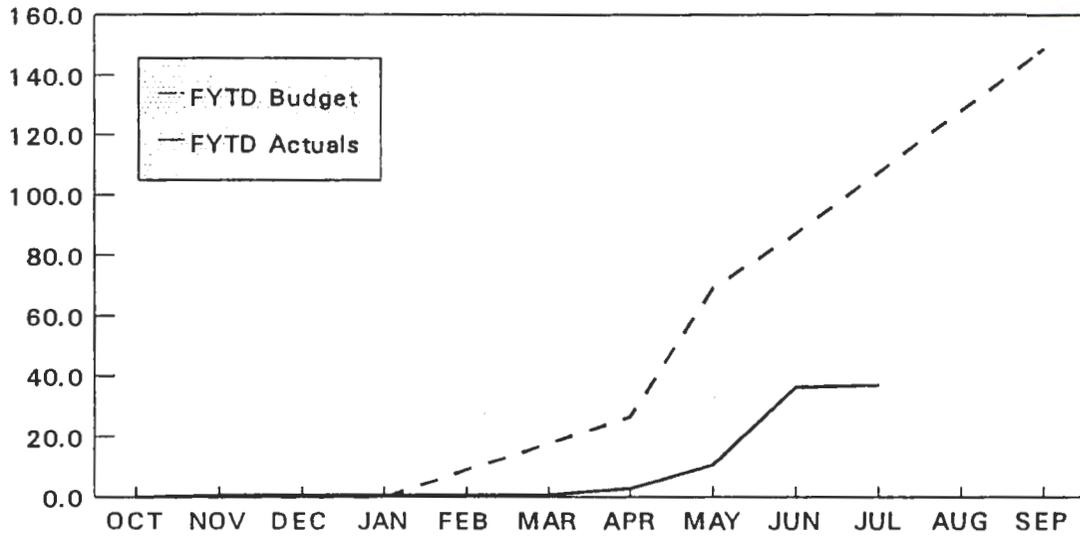

FYTD Budget	0.0	0.0	0.0	0.0	8.9	17.7	26.6	69.2	87.2	107.7	128.1	148.6
FYTD Actuals	0.0	0.5	0.5	0.5	0.7	0.7	2.8	10.6	36.3	37.0		
Spending Var	0.0	-0.5	-0.5	-0.5	8.2	17.0	23.8	58.6	50.9	70.7		

Variance Explanation: The spending variance results from using fewer resources than expected to prepare draft sections of the report. It also results from the contract costs for work performed that have not been costed. The effort, however, is on schedule and is likely to end the FY under budget. This chart is prepared in thousands to provide meaningful data. The Budget Baseline Summary table shows zero for FY to date budget and FY to date actual because that table is in millions.

9 3 1 3 1 2 6 1 5 3 4

MAJOR MILESTONE: M-05-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. E. Gerton

MANAGER: R. E. Raymond

BASELINE DATE: September 1995

PROJECTED DATE: TBD

DESCRIPTION: Complete single-shell tank (SST) interim stabilization.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-05-03	Interim stabilize an additional four SSTs.	9/91	TBD
M-05-04	Interim stabilize an additional nine SSTs.	9/92	TBD
M-05-05	Interim stabilize an additional 11 SSTs.	9/93	TBD
M-05-17C	Provide to EPA and Ecology the draft curriculum for the upgraded Maintenance Training Program, and an implementation schedule for that training.	6/94	6/94
M-05-17B	Complete Nuclear Operator training.	12/93	12/93

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including probable revision of this milestone.
- Received the Justification for Continued Operation Addendum to allow progress to resume on preparing to interim stabilize two tanks in Tank Farm 241-BY and three tanks in Tank Farm 241-C. This was a major hurdle in this activity and represents significant progress for this program.
- Completed the integrity assessment of the waste transfer lines.
- Completed the engineering assessments necessary to provide final determination and documentation that SST 241-SX-102 is not leaking.
- Completed actions required to remove two SSTs from the ferrocyanide watchlist: 241-BX-110 and -111. This clears an important step in preparing to pump these two SSTs.

9 3 1 3 1 6 1 6 3 5

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Begin emergency pumping of SST 241-BX-111 and pumping of SST 241-BX-110. The pump in 241-BX-111 will be replaced next month.
- Complete safety analysis report addendum to allow alternative methods for transfer of RAD waste within SST farms. This report is now in RL for review.
- Continue restoration of double-contained receiver tank 244-U.

MILESTONE STATUS/PROBLEMS/ISSUES

- RL submitted a draft Tri-Party Agreement Change Control Form to the regulators that would add the start of pumping SST 241-BX-111 in August 1993 as a new interim milestone. Ecology has rejected this approach. RL is reviewing its options before deciding its next step.
- A "Creation of Danger," as defined in Article 31 of the Tri-Party Agreement, was declared on January 28, 1992. To protect worker safety, a work restriction was placed on all SST farms, and fresh air is required to operate within the boundaries of three farms. On February 28, 1992, all waste transfers in the 200-Area tank farms were halted because of concerns on fissile material inventory. The cessation on waste transfers continues. The impacts to the Tri-Party Agreement will result in a change request.
- A safety question was raised about the hazards of higher temperatures that could result in the SSTs when liquid is removed from them. Analyses and studies continue on this question.
- This milestone is being reevaluated under the New Technical Strategy of the TWRS; therefore, the negotiations may result in changes to this milestone. A public involvement program is in place, and renegotiations of this milestone are in progress.

9 3 1 3 1 6 3 6

\$ Millions

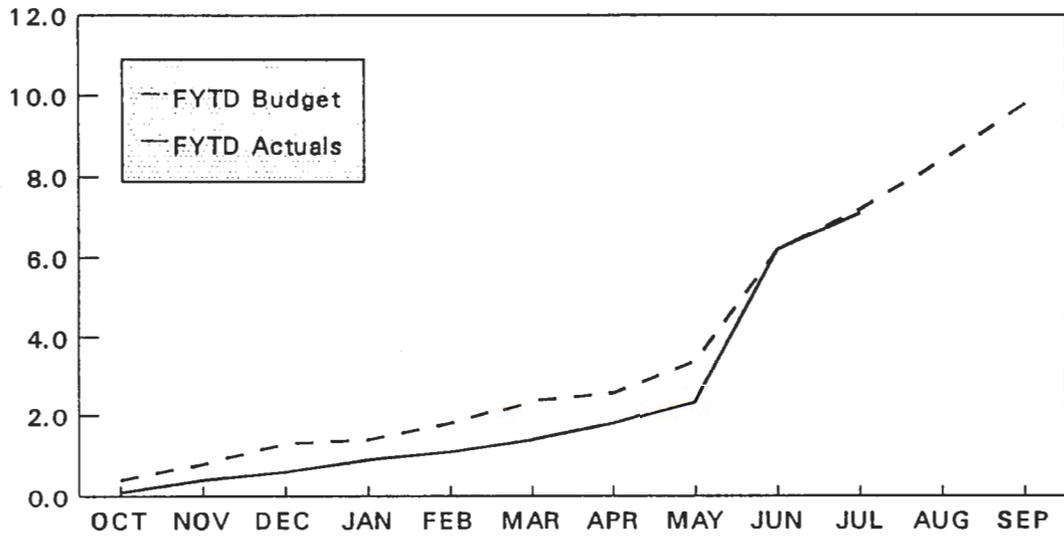

FYTD Budget	0.4	0.8	1.3	1.4	1.8	2.4	2.6	3.4	6.2	7.2	8.4	9.8
FYTD Actuals	0.1	0.4	0.6	0.9	1.1	1.4	1.8	2.4	6.2	7.1		
Spending Var	0.3	0.4	0.7	0.5	0.7	0.9	0.8	1.0	0.0	0.1		

Variance Explanation: None required.

9 8 1 3 7 2 6 1 6 3 7

This page intentionally left blank.

9 3 1 3 0 2 6 1 6 3 8

MAJOR MILESTONE: M-06-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: L. Erickson

MANAGER: W. C. Miller

BASELINE DATE: June 1994

PROJECTED DATE: June 1994

DESCRIPTION: Develop SST waste retrieval technology and complete scale-model testing.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including possible revision of this milestone. Continuing discussions cover the recommended milestone program baseline.
- Completed testing on the sludge removal and conveyance system.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Submit, review, and obtain regulator concurrence on the M-06 definition plan by September 1993.
- Experimentally optimize retrieval rates with computer modeling. Define the airlift conveyance system limits.

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

93133261609

\$ Millions

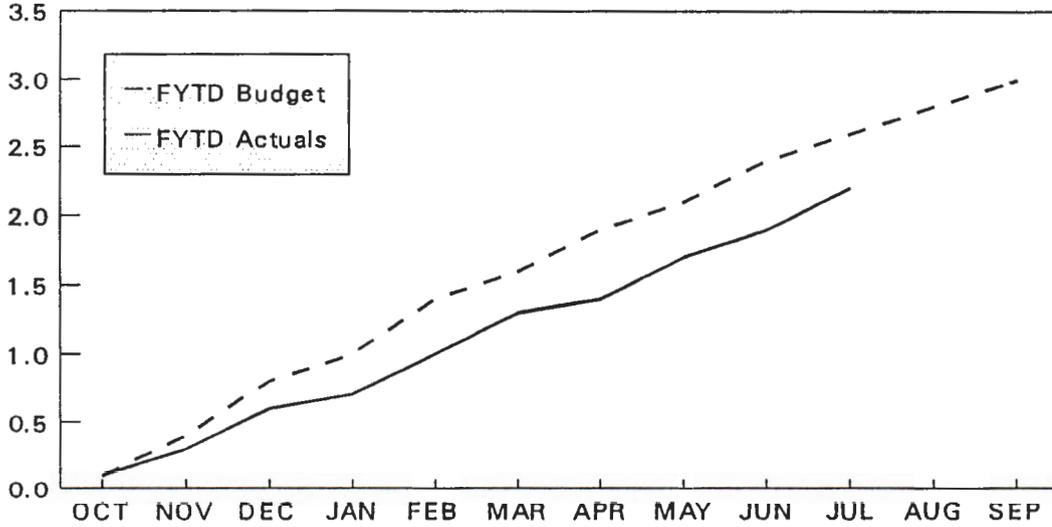

FYTD Budget	0.1	0.4	0.8	1.0	1.4	1.6	1.9	2.1	2.4	2.6	2.8	3.0
FYTD Actuals	0.1	0.3	0.6	0.7	1.0	1.3	1.4	1.7	1.9	2.2		
Spending Var	0.0	0.1	0.2	0.3	0.4	0.5	0.5	0.4	0.2	0.4		

Variance Explanation: The cost underrun results from contract procurement commitments that have not been costed as expected.

9 3 1 3 0 2 6 1 6 3 0

MAJOR MILESTONE: M-07-00
 STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: L. Erickson

MANAGER: W. C. Miller

BASELINE DATE: October 1997

PROJECTED DATE: October 1997

DESCRIPTION: Initiate full-scale demonstration of waste retrieval technology.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including probable revision of this milestone. Continuing discussions explained the recommended milestone program baseline, as well as discussions on tank farm closure. Barrier technology and application requirements were also discussed.
- Continued preparation of environmental and regulatory compliance documentation as required by *Resource Conservation and Recovery Act (RCRA)*, *Washington Clean Air Act of 1967*, and *National Environmental Policy Act (NEPA)*.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Develop a detailed plan for M-07-00 achievement, integrated with milestone M-06-00 ("Develop SST Waste Retrieval Technology") and the Underground Storage Tank Integrated Demonstration activities. Propose revisions to the M-07 interim milestones based on the detailed schedules.
- Develop and present to the regulators a position paper on tank waste retrieval program regulatory compliance issues.

MILESTONE STATUS/PROBLEMS/ISSUES


- Preliminary assessments of the impacts of performing NEPA analyses (environmental assessment or environmental impact statement) suggest they could substantially delay this program.
- The preliminary strategy for SST retrieval includes two reference technologies: sluicing and long-reach manipulator systems. The retrieval demonstration under M-07 will use sluicing technology.

9 3 1 3 1 6 1 1

Significant development work is required before other retrieval technologies can be used. The long-reach manipulator system (or alternative technology) will be deployed to complete the retrieval demonstration if sluicing cannot achieve the 95-percent waste retrieval criteria for the M-07 demonstration.

- The preliminary studies on subsurface barriers show this technology is in its infancy. The potential that subsurface barriers be required as part of this milestone will practically ensure that the milestone could not be met as scheduled, and the benefit to the environment is questionable. The utilization of surface barriers would provide similar protection to groundwater by preventing precipitation from recharging the vadose zone.
- This milestone is being reevaluated under the New Technical Strategy of the TWRS. The negotiations may result in changes to this milestone. A public involvement program is in place, and renegotiations of this milestone are in progress.

\$ Millions

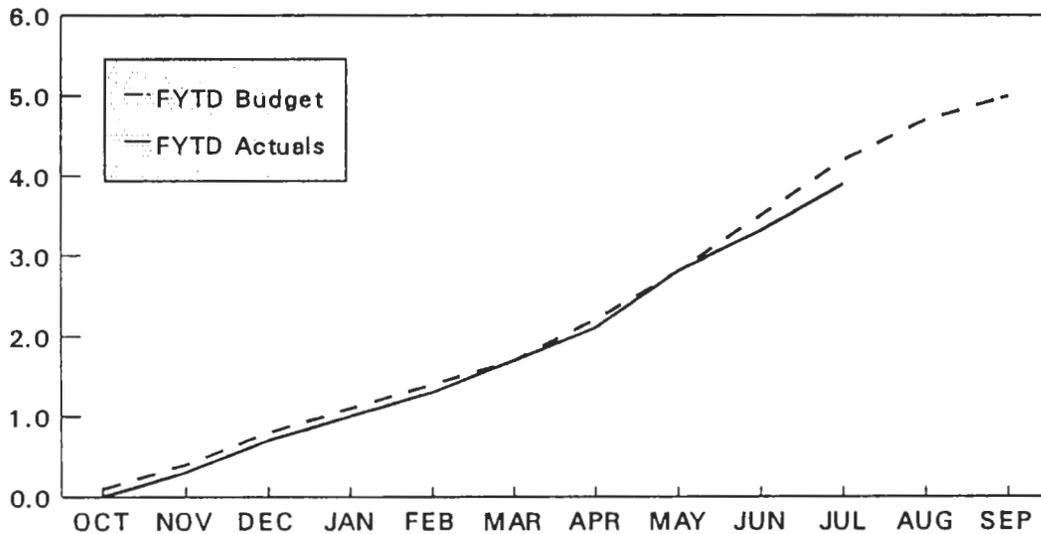

FYTD Budget	0.1	0.4	0.8	1.1	1.4	1.7	2.2	2.8	3.5	4.2	4.7	5.0
FYTD Actuals	0.0	0.3	0.7	1.0	1.3	1.7	2.1	2.8	3.3	3.9		
Spending Var	0.1	0.1	0.1	0.1	0.1	0.0	0.1	0.0	0.2	0.3		

Variance Explanation: None required.

951701612

MAJOR MILESTONE: M-08-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: L. Erickson

MANAGER: W. C. Miller

BASELINE DATE: June 2004

PROJECTED DATE: June 2004

DESCRIPTION: Initiate full-scale tank farm closure demonstration project.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including probable revision of this milestone. Continuing discussions explained the recommended milestone program baseline, as well as discussions on tank farm closure. Also discussed barrier technology and application requirements.

PLANNED ACTIONS FOR THE NEXT 6 MONTHS


- Complete a tank farm retrieval and closure program plan.

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.
- The preliminary studies on subsurface barriers indicate this technology is in its infancy. The potential that subsurface barriers be required as part of this milestone will practically ensure that the milestone cannot be met as scheduled and the benefit to the environment is questionable. The utilization of surface barriers would provide similar protection to groundwater by preventing the recharge of the vadose zone through precipitation.
- This milestone is being reevaluated under the new technical strategy of the TWRS. This milestone may be modified by the TWRS negotiations. A public involvement program is in place, and renegotiations of this milestone are in progress by the three parties.

9 3 1 3 2 6 1 6 1 3

\$ Millions

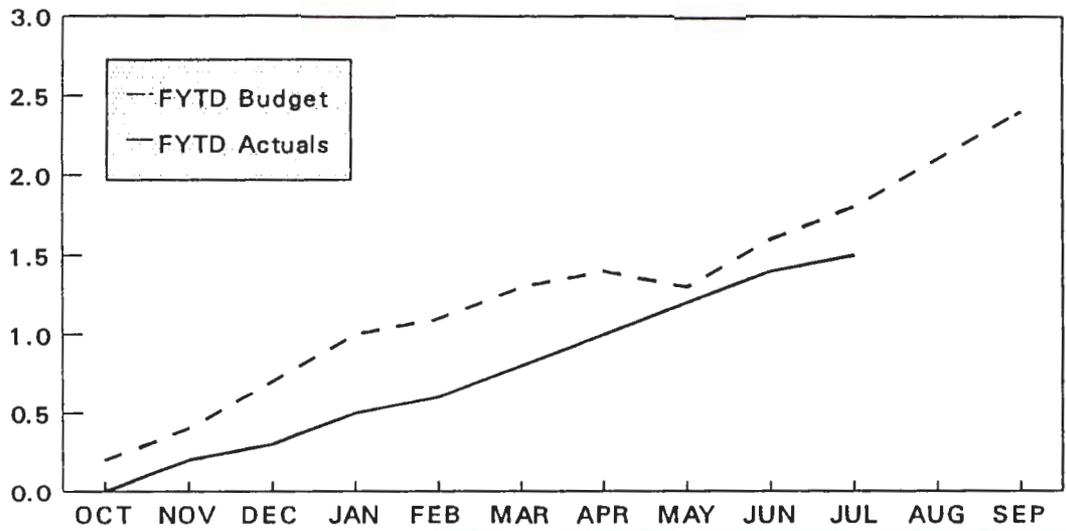

FYTD Budget	0.2	0.4	0.7	1.0	1.1	1.3	1.4	1.3	1.6	1.8	2.1	2.4
FYTD Actuals	0.0	0.2	0.3	0.5	0.6	0.8	1.0	1.2	1.4	1.5		
Spending Var	0.2	0.2	0.4	0.5	0.5	0.5	0.4	0.1	0.2	0.3		

Variance Explanation: Variance is caused by difficulties in acquiring personnel to perform technology development and program support tasks.

9 3 1 3 0 6 1 4

MAJOR MILESTONE: M-09-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. D. Freeberg

MANAGER: T. M. Wintczak

BASELINE DATE: June 2018

PROJECTED DATE: June 2018

DESCRIPTION: Complete closure of all 149 SSTs.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including probable revision of this milestone. Continuing discussions explained the recommended milestone program baseline, as well as discussions on tank farm closure. Also discussed barrier technology and application requirements.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Continue to redefine SST waste disposal strategy under the TWRS Decision Plan.
- Issue in the *Federal Register* a notice of intent for the TWRS Environmental Impact Statement.
- Begin the next revision to the SST Closure/Corrective Action Work Plan, a precursor document for the SST Closure Plan.

MILESTONES STATUS/PROBLEMS/ISSUES

- This milestone is on schedule; however, it may be in jeopardy if preclosure activities are not accelerated. Several activities require acceleration: Supplemental Environmental Impact Statement and Record of Decision preparation, SST Waste and Field Characterization, Technology Development, and concurrent permitting with facility design.
- This milestone is being reevaluated under the new technical strategy of the TWRS; therefore, this milestone is subject to modification under the TWRS negotiations. A public involvement program is in place, and renegotiations of this milestone are in progress by the three parties.

9 2 1 3 0 6 1 9 0 3 1 9 9 6

\$ Millions

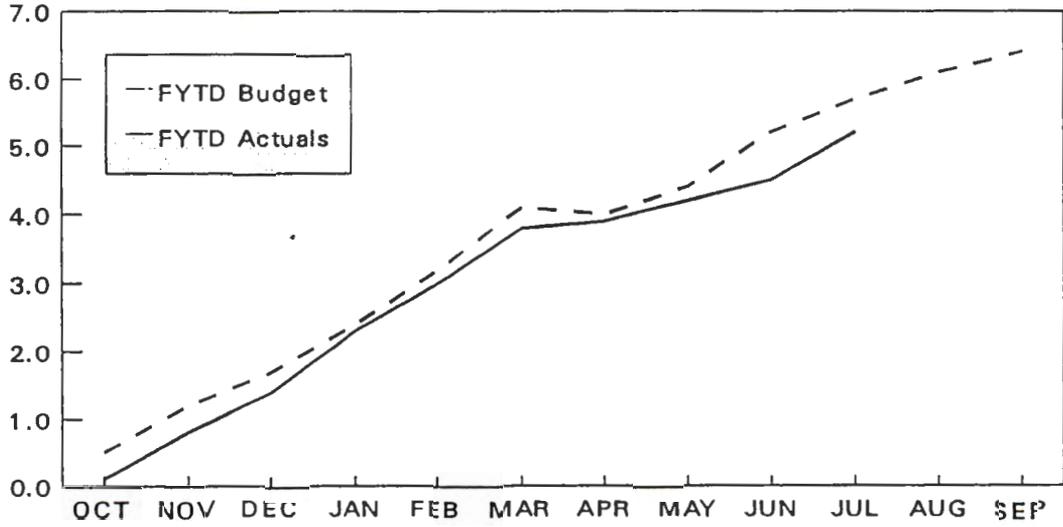

FYTD Budget	0.5	1.2	1.7	2.4	3.2	4.1	4.0	4.4	5.2	5.7	6.1	6.4
FYTD Actuals	0.1	0.8	1.4	2.3	3.0	3.8	3.9	4.2	4.5	5.2		
Spending Var	0.4	0.4	0.3	0.1	0.2	0.3	0.1	0.2	0.7	0.5		

Variance Explanation: None required.

9313161616

MAJOR MILESTONE: M-10-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. E. Gerton

MANAGER: J. G. Propson

BASELINE DATE: September 1998

PROJECTED DATE: September 1998

DESCRIPTION: Complete analyses of at least two complete core samples from each SST.

PAST DUE AND SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-10-07	Obtain 24 core samples from 12 SSTs.	9/93	9/93
M-10-13	Restore rotary mode sampling capability at the Hanford Site.	9/93	9/93

ACCOMPLISHMENTS

- Continued negotiations with Ecology and EPA on TWRS rebaselining, including probable revision of this milestone. Substantial agreement has been reached on the recommended changes to a new milestone program baseline. These negotiation sessions also continued discussions with the regulators on a new HQ direction that proposes the SST Characterization Program and related Tri-Party Agreement milestones be reevaluated to reflect retrieval requirements. Characterization data is required to (1) resolve tank safety issues, (2) develop retrieval technologies, and (3) identify pretreatment technologies. Changes to the baseline will need to be reflected in the Tri-Party Agreement major milestone M-10-00.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Obtain core samples from SSTs 241-C-106, -C-108, -C-111, and -T-101. All of these SSTs are safety issue SSTs.
- Continue rotary mode sampling testing and implementation.
- Issue the TWRS Waste Characterization Plan. This rewrite of the SST Waste Characterization Plan will incorporate all TWRS requirements into a single plan.

MILESTONE STATUS/PROBLEMS/ISSUES

- The major milestone is on schedule; however, interim milestones M-10-07 through M-10-12 are under evaluation. Several actions can be taken to ensure meeting these milestones, both internally and with the regulators. These are being discussed with the regulators.
- The core sampling program is in a technical stand-down because of a possible problem with sample recovery. Less material is being recovered than is expected. Core samples were taken from SST 241-T-105, and the problem appears to have persisted. Until this is resolved, no further core samples are being taken.
- This milestone is being reevaluated under the new technical strategy of the TWRS; therefore, this milestone is subject to modification under the TWRS negotiations. A public involvement program is in place, and renegotiations of this milestone are in progress by the three parties.

9 3 1 9 3 1 3 6

\$ Millions

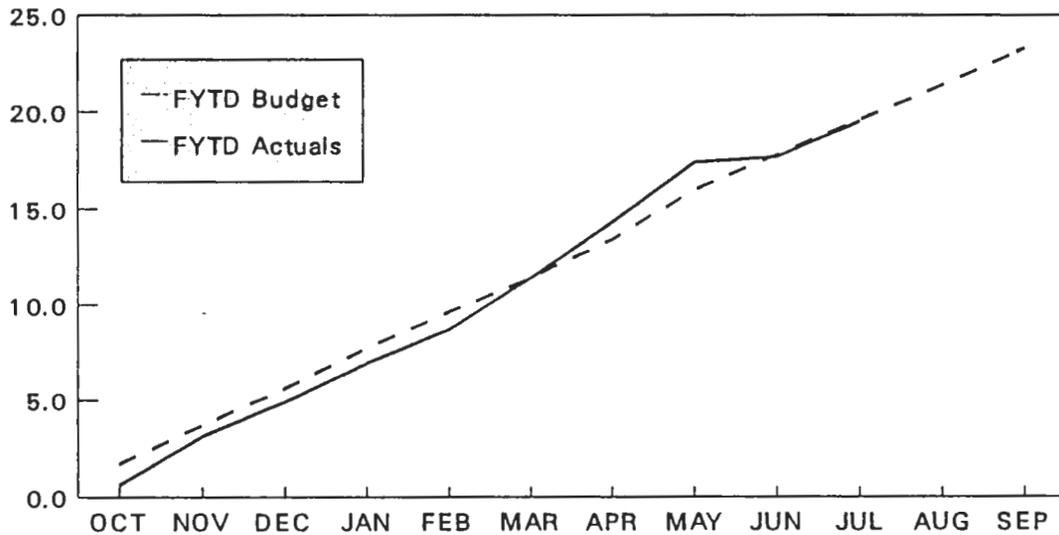

FYTD Budget	1.7	3.7	5.6	7.7	9.6	11.4	13.4	16.0	17.8	19.6	21.4	23.3
FYTD Actuals	0.6	3.1	4.9	6.9	8.7	11.4	14.3	17.4	17.7	19.5		
Spending Var	1.1	0.6	0.7	0.8	0.9	0.0	-0.9	-1.4	0.1	0.1		

Variance Explanation: None required.

**MAJOR MILESTONE: M-11-00
STATUS FOR END OF MONTH: JULY 1993**

DOE DIRECTOR: J. M. Hennig

MANAGER: M. L. Bell

BASELINE DATE: June 1994

PROJECTED DATE: June 1994

DESCRIPTION: Complete construction and initiate operations of expanded laboratory hot cells for high-level radioactive mixed waste.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Construction:
 - Completed installing the built-up roof, interior insulation, sheetrock and fire system piping.
 - Received final manipulators and all shielding windows.
 - Completed welding and grinding on load in-load out and sample preparation compartments.
 - Started installation and testing on hot cell drain lines.
- Startup Activities:
 - Submitted the level 3 startup schedule for final approval.
 - Completed the DOE Order compliance review.
 - Submitted a draft startup definition for review.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Construction:
 - Complete attachment of all transfer drawers and compartments to the hot cell.
 - Complete installation and testing of hot cell drain lines.
 - Complete installation of electrical, ventilation, and piped services in and around the hot cell.

6
1
9
1
9
1
3
1
3
9

- Test sample transfer cart.
- Install acoustical tile ceiling and room lighting.
- Startup Activities:
 - Approve startup schedule by August 20, 1993.
 - Begin operational readiness review process.
 - Identify equipment required for startup and prepare purchase orders.

MILESTONE STATUS/PROBLEMS/ISSUES

None.

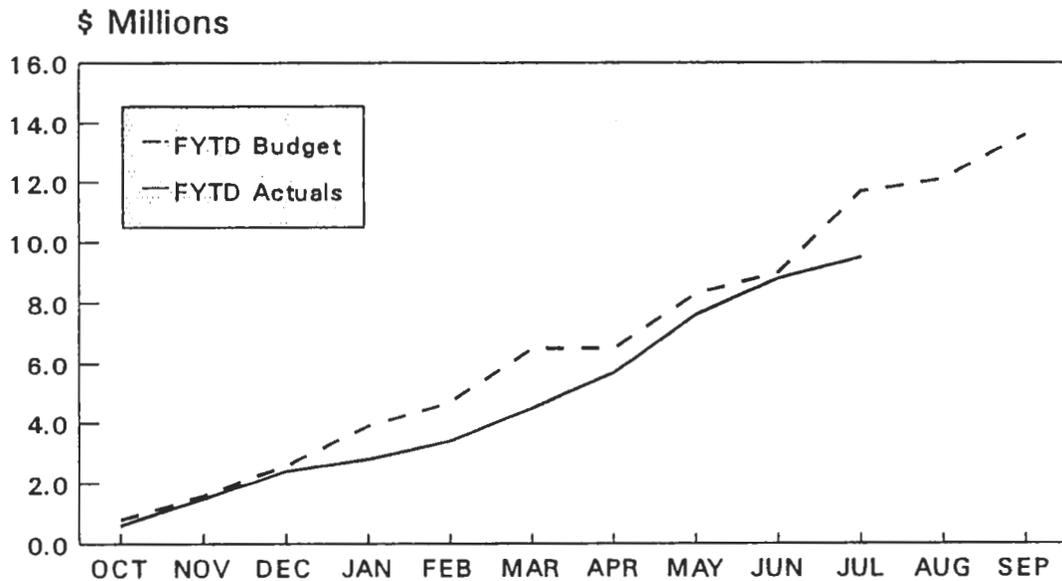


FYTD Budget	0.8	1.6	2.6	3.9	4.7	6.5	6.5	8.3	9.0	11.7	12.1	13.6
FYTD Actuals	0.6	1.5	2.4	2.8	3.4	4.5	5.7	7.6	8.8	9.5		
Spending Var	0.2	0.1	0.2	1.1	1.3	2.0	0.8	0.7	0.2	2.2		

Variance Explanation: Environmental Hot Cell Expansion work, project W-041H, originally scheduled to end in FY 1993, was rescheduled to end in June 1994. Capital budgets associated with this work have not been realigned with the revised construction schedule, resulting in unrealistic FY to date budget figures. This project is proceeding at the revised schedule and within budget. The spending variance for the project will be eliminated as the project nears completion.

9 3 1 3 1 2 6 1 5 1 0

\$ Millions

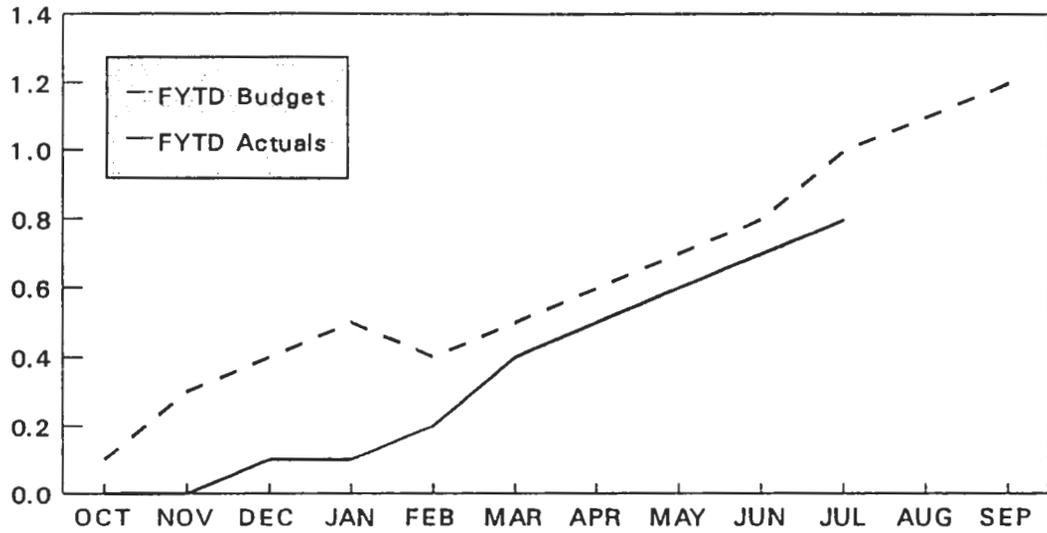

FYTD Budget	0.1	0.3	0.4	0.5	0.4	0.5	0.6	0.7	0.8	1.0	1.1	1.2
FYTD Actuals	0.0	0.0	0.1	0.1	0.2	0.4	0.5	0.6	0.7	0.8		
Spending Var	0.1	0.3	0.3	0.4	0.2	0.1	0.1	0.1	0.1	0.2		

Variance Explanation: The OU 100-HR-2 work plan was prepared in-house by Westinghouse Hanford Company rather than by an offsite subcontractor. Additionally, the work plan references existing approved work plans, which required less document preparation.

93181161512

MAJOR MILESTONE: M-14-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: M. L. Bell

BASELINE DATE: October 1995

PROJECTED DATE: October 1995

DESCRIPTION: Provide low-level mixed waste laboratory services.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-14-02	Complete construction of a 27-module Waste Sampling and Characterization Facility (WSCF).	10/93	10/93
M-14-03	Initiate WSCF operations.	4/94	4/94

ACCOMPLISHMENTS

- Construction (core facility):
 - Assembled all modules that constitute the Analytical Laboratory. Utilities are being connected and readied for testing.
- Construction (auxiliary structures):
 - Installed electrical, heating, ventilating, and air conditioning, plumbing, and computer room access flooring for the Environmental Data Remedial Tracking Facility (Building 6270).
 - Completed mechanical and electrical installations for the Mobile Laboratory Storage Facility (Building 6269).
 - Completed refrigerated storage, high-density shelving, and electrical and mechanical installations for the Environmental Sample Archive Facility (Building 6267)
 - Completed construction of the Utility Building (6265) with the exception of punch list items.
- Startup Activities:
 - Issued the laboratory charter, Maintenance Implementation Plan, Septic System Operating and Maintenance Manual, and Sample Screening Plan; drafted the Readiness Review Board Implementation Plan; and finalized the Final Safety Analysis Report.
 - Continued ramp-up of the operating staff.

9513151033

- Commercial Laboratory:
 - Received DOE approval for award recommendation packages on July 30, 1993. Westinghouse Hanford Company executed Purchase Order awards with IT and Lockheed on July 30, 1993. TMA/Weston were notified of a third award which will be executed after remaining administrative issues are resolved.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Construction:
 - Complete WSCF construction. Complete receipt, assembly, and testing of Analytical Laboratory.
- Startup Activities:
 - Receive and install analytical equipment and conduct operation testing.
 - Obtain and train new staff and start operational readiness review.
- Commercial Laboratory:
 - Initiate and complete assessments of facilities performing work under the new awards. Transition analytical workload from current contracts to the new laboratory contractors.

MILESTONE STATUS/PROBLEMS/ISSUES

- The WSCF module vendor went into default. This caused a delay in delivery of the modules. Immediate actions were taken to minimize the delay of the remaining modules to the construction site. All module shipments have now been received on site, but require rework and testing before any cost or schedule impact can be fully determined. We are now assessing impacts to the total estimated cost or schedule. Such impacts, if any, will be communicated to EPA and Ecology when defined.

9 5 1 9 9 1 9 6

\$ Millions

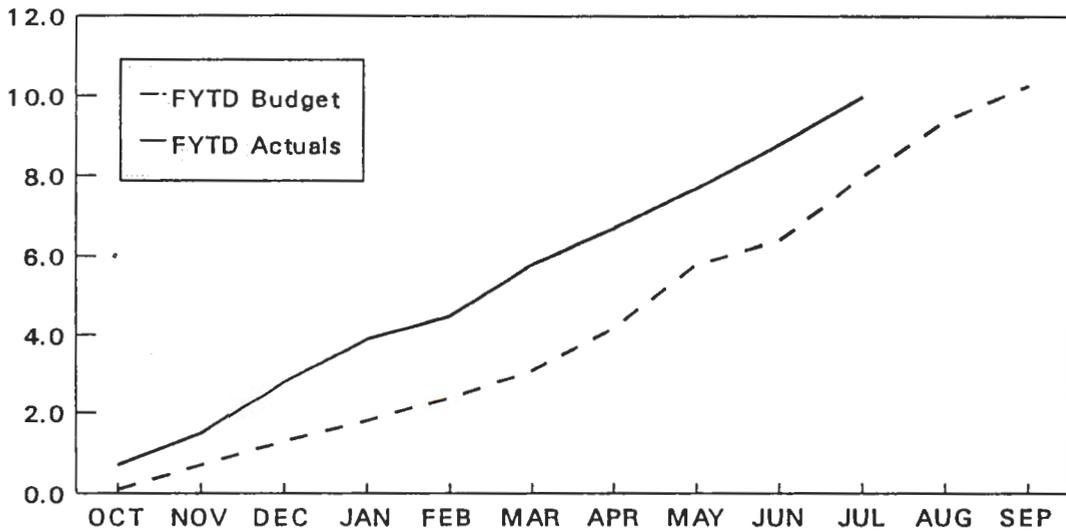

FYTD Budget	0.1	0.7	1.3	1.8	2.4	3.1	4.2	5.8	6.4	8.0	9.4	10.3
FYTD Actuals	0.7	1.5	2.8	3.9	4.5	5.8	6.7	7.7	8.8	10.0		
Spending Var	-0.6	-0.8	-1.5	-2.1	-2.1	-2.7	-2.5	-1.9	-2.4	-2.0		

Variance Explanation: The cost overrun is caused by the exclusion of previous years' capital budgets. Spending rates to support the April 1994 WSCF startup continue as planned. With previous years' capital budget included, trends indicate this project will be completed at the approved project budget level. This may be impacted by the recent contract default of U.S. Modular.

9 5 1 3 1 2 6 1 6 . 5 0

This page intentionally left blank.

9 3 1 3 0 2 6 1 6 5 6

MAJOR MILESTONE: M-15-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. D. Freeberg

MANAGER: T. M. Wintczak

BASELINE DATE: September 2005

PROJECTED DATE: September 2005

DESCRIPTION: Complete the RI/FS or RCRA RFI/CMS process for all OUs.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-15-02E	Submit draft barrier constructability report to EPA and Ecology.	1/31/94	1/31/94
M-15-03B	Submit RI Phase II report for 300-FF-1 to EPA and Ecology.	12/31/93	12/31/93
M-15-05A	Submit OU 100-HR-1 Limited Field Investigation (LFI) Report to Ecology and EPA.	8/9/93	8/9/93
M-15-05B	Complete OU 100-HR-1 Treatability Study Activities.	11/30/93	11/30/93
M-15-06A	Submit OU 100-HR-3 LFI Report to Ecology and EPA.	10/31/93	10/31/93
M-15-06B	Complete OU 100-HR-3 Treatability Study Activities.	11/30/93	11/30/93
M-15-07A	Submit OU 100-DR-1 LFI Report to Ecology and EPA.	08/09/93	08/09/93
M-15-08C	Submit OU 100-BC-1 Treatability Study Report to Ecology and EPA.	1/31/94	1/31/94
M-15-09B	Submit OU 100-BC-5 LFI Report to Ecology and EPA.	8/31/93	8/31/93
M-15-10A	Submit validated data of all sampling activities associated with Sections 5.1.1.2, "Source Investigation," and 5.1.1.5, "Vadose Zone Investigation," for OU 100-KR-1 to Ecology and EPA.	10/31/93	10/31/93
M-15-11B	Submit OU 100-KR-4 LFI Report to Ecology and EPA.	1/12/94	1/12/94

9 3 1 3 0 6 1 6 7

Milestone	Description	Baseline	Projected
M-15-13A	Submit validated data of all sampling activities associated with Sections 5.1.1.2, "Source Investigation," and 5.1.1.5, "Vadose Zone Investigation," for OU 100-FR-1 to Ecology and EPA.	11/31/93	11/31/93
M-15-13F	Submit OU 100-FR-3 LFI Report to Ecology and EPA.	4/14/94	4/14/94

ACCOMPLISHMENTS

- Submitted the draft OU 300-FF-5 F/S Phase I and II report to EPA and Ecology. This completes interim milestone M-15-04A.
- Submitted the OU 100-BC-1 LFI report and qualitative risk assessment to the regulators. This completes interim milestone M-15-08B.
- Completed OU 100-BC-2 intrusive field investigation at crib 116-C-2A.
- Submitted the OU 100-KR-4 second round groundwater data validation report to RL and the regulators.
- Issued the 100-F Reactor site technical baseline report to RL.
- Received regulator approval of the description of work for OU 100-DR-2.
- Incorporated comments on the LFI and qualitative risk assessment reports for OU 100-HR-1.
- Submitted the OU 100-HR-3 fourth round data validation report to RL and the regulators.
- Submitted the OU 100-HR-3 excavation test plan to RL and the regulators.
- Completed surface radiation survey (about 200 acres) at OU 100-NR-1 using the new Rad Rover II.
- Received approval of the NEPA documentation (categorical exclusion) for construction of the prototype barrier at OU 200-BP-1.
- Completed the public review of the treatability test plan for the prototype barrier.
- Prepared and submitted test pit sampling descriptions of work at OU 200-UP-2 for review and comment by the regulators.
- Completed disposition of regulator comments on the OU 200-UP-2 work plan and sent it out for public review.


- Finalized waste control plans for OU 200-UP-2 LFI and Pond 216-U-10 test pits and the crib borings.
- Submitted the OU 200-UP-2 descriptions of work at Pond 216-U-10 for review and approval.
- Submitted the revised OU 300-FF-1 RI Phase I Remedial Investigation to the regulators for review.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Submit the LFI report for OU 100-DR-1 to RL and regulators August 9, 1993.
- Perform the OU 100-BC-5 fifth round of groundwater sampling in September 1993.
- Submit the OU 100-HR-3 LFI report to the regulators on October 31, 1993.
- Complete the OU 100-HR-3 fifth round of groundwater sampling in August 1993.
- Complete OU 200-BP-1 eighth round of groundwater sampling by August 1993.
- Begin construction of the Hanford Prototype Barrier in September 1993.
- Complete regulator comment disposition on the OU 200-UP-2 work plan schedule and approve the work plan to begin field activities.
- Begin preparation of the work plan for OU 200-BP-5.
- Begin preparation of the work plan for OU 200-BP-11.

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

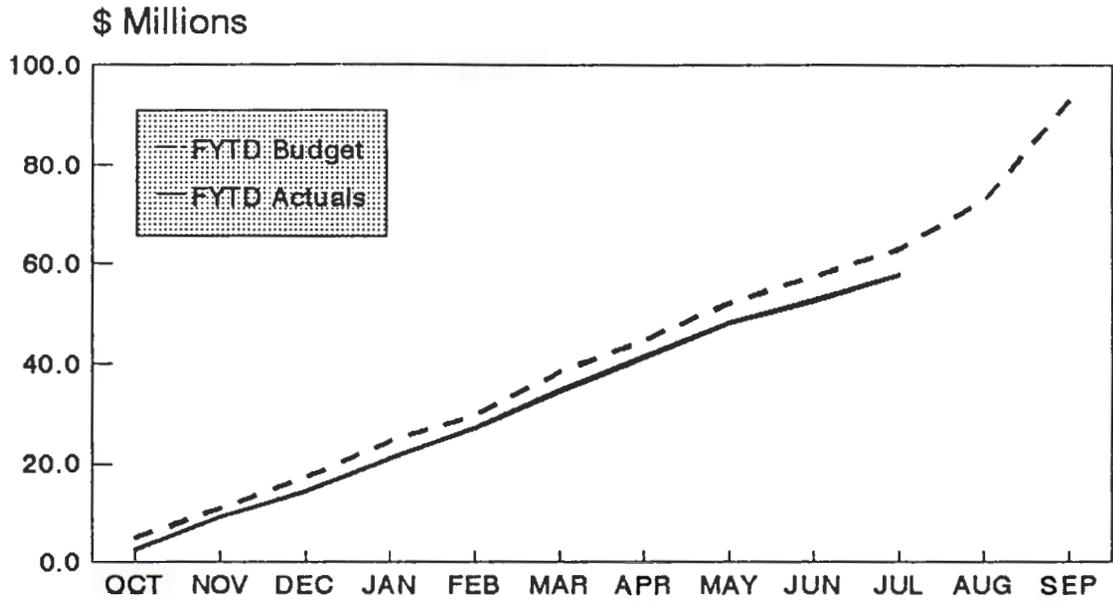

FYTD Budget	4.6	11.0	17.2	24.7	29.9	38.5	44.8	52.2	57.6	63.0	73.0	93.0
FYTD Actuals	2.3	9.1	14.3	21.2	27.2	34.7	41.5	48.1	52.8	57.8		
Spending Var	2.3	1.9	2.9	3.5	2.7	3.8	3.3	4.1	4.8	5.2		

Variance Explanation: None required.

0001905116

MAJOR MILESTONE: M-16-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. D. Freeberg

MANAGER: T. M. Wintczak

BASELINE DATE: September 2018

PROJECTED DATE: September 2018

DESCRIPTION: Complete the remedial actions for all OUs.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Perforated four existing wells, completed one new well, and started two new wells to be included in the carbon tetrachloride extraction well network. This amounts to a total of 34 wells drilled or modified to date for vapor extraction purposes.


PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Complete remediation of the Riverland Rail site by September 1993.
- Complete disposal of the four remaining drums from Sodium Dichromate that are considered Hazardous Waste.
- Reseed and revegetate at the Sodium Dichromate ERA site in the fall.
- Complete N Springs Expedited Response Action proposal (August 1993).
- Complete Burial Ground 618-11 Expedited Response Action proposal (August 1993).

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

1993071651

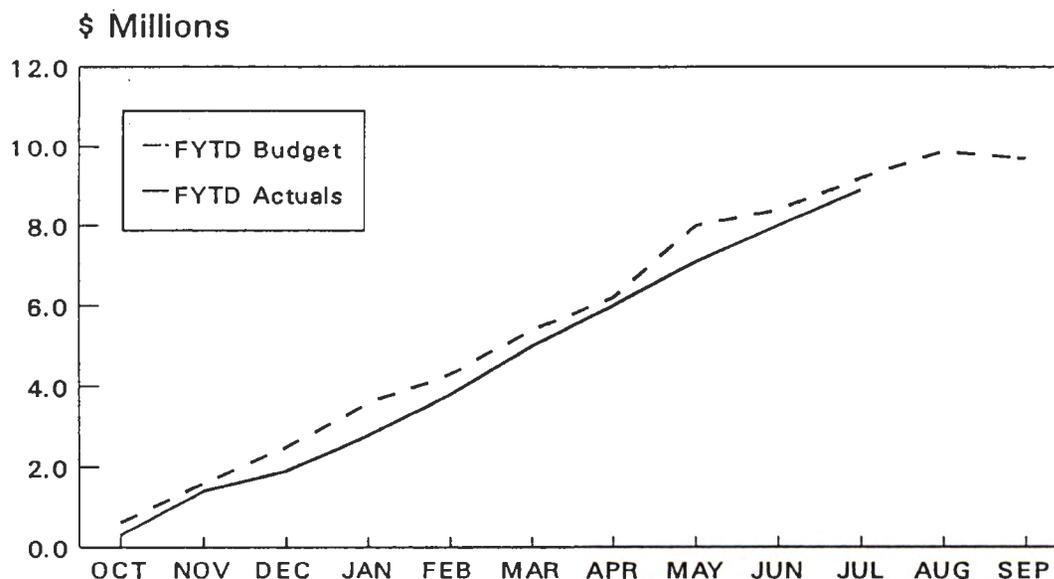

FYTD Budget	0.6	1.6	2.5	3.6	4.3	5.4	6.2	8.0	8.4	9.2	9.9	9.7
FYTD Actuals	0.3	1.4	1.9	2.8	3.8	5.0	6.0	7.1	8.0	8.9		
Spending Var	0.3	0.2	0.6	0.8	0.5	0.4	0.2	0.9	0.4	0.3		

Variance Explanation: None required.

Change from June budget: Submitted a class I change request to reduce the N Springs ERA funding. The N Springs scope was delayed due to comment reviews with RL and the regulators about the EE/CA and remediation approach to be taken. The funding was reprogrammed to other ER Program work scope.

MAJOR MILESTONE: M-17-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: D. E. Kelley

M-17-00A:

BASELINE DATE: June 1995

PROJECTED DATE: June 1995

DESCRIPTION: Complete liquid effluent treatment facilities and upgrades for Phase I effluents.

M-17-00B:

BASELINE DATE: October 1997

PROJECTED DATE: October 1997

DESCRIPTION: Implement best available technology/all known, available, and reasonable methods of prevention, control, and treatment for all Phase II liquid effluents at the Hanford Site.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-17-06F*	Cease discharge of the 300 Area Process Sewer to the western-most section of the 300 Area Process Trenches (i.e., west process trench).	12/92	12/92
M-17-06G*	Limit discharges to the 300 Area Process Trench to less than or equal to 325 gallons per minute, averaged over the calendar month.	5/93	5/93
M-17-06H	Complete installation of the 384 Power House Building cooling tower equipment.	9/93	9/93
M-17-06I	Complete closed loop cooling for selected equipment in Building 325 (as provided by Project D-402), Building 306-W (as provided by Small Project ER 4039), and Building 326 (as provided by Project D-403).	12/93	12/93

9 5 1 5 0 5 1 6 0 3

Milestone	Description	Baseline	Projected
M-17-16D	Implement closed loop cooling for Buildings 291-Z, 234-5Z, and 236-Z, as provided by "291-Z Closed Loop Cooling" (Project C-040) and "Plutonium Finishing Plant Liquid Low-Level Waste System Modification" (Project B-680H). Reduce the discharge to Crib 216-Z-20 to less than or equal to 75 gallons per minute, averaged over the calendar month.	1/94	1/94

*Interim milestones M-17-06F and M-17-06G were added this month to the milestone listing via Tri-Party Agreement change request M-17-93-03. Actions specified were completed before approval of the change request.

ACCOMPLISHMENTS

- Obtained approval of change request M-17-93-03, which added six additional interim milestones that address the interim operating restrictions for the 300 Area Process Sewer discharge to the 300 Area Process Trenches.
- Obtained approval of change request M-17-93-05, which allowed for changes to the analytical methods in the Sampling and Analyses Plans to those that are now on contract with Hanford Analytical Services Management. After approval of this change request, the approved methods were entered into the Liquid Effluent Monitoring Information System.
- Submitted the groundwater assessment plan to EPA and Ecology for the 100-D Ponds in July 1993 (milestone M-17-13).
- Transmitted a submittal to EPA, Headquarters, and held a followup meeting in support of the delisting petition that will be completed in August 1993. This document detailed the extensive testing completed on surrogate feed developed to establish an operating envelope for the 200 Area Effluent Treatment Facility.
- Submitted the 80-percent design report to EPA and Ecology for the 200 Area Effluent Treatment Facility (Project C-018H) disposal site and treatment facility.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Submit groundwater assessment plans to EPA and Ecology for Liquid Wastewater Disposal Facility 1325-N, Crib 216-W-LWC, Powerhouse Pond 284-W, and Pond 2101-M by September 1993 (milestone M-17-13).
- Submit the State Waste Discharge permit application to Ecology for the 200 Area Effluent Treatment Facility (Project C-018H) disposal site.

9 1 1 3 1 6 1 5 5 4


- Submit the addendum to the WAC 173-240, *Engineering Report to Ecology for the 200 Area Effluent Treatment Facility* (Project C-018H). The addendum will address pilot plant test results.
- Submit the addendum to the WAC 173-240, *Engineering Report to Ecology for the 200 Area Treated Effluent Disposal Site* (Project C-018H) disposal site characterization work plan. This report will transmit the results of the site characterization activities for the 200 Area Treated Effluent Disposal Site (Project C-018H).
- Obtain Key Decision 1, approval to proceed with advanced conceptual design, from HQ for Project W-252 ("200 Area Phase II Stream Treated Effluent Disposal Facility").
- Obtain approval from HQ for rebaselining of the Hanford Environmental Compliance Line Item to include additional scope to implement Best Available Treatment Technology for UO₃ Plant wastewater and process condensate, T Plant wastewater and laboratory wastewater, 284 West Powerhouse wastewater, and the 2101-M Laboratory wastewater.

MILESTONE STATUS/PROBLEMS/ISSUES

- The milestone is on schedule.
- We have maintained compliance with all effluent flow restrictions contained in Tri-Party Agreement milestone M-17.
- HQ has delayed approval for rebaselining of the Hanford Environmental Compliance Line Item to include additional scope to implement Best Available Treatment Technology for UO₃ Plant wastewater and process condensate, T Plant wastewater and laboratory wastewater, 284 West Powerhouse wastewater, and the 2101-M Laboratory wastewater.

9 0 1 3 1 2 6 1 6 5

\$ Millions

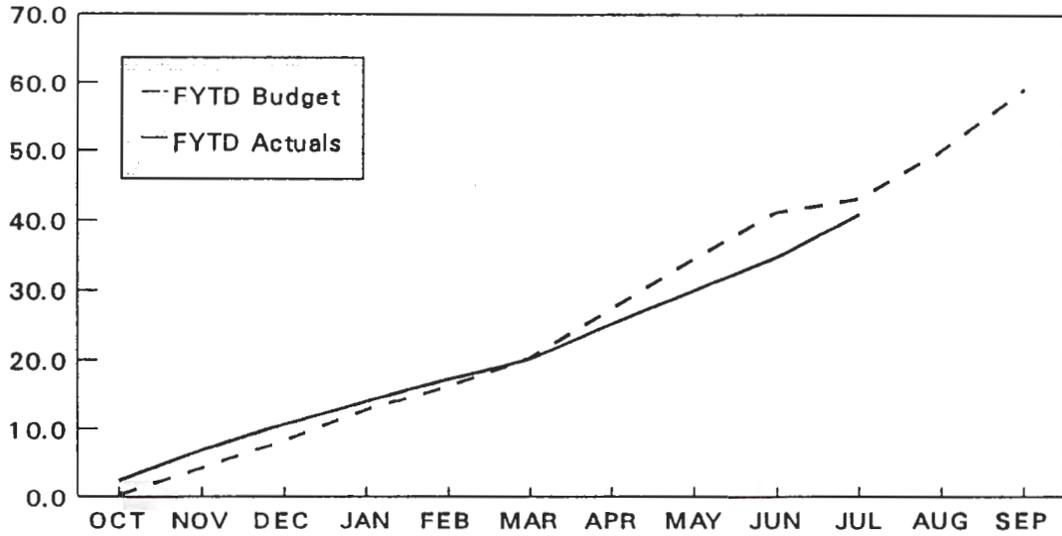

FYTD Budget	0.3	4.3	8.3	12.9	16.2	20.4	27.5	34.7	41.3	43.3	50.1	59.2
FYTD Actuals	2.4	6.9	10.7	14.1	17.3	20.2	25.3	30.1	34.9	41.0		
Spending Var	-2.1	-2.6	-2.4	-1.2	-1.1	0.2	2.2	4.6	6.4	2.3		

Variance Explanation: None required.

Change from June budget: The reduction in budget-at-completion resulted from the decision to have more construction work performed by fixed price contract instead of onsite forces. This decision is based on a soils investigation indicating the potential for contamination along the proposed pipeline route to be less severe than originally envisioned. Additional cost savings result from savings achieved in project design and the 200 Areas Treated Effluent Disposal Facility being declared a "general use facility," which made preparation of planned safety documentation unnecessary.

MAJOR MILESTONE: M-18-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: R. J. Roberts

BASELINE DATE: March 1997

PROJECTED DATE: March 1997

DESCRIPTION: Complete Waste Receiving and Processing (WRAP) Facility, Module 1, construction and initiate operations.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued discussions about the RCRA permit application at the monthly Tri-Party Agreement Unit Managers' meeting.
- Completed procurement of the WRAP Facility, Module 1, "one trip" system for waste load out. Began testing of the system.
- Completed testing of the British Nuclear Fuels, Ltd, glovebox sphincter seal for potential use in WRAP Facility, Module 1.
- Obtained approval from the EPA for one of three air permits needed to support the start of WRAP Facility, Module 1, construction.


PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Begin construction of the WRAP Facility, Module 1.
- Complete glovebox testing.
- Complete the preliminary safety analysis report for the WRAP Facility, Module 1.
- Prepare construction bid packages for WRAP Facility, Module 1. These bid packages will cover major components of the WRAP Facility (e.g., electrical system, heating and ventilating system, fire protection system). Private firms will bid on these packages.

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

9 3 1 3 1 5 5 7

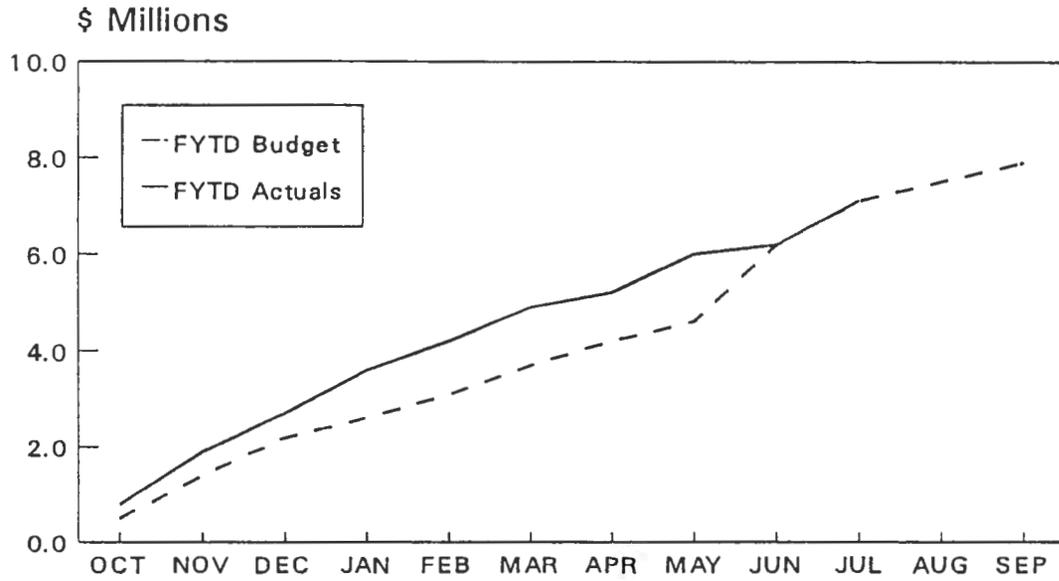

FYTD Budget	0.5	1.4	2.2	2.6	3.1	3.7	4.2	4.6	6.2	7.1	7.5	7.9
FYTD Actuals	0.8	1.9	2.7	3.6	4.2	4.9	5.2	6.0	6.2	7.1		
Spending Var	-0.3	-0.5	-0.5	-1.0	-1.1	-1.2	-1.0	-1.4	0.0	0.0		

Variance Explanation: None required.

9 2 1 3 1 6 1 5 0 3

MAJOR MILESTONE: M-19-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: R. J. Roberts

BASELINE DATE: September 1999

PROJECTED DATE: September 1999

DESCRIPTION: Complete WRAP Facility, Module 2, construction and initiate operations.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
None.			

ACCOMPLISHMENTS

- Continued the waste formulation for the waste immobilization demonstration testing.
- Issued interim report for initial in drum mixing tests for the WRAP Facility, Module 2B.
- Continued update of the process flow diagrams for grout and polymer immobilization to support the start of Title I design.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Continue preparation of the advanced conceptual design for the WRAP Facility, Module 2A.
- Obtain approval of change request M-19-91-01 from Ecology and EPA.
- Continue with waste form verification and in-drum mixing testing.
- Begin activities for the development of the WRAP Facility, Module 2A, preliminary safety analysis report.
- Obtain Key Decision 1 for the WRAP Facility, Module 2A, from HQ. This decision is required to proceed into definitive design of the project.

MILESTONE STATUS/PROBLEMS/ISSUES


- Technical issues associated with the Waste Isolation Pilot Plant waste acceptance criteria continue to impact the design of the WRAP Facility, Module 2. A strategy for the WRAP Facility, Module 2B, is being evaluated in light of the Waste Isolation Pilot Plant waste acceptance criteria issues. Work on the portion of the WRAP Facility, Module 2

6
9
1
9
3
0
1
3
9

(i.e., the WRAP Facility, Module 2B), that will receive and process remote-handled transuranic waste contaminated hazardous waste (i.e., mixed remote-handled transuranic waste) is behind schedule. The portion of the WRAP Facility, Module 2, that is not affected by the Waste Isolation Pilot Plant waste acceptance criteria (i.e., the WRAP Facility, Module 2A) remains on schedule. The submodularization of the WRAP Facility, Module 2, is reflected in change request M-19-91-01. Ecology and EPA continue to review this change request.

- WRAP Facility, Module 2A, is on schedule for September 1999, the Tri-Party Agreement milestone M-19-00 due date.

\$ Millions

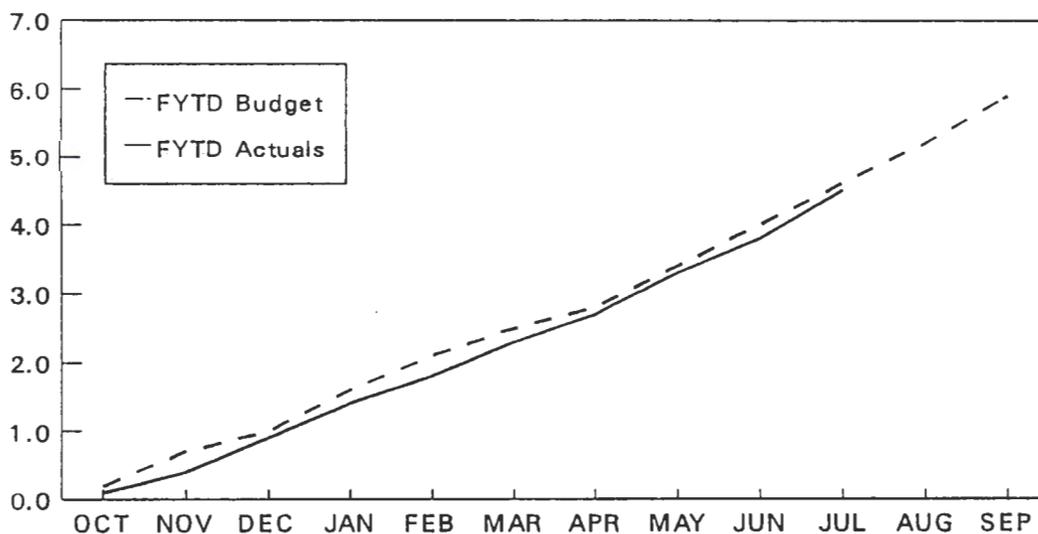

FYTD Budget	0.2	0.7	1.0	1.6	2.1	2.5	2.8	3.4	4.0	4.6	5.2	5.9
FYTD Actuals	0.1	0.4	0.9	1.4	1.8	2.3	2.7	3.3	3.8	4.5		
Spending Var	0.1	0.3	0.1	0.2	0.3	0.2	0.1	0.1	0.2	0.1		

Variance Explanation: None required.

9 0 1 3 1 5 1 6 7 0

MAJOR MILESTONE: M-20-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. D. Bauer

MANAGER: S. M. Price

BASELINE DATE: May 1996

PROJECTED DATE: May 1996

DESCRIPTION: Submit Part B permit applications or closure plans for all RCRA treatment, storage, and disposal units.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-20-30	Submit 303-M Oxide Facility Part B.	10/92	Dispute ^a
M-20-42	Submit Thermal Treatment Part B to Ecology and EPA (T-X-3).	12/93	12/94 ^a
M-20-50	Submit 200 Area Effluent Treatment Facility ^b Part B.	8/93	8/93
M-20-31	Submit 1301-N/1325-N Closure Plan/Post-Closure Plan (D-1-2)	5/94	5/94

^aSee "Milestone Status/Problems/Issues."

^bThe unit name has been changed from the 242-A Evaporator/Plutonium-Uranium Extraction (PUREX) Plant Process Condensate Treatment Facility to the 200 Area Effluent Treatment Facility.

ACCOMPLISHMENTS

- Submitted revised Hanford Facility Dangerous Waste Part A Permit Application Form 3s for the 325/3100 Hazardous Waste Treatment Unit and the T Plant Complex to Ecology (see "Milestone Status/Problems/Issues").
- Submitted Notice of Deficiency Response Tables for the Grout Treatment Facility, DST System, Central Waste Complex (formerly known as the Hanford Central Waste Complex-Radioactive Dangerous Waste Storage Facility), and 222-S Laboratory Complex portions of the Hanford Facility Dangerous Waste Permit Application.
- Submitted a Notice of Deficiency Response Tables for the Hexone Storage and Treatment Facility.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS

- Submit a Notice of Intent to expand treatment and storage capacities of the DST system.

9313161671

- Respond to Notices of Deficiency for the following Hanford Facility Dangerous Waste Permit Application portions: 305-B Storage Unit, Revision 1 (M-20-08, submitted November 1990) and the 616 Nonradioactive Dangerous Waste Storage Facility, Revision 2 (M-20-02, submitted October 1991).
- Respond to the Notice of Deficiency for the 100-D Ponds Closure Plan (M-20-40, submitted February 26, 1993).
- Revise 304 Concretion Facility Closure Plan, 303-K Radioactive Mixed Waste Storage Facility Closure Plan, and 216-B-3 Pond System Closure/Postclosure Plan to reflect agreements reached with Ecology on Notice of Deficiency comments.
- Submit revised Hanford Facility Dangerous Waste Part A Permit Application Form 3s for the 207-A South Retention Basin, 200 Area Effluent Treatment Facility, PUREX Plant, and Pond 216-B-3.
- Submit the 200 Area Effluent Treatment Facility Part B permit application to Ecology and the EPA in compliance with milestone M-20-50.
- Submit a change request to Tri-Party Agreement milestone M-20-24 to require submittal of a closure plan for the PUREX Plant in November 1994.

MILESTONE STATUS/PROBLEMS/ISSUES

- M-20-30, "Submit 303-M Oxide Facility Part B to Ecology and EPA"--RL submitted to Ecology a request to withdraw the Part A permit application for the 303-M Oxide Facility and a change request to delete the milestone. Ecology denied both. RL then prepared a notice of dispute and met with Ecology to begin resolution. During the February Project Managers' meeting, Ecology requested that RL consider integrating the RCRA closure and *Comprehensive Environmental Response Compensation and Liability Act* (CERCLA) past practice remediation, keeping the Part A permit application in place, and requesting relief from some of the administrative interim status requirements. Later, the Ecology Project Manager directed RL to discuss this issue with the Ecology Kennewick Office. During a March 16, 1993, meeting, Ecology stated its position is to conduct limited sampling, submit a RCRA closure plan, decontaminate and decommission the building, and leave the concrete slab for protection of Burial Ground 618-1. A letter is being prepared to transmit a Tri-Party Agreement issue resolution worksheet reflecting RL's position to delay any action for this treatment, storage, and disposal unit until the OU remediation is completed.
- M-20-50, "Submit 200 Area Effluent Treatment Facility Part B"--Work is proceeding on schedule to meet the milestone. The Part B permit application was transmitted to RL for certification on July 30, 1993.
- M-20-42, "Submit Thermal Treatment (T-X-3) Part B to Ecology and EPA"--Development of the Part B application for this unit has identified several issues to be resolved before a technically accurate and complete


9 0 1 3 1 0 1 6 7 2

application can be prepared. RL submitted a change package (M-20-92-7), delaying the December 31, 1993, submittal of this Part B permit application for 1 year, on June 9, 1993. EPA and Ecology have given verbal approval of the change package and signature approval is expected at the August Project Managers' meeting. (Note: This change package was approved at the August 3rd Project Managers' meeting.)

- M-20-09, "Submit 216-B-3 Pond Closure/Postclosure Plan to Ecology and EPA"--A strategy and schedule is being prepared to combine remediation activities of the past practice Operable Unit 200-BP-11, with the closure activities of the 216-B-3 Pond System. This strategy supports the activities needed to administratively clean close the 216-B-3A, 216-B-3B, and 216-B-3C lobes by June 1995. Closure of the 216-B-3 Pond and 216-B-3-3 Ditch will be integrated with the RCRA Past Practice activities for the OU. The three parties must decide on this strategy to allow for continued use of the 216-B-3B and -3C lobes to support liquid effluent disposal (216 Consent Order). This integration information was discussed with the Ecology Kennewick Office. Discussions with Ecology are continuing. A change request for the OU, incorporating the proposed strategy, was prepared.
- M-20-02, "Submit 616 Storage Facility Part B to Ecology and EPA--RL received a formal Notice of Deficiency for this unit's permit application on June 16, 1993. This Notice of Deficiency specifically addressed the 616 Storage Facility waste analysis plan. The date for submittal of waste analysis plan information, to satisfy this notice of deficiency, has been extended from July 30 to August 31, 1993. We are now working to resolve this Notice of Deficiency.
- M-20-08, "Submit 305-B Storage Unit Part B to Ecology and EPA--RL received a formal request for this unit's permit application on June 16, 1993. This Notice of Deficiency specifically addressed the 305-B waste analysis plan. The date for submittal of waste analysis plan information, to satisfy this Notice of Deficiency, has been extended from July 30 to August 31, 1993. We are now working to resolve this Notice of Deficiency.
- Hanford Facility Dangerous Waste Permit (Hanford Facility Permit)--On July 28, 1993, RL received from EPA the HSWA Portion of the draft Hanford Facility Permit. On July 29, 1993, RL received a letter from Ecology with portions of the draft Hanford Facility Permit related to some of the 15 identified issues. The remainder of the text is expected by August 18, 1993. Ecology will accept comments on the first portions until August 11, and on the remainder until August 31, 1993. A teleconference is scheduled on the HSWA portion on August 13, 1993. The Ecology letter included a schedule for the reissuance of the draft Hanford Facility Permit, with the 60-day public comment period commencing on September 15, 1992.
- T Plant Complex--On July 26, 1993, Ecology formally denied Revision 1 of the T Plant Complex Part A permit application, Form 3. As the basis for denial, Ecology's cited the failure of five tank systems included in the revision "to meet interim status standards due to the lack of adequate secondary containment and leak detection capabilities." Ecology also

expressed concern about adequate secondary containment for storage of containerized waste outside Buildings 221-T and 2706-T. Ecology's approval of Revision 1 is contingent upon a setting a compliance schedule to address secondary containment requirements.

\$ Millions

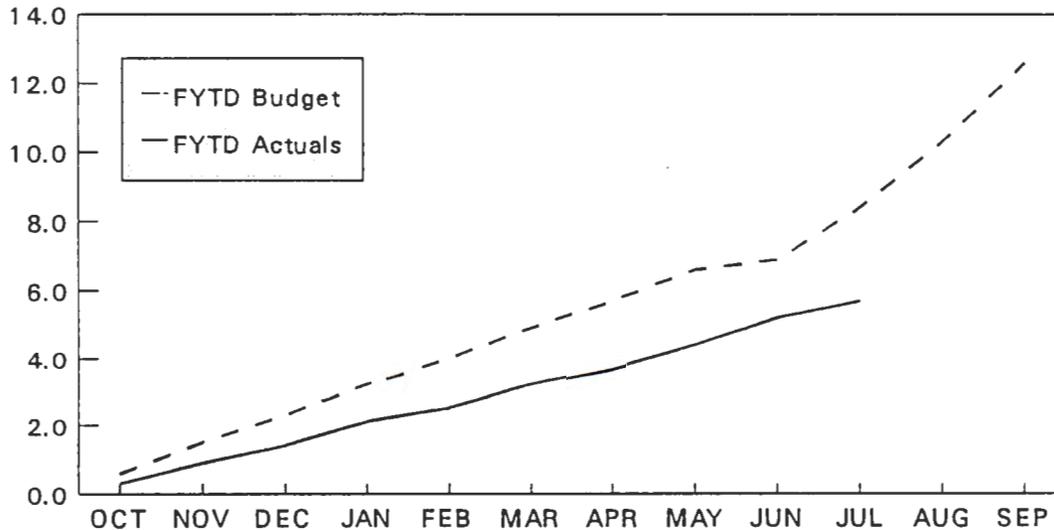

FYTD Budget	0.6	1.5	2.3	3.2	4.0	4.9	5.7	6.6	6.9	8.4	10.3	12.6
FYTD Actuals	0.3	0.9	1.4	2.1	2.5	3.2	3.7	4.4	5.2	5.7		
Spending Var	0.3	0.6	0.9	1.1	1.5	1.7	2.0	2.2	1.7	2.7		

Variance Explanation: The cost underrun is caused by continued delays in Ecology's review of Closure Plans, Part B Permit applications, and notice of deficiency responses. Less money has been spent than was planned to support revisions of these documents.

9 3 1 3 1 5 1 6 7 4

MAJOR MILESTONE: M-24-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: R. R. Thompson

BASELINE DATE: December 1993

PROJECTED DATE: December 1993

DESCRIPTION: Install RCRA groundwater monitoring wells at the rate of 29 in CY 1989, 30 in CY 1990, and up to 50 per year thereafter as specified by agreed interim milestones until all land disposal units and SSTs are determined to have RCRA-compliant monitoring systems

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-24-00E	Install a maximum of 50 wells for CY 1993.	12/93	12/93
M-24-30 **	Install one additional RCRA well around Crib 1325-N (3 total).	12/93	4/93
M-24-31	Install two additional RCRA wells around the low-level burial grounds (81 total).	12/93	12/93
M-24-32	Install three additional RCRA wells around the Grout Treatment Facility (13 total).	12/93	12/93

ACCOMPLISHMENTS

- Fixed price contractor began drilling during July and was making progress toward total depth on the first hole by the end of the month.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Complete drilling activities for CY 1993 wells.

MILESTONE STATUS/PROBLEMS/ISSUES

- After identifying seven locations for new wells in CY 1993, Ecology and RL agreed that monitoring to be accomplished by one of the wells originally proposed at Crib 1325-N can be accomplished by an existing well. Change request M-24-93-1, which reduces this milestone by one well, received final approval on August 3. Thus, one of the interim milestones M-24-30 was completed on April 22, 1993.

9 3 1 3 1 3 6 1 6 7 5

\$ Millions

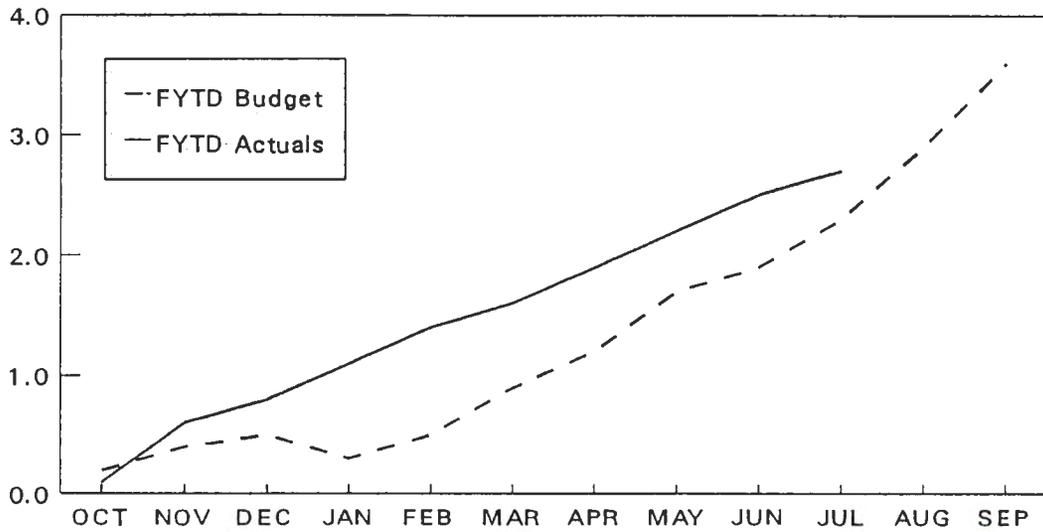

FYTD Budget	0.2	0.4	0.5	0.3	0.5	0.9	1.2	1.7	1.9	2.3	2.9	3.6
FYTD Actuals	0.1	0.6	0.8	1.1	1.4	1.6	1.9	2.2	2.5	2.7		
Spending Var	0.1	-0.2	-0.3	-0.8	-0.9	-0.7	-0.7	-0.5	-0.6	-0.4		

Variance Explanation: The spending variance through June is an artificial variance resulting primarily from a reduction in the Line Item cost account plan 3A6A01 for Project W-017H, "Well Installation." RL deobligated \$750,000 of the project's funds with Project Authorization Mod 9 issued on December 22, 1992. This reduction was included in the cost account plan in January 1993 and, therefore, appears as a reduction in FY 1993. Adjusting for the deobligation, the variance is within reporting tolerance and no explanation is required.

9 1 5 1 5 7 6

MAJOR MILESTONE: M-26-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: J. M. Hennig

MANAGER: C. J. Geier

BASELINE DATE: April 1993

PROJECTED DATE: April 1993

DESCRIPTION: Submit annual Hanford land disposal restrictions (LDR) report in accordance with the LDR Plan to cover the period from April 1 through March 31.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-26-01D	Submit an annual Hanford LDR Report in accordance with the LDR Plan to cover the period from April 1 of the previous year through March 31 of the reporting year.	4/30/94	4/30/94

ACCOMPLISHMENTS

- Received regulator comments on the 1993 LDR Report.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Resolve any regulator comments on the 1993 LDR Report and receive regulator approval of the document.

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

9 3 1 3 0 6 1 6 7 7

\$ Thousands

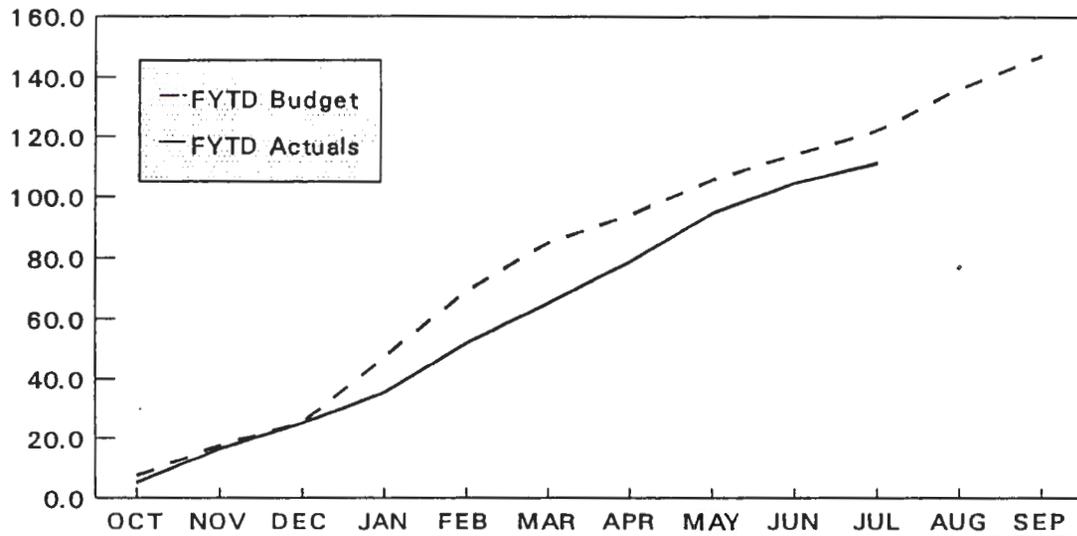

FYTD Budget	7.5	17.7	25.5	47.4	69.4	85.3	94.3	105.8	114.4	122.4	136.6	147.1
FYTD Actuals	5.3	16.4	25.1	35.6	52.0	65.4	79.1	94.8	104.8	111.6		
Spending Var	2.2	1.3	0.4	11.8	17.4	19.9	15.2	11.0	9.6	10.8		

Variance Explanation: None required. This chart is prepared in thousands to provide meaningful data. The Budget Baseline Summary table shows zero because it is in millions.

9 3 1 3 0 1 6 1 6 7 8

MAJOR MILESTONE: M-30-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. D. Freeberg

MANAGER: T. M. Wintczak

BASELINE DATE: September 1993

PROJECTED DATE: September 1993

DESCRIPTION: Complete integrated general investigations and studies for the 100 Area.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-30-05	Complete installation of all-field instrumentation and initiate monitoring activities necessary to perform long-term aquifer river investigations.	9/93	9/93

ACCOMPLISHMENTS

- Continued conductivity data collection project at 100-H Area. The project measures conductivity in the river, river bank seepage, and a nearby groundwater well.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Install automated river level recorder station at 100-N Area and automated water level recorders in 100-N Area wells. Obtain profiles of conductivity in shoreline wells and borehole velocity measurements from 100-H Area wells.
- Receive regulators' concurrence on M-30-05 obligations based on discussions at the July unit managers' meeting (100 Area National Priorities Listing Agreement 52).

MILESTONE STATUS/PROBLEMS/ISSUES

- This milestone is on schedule.

9 3 1 3 1 6 7 9

\$ Millions

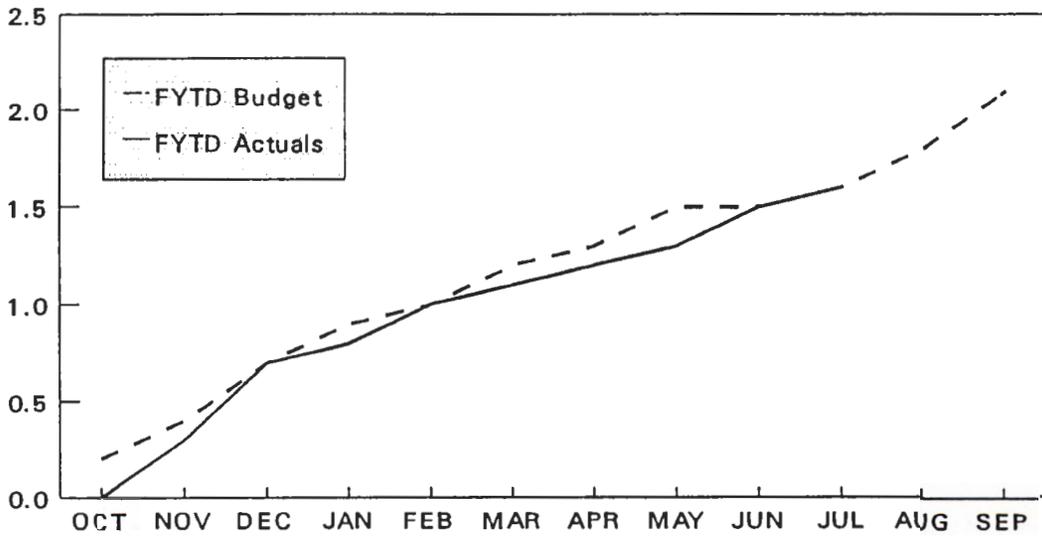

FYTD Budget	0.2	0.4	0.7	0.9	1.0	1.2	1.3	1.5	1.5	1.6	1.8	2.1
FYTD Actuals	0.0	0.3	0.7	0.8	1.0	1.1	1.2	1.3	1.5	1.6		
Spending Var	0.2	0.1	0.0	0.1	0.0	0.1	0.1	0.2	0.0	0.0		

Variance Explanation: None required.

Change from June budget: Reprogrammed underruns in this milestone's scope (river monitoring and sampling program) were redistributed to other Environmental Restoration scope through a class I programmatic change request.

9 5 1 8 1 3 6 1 6 0 0

MAJOR MILESTONE: M-31-00
STATUS FOR END OF MONTH: JULY 1993

DOE DIRECTOR: R. W. Brown

MANAGER: R. L. Fritz

BASELINE DATE: TBD

PROJECTED DATE: TBD

DESCRIPTION: Provide additional DST capacity. Construction complete.

PAST DUE OR SUPPORTING INTERIM MILESTONE(S) FOR THE NEXT 12 MONTHS

Milestone	Description	Baseline	Projected
M-31-02	Recommend additional tank milestones.	09/30/92	08/31/93

ACCOMPLISHMENTS

- Released the advanced conceptual design.
- Completed the underground tank standard design criterion 4.3 and sent it out for final review and approval.
- Completed the hazards and operational study.

PLANNED ACTION(S) FOR THE NEXT 6 MONTHS


- Complete the Project Management Plan.
- Obtain approval on Level 0 change request for project rescoping.
- Complete the draft preliminary safety analysis report.
- Continue preliminary design of the New Multi-Function Waste Tank Facility.

MILESTONE STATUS/PROBLEMS/ISSUES

- The multi-function waste tank facility project is working to current baselines and limited scope until HQ approves the Level 0 change request.
- Milestone M-31-02 is included in the negotiations now under way. This milestone will be deleted and a new milestone will be generated for future tanks.

9 5 1 3 7 2 6 1 6 3 1

\$ Millions

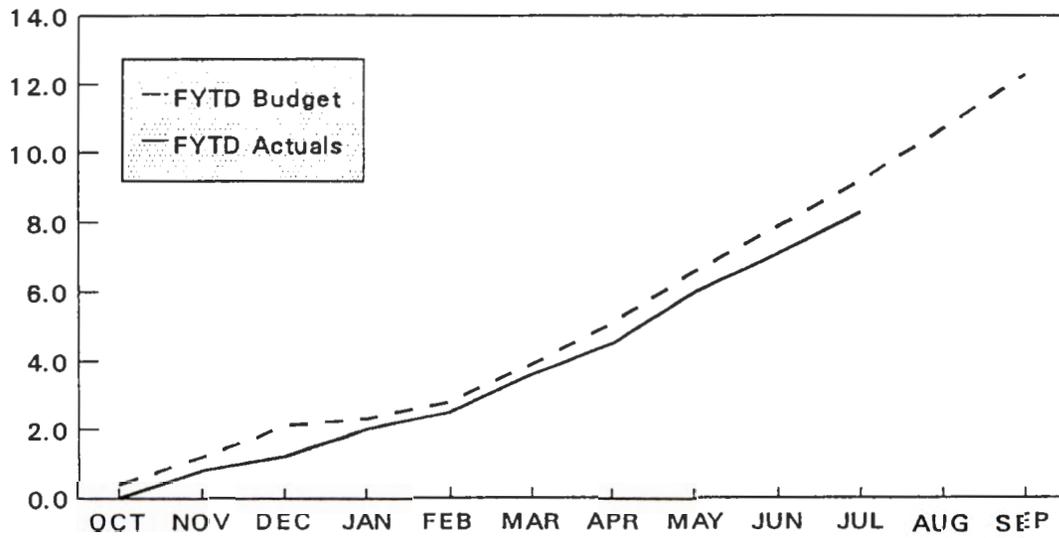

FYTD Budget	0.4	1.2	2.1	2.3	2.8	3.9	5.1	6.6	7.9	9.2	10.7	12.3
FYTD Actuals	0.0	0.8	1.2	2.0	2.5	3.6	4.5	6.0	7.1	8.3		
Spending Var	0.4	0.4	0.9	0.3	0.3	0.3	0.6	0.6	0.8	0.9		

Variance Explanation: The variance is primarily the result of Title I work, and result from two drivers: (1) Kaiser Engineers Hanford did not ramp up as fast as was expected and (2) subsurface investigation is running behind schedule as a result of a change in the method of performance from the original plan.

93131692

DISTRIBUTION

Number of copies

Number of copies

OFFSITE

OFFSITE

4 U.S. Department of Energy -
Headquarters
19901 Germantown Road
Germantown, MD 20874

S. P. Cowan EM-30
C. G. Halsted RP-13
J. C. Lehr EM-442
R. Martinez EM-322

19 Washington State Department
of Ecology
Olympia, WA 98504

J. Breckel
J. Denkers
D. Jansen (12)
D. Josue (2)
M. Riveland
D. Silver
R. Stanley
Mail Stop PV-11

40 Nuclear Waste Advisory
Council
Department of Ecology
Olympia, WA 98504

Donna Baldonado
K. Lyal
Mail Stop PV-11

3 U.S. Department of Energy -
Headquarters
1000 Independence Avenue SW
Washington, DC 20585

J. E. Lytle EM-30
K. I. Taimi EH-22
J. C. Tseng EH-20

1 PRC Environmental Management

D. Lacombe
1411 4th Avenue, Suite 720
Seattle, WA 98101

2 U.S. Environmental Protection
Agency
1200 Sixth Avenue
Seattle, WA 98101

G. Hofer
R. F. Smith
Hazardous Waste Division
(M/C HW-111)

6 Confederated Tribes of the
Umatilla Indian Reservation

Elwood Patawa, Chairman
P.O. Box 638
Pendleton, OR 97801

1 Nez Perce Tribal Executive
Council

S. N. Penney, Chairman
P.O. Box 305
Lapwai, ID 83540

1 Oregon Department of Energy

D. Stewart-Smith
625 Marion Street NE
Salem, OR 97310

1 Yakima Tribal Council

Wilfred Yallup, Chairman,
Yakima Indian Nation
P.O. Box 151 (Fort Road)
Toppenish, WA 98948

1 Sierra Club Northwest Office
1516 Melrose Avenue
Seattle, WA 98122

1 Dr. Ruth F. Wiener
Environmental Eval. Group
7007 Wyoming N.E., F-2
Albuquerque, NM 87109

9 3 1 3 0 1 6 0 3

DISTRIBUTION (cont)

Number of copies

Number of copies

OFFSITE

OFFSITE

- 1 Charlotte Denniston
Greenpeace
11815 - 20th SW
Seattle, WA 98146
- 1 John Lindsay, President
Tri-City Industrial
Development Council
901 N. Colorado
Kennewick, WA 99336
- 1 Diana Bradshaw
Audobon Society of Portland
5151 Northwest Cornell Road
Portland, OR 97210
- 1 Don Reicher
Natural Resources Defense
Council
1350 New York Avenue NW
Suite 300
Washington, DC 20005
- 1 Bill Mitchell
Nuclear Safety Campaign
1914 North 34th Street, 407
Seattle, WA 98103
- 1 Jim Thomas
Hanford Education Action
League
1720 N. Ash
Spokane, WA 99205
- 1 Richard Belsey, M.D.
Oregon Health Sciences
Department of Clinical
Pathology L471
030 S.W. Ridge Drive
Portland, OR 97219-6566
- 1 W. Staubitz
U.S. Geological Survey
1201 Pacific Avenue
Suite 6000
Tacoma, WA 98402

- 1 Physicians for Social
Responsibility
4534 1/2 University Way NE
Seattle, WA 98105
- 3 SAIC
1845 Terminal Drive
Suite 202
Richland, WA 99352

Karen Doeblin
Stephanie Johanson
Jerry D. White
- 1 Charles W. F. Bell,
Staff Director
Oregon Fellowship for
Reconciliation
1422 S.E. Tacoma
Portland, OR 97202
- 1 Director
Franklin County Emergency
Management
1016 N. 4th Avenue
Pasco, WA 99301
- 1 David W. Stevens
P.O. Box 214
Olympia, WA 98507-0214
- 1 James Monteith
Oregon Natural Resources
Council
1161 Lincoln Street
Eugene, OR 97401
- 1 Norm Buske
Search Technical Services
Star Route Box 17
Davenport, WA 99112
- 1 Steve Binney
Radiation Center, A100
Oregon State University
Corvallis, OR 97331-5903

9 9 1 3 1 6 3 4

DISTRIBUTION (cont)

Number of copies

Number of copies

OFFSITE

OFFSITE

- 1 Russ Kevin Childers
223 14th E. 201
Seattle, WA 98112
- 1 Joanne Oleksiak, Director
Hanford Clearinghouse
2829 SE Belmont, 308
Portland, OR 97214
- 1 F. R. Cook
2552 Harris Avenue
Richland, WA 99352
- 1 Leonard Palmer
Portland State University
P.O. Box 751
Portland, OR 97207
- 1 Cindy De Bruler
Columbia River United
P.O. Box 667
Bingen, WA 98605
- 1 Ray Paris
Oregon State Health Division
State Office Building
Portland, OR 97204
- 1 Lloyd K. Marbet
Forlaws on Board
19142 S. Bakers Ferry Road
Boring, OR 97009
- 1 Cathy Kirkham
Greenpeace
4649 Sunnyside Avenue
Seattle, WA 98103
- 1 Ralph Patt
Water Resources Department
555 13th Street, NE
Salem, OR 97301
- 6 DNFSB
Tim Dwyer
625 Indiana Avenue, NW
Suite 700
Washington, D.C. 20004

- 1 Tommy Parkhill
U.S. Army Corps of Engineers
Walla Walla District
Walla Walla, WA 99362-9265
- 2 Gerald Pollet, Ex. Director
Heart of America Northwest
1305 4th Avenue, 208
Seattle, WA 98101
- 1 Norma Jean Germond
League of Women Voters
224 Iron Mountain Boulevard
Lake Oswego, OR 97034
- 1 Rep. Lane Bray
Washington State House of
Representatives
John L. O'Brien Building
Room 335
Olympia, WA 98504
- 1 Mike Fox, President
Hanford Family
P.O. Box 1462
Richland, WA 99352
- 1 Rep. Curtis Ludwig
Washington State House of
Representatives
John L. O'Brien Building
Room 336
Olympia, WA 98504
- 5 Kristine Gebbie
Department of Health
1300 Quince
Olympia, WA 98504
- 1 Senator Jim Jesernig
Washington State Senate
411 JAC Building
Olympia, WA 98504

9 8 1 3 0 2 6 1 6 3 5

DISTRIBUTION (cont)

Number of copies

Number of copies

OFFSITE

OFFSITE

- 1 Sharon Kophs
Westinghouse
North 221 Wall Street
Suite 446
Spokane, WA 99201
- 1 Rep. Bill Grant
Washington State House of
Representatives
John L. O'Brien Building
Room 243
Olympia, WA 98504
- 1 C. R. DeLannoy
Golder and Associates
1933 Jadwin Avenue
Suite 125
Richland, WA 99352
- 1 John Ringle
Graduate School
Administrative Services
A-300
Oregon State University
Corvallis, OR 97731
- 1 Senator Patty Murray
B-34 Dirksen
Senate Office Building
Washington, D.C. 20510
- 1 Curt Koegen
Operating Engineers
Local 370
2015 W. Yakima
Pasco, WA 99301
- 1 Senator Slade Gorton
730 Hart
Senate Office Building
Washington, DC 20510
- 1 Rep. Jay Inslee
House Office Building
1431 Longworth
Washington, DC 20575

- 1 Ms. Sandi Strawn, Chair
Benton County Board of
Commissioners
P.O. Box 190
Prosser, WA 99350-0190
- 1 Mr. John Thomas
Benton County Treasurer
P.O. Box 630
Prosser, WA 99350-0630

B&W Nuclear Environment Services

- 1 Gary W. Smith
2200 Langhorne Plaza
Lynchburg, VA 24501
- 1 Kevin Kelly
J. M. Montgomery Engineers
1933 Jadwin, Suite 125
Richland, WA 99352

ONSITE

- 6 U.S. Environmental Protection Agency
D. R. Sherwood B5-01
- 1 Hanford Environmental Health Foundation
B. B. Milburn B2-75
- 7 Kaiser Engineers Hanford
K. J. Dempsey E6-20
R. T. French E6-61
K. L. Kehler E6-21
S. L. Perry S2-54
J. R. Schroeder S2-53
R. M. Tanner S2-54
T. L. Watson S3-10
- 1 Mac Technical Services
L. Soler A4-35

9 5 1 1 6 3 6

DISTRIBUTION (cont)

Number of copies

Number of copies

ONSITE

ONSITE

11 Pacific Northwest Laboratory
 W. F. Bonner P7-41
 H. C. Burkholder P7-41
 T. D. Chikalla P7-75
 M. S. Hanson K1-51
 M. W. McCoy P7-68
 R. D. Sharp K7-98
 H. W. Slater P7-40
 L. E. Thompson P7-34
 P. J. Turner P7-34
 J. W. Wald K2-22
 Technical Files K1-11

63 U.S. Department of Energy, Richland Field Office

J. H. Anttonen A5-10
 C. V. Banks A5-16
 J. D. Bauer A5-15
 T. A. Bauman A7-75
 G. E. Bishop R2-62
 G. J. Bracken A4-02
 K. W. Bracken A5-10
 J. J. Broderick A7-27
 R. W. Brown R3-73
 D. C. Bryson R3-80
 K. D. Cameron A5-04
 C. E. Clark A5-15
 J. M. Clark A4-02
 P. K. Clark R3-80
 S. S. Clark R3-81
 M. Dev A5-16
 J. K. Erickson A5-19
 L. Erickson A5-16
 R. D. Freeberg A5-19
 M. J. Furman R3-80
 R. E. Gerton A4-02
 E. D. Goller A5-19
 J. D. Goodenough A5-19
 R. F. Guercia R3-81
 A. C. Harris A5-19
 J. M. Hennig R3-80
 N. M. Highland A7-29
 R. G. Holt A5-15
 L. A. Huffman A5-16
 J. R. Hunter R3-81

R. D. Izatt A3-42
 G. R. Konzek R3-73
 R. N. Krekel A5-15
 P. J. Krupin A5-15
 L. E. Little A3-42
 A. E. Lorenz A7-89
 L. S. Mamiya R3-80
 R. G. McLeod A5-19
 J. E. Mecca R3-81
 P. M. Pak A5-19
 J. C. Peschong A5-16
 M. J. Plahuta A7-27
 R. O. Puthoff A5-10
 J. E. Rasmussen A5-15
 A. L. Rodriguez A5-15
 R. M. Rosselli A7-70
 W. A. Rutherford A5-04
 R. P. Saget A5-52
 R. K. Stewart A5-19
 J. J. Sutey A5-90
 D. W. Templeton R3-81
 N. G. Thomas A7-27
 K. M. Thompson A5-15
 H. R. Trumble A5-19
 J. D. Wagoner A7-50
 N. A. Werdel A5-19
 W. A. White A7-27
 J. W. Wiley A6-54
 L. C. Williams A5-18
 S. H. Wisness A5-15
 J. K. Yerxa A5-15
 Reading Room H2-53

119 Westinghouse Hanford Company

T. M. Anderson B3-01
 J. N. Appel S4-58
 L. D. Arnold B2-35
 B. A. Austin B2-35
 H. Babad R2-78
 M. L. Bell T6-16
 P. J. Bence G1-76
 J. D. Berger L0-18
 M. V. Berriochoa B3-30
 T. D. Blankenship B1-58
 R. J. Bliss B3-04
 L. E. Borneman B2-35
 R. J. Bottenus T3-28

9 3 1 3 1 2 6 1 6 3 7

DISTRIBUTION (cont)

Number of copies

Number of copies

ONSITE

ONSITE

Westinghouse Hanford Company
(cont)

R. C. Bowman	H6-24
S. L. Brey	T6-12
L. C. Brown	H6-20
M. C. Brown	B2-35
J. G. Burk Jr.	B3-25
F. T. Calapristi	B2-35
A. S. Carlson	B3-35
G. D. Carpenter	H6-30
R. R. Disibio	B3-02
W. T. Dixon	B2-17
V. R. Dronen	R3-42
J. A. Eacker	R2-50
J. O. Elsethagen	A2-50
J. L. Epstein	R4-01
B. G. Erlandson	H6-21
G. W. Faulk	T3-28
K. R. Fecht	H6-06
G. D. Forehand	B2-35
M. R. Fox	B2-17
R. L. Fritz	R3-49
J. C. Fulton	R2-31
C. J. Geier	H6-21
C. K. Girres	N3-11
A. Greenberg	S4-01
M. L. Grygiel	B1-58
K. A. Hadley	R3-56
V. W. Hall	B1-59
W. H. Hamilton	N3-10
D. R. Herman	S4-01
R. C. Hill	B4-53
J. O. Honeyman	B2-30
M. C. Hughes	R2-81
P. H. Jacobsen	N3-13
S. M. Joyce	H1-61
R. J. Julian	T3-28
J. R. Kasper	R2-50
D. E. Kelley	R3-46
J. R. Kelly	R3-28
J. H. Kessner	H4-23
J. R. Knight	B3-04
M. K. Korenko	B3-08
E. J. Kosiancic	T6-16
O. S. Kramer	B2-35
J. H. Larue	G6-16
G. J. LeBaron	S6-19

R. E. Lerch	B3-63
D. W. Lindsey	B2-35
M. K. Mahaffey	L4-73
M. M. McCarthy	N3-13
H. E. McGuire	B3-63
W. C. Miller	B1-58
D. A. Moore	H4-57
R. D. Morrison	B2-35
D. J. Newland	B1-58
D. H. Nyman	G6-02
W. R. Ower	R1-48
D. B. Pabst	B2-35
M. A. Payne	R2-50
R. D. Pierce	N3-13
L. L. Powers	L4-96
S. M. Price	H6-23
J. G. Propson	R2-18
R. E. Raymond	R1-80
W. A. Retterer	S2-93
R. C. Roal	S6-08
R. J. Roberts	N3-13
F. A. Ruck	H6-23
W. G. Ruff	R3-50
J. A. Seamans	N2-04
J. O. Skolrud	H6-02
R. A. Smith	G6-02
C. R. Stroup	H1-61
D. J. Swaim	B3-51
J. A. Swenson	G6-45
R. R. Thompson	N1-73
J. E. VanBeek	R3-27
T. B. Veneziano	L4-96
M. L. Vodney	G6-02
E. C. Vogt	T5-50
J. L. Waite	B2-35
D. J. Watson	X0-41
T. M. Wintczak	H6-27
D. D. Wodrich	R2-31
R. D. Wojtasek	H6-27
C. D. Wollam	S6-19
D. E. Wood	H0-32
R. F. Wood	R4-01
J. A. Yount	L5-63
W. F. Zuroff	R2-14

9 3 1 9 3 1 6 3 3

ORIGINAL

Date Received: 8-31-93 CW	INFORMATION RELEASE REQUEST	Reference: WHC-CM-3-4
-------------------------------------	------------------------------------	--------------------------

Complete for all Types of Release

Purpose <input type="checkbox"/> Speech or Presentation <input type="checkbox"/> Full Paper (Check only one suffix) <input type="checkbox"/> Summary <input type="checkbox"/> Abstract <input type="checkbox"/> Visual Aid <input type="checkbox"/> Speakers Bureau <input type="checkbox"/> Poster Session <input type="checkbox"/> Videotape	<input type="checkbox"/> Reference <input type="checkbox"/> Technical Report <input type="checkbox"/> Thesis or Dissertation <input type="checkbox"/> Manual <input type="checkbox"/> Brochure/Flier <input type="checkbox"/> Software/Database <input type="checkbox"/> Controlled Document <input checked="" type="checkbox"/> Other	ID Number (include revision, volume, etc.) WHC-MR-0403-9 List attachments. Date Release Required <p style="text-align: center;">August 26, 1993</p>
---	---	---

Title Tri-Party Agreement Milestone Summary - July 1993	Unclassified Category UC-	Impact Level
--	-------------------------------------	--------------

New or novel (patentable) subject matter? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes If "Yes", has disclosure been submitted by WHC or other company? <input type="checkbox"/> No <input type="checkbox"/> Yes Disclosure No(s).	Information received from others in confidence, such as proprietary data, trade secrets, and/or inventions? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Identify)
---	---

Copyrights? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes If "Yes", has written permission been granted? <input type="checkbox"/> No <input type="checkbox"/> Yes (Attach Permission)	Trademarks? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Identify)
---	---

Complete for Speech or Presentation

Title of Conference or Meeting	Group or Society Sponsoring
Date(s) of Conference or Meeting	City/State
Will proceedings be published? <input type="checkbox"/> Yes <input type="checkbox"/> No	Will material be handed out? <input type="checkbox"/> Yes <input type="checkbox"/> No

Title of Journal

CHECKLIST FOR SIGNATORIES

Review Required per WHC-CM-3-4	Yes	No	Reviewer - Signature Indicates Approval
			Name (printed) Signature Date
Classification/Unclassified Controlled Nuclear Information	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Patent - General Counsel	<input checked="" type="checkbox"/> <i>CW</i>	<input checked="" type="checkbox"/>	<i>Per OGC memo dated 2-4-93</i>
Legal - General Counsel	<input checked="" type="checkbox"/> <i>CW</i>	<input checked="" type="checkbox"/>	<i>Per OGC memo dated 2-4-93</i>
Applied Technology/Export Controlled Information or International Program	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
WHC Program/Project	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>Becky Austin</i> <i>[Signature]</i>
Communications	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<i>[Signature]</i> <i>8/20/93</i>
RL Program/Project	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>Steven Wisness</i> <i>[Signature]</i>
Publication Services	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>[Signature]</i> <i>8/31/93</i>
Other Program/Project	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Information conforms to all applicable requirements. The above information is certified to be correct.

<table style="width:100%;"> <tr> <td style="width:30%;">References Available to Intended Audience</td> <td style="width:10%;">Yes <input checked="" type="checkbox"/></td> <td style="width:10%;">No <input type="checkbox"/></td> </tr> <tr> <td>Transmit to DOE-HQ/Office of Scientific and Technical Information</td> <td><input type="checkbox"/></td> <td><input checked="" type="checkbox"/></td> </tr> <tr> <td>Author/Requestor (Printed/Signature)</td> <td colspan="2">Date</td> </tr> <tr> <td>Frank Calapristi</td> <td colspan="2"></td> </tr> <tr> <td>Intended Audience</td> <td colspan="2"> <input type="checkbox"/> Internal <input type="checkbox"/> Sponsor <input checked="" type="checkbox"/> External </td> </tr> <tr> <td>Responsible Manager (Printed/Signature)</td> <td colspan="2">Date</td> </tr> <tr> <td>Frank Calapristi <i>[Signature]</i></td> <td colspan="2"><i>8/16/93</i></td> </tr> </table>	References Available to Intended Audience	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>	Transmit to DOE-HQ/Office of Scientific and Technical Information	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Author/Requestor (Printed/Signature)	Date		Frank Calapristi			Intended Audience	<input type="checkbox"/> Internal <input type="checkbox"/> Sponsor <input checked="" type="checkbox"/> External		Responsible Manager (Printed/Signature)	Date		Frank Calapristi <i>[Signature]</i>	<i>8/16/93</i>		<p style="text-align: center;">INFORMATION RELEASE ADMINISTRATION APPROVAL STAMP</p> <p>Stamp is required before release. Release is contingent upon resolution of mandatory comments.</p> <div style="text-align: center;">  </div>
References Available to Intended Audience	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>																				
Transmit to DOE-HQ/Office of Scientific and Technical Information	<input type="checkbox"/>	<input checked="" type="checkbox"/>																				
Author/Requestor (Printed/Signature)	Date																					
Frank Calapristi																						
Intended Audience	<input type="checkbox"/> Internal <input type="checkbox"/> Sponsor <input checked="" type="checkbox"/> External																					
Responsible Manager (Printed/Signature)	Date																					
Frank Calapristi <i>[Signature]</i>	<i>8/16/93</i>																					
Date Cancelled	Date Disapproved																					

DISTRIBUTION (cont)

Number of copies

ONSITE

Westinghouse Hanford Company
(cont)

Central Files	L8-04
Document	
Processing and	
Distribution (2)	L8-15
EDMC (7)	H6-08
Hanford Technical	
Library	P8-55
Information	
Release	
Administration (3)	A3-36
Correspondence	
Control	A3-01

9
1
0
1
6
1
0
1
3
1
0
9
