

**START**

01-988.0010

BHI-CP-00011

Rev. C1

# 200-BP-5 Unit #1 Pilot-Scale Groundwater Treatment System Acceptance Test/Operational Test Procedure

## Authors


A.L. Huegel  
J.W. Green

Date Published  
October 1994



Prepared for the U.S. Department of Energy  
Office of Environmental Restoration and  
Waste Management

**Bechtel Hanford, Inc.**  
Richland, Washington



Approved for Public Release

200-BP-5 UNIT #1  
PILOT-SCALE GROUNDWATER TREATMENT SYSTEM  
ACCEPTANCE TEST/OPERATIONAL TEST PROCEDURE

Revision No. 1

Issue Date **OCT 24 1994**

Impact Level A QS  
*MESZ*

Prepared by: A. L. Huegel and J. W. Green

Reviewed by: *MD Baker* 10/21/94  
*FOR* D.B. Erb  
200-BP-5, Unit Task Lead

Reviewed by: *S.O. DeLeon* 10/21/94  
S.O. DeLeon  
Quality Assurance

Reviewed by: *CH St. John* 10/21/94  
C.H. St. John  
Health and Safety

Reviewed by: *C.J. Manley for*  
R.J. Fabre  
Field Support Services

Approved by: *J. Zoghbi* 10/22/94  
J.G. Zoghbi  
200 Area Project Manager

Controlled Copy No. 19

BHI-OP-00011 \*  
REV: 01\* *lmm*  
OU: 200-BP-5 *10/24/94*  
TSD: N/A  
ERA: N/A

APPROVAL PAGE

Title of Document: 200-BP-5 Unit #1 Pilot-Scale Groundwater Treatment System  
Acceptance Test/Operational Test Procedure

Author(s): A.L. Huegel  
J.W. Green

Approval: J.G. Zoghbi, 200 Area Project Manager

*Joseph Zoghbi*  
\_\_\_\_\_  
Signature

*10/22/94*  
\_\_\_\_\_  
Date

*lmm*  
*10/24/94*

\* Rev. 0 of this document was issued as BHI-00015, Rev. 00, same title, dated September 24, 1994.

The approval signature on this page indicates that this document has been authorized for information release to the public through appropriate channels. No other forms or signatures are required to document this information release.

In some cases, for documents in process or previously issued with a WHC document number before July 1, 1994, this page will appear in documents identified with WHC document numbers. No other forms are required for these documents.

BHI-PC *10/24/94*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

**CONTENTS**

1.0 GENERAL ..... 3

2.0 EQUIPMENT SETUP .. . . . . 4

3.0 COMPONENT INSPECTION AND DOCUMENTATION ..... 6

4.0 ACCEPTANCE TEST PROCEDURE (ATP) .. . . . . 9

5.0 OPERATIONAL TEST PROCEDURE ..... 13

6.0 INSTRUMENT AND PROCESS CONTROL TEST ..... 16

7.0 FAILSAFE MOTOR-OPERATED VALVES .. . . . . 17

8.0 EMERGENCY SHUTDOWN SWITCHES ..... 19

**FIGURES:**

1. Process Flow Diagram, BY Cribs Pilot Groundwater Treatment System ..... 21

2. 200-BP-5 Reverse Well Programmable Logic Controller  
Ladder Logic Diagram ..... 23

3. One-Line Electrical Diagram Reverse Well Pilot Groundwater  
Treatment System, 200-BP-5 Plume No. 1 ..... 31

## 1.0 GENERAL

- 1.1 The purpose of this procedure is to outline the various steps necessary to verify the operability and completeness of the 200-BP-5 Reverse Well treatment system equipment and to verify that the system is installed in accordance with the design drawings, Figures 1 through 3.
- 1.2 Prior to the Functional Acceptance Test, all available instrumentation, wiring, and controls will have been installed and tested for loop integrity.
- 1.3 The Pilot-Scale Treatment System will commence operations by filling the influent storage tank on a 6-8 hour/day basis, eventually working up to 24 hours/day. The treatment system then processes this influent and fills the effluent surge tank for discharge of the treated influent into a disposal well. Injection into the disposal well can occur on a 24 hour/day basis because of safety interlocks built into the system. Performance of this Acceptance Test Procedure/Operational Test Procedure (ATP/OTP) will not test the Optional equipment as noted on the Process Flow Diagram, Figure 1. These optional ATP/OTP operations may be installed after it has been determined that they are required, and this procedure will be revised to provide for their testing.
- 1.4 The Treatment System is operated generally in a manual mode, utilizing interlocks for shutting down the system to protect equipment and prevent overflow of the Influent and Effluent Storage Tanks and other safety concerns. The interlocks are shown on the Electrical Control Ladder Diagrams, Figure 2
- 1.5 The test shall be performed by at least two individuals, a test director and a verifier. The test director shall be from engineering and shall be familiar with the system. The verifier can be an individual from quality assurance, operations, or field engineering. Historically, performance of the ATP/OTP has been for training of new operators/field personnel by utilizing them as verifiers. If more than one verifier is used, they may also sign as witnessing the test. At completion of the first, or functional, part of the test (before waterflows), Quality Assurance will verify the first part of the testing for completeness. Following completion of the final portion of the test, Quality Assurance will verify testing for completeness. QA will verify completion of each section.
- 1.6 Acceptable and Not Acceptable as used in this ATP/OTP are defined to mean that the question asked or function check requested by the inquiry/test procedure is to verify whether a piece of equipment exists (or does not), or that function happens (or does not). For example, if the equipment exists, it is Acceptable; if not, it is Not Acceptable. If a function performs as it is supposed to do, it is Acceptable; if not, it is Not Acceptable. All Not Acceptable Items will be logged on a "Punch List" and attached to this ATP/OTP.

**2.0 EQUIPMENT SETUP**

Set up the Influent and Effluent pump skids and the Process System skid for performing the Acceptance and Operational Tests per the following.

- 2.1** Position the skids approximately as shown on the site plan and connect between the skids with quick disconnect hoses as follows:
- 2.1.1 Connect the extraction well pump discharge to the influent storage tank inlet.
  - 2.1.2 Connect the influent storage tank outlet to the influent pump skid suction.
  - 2.1.3 Connect the influent pump skid discharge to the process skid influent pipe manifold inlet.
  - 2.1.4 Connect the process skid influent pipe manifold outlet to the first column inlet.
  - 2.1.5 Connect the selected first ion exchange column outlet to the selected second column inlet.
  - 2.1.6 Connect the second ion exchange column outlet to the third column inlet.
  - 2.1.7 Connect the third column outlet to the fourth column inlet.
  - 2.1.8 Connect the fourth column outlet to the process system skid effluent pipe manifold inlet
  - 2.1.9 Connect the process system skid effluent pipe manifold discharge to the Effluent Storage Tank inlet.
  - 2.1.10 Connect the Effluent Storage Tank outlet to the Effluent Pump skid suction manifold.
  - 2.1.11 Connect the Effluent Pump skid discharge to the disposal well.
- 2.2** Verify that the pressure gauges are properly installed and calibrated.
- Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_
- 2.3** Verify that the flow meters and rotameters are properly installed and operable.
- Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.4** Verify that all valves, including motorized ball valves (MBV's), are properly installed and operable.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.5** Verify that the influent and effluent storage tank sight gages are properly installed and operable. Sight gages will be drained and valved off during winter months when there is potential for freezing conditions.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.6** Verify that all instrument cables between sensors and monitors are connected.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.7** Verify that all electrical power and electrical interconnections are installed per the One-Line Diagram, Figure 3, and the Electrical Control Ladder Diagram, Figure 2.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.8** Verify that filter bags are installed in influent filter housing pairs F-1 and F-2.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.9** Verify that filter cartridges are installed in effluent filter housing pairs F-3 and F-4.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 2.10** Verify that bone char is loaded in the first column(s). Verify that clinoptilolite is loaded in the second column(s). Verify that 50% bone char and 50% clinoptilolite are loaded in the third column(s). Verify that granulated activated carbon is loaded in the fourth column. Record the depths of adsorbent in each column: Column #1 \_\_\_\_, Column #2 \_\_\_\_, Column #3 \_\_\_\_, Column #4 \_\_\_\_.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

Section 2.0 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

**3.0 COMPONENT INSPECTION AND DOCUMENTATION****3.1 Mechanical**

Refer to Process Flow Diagram, Figure 1. After the equipment has been set up, perform an equipment inspection and verify that all components are installed according to drawings. If the drawings do not represent the actual installation, As-Built the drawings, and after approval by engineering, attach to this procedure. Utilize the equipment listed under Section 3.2 below for equipment component check.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

**3.2 Documentation**

Verify that vendor information is available for the following equipment. The Vendor Information will be placed in the Project Files.

- 3.2.1 Extraction Well Pump
- 3.2.2 Influent Pumps
- 3.2.3 Process Pump
- 3.2.4 Effluent Pumps
- 3.2.5 Filters, Influent and Effluent
- 3.2.6 Ion Exchange Columns
- 3.2.7 Influent/Effluent Storage Tanks
- 3.2.8 Process Water Tank
- 3.2.9 Failsafe Motor-Operated Ball Valve
- 3.2.10 Air Release Valves
- 3.2.11 Flowmeters
- 3.2.12 Flow Switches
- 3.2.13 Rotameters
- 3.2.14 Level Indicators/Controls
- 3.2.15 Pressure Gauges
- 3.2.16 Differential Pressure Indicator/Transmitter
- 3.2.17 Temperature Indicator/Transmitter
- 3.2.18 Dissolved Oxygen Monitor
- 3.2.19 Turbidity Monitor
- 3.2.20 pH Indicator/Transmitter
- 3.2.21 Flex Hose
- 3.2.22 Flexible Connectors
- 3.2.23 Adsorbent
- 3.2.24 Bone Char
- 3.2.25 Programmable Logic Controller
- 3.2.26 Annunciator

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

### 3.3 Electrical

Refer to One Line Electrical Diagram, Figure 3. Verify that electrical installation is complete. Verification includes checking for installation in accordance with the National Electrical Code (NEC).

3.3.1 Verify installation of power feed from generator to main control panel on process treatment system.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

3.3.2 Verify installation of 480-VAC, 3-phase power feed from main control panel on Process Treatment Skid to the following pumps:

- Extraction well pump
- Influent pump station
- Process pump
- Effluent pump station

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

3.3.3 Verify 120-VAC auxiliary/control wiring from main control panel to:

- Extraction well
- Influent storage tank
- Influent pumping station
- Process treatment system
- Effluent storage tank
- Effluent pumping station
- Disposal well

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

3.3.4 Verify installation of 240-VAC, single-phase power feed from main control panel to:

- 240 V Receptacles for Air Compressor located at influent pumping station, process treatment system, and effluent pumping station.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 3.3.5 Verify signal wiring from transmitters to main control panel.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 3.3.6 Grounding System

- Verify that the Process Treatment System is properly grounded.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the Influent pumping station is properly grounded.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the Influent storage tanks are properly grounded.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the Process water tank is properly grounded (if applicable).

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the Effluent pumping station is properly grounded.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the Effluent storage tanks are properly grounded.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- Verify that the power generator(s) is properly grounded

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 3.3.7 Power Source Check, Generator - Verify that the generator output is 480 VAC, 3 phase, 60 HZ to ensure compatibility with load.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 3.3.8 Instrument panel - Test annunciators, alarms, and reset for proper operation.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 3.3.9 Check pump motors, Influent Pumps (P-2A, P-2B), Process Pump

(P-3), Effluent Pumps (P-5A, P-5B) for proper rotation. Briefly activate each pump pushbutton to bump the motors and visually verify proper rotation as noted by movement of motor fan in direction of rotational arrow.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

Section 3.0 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_

#### 4.0 ACCEPTANCE TEST PROCEDURE (ATP)

This portion of the test procedure will establish flow of clean water through process components to verify operability of pumps, verify interlocks and their shutdown capabilities, test failsafe motor-operated valves for closure on power failure, and test emergency shutdown switch.

##### 4.1 Pumps

###### 4.1.1 Extraction Well Pump

- Open motor-operated ball valve. **MBV-1.**
- Open ball valves **BV-1, BV-2, BV-4, BV-7, BV-8, BV-10, and BV-18.**
- Start Extraction Well Pump.
- Watch for flow at FIT-1 AND FI-1.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

###### 4.1.2 Influent Pumps (Note: The Influent Storage Tank must have liquid in the tank for this test). Ensure pump is primed.

###### 4.1.2.1 Pump P-2A

- Open MBV-2 (outlet from the Influent Storage Tank).
- Open ball valves **BV-11, BV-19, BV-30, BV-32, BV-33, BV-44, BV-50, BV-51, BV-55B, BV-56, BV-59, BV-62B, BV-64G, BV-64, BV-69, BV-64C, BV-64D, BV-64H, BV-64I, BV-64J, BV-64K, BV-70, BV-71, and BV-80.**
- Start Influent Pump P-2A.
- Watch for flow at FIT-2.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

###### 4.1.2.2 Pump P-2B

- Open MBV-2 (outlet from the Influent Storage Tank).
- Open ball valves **BV-11, BV-19, BV-30, BV-34, BV-35, BV-44,**

**BV-50, BV-51, BV-55B, BV-56, BV-59, BV-62B, BV-64G, BV-64, BV-69, BV-64D, BV-64H, BV-64I, BV-64K, BV-70, BV-71, and BV-80.**

- Start Influent Pump P-2B.
- Watch for flow at FIT-2.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

4.1.3 Process Pump, P 3 (Note: This pump is used for backwashing the columns and as a sump pump as required).

- Connect hose from the Process Water Tank (noting that there is water in the Process Water Tank) to the suction of P-3, and hose from the pump discharge to the Effluent surge Tank.
- Open **BV-41** and **BV-42**.
- Start Pump P-3.
- Watch for makeup of FS-4.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

4.1.4 Effluent Pumps (Note: The Effluent Storage Tank must have liquid in the tank for this test).

4.1.4.1 Pump P-5A (Effluent Pump)

- Open ball valves **MBV-6** (if applicable), **BV-72, BV-81, BV-87, BV-90, BV-92, BV-93, BV-98, BV-99, BV-102, BV-103, BV-110, BV-111, and BV-112.**
- Start Effluent Pump P-5A.
- Watch for flow at FIT-5.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

4.1.4.2 Pump P-5B (Effluent Pump)

- Open ball valves **MBV-6** (if applicable), **BV-72, BV-81, BV-87, BV-90, BV-94, BV-95, BV-98, BV-99, BV-102, BV-103, BV-110, BV-111, and BV-112.**
- Start Effluent Pump P-5B.
- Watch for flow at FIT-5.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 4.2 Level Switches

The level switches will be functionally checked by shorting out the input to the level control relay and checking for the proper diagnostic and

annunciation of alarms that will indicate actuation of the appropriate level control relay.

4.2.1 Open the probe circuits to simulate a low level for the following level switches and verify that both the diagnostic and annunciator lights actuate:

	Accept	Not Accept
LSL-1 (Extraction Well, Low)	_____	_____
LSL-2 (Influent Tank, Low)	_____	_____
LSL-5 (Effluent Tank, Low)	_____	_____

4.2.2 Short the probe circuits to simulate a high level for the following level switches and verify that both the diagnostic and annunciator lights actuate:

	Accept	Not Accept
LSH-1 (Influent Tank, High)	_____	_____
LSHH-1 (Influent Tank, High-High)	_____	_____
LSH-2 (Effluent Tank, High)	_____	_____
LSHH-2 (Effluent Tank, High-High)	_____	_____
LSH-3 (Disposal Well, High)	_____	_____

#### 4.3 Flow Switches

The flow switches will be functionally tested by manually retracting the paddle to simulate a flowing condition and checking for proper annunciator light actuation that will indicate flow.

	Accept	Not Accept
FS-1	_____	_____
FS-2	_____	_____
FS-3	_____	_____
FS-4	_____	_____
FS-5	_____	_____
FS-6	_____	_____

#### 4.4 Differential Pressure Indicating Transmitters, DPITs



PDIT-3 \_\_\_\_\_  
PDIT-4 \_\_\_\_\_

#### 4.4.3 Effluent Filters

- Close **BV-90, 99, 103.**
- Set air compressor at 30 psi, connect air hose to AC-9.
- Open ball valves: **BV-92, BV-93, BV-94, BV-95, BV-98, BV-100, BV-101, BV-102.**
- Verify that hose from Effluent Pump manifold to Disposal Well manifold (location of AC-9) is connected.
- Start air compressor and allow piping to pressurize to 30 psi.
- Disconnect low pressure side of differential pressure transmitter PDIT-5. Verify actuation of high differential pressure alarm annunciator. Reconnect the tubing to the transmitter before continuing.

Accept Not Accept

PDIT-5 \_\_\_\_\_

Section 4 completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

## 5.0 OPERATIONAL TEST PROCEDURE

In this portion of the test procedure, the process treatment system will be configured and flow of potable water established to verify operability. Align valves to allow establishing flow from the Extraction Well Pump to the Influent Storage Tank, then from either of the Influent Pumps through either of the Filters and two to four Columns in series flow and on to the Effluent Storage Tank. When the Effluent Storage Tank contains sufficient water, establish flow via the Effluent Pumps to the Disposal Well.

NOTE: Flow will be established by manually aligning valves, starting pumps. Storage tank levels will be monitored via level indicators with the sight glasses as a backup. Differential pressures of the filters and Columns will be monitored via differential pressure indicators/transmitters as well as pressure gages.

### 5.1 Starting Extraction Well Pump

5.1.1 Open Motorized Ball Valve, **MBV-1** in "Open" mode.

5.1.2 Open ball valves **BV-1, BV-2, BV-4, (BV-6 or, BV-7 & BV-8), BV-9, BV-10, and BV-18.**

- 5.1.3 Start the Extraction Well Pump by holding in the "Start" pushbutton until flow is established. Watch for flow on FIT-1 and makeup of Flow Switch FS-1, then release the pushbutton.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 5.1.4 Verify that the following annunciator and diagnostic lights are not illuminated:

Influent Surge Tank Level High, LSH-1  
Extraction Well Level Low, LSL-1  
No Flow From Extraction Well Pump, FS-1  
Influent Surge Tank Level High-High, LSHH-1

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 5.1.5 Set MBV-1 selector switch to "Auto." Stop Extraction Well Pump P-1 by pushing the "Stop" pushbutton. Verify MBV-1 closes.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

## 5.2 Establishing Flow from the Influent Storage Tank

- 5.2.1 When the Influent Storage Tank is at an appropriate level, open **MBV-2** in the "Open" mode.

- 5.2.2 Open ball valves **BV-11, BV-19, BV-30, BV-34, BV-35, BV-38, BV-39, BV-40, BV-41, BV-45, BV-46, BV-47, BV-48, BV-44, BV-50, BV-51, BV-55B, BV-56, BV-59, BV-62B, BV-64G, BV-64, BV-69, BV-64C, BV-64D, BV-64H, BV-64I, BV-64J, BV-64K, BV-66, BV-70, BV-71, and BV-80.**

- 5.2.3 Start either Influent Pump P-2B by holding in the "Start" pushbutton until flow is established. Watch for flow on FIT-2 and makeup of FS-2, FS-3, and FS-4.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- 5.2.4 Verify that the following annunciator and diagnostic lights are not illuminated.

No Flow to Influent Pumps, FS-2  
Loss of Flow in Hose to Pipe Manifold, FS-3  
Loss of Flow in Hose to Effluent Surge Tank, FS-4  
Influent Surge Tank Level Low, LSL-2  
Effluent Surge Tank Level High, LSH-2  
Effluent Surge Tank Level High-High, LSHH-2

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

5.2.5 When flow has been established through the system and is at steady state, take readings of flow, pressure, and pressure differential on filters and Columns.

Flow Readings: \_\_\_\_\_

Pressure Readings: \_\_\_\_\_

Differential Pressure Readings:

DPIT 1	_____	Influent filters
DPIT 2	_____	Tnk-3
DPIT 3	_____	Tnk-4
DPIT 4	_____	Tnk-5
DPIT 5	_____	Effluent filters

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

5.2.6 Set MBV-2 selector switch to "Auto." Stop Influent Pump P-2B by pushing the "Stop" pushbutton. Verify MBV-2 closes.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

### 5.3 Starting Effluent Pump

5.3.1 Open ball valves **BV-72, BV-81, BV-87, BV-90, (BV-92 & BV-93, or BV-94 and BV-95), BV-98, BV-99, BV-102, BV-103, BV-110, BV-111, and BV-112.**

5.3.2 Start either Pump P-5A or 5B by holding in the "Start" pushbutton until flow is established. Watch for flow on FIT-3 and makeup of FS-5 and FS-6.

5.3.3 Verify that the following annunciator lights on the annunciator panel are not illuminated:

Disposal Well Level High-High, LSHH-3  
Effluent Surge Tank Level Low, LSL-3  
No Flow to Effluent Pumps, FS-5  
No Flow to Disposal Well, FS-6

5.3.4 When flow has been established though the system and is at steady

state, take readings of flow, pressure, and pressure differential on the filters.

Flow Readings: \_\_\_\_\_

Pressure Readings: \_\_\_\_\_

Differential Pressure Readings: \_\_\_\_\_

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

Section 5 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

## 6.0 INSTRUMENT AND PROCESS CONTROL TEST

6.1 This portion of the test procedure will test the control system interlocks.

6.2 Each interlock will be tested by shorting out the appropriate level relays or by filling and emptying tanks with water (if available), and verifying that each will stop the appropriate pump or close the appropriate motor operated valve.

6.3 Start extraction well pump; restart after each test.

- LSL-1 (Low Level, Extraction Well), Action: Stop P-1

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- LSH-1 (High Level, Influent Tank), Action: Alarm (check this)

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- LSHH-1 (Hi-Hi Level, Influent Tank), Action: Stop P-1

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-1 (No Flow, hose to Influent Tank), Action: Stop P-1

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

6.4 Start Influent Pump P-2A or P-2B, restart after each test.

- LSL-2 (Low Level, Influent Tank), Action: Stop P-2A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- LSH-2 (High Level, Effluent Tank), Action: Alarm (check this)

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- LSHH-2 (High-High Level, Effluent Tank), Action: Stop P-2A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-2 (No Flow, to Influent Pumps), Action: Stop P-2A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-3 (No Flow, Hose to Process Skid), Action: Stop P-2A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-4 (No Flow, Hose to Effluent Tank), Action: Stop P-2A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

**6.5 Start Effluent Pump P-5A or P-5B, restart after each test.**

- LSL-3 (Low Level, Effluent Tank), Action: Stop P-5A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- LSH-3 (High Level, Disposal Well), Action: Stop P-5A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-5 (No Flow, Hose to Effluent Skid), Action: Stop P-5A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

- FS-6 (No Flow, Hose to Well), Action: Stop P-5A/B

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

Section 6 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

**7.0 FAILSAFE MOTOR-OPERATED VALVES**

The Failsafe Motor-Operated Ball Valves will be tested to verify the capability of closing on loss of power and for the ability to be actuated via the battery pack after

a power failure. The battery pack consists of a 24-VDC battery that is the backup power source for the 24-VDC motor that operates the valve and has a charger that keeps the battery charged when normal power (120 VAC) is on. At the present time, only the Influent Storage Tank has been fitted with the Failsafe Motor-Operated Valves, MBV-1 and MBV-2. When MBV-5 and MBV-6 are installed, this procedure will be revised to provide for testing them according to this procedure.

**7.1** The failsafe feature of Motor-Operated Ball Valves MBV-1 and MBV-2 will be tested for closure on loss of power. These valves are located at the influent tank and are to prevent spilling of tank contents to the ground in the event of a power failure. These valves will be checked in the manual and automatic modes.

**7.2** MBV-1, Manual Mode

- 7.2.1 Set MBV-1 "Auto-Open-Close" switch to "Open" to open valve.
- 7.2.2 Verify that valve is open.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

**7.3** MBV-1, Automatic Mode

- 7.3.1 Set MBV-1 "Auto-Open-Close" switch to "Auto."
- 7.3.2 Start Pump P-1 (Well Pump) and watch for valve to open.
- 7.3.3 Open the panelboard circuit for MBV-1 by turning off the 120 VAC power to failsafe unit and verify closure of valve on loss of power.
- 7.3.4 Close panelboard circuit by reapplying 120 VAC to failsafe unit to open valve, then shut off Well Pump P-1 and verify that valve closes when P-1 shuts down.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

**7.4** MBV-2, Manual Mode

- 7.4.1 Set MBV-2 "Auto-Open-Close" switch to "Open" to open valve.
- 7.4.2 Verify that valve is open.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

**7.5** MBV-2, Automatic Mode

- 7.5.1 Set MBV-2 "Auto-Open-Close" switch to "Auto."
- 7.5.2 Start Influent Pump P-2A, or P-2B and watch for valve to open.  
(Note: Pumps are wired so that both cannot be started at the same time.)
- 7.5.3 Open panelboard circuit for MBV-2 by turning off the 120 VAC to

failsafe unit and verify closure of valve on loss of power.

- 7.5.4 Close panelboard circuit by reapplying 120 VAC to failsafe unit to open valve, then shut off whichever pump is running (P-2A or P-2B) and verify that valve closes when pump shuts down.

Acceptable \_\_\_\_\_ Not Acceptable \_\_\_\_\_

Section 7 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

**8.0 EMERGENCY SHUTDOWN SWITCHES**

- 8.1 The emergency shutdown switch (or switches) will shut down the Treatment System in case of an emergency. Items included in this emergency shutdown include the Well Pump, Influent Pumps, Effluent Pumps, and Failsafe Motor Operated Valves.
- 8.2 Verify system is operating: Well Pump P-1, Influent Pump (P-2A or 2B), and Effluent Pump (P-5A or 5B) are operating, and that Failsafe Motor Operated Valves are open.
- 8.3 Actuate Emergency Shutdown (Switches) and verify shutdown of pumps and closure of valves.

	Acceptable	Not Acceptable
P-1	_____	_____
P-2A/2B	_____	_____
P-5A/5B	_____	_____
MBV-1	_____	_____
MBV-2	_____	_____

Section 8 was completed as noted. QA \_\_\_\_\_ Date: \_\_\_\_\_

APPENDIX

FIGURES

1.....Process Flow Diagram Reverse Well Pilot Groundwater  
Treatment System.....~~19~~ 21


2 200-BP-5 Reverse Well Programmable Logic Controller  
Ladder Logic Diagram.....~~20~~ 23

3 One Line Electrical Diagram Reverse Well Pilot Groundwater  
Treatment System 200-BP-5 Plume No. ~~2~~.....~~24~~ 31

*lmm*  
*10/24/94*

*1*  
*lmm*  
*10/24/94*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

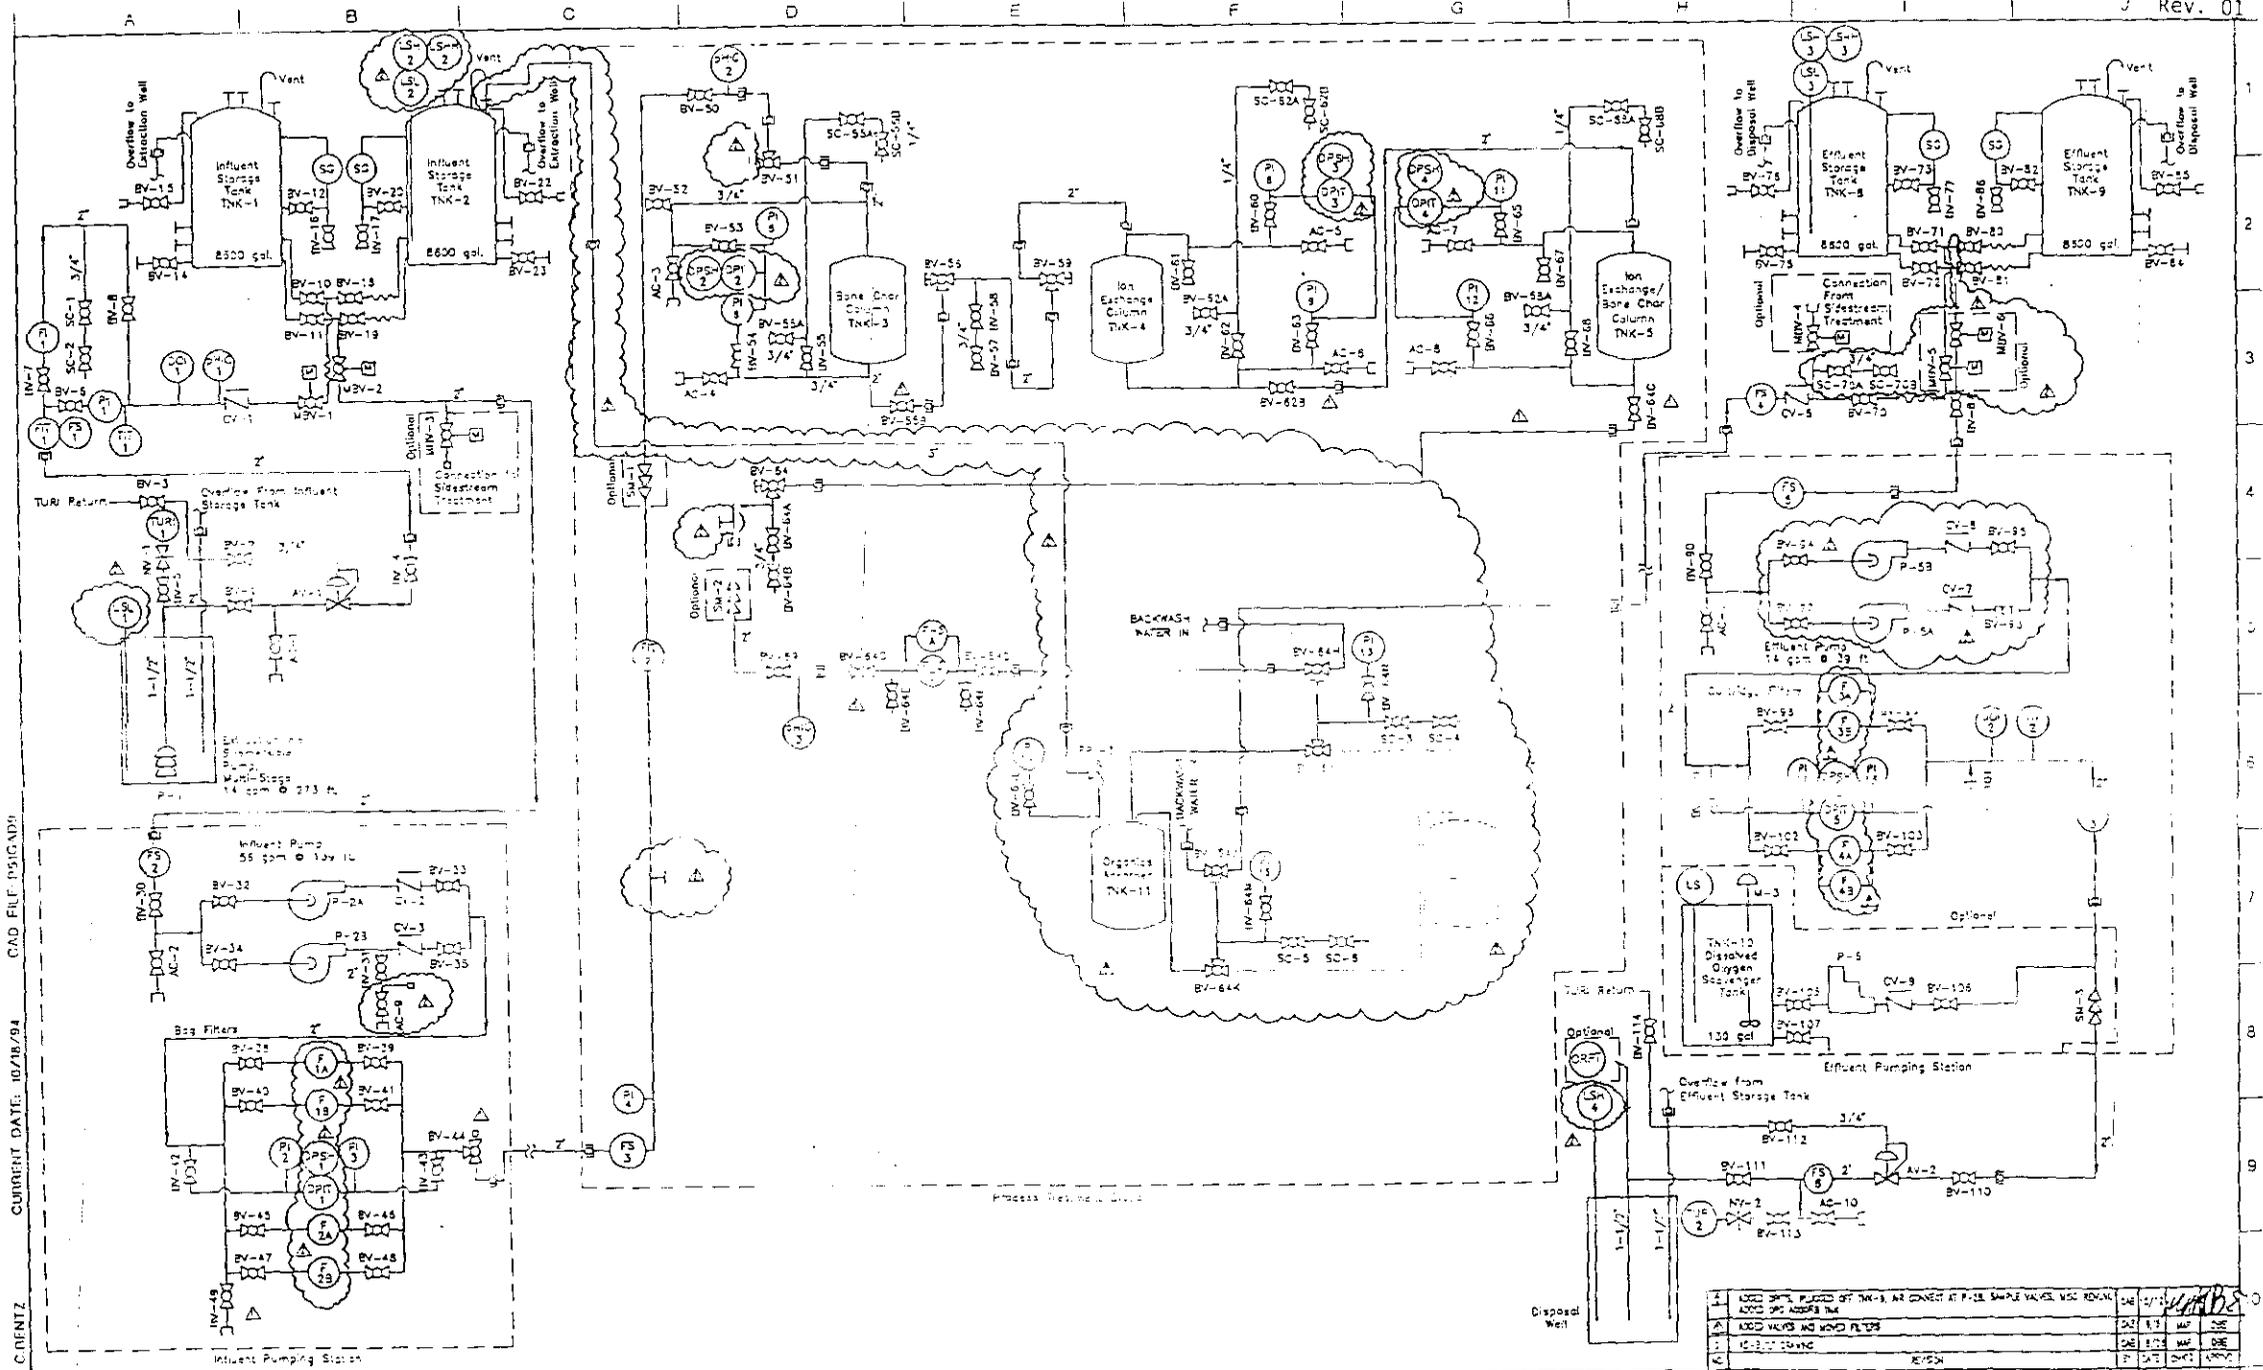

CLIENT BY: C. BENTZ  
 CURRENT DATE: 10/18/94  
 CAD FILE: P51G.ADS

CONFIDENTIAL PROPERTY OF IT HANFORD, INC. The drafting and the information contained herein was prepared for the use of the client and is not to be distributed outside the client's organization without the written consent of IT Hanford, Inc. All rights reserved. No part of this document may be reproduced or transmitted in any form or by any means electronic or mechanical, including photocopying, recording, or by any information storage and retrieval system, without the prior written permission of IT Hanford, Inc.	DRAWN BY: C. BENTZ CHECKED BY: J. COLESON ENG. CHK: W. FRANK PROJECT LEAD: C. BENTZ DATE: 8/12/94
---	---

COMPUTER GENERATED DRAWING  
 NO MANUAL CHANGES ALLOWED  
 PROJECT NO: P51G





UNDER CONTRACT TO  
 BECHTEL HANFORD, INC.  
 RICHLAND, WASHINGTON

PROCESS FLOW DIAGRAM  
 REVERSE WELL  
 PILOT GROUNDWATER TREATMENT SYSTEM  
 200-BP-S PLUME NO. 1  
 HANFORD SITE

SHEET NO. 1	DATE: 8/12/94	BY: C. BENTZ
DRAWING NO. P51G.A-23	DATE: 8/12/94	BY: C. BENTZ
REVISION 2	DATE: 8/12/94	BY: C. BENTZ

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

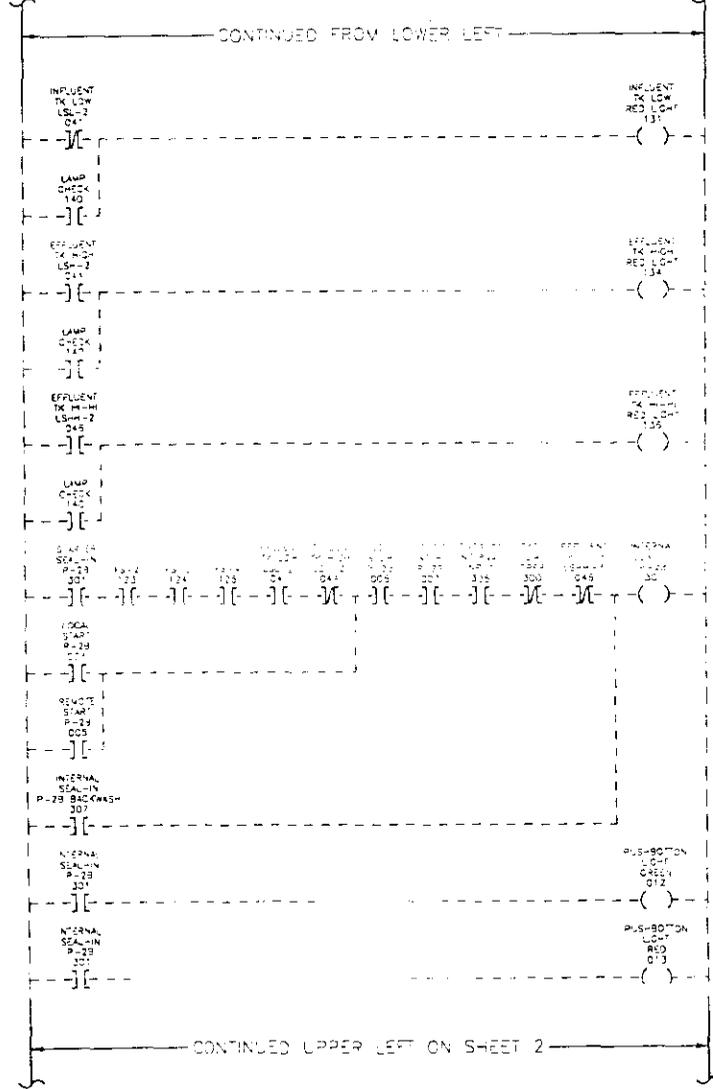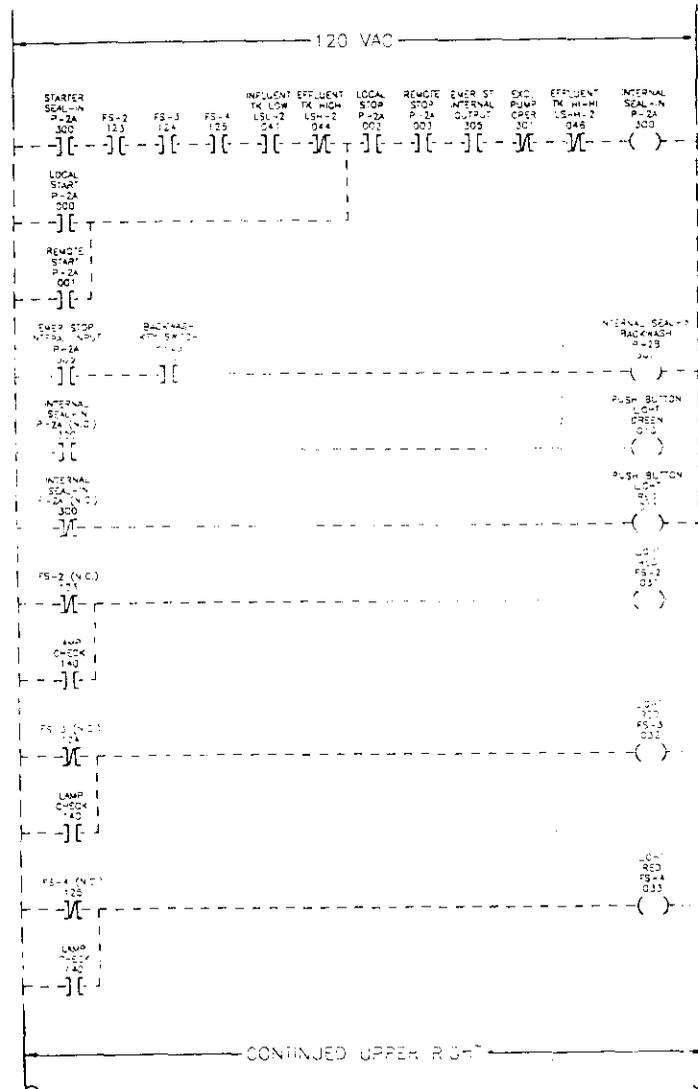

NOTES

NO.	DATE	DESCRIPTION	BY	CHKD	APP'D
1	12-20-84				

**U.S. DEPARTMENT OF ENERGY**  
DOE FIELD OFFICE, RICHLAND  
HANFORD ENVIRONMENTAL RESTORATION PROGRAM

BECHTEL HANFORD INC. RICHLAND, WASHINGTON	IT HANFORD INC. RICHLAND, WASHINGTON
--	---

**200-BP-5 REVERSE WELL  
PROGRAMMABLE LOGIC CONTROLLER  
LADDER LOGIC DIAGRAM**


BECHTEL JOB NO.	DOE CONTRACT NO.	CADD FILENAME
22192	DE-AC06-93RL12367	PLC-BPL1
DRAWING NO.		
200-BP-5		

Sheet 1 of 4


*Handwritten initials/signature*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

CONTINUED FROM LOWER RIGHT OF SHEET 1

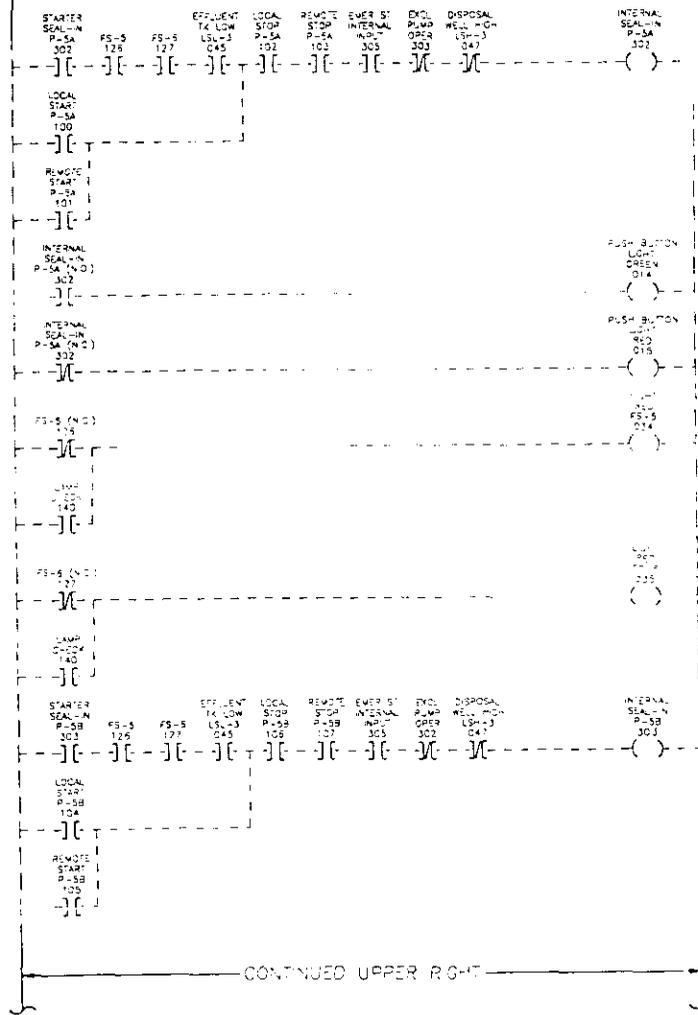

CONTINUED FROM LOWER LEFT

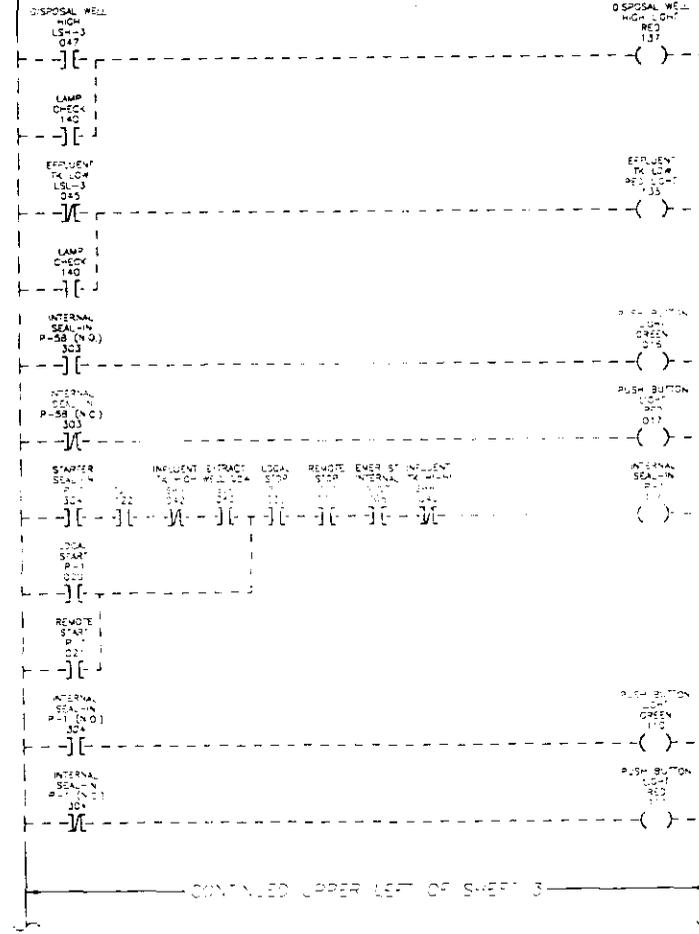

CONTINUED UPPER LEFT OF SHEET 3

NOTES

LEGEND

REV	DATE	DESCRIPTION	BY	CHK	APP

U.S. DEPARTMENT OF ENERGY  
DOE FIELD OFFICE, RICHLAND  
HANFORD ENVIRONMENTAL RESTORATION PROGRAM

BECHTEL HANFORD INC.      IT HANFORD INC.  
RICHLAND, WASHINGTON      RICHLAND, WASHINGTON

200-BP-5 REVERSE WELL  
PROGRAMMABLE LOGIC CONTROLLER  
LADDER LOGIC DIAGRAM



BECHTEL JOB NO.	DOE CONTRACT NO.	CADD FILENAME
22192	DE-AC06-93RL12367	PLC-BPL2

DRAWING NO.  
200-BP-5

Sheet 2 of 4

*MAO*  
*Jat*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

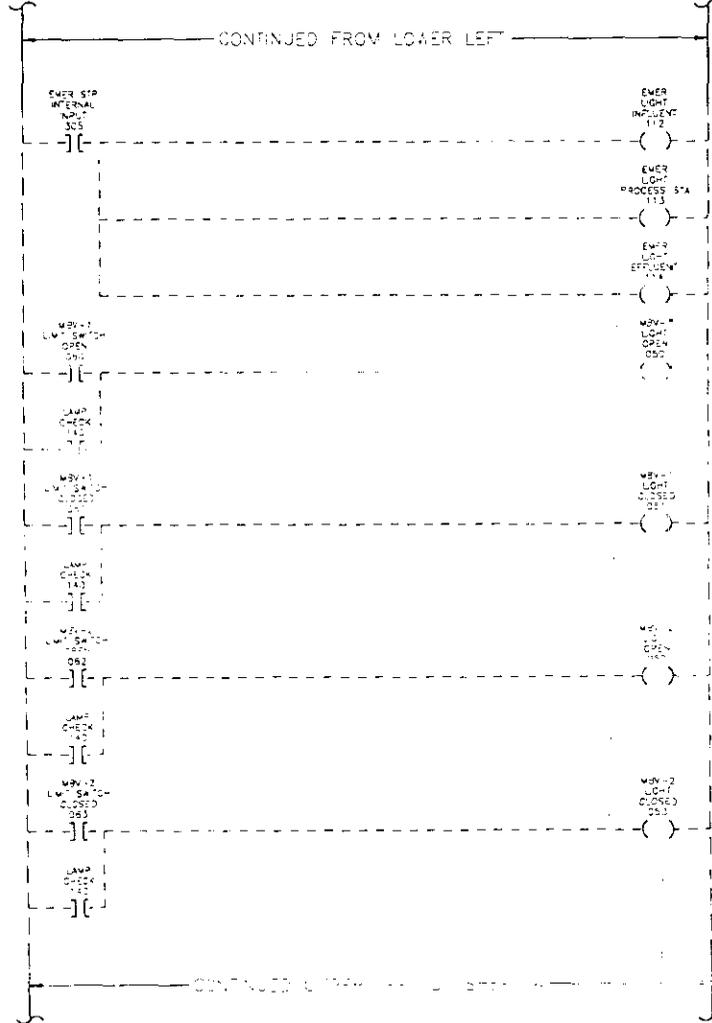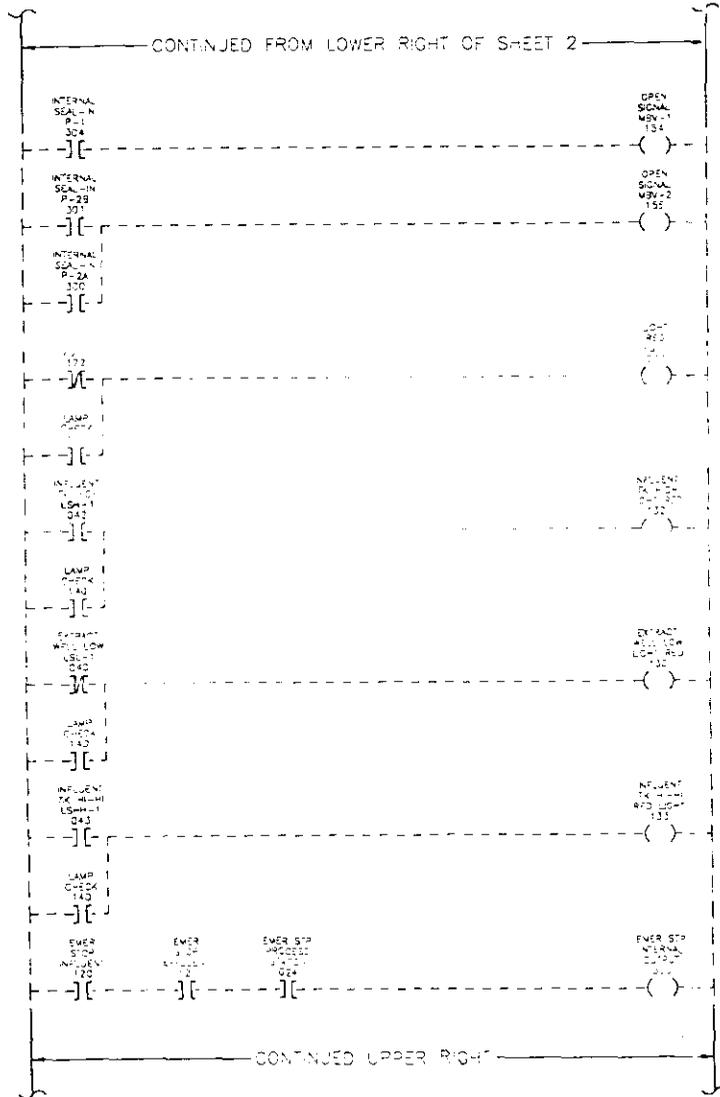

NOTES

---

REVISIONS

NO.	DATE	DESCRIPTION	BY	CHKD	APP'D
1	12-20-14				

U.S. DEPARTMENT OF ENERGY  
DOE FIELD OFFICE, RICHLAND  
HANFORD ENVIRONMENTAL RESTORATION PROGRAM

BECHTEL HANFORD INC. RICHLAND, WASHINGTON	IT HANFORD INC. RICHLAND, WASHINGTON
--	---

200-BP-5 REVERSE WELL  
PROGRAMMABLE LOGIC CONTROLLER  
LADDER LOGIC DIAGRAM



BECHTEL JOB NO.	DOE CONTRACT NO.	CADD FILENAME
22192	GE-ACC6-93RL12387	PLC-BPL3

DRAWING NO.  
200-BP-5

Sheet 3 of 4

*MAF*  
*JAD*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

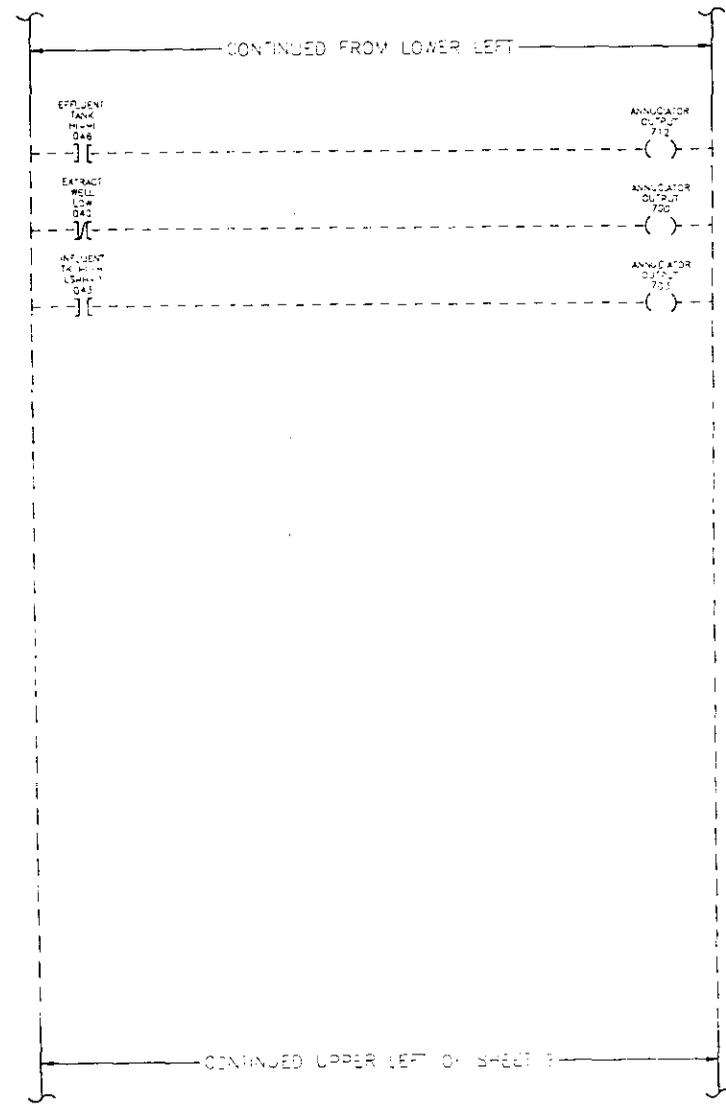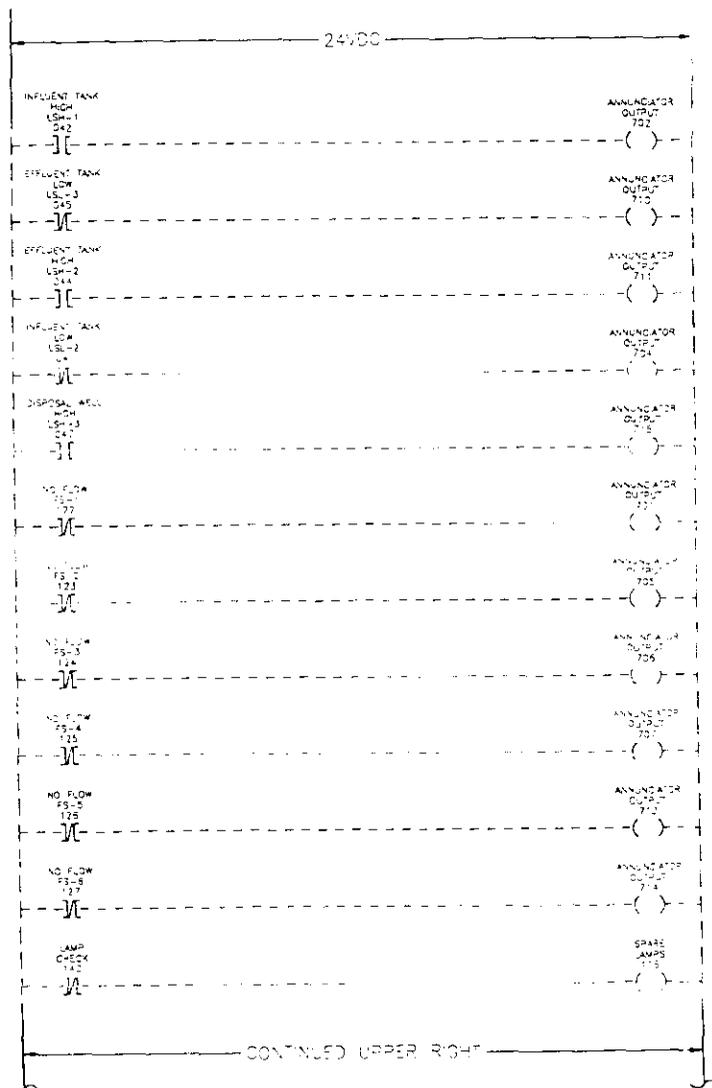

NOTES

REVISIONS

REV	DATE	DESCRIPTION	BY	CHKD	APPD
1	12-20-94	X			

SCALE: 1" = 12"

U.S. DEPARTMENT OF ENERGY  
DOE FIELD OFFICE, RICHLAND  
HANFORD ENVIRONMENTAL RESTORATION PROGRAM

BECHTEL HANFORD INC. RICHLAND, WASHINGTON      IT HANFORD INC. RICHLAND, WASHINGTON

200-BP-5 REVERSE WELL  
PROGRAMMABLE LOGIC CONTROLLER  
LADDER LOGIC DIAGRAM

BECHTEL JOB NO. 22192	DOE CONTRACT NO. DE-AC06-93RL12367	CAOD FILENAME PLC-BPL4
DRAWING NO. 200-BP-5		

Sheet 4 of 4

*MAF*

**THIS PAGE INTENTIONALLY  
LEFT BLANK**



THIS PAGE INTENTIONALLY  
LEFT BLANK

**DISTRIBUTION**Onsite (22 copies)**Controlled**

J. G. Zoghbi	H4-79
R. J. Fabré	H6-03
C. H. St. John	N3-06
S. O. DeLeon	H4-16
D. B. Erb	H6-01
J. W. Green	H6-02
M. A. Frank (3)	H6-03
A. L. Huegel (3)	H6-03
TW Spicer	T1-95
KR Porter	H6-01
MD Baker	H6-04
GC Henckel	H6-02
EPIC (2)	H6-08
ERC	H6-07
ERE Project File	H6-08
Procedures Coordination	H4-79
Resource Center	N3-05

**Uncontrolled**

AG Dada	H4-80
M Hyman	H4-79

**THIS PAGE INTENTIONALLY  
LEFT BLANK**

951738122

<b>Bechtel Hanford, Inc.</b>	<b>TRANSMITTAL FOR CONTROLLED PROCEDURES</b>
------------------------------	--


EPIC 19 H6-08	Transmittal No. TR-OP-17	Date 10-25-94
	Document No./Title of Manual BHI-OP-00011	

The procedure(s) listed below are being issued by BHI Procedures Coordination as new or revised procedures.

PROCEDURE NO.	REV. NO.	TITLE
BHI-OP-00011	1	200-BP-5 Unit #1 Pilot-Scale Groundwater Treatment System Acceptance Test/Operational Test Procedure
		<b>NOTE: Rev. 0 of this document was previously issued as BHI-00015, same title, dated 09/24/94. (BHI-OP-00011 supersedes rev. 0)</b>

**Receipt Acknowledgment**

I acknowledge receipt of the procedure(s) listed above. These procedures have been appropriately inserted and the superseded material removed and disposed of.

Signature:  Date: 11-22-94

New address if different than listed above \_\_\_\_\_

**PLEASE RETURN THIS SIGNED TRANSMITTAL WITHIN TEN WORKING DAYS TO**  
BHI Procedures Coordination/Natalie Maiuri  
372-9555  
H4-79

BHI-DC-001 (8/94)

**PLEASE DO NOT STAPLE OR TAPE**

**THIS PAGE INTENTIONALLY  
LEFT BLANK**
