

200 AREA PROJECT MANAGERS MEETING (PMM) MAY 15, 2025

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Contractor for the U.S. Department of Energy
under Contract 89303320DEM000030



P.O. Box 1464
Richland, Washington 99352

200 AREA PROJECT MANAGERS MEETING (PMM) MAY 15, 2025

Date Published
May 2025

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Contractor for the U.S. Department of Energy
under Contract 89303320DEM000030

 **CPC**
Central Plateau
Cleanup Company
P.O. Box 1464
Richland, Washington 99352

APPROVED
By Lynn M Ayers at 11:22 am, May 22, 2025

Release Approval

Date

TRADEMARK DISCLAIMER

Reference herein to any specific commercial product, process, or service by tradename, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

This report has been reproduced from the best available copy.

Printed in the United States of America

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
March – April Data
Agenda
May 15, 2025

Milestones and OU Status- March - April Data

- Integrated Disposal Facility (IDF) (Carmen Rodriguez)
- 200-PW-1/3/6 and 200-CW-5 (Mohammed Gorashi)
- U Plant Canyon (Mohammed Gorashi)
- Canyon Facilities (Mohammed Gorashi)
- 200-CB-1 (B Plant) (Naomi Jaschke)
- 200-CP-1 (PUREX) (Jason Capron)
- 200-CR-1 (Naomi Jaschke)
- 200-DV-1 (Deep Vadose Zone) (Kate Cline)
- 200-EA-1 (Jason Capron/Kate Cline)
- 200-IS-1 (Jason Capron/Kate Cline)
- 200-SW-2 (Jason Capron/Kate Cline)
- 200-SW-1/NRDWL (Manuel Lopez)
- 200-IA-1 (Patrick Brice)
- 200-OA-1, Outer Area, 200-CW-1, 200-CW-3 (Carmen Rodriguez)
- 200-BC-1 and 200-WA-1 (Jason Capron/Kate Cline)
- 200-BP-5 and 200-PO-1 (John Virgin)
- 200-UP-1 (Kate Cline)
- 200-ZP-1 (Kate Cline)
- 200 West Pump & Treat Facility (Patrick Brice)
- M-024 Well Installation (Kaitlyn Nelson)
- Hanford Annual Groundwater Sampling Program Performance
- Central Plateau Milestone Status
- Documents for the Administrative Record and Approved TPA Change Notices

Action Items

Closing Comments (all)

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Attendance List
Joined via Teams
May 15, 2025

NAME	ORGANIZATION	EMAIL
ALEXANDER, DEB	ECY	DEBRA.ALEXANDER@ECY.WA.GOV
AROLA, CRAIG	CPCC	CRAIG_C_AROLA@RL.GOV
AUKERMAN, LAURA	DOH	LAURA.AUKERMAN@DOH.WA.GOV
BOUNDS, CYNTHIA	HMIS	CYNTHIA_L_BOUNDS@RL.GOV
BRASHER, STEPHANIE	HMIS	STEPHANIE_L_BRASHER@RL.GOV
BRICE, PATRICK	DOE	PATRICK.BRICE@HANFORD.GOV
CAPRON, JASON	DOE	JASON.CAPRON@HANFORD.GOV
CARTER, RYAN	CPCC	RYAN_M_CARTER@RL.GOV
CLINE, KATE	DOE	KATE.CLINE@HANFORD.GOV
DAY, GARRETT	ECY	GARRETT.DAY@ECY.WA.GOV
DENTON, ERIC	CPCC	ERIC_T_DENTON@RL.GOV
FROHLING, ELYSE	CPCC	ELYSE_E_FROHLING@RL.GOV
GABE, BOHNEE	HNRTC	GABEB@NEZPERCE.ORG
GLICK, CATHERINE	ECY	CGLI461@ECY.WA.GOV
GLOSSBRENNER, ELLWOOD	DOE	ELLWOOD.GLOSSBRENNER@HANFORD.GOV
GORASHI, MOHAMMED	DOE	MOHAMMED.GORASHI@HANFORD.GOV
JASCHKE, NAOMI	DOE	NAOMI.JASCHKE@HANFORD.GOV
JONES, MICHELLE	ECY	MICHELLE.JONES@ECY.WA.GOV
LEPAGE, JANE	DOH	JANE.LEPAGE@DOH.WA.GOV
LIEBRECHT, TABITHA	ECY	TLIE461@ECY.WA.GOV
LOPEZ-LOPEZ, MANNY	DOE	MANUEL.LOPEZ-LOPEZ@HANFORD.GOV
MCCARTNEY, ANNE	EPA	MCCARTNEY.ANNE@EPA.GOV
MEDINA, AHTZIRY	YN	AMEDINA@YNERWM.COM
NELSON, KAITLYN	DOE	KAITLYN.NELSON@HANFORD.GOV
O'MARA, LAURA	CPCC	LAURA_K_OMARA@RL.GOV
ROBSON, KALI	YN	KROBSON@YNERWM.COM
SCHRAMM, GEOFF	EPA	SCHRAMM.GEOFF@EPA.GOV
SERAFIN, BILLIE	CPCC	BILLY_J_SERAFIN@RL.GOV
SICILIA, TOM	ODOE	TOM.SICILIA@ENERGY.OREGON.GOV
SINGLETON, DEBORAH	CPCC	DEBORAH_G_SINGLETON@RL.GOV

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Attendance List
Joined via Teams
May 15, 2025

NAME	ORGANIZATION	EMAIL
TOSCH, MCLURE	YN	MTOSCH@YNERWM.COM
TURNER, MIKE	HMIS	MICHAEL_J_TURNER@RL.GOV
WANG, LI	YN	LWANG@YNERWM.COM
VIRGIN, JOHN	DOE	JOHN.VIRGIN@HANFORD.GOV

**Tri-Party Agreement (TPA)
 200 AREA PROJECT MANAGERS MEETING
 Meeting Minutes Approval
 200 Area Groundwater and Source Operable Units
 May 15, 2025**

SIGNATURES:

In accordance with the Tri-Party Agreement Section 4.1, Project Manager Role, any agreements and commitments resulting from the meeting will be prepared and signed by all parties as soon as possible after the meeting. The undersigned indicate by their signatures (or their delegate’s signature) that these meeting minutes reflect the actual discussion during this meeting. Signatures denote concurrence with the agreements and commitments resulting from this meeting and do not imply agreement with statements made during this meeting. Attachments to these meeting minutes are provided for informational purposes only.

APPROVAL: NAOMI JASCHKE Digitally signed by NAOMI JASCHKE
Date: 2025.05.28 08:38:49 -07'00' **DATE:** _____
200 Area Project Manager, HFO

APPROVAL: KELLY EBERT Digitally signed by KELLY EBERT
Date: 2025.06.09 07:07:05 -07'00' **DATE:** _____
200 Area Project Manager, HFO

APPROVAL: *Debra J. Alexander* Digitally signed by Alexander, Debra (ECY)
Date: 2025.06.12 01:24:27 -07'00' **DATE:** _____
200 Area Project Manager, Ecology

APPROVAL: *GS* Digitally signed by Schramm, Geoff
Date: 2025.06.09 09:04:36 -07'00' **DATE:** _____
200 Area Project Manager, EPA

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

M-016-200

Integrated Disposal Facility – IDF

Ecology Lead

HFO – C. Rodriguez, CPCCo – Tim Wintle, Bob Bullock

Milestone M-062-57: *Integrated Disposal Facility Operational.*

- Due Date: 9/30/2023, Status: Completed 4/03/2023, reference letter [23-PFD-000808](#) submitted to Ecology.
- Final Class 3 Permit Modification (Active-Life): Complete - issued Sep 25, 2024 (24-NWP-160). Includes merging with the Class 3 Permit Modification for the Leachate Collection System.
- A revised Draft Class 1 permit modification to add a topographical map of IDF to Part A of the dangerous waste permit. Completed 03/04/2025.
- Permit modification documenting procedure for performing the loading calculation for operation of equipment on the cell floor. Completed 02/13/2025.
- Draft Class 1 permit modification to incorporate the SWTRD and make clarifications to Appendix BB. Completed 03/07/2025.
- Miscellaneous facility projects including lighting upgrades on the exterior of the inspection buildings and in the equipment laydown area, and paving of the entrance roads into IDF have been completed.
- Performed Mock-up of ILAW container shipment from WTP to IDF using glass filled containers.

Regulatory Agency Comments: None

200-PW-1/3/6 and CW-5

EPA Lead

HFO – M. Gorashi, CPCCo – Deborah Singleton

- Limited funding is provided to support replanning.
- Please note that EPA has not agreed to any delays in this schedule and expects the RD/RAWP schedule to be followed since it is an enforceable part of the remedial action work plan. Any proposed changes to the schedule need to be discussed in a timely manner.
- A limited RD/RAWP revision was completed to update the schedule for the PW-3 and CW-5 remediation scope.

Regulatory Agency Comments: None

U Plant Canyon

EPA Lead

HFO – M. Gorashi, CPCCo – TBD “Will be updated when information is available”.

Milestone M-016-200A: *Complete U Plant canyon (221 U facility) demolition.*

- Due Date: 9/30/2024, Status: In Abeyance. Milestone identified to be In Abeyance by Inter-Agency Management Integration Team ([IAMIT Determination 2021-002](#)) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-016-200B: *Complete U Plant (221 U facility) Barrier Construction.*

- Due Date: 9/30/2027, Status: In Abeyance. Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

Reference [EPA letter dated 9/18/2024](#), “Deadline in 221-U Facility ROD for TRUW Shipment” regarding the D10 Container that was removed from the 221-U Facility (U Plant Canyon) in 2012 and is currently stored in the CWC awaiting shipment to WIPP.

- EPA letter states, within 180 days, by 3/17/2025, negotiate revised due dates for the two existing 221-U Facility interim milestones (M-016-200A and M-016-200B) and new 2 interim milestones for disposal of the RH TRUW and development of a draft Remedial Action Completion Report (RACR) for EPA review once the remedy has been fully constructed according to the ROD and RD/RA Work Plan.
- U Plant Canyon scope will be negotiated under the [Agreement in Principle \(AIP\)](#) to negotiate the M-015, M-016, M-085 major and interim milestones.

Regulatory Agency Comments: None

Canyon Facilities

EPA/Ecology Lead

HFO – M. Gorashi, CPCCo –Deborah Singleton

Surveillance & Maintenance Activities:

- Drafted work packages to support upcoming filter changes at B Plant and REDOX.
- Completed HEPA filter changeout at PUREX.
- Completed roof/structure inspections of ancillary buildings around REDOX.
- Continued demobilization activities at PUREX, 231Z, and 224B.

B Plant:

Milestone M-085-76: *Initiate Response Actions for B Plant Remedial/Removal Action Work Plan.*

- Due date: 9/30/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

REDOX:

- Nothing new to report.

PUREX:

Milestone M-085-84: *Initiate Response Actions for PUREX in accordance with Schedule in Approved Remedial/RAWP.*

- Due date: 9/30/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Milestone M-085-84B: *Complete Demolition of PUREX Ancillary Facilities 203A Building/Tank Yard and 205A Building.*

- Due date: 9/30/2023, Status: Completed 9/18/2023.
- Facility status change forms ([FSCF 211A D4-PUREX-007](#), [FSCF 203A D4-PUREX-005](#) and [FSCF 205A D4-PUREX-006](#)) were signed March 6 and March 10 and are in the Administrative Record.

Milestone M-085-84C: *Complete Infrastructure Upgrades to Support Demolition Preparation of the PUREX Complex.*

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

- Due date: 1/31/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Milestone M-085-84D: *Initiate Utility System Isolations for the PUREX Complex.*

- Due date: 9/30/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Milestone M-085-85: *Complete 202A PUREX Canyon Cold and Dark Indices to Establish Electrical/Mechanical Isolation.*

- Due date: 9/30/2024, Status: Completed 9/05/2024.
- Reference HFO letter [24-PFD-0070](#), which documents completion of this milestone on 9/05/2024.

Milestone M-085-86: *Submit a Modification to the PUREX RAWP a Schedule for White Powder Removal.*

- Due date: 3/30/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Regulatory Agency Comments: EPA – Requesting discussion on interim milestones for U Plant scope.

200-CB-1 (B Plant)

Ecology Lead

HFO – Naomi Jaschke, CPCCo – Elyse Frohling

- Nothing new to report. No FY25 work planned.

Milestone M-085-70: *Submit to Ecology a RI/FS Work Plan for 200-CB-1.*

- Due date: 09/30/2019; Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-037-28: *Submit a Coordinated Closure (CC) Proposal as a permit modification request for TSDs in 221-B Canyon Facility.*

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-CB-1 OU, but no later than 9/30/2034; Status: On Schedule.

Regulatory Agency Comments: None

200-CP-1 (PUREX)

Ecology Lead

HFO – Jason Capron, CPCCo – Elyse Frohling

- Ecology comments on the Draft RI/FS Work Plan were resolved 5/2/24. The document is being prepared for final Rev, 0 approval awaiting a TPA Milestone date for Chapter 6 “Project Schedule”.

Milestone M-037-29: *Submit Coordinated Closure Proposal as a permit modification request pursuant to WAC 173-303-830(4) for the following TSD Units: PUREX Tunnels 1 and 2 and all TSD Units in the PUREX Canyon Facility.*

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-CP-1 OU, but no later than 9/30/2034;
Status: On Schedule.

Regulatory Agency Comments: None

200-CR-1 (REDOX)

EPA Lead

HFO – Naomi Jaschke, CPCCo – Elyse Frohling

- Nothing new to report.

Milestone M-085-90: *Submit Remedial Investigation/Feasibility Study Work Plan for 200-CR-1 to EPA*

Due date: 09/30/2026; Status: At Risk.

Regulatory Agency Comments: EPA does not consider this at risk until formal notification has been received as part of the comprehensive cleanup negotiations.

200-DV-1

Ecology Lead

HFO – Kate Cline, CPCCo – Ryan Carter

- Experiments testing different technologies for deployment in the vadose zone, perched water, or as a permeable reactive barrier at the water table below 200-DV-1 OU continue.

Milestone M-015-110B: *Submit Corrective Measures Study & Feasibility Study Report and Proposed Plan/Proposed Corrective Action Decision for the 200-DV-1 OU to Ecology.*

- Due date: 09/30/2023, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

**The volume of groundwater treated, and mass of constituents extracted from 200-DV-1 Perched Water
During March – April 2025**

Month	Volume (gal)	Uranium (kg)	Technetium-99 (Ci)
March	28,000	5.01	4.5x10 ⁻³
April	23,000	4.63	4.1x10 ⁻³

Note - numbers shown are estimates; actual numbers are reported in the annual P&T reports.

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Cumulative values of the volume of groundwater treated and mass of constituents extracted from 200-DV-1 Perched Water

	Volume (gal)	Uranium (kg)	Technetium-99 (Ci)
Cumulative (2019 to current)	1,868,000	368.8	2.8x10 ⁻¹
Cumulative FY2025	93,000	33.44	2.49x10 ⁻²
Cumulative FY2024	261,000	50.89	3.43x10 ⁻²
Cumulative FY2023	308,000	71.1	5.57x10 ⁻²
Cumulative FY2022	307,000	64.5	5.17 x10 ⁻²
Cumulative FY2021	310,000	66	5.29 x10 ⁻²
Cumulative FY2020	208,000	38.4	3.57x10 ⁻²
Cumulative FY2019	294,000	48.8	3.71x10 ⁻²

Note - Numbers shown are estimates; actual numbers are reported in the annual P&T reports.

Note - Values include treatability test extraction and removal action extraction.

Note - Interpolated data method was used to recalculate mass constituents extracted and volume of groundwater treated

Regulatory Agency Comments: None

200-EA-1

Ecology Lead

HFO – Jason Capron/Kate Cline, CPCCo – Elyse Frohling

- 200-EA-1 RI/FS Work Plan, Draft B was submitted to Ecology on June 11, 2024, for review (reference letter [24-SGD-0029](#)). Review was extended to November 14, 2024 (reference Ecology letter [24-NWP-158](#)). Ecology comments received November 14, 2024 (reference [24-NWP-210](#)). HFO is dispositioning Ecology comments and is preparing for additional meetings to resolve comments. HFO and Ecology agreed to an extension for comment disposition to June 16, 2025 (reference [24-NWP-221](#)).

Milestone M-015-92B: *Submit RFI/CMS & RI/FS Report and Proposed Corrective Action Decision/Proposed Plan for the 200-EA-1 OU (Central Plateau 200 East Inner Area) to Ecology.*

- Due date: 11/30/2022, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-037-20: *Submit Coordinated Closure Proposal for 4 Specified TSDs if Requesting Use of Alternative Closure Requirements*

- Due date: Submit concurrently with M-015-92B (currently In Abeyance).

Milestone M-037-21: *Submit Coordinated Closure Proposal as a permit modification request pursuant to WAC 173-303-830(4) for the following TSD Units: 216-A-29 Ditch, 216-A-36B Crib, 216-A-37-1 Crib, and 216-B-63 Trench.*

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-EA-1 OU, but no later than 9/30/2034.
- Status: On Schedule.

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Milestone M-015-92E: *Submit Draft CCF to Establish Schedule for Activities in the 200-EA-1 OU RFI/CMS/RI/FS Work Plan.*

- Due Date: 1/31/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Regulatory Agency Comments: None

200-IS-1

Ecology Lead

HFO – Jason Capron/Kate Cline, CPCCo – Dave Becker

- Nothing new to report. No FY25 work planned.

Milestone M-015-112: *Submit Draft B, 200-IS-1 OU Pipeline System Waste Sites RFI/CMS/RI/FS work plan to Ecology, including a schedule of completion dates for major tasks and deliverables.*

- Due date: 11/30/2020, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-92F: *Submit Draft CCF with Date for Milestone M-015-112 for Submittal of 200-IS-1 OU RFI/CMS/RI/FS WP.*

- Due date: 7 days after approval of the 200-EA-1 OU Work Plan, Rev. 0, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Milestone M-015-92C: *Submit the RFI/CMS & RI/FS Report and Proposed Corrective Action Decision/Proposed Plan for the 200-IS-1 OU to Ecology.*

- Due date: 3/31/2023, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-037-25: *Submit CCP for Inactive SST Components Outside WMAs if Requesting Alternative Closure Requirements.*

- Due date: Submit concurrently with M-015-92C (currently In Abeyance)

Milestone M-037-24: *Submit Coordinated Closure Proposal as a permit modification request pursuant to WAC 173-303-830(4) for the following TSD Units: 241-CX Tank System (CX-70, CX-71, and CX-72) and Inactive SST Components outside the WMAs.*

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-IS-1 OU, but no later than 9/30/2034.
Status: On Schedule.

Regulatory Agency Comments: None

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

200-SW-2

Ecology Lead

HFO – Jason Capron/Kate Cline, CPCCo – Dave Becker

- Nothing new to report. No FY25 work planned.

Milestone M-015-93C: *Initiate Characterization Field Work for 200-SW-2 Operable Unit Landfills.*

- Due date: 09/30/2018, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-93B: *Submit RFI/CMS & RI/FS Report and Proposed CAD/PP for 200-SW-2 OU.*

- Due date: 01/31/2023, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-037-26: *Submit CCP for Green Island TSDs in LLBG if Requesting Use of Alternative Closure Requirements.*

- Due date: Submit concurrently with M-015-93B (currently In Abeyance).

Milestone M-037-27: *Submit Coordinated Closure Proposal as a permit modification request pursuant to WAC 173-303-830(4) for the following TSD Units: Low-Level Burial Grounds Green Islands*

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-SW-2 OU, but no later than 9/30/2034. Status: On Schedule.

Milestone M-037-30: *Submit a Class 3 DWP with 90% Design and Proposed Closure Schedule for LLBG Trenches 31 and 34*

- Due Date: 9/30/2033, Status: On Schedule.
- [TPA CCF M-37-23-01](#) approved 3/22/2024 established this milestone.

Target Date M-037-30-T01: *Submit a Class 3 DWP with Post-Closure Schedule for LLBG Trenches 31 and 34*

- Due Date: 180 days after Ecology's approval of the 90% cover design submitted in Milestone M-037-30. Status: On Schedule.
- [TPA CCF M-37-23-01](#) approved 3/22/2024 established this target date.

Target Date M-037-30-T02: *Submit a Construction Quality Assurance Plan as Class 3 DWP for LLBG Trenches 31 and 34*

- Due Date: 9/30/2033. Status: On Schedule.
- [TPA CCF M-37-23-01](#) approved 3/22/2024 established this milestone.

Regulatory Agency Comments: None

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

200-SW-1/NRDWL

Ecology Lead

HFO – M. Lopez, CPCCo – Bob Bullock

- The 60% design for the NRDWL cover is complete.
- On 4/25/2023, RL and Ecology approved TPA Change Control Form M-16-23-01, which created two new TPA interim Milestones M-016-210 and M-016-211 for submittal of permit modification requests for closure of NRDWL, including the contiguous SWL.
- Final Status closure plan for NRDWL per agreement and in coordination with TPA Milestones M-016-210 and M-016-211. The plan was formally submitted to Ecology on February 22, 2024, by HFO letter. Drafted plan accepted and locked down by Ecology on May 15, 2024 [24-NWP-100].
- The section on soil gas monitoring is “RESERVED”. Ecology will internally discuss the current soil gas monitoring at locations around the perimeter of SWL. The soil gas monitoring at NRDWL ended with the conclusion of the NRDWL soil gas study in 1997.

Milestone M-016-210: *Submit PMR with 90% Design for Final Landfill Cover, Including Closure Schedule for NRDWL and SWL.*

- Due date: 08/31/2026, Status: On Schedule.

Milestone M-016-211: *Submit PMR with Updated Post-Closure Pan, Including Groundwater Monitoring Plan for NRDWL and SWL.*

- Due date – 180 days after Ecology’s approval of the 90% cover design submitted in Milestone M-016-210; Status: On Schedule.

Regulatory Agency Comments: ECY (possibly EPA) request meeting to discuss the reported correlation between precipitation and leachate recovery. DOE/RL-2015-21, Rev 10.

200-IA-1

EPA and Ecology Joint Lead

HFO – Patrick Brice, CPCCo – Dave Becker

- The Focused Feasibility Study (FFS) for the 200-IA-1 OU was transmitted to EPA and Ecology as Draft A on March 25, 2022. EPA and Ecology reviewed the Draft A document; EPA transmitted review comments on April 21, 2022, and Ecology transmitted review comments on April 28, 2022. On June 2, 2022, as a result of comments received preparation of the FFS and Proposed Plan was paused to facilitate planning for supplemental characterization of representative sites.
- Supplemental characterization field work began on May 29, 2024, with the collection of near-surface soil samples. Subsurface sampling via direct push began on September 11, 2024, and was completed March 2, 2025.
- Completed supplemental characterization data verification and validation April 30, 2025.

Regulatory Agency Comments: ECY requests meeting to discuss data once preliminary results are available. (Kim Welsch, Cascade Galasso-Irish).

200-OA-1, Outer Area, 200-CW-1, and 200-CW-3

EPA Lead

HFO – C. Rodriguez, CPCCo – Travis Creach

- Nothing new to report. No FY25 work planned.

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Milestone M-015-38B: *Submit FS/PP for 200-CW-1, 200-CW-3 and 200-OA-1 OUs to EPA.*

- Due date: 07/31/2023, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-037-22: *Submit CC Proposal for 2 Specified TSDs if Requesting Use of Alternative Closure Requirements.*

- Due Date: Submit concurrently with M-015-38B (currently In Abeyance).

Milestone M-037-23: *Submit Coordinated Closure Proposal as a permit modification request pursuant to WAC 173-303-830(4) for the following TSD Units: 216-B-3 Main Pond system and 216-S-10 Pond and Ditch.*

- Due Date: Within 270 days of the last CAD/ROD signature for the 200-OA-1 OU, but no later than 9/30/2034; Status: On Schedule.

Regulatory Agency Comments: Ecology asking about doing a cost of removing railroad lines for future use.

200-BC-1 and 200-WA-1

EPA Lead

HFO – Jason Capron/Kate Cline, CPCCo – Elyse Frohling

- 200-WA-1 RI/FS and 200-BC-1 Work Plan have been revised to incorporate the RASCAL approach and address other EPA work plan requested changes. The final Revision 1 was transmitted and approved 3/7/24.
- Completed 200-BC-1 modeling per the work plan (Task 4).
- DQO presentation for 200-BC-1 presented to EPA March 6, 2025. Continuing with development of a supplemental characterization sampling and analysis plan.

Milestone M-015-98: *Complete remedial investigation of U Plant related waste sites located in 200-WA-1 in accordance with the WA-1 RI/FS Work Plan.*

- Due date 06/30/2019, Status: In Abeyance.
- Milestone identified to be In Abeyance by IAMIT Determination 2021-002 until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-99: *Complete remedial investigation of PFP related waste sites located in 200-WA-1 in accordance with the 200-WA-1 and 200-BC-1 RI/FS Work Plan.*

- Due date 12/31/2019, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-84: *Complete RI of 200-WA-1 and 200-BC-1 Waste Sites in Accordance with RI/FS Work Plan.*

- Due date 12/31/2021, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-91B: *Submit FS/PP for the 200-BC-1/200-WA-1 OUs to EPA.*

- Due date 07/31/2023, Status: In Abeyance.
- Milestone identified to be In Abeyance by [IAMIT Determination 2021-002](#) until such time as the Parties agree to an enforceable date for the milestones or the Adaptive Milestone Approach is discontinued.

Milestone M-015-91D: *Submit Draft CCF to Establish Schedule for Activities in the 200-WA-1 & 200-BC-1 OUs RI/FS Work Plan.*

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

- Due Date: 01/31/2025, Status: In Abeyance.
- On December 2, 2024, the Parties signed an [AIP](#) to enter into formal negotiations on TPA Major Milestones M-015-00, M-016-00, and M-085-00 and interim milestones, placing this milestone in abeyance.

Regulatory Agency Comments: None

200-BP-5 and 200-PO-1

Ecology Lead

HFO – John Virgin, CPCCo – Elyse Frohling

Five of the six Addenda to the Remedial Design/Remedial Action Work Plan for the Interim Remedial Action have been completed. The Sampling and Analysis Plan for Drilling the Performance Monitoring Plan Wells in the 200-BP-5 and 200-PO-1 Groundwater Operable Units (DOE/RL-2020-41-ADD 6) is being developed.

- The HFO transmitted the Hydrologic Test Plan (ADD 4) Rev. 0 and Remedial Design Report (ADD 5) Rev. 0 on April 24, 2025.
- Comment responses to Agency review of the Draft A 200-BP-5 PMP Drilling SAP (ADD6) are anticipated to be completed in early May.
- Extraction wells 299-E27-157 in 200-BP-5 near the C Farm and 299-E27-240 near the A-AX Farms in 200-PO-1 have been completed. Sampling began in February under the Performance Monitoring Plan (Addendum 1 to the RD/RA Work Plan). Concentrations of technetium-99 in February were 6,050 pCi/L and 2,820 pCi/L for wells 299-E27-157 and 299-E25-240 respectively. These wells will be connected to the pump and treat network later in 2025.
- Comment concurrence for HFO review for DOE/RL-2014-31 *Sampling and Analysis Plan for the 200-PO-1 Groundwater Operable Unit* has been completed, and preparation of Draft A is ongoing. This SAP identifies monitoring to support the post-RI period until a remedial action decision is made.
- Clearance and transmittal process for the Draft A DOE/RL-2014-33 *Sampling and Analysis Plan for the 200-BP-5 Groundwater Operable Unit* is anticipated to be completed in May. This SAP identifies monitoring to support the post-RI period until a remedial action decision is made. A DQO presentation was provided on April 23, 2025, in preparation for document submittal.

**The volume of groundwater treated, and mass of constituents extracted from 200-BP-5
During March - April 2025**

Month	Volume (mgal)	Cyanide (kg)	Uranium (kg)	Technetium-99 (Ci)	Iodine-129 (Ci)*
March	6.46	2.05	1.8	7.29x10 ⁻²	3.25x10 ⁻⁵
April	6.96	2.19	1.9	7.8x10 ⁻²	3.49x10 ⁻⁵

Note – values shown are accumulated and reported in the annual P&T reports.

* Removed from the aquifer but not treated before injection into the 200 West aquifer with the 200 West P&T treated effluent.

Cumulative volume of treated groundwater and mass of constituents extracted from 200-BP-5

	Volume (mgal)	Cyanide (kg)	Uranium (kg)	Technetium-99 (Ci)	Iodine-129 (Ci)*
Cumulative (2019 to current)	515.66	233.75	162.6	6.64	3.7 x10 ⁻³
Cumulative CY2025	25.03	8.83	7.06	0.29	1.21x10 ⁻⁴
Cumulative CY2024	76.75	32.39	24.1	0.95	3.8 x10 ⁻⁴
Cumulative CY2023	80.72	35.42	25.4	1.00	5.9 x10 ⁻⁴
Cumulative CY2022	82.59	37.80	25.4	0.96	5.1 x10 ⁻⁴

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Cumulative CY2021	83.80	43.55	24.9	1.09	6.2 x10 ⁻⁴
Cumulative CY2020	60.40	19.00	26.3	1.01	5.3x10 ⁻⁴
Cumulative CY2019	84.83	48.92	23.3	1.06	8.2x10 ⁻⁴

Note – numbers shown are estimates; actual numbers are reported in the annual P&T reports.

Note – values include treatability test extraction and removal action extraction.

Note- Interpolated method was used to calculate mass of extracted contaminants.

* Removed from the aquifer but not treated before injection into the 200 West aquifer with the 200 West P&T treated effluent.

Regulatory Agency Comments: None

200-UP-1

EPA Lead

HFO – Kate Cline, CPCCo – Ryan Carter

- Submitted Draft A of DOE/RL-2014-27, Rev 3, Sampling and Analysis Plan for Remediation Wells in the 200-UP-1 Operable Unit to EPA for review.

The volume of groundwater treated, and mass of constituents extracted from 200-UP-1 during – March - April 2025

Month	Volume (kgal)	Carbon Tetrachloride (kg)	Chromium (kg)	Uranium (kg)	Nitrogen in NO3 (kg)*	Nitrate (kg)*	Iodine-129 (Ci)*	Technetium-99 (Ci)	Cyanide (kg)
March	10,380	0.9	0.37	0.46	1,054	4,667	3.23E-05	2.5E-02	NR
April	10,933	0.9	0.38	0.50	1096	4,858	3.48E-05	2.6E-02	NR

	Volume (kgal)	Carbon Tetrachloride (kg)	Chromium (kg)	Uranium (kg)	Nitrogen in NO3 (kg)*	Nitrate (kg)*	Iodine-129 (Ci)*	Technetium-99 (Ci)	Cyanide (kg)
Cumulative (2019 to current)	766,409	151.31	26.80	57.87	103,990**	460,674**	2.39E-03	2.02	766,409
Cumulative FY2025	54,826	6.32	2.40	3.15	338	30,305	1.96E-04	1.62E-01	54,826
Cumulative FY2024	115,025	14.05	3.83	9.28	12,894	57,124	3.48E-04	2.61 x10 ⁻¹	NR
Cumulative CY2023	108,467	15.43	3.50	6.47	13,456	59,612	3.18E-04	2.49 x10 ⁻¹	NR
Cumulative CY2022	110,562	19.66	3.70	5.89	14,767	65,417	3.87E-04	2.67x10 ⁻¹	NR
Cumulative CY2021	110,975	23.72	4.04	8.04	15,256	67,584	3.27E-04	3.09x10 ⁻¹	NR
Cumulative CY2020	128,445	36.51	4.88	11.30	19,183	84,982	4.48E-04	3.78E-01	NR
Cumulative CY2019	123,331	36.50	4.46	13.07	21,488	95,193	3.69E-03	3.97E-01	NR

Note - numbers shown are estimates; actual numbers are reported in the annual P&T reports.

Note- Interpolated method used to calculate mass of extracted contaminants. Note – values include available data from extraction before 200W Pump & Treat operation.

* Removed from the aquifer, but not treated before injection into the 200 West aquifer with the 200 West P&T treated effluent

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

** Represents the total nitrate mass in extracted groundwater by the 200-UP-1 remedial action. Nitrate treatment was suspended in October 2019 for the 200-ZP-1 OU Optimization Study. Prior to suspension of biological treatment, a total of 132,308 kg of nitrate (29,888 kg nitrogen in NO₃) was removed from groundwater extracted from the 200-UP-1 OU.

NR = not reported

Regulatory Agency Comments: None

200-ZP-1

EPA Lead

HFO – Kate Cline, CPCCo – Ryan Carter

- Continued implementing the Optimization Study Plan (DOE/RL-2019-38, Rev. 0) to collect the data needed to evaluate remedy performance enhancements and remedy configuration changes associated with P&T operations.
- Submitted Draft A of DOE/RL-2008-78, Addendum 1, *200-ZP-1 Operable Unit Remediation Well Installation Sampling and Analysis Plan* to EPA for review.
- Sampling for total and free cyanide continues at monthly and quarterly frequencies at wells within the ZP-1 OU and at the 200 West P&T. Monitoring wells 299-W10-26 and 299-W14-18 continue to be above 200 µg/L federal MCL for total cyanide (993 and 928 µg/L, respectively in March 2025).
- The 200-ZP-1 extraction well pumping continued at an average flow rate of approximately 2,915 gpm and 2,789 gpm for March and April, respectively.

The volume of groundwater treated, and mass of constituents extracted from 200-ZP-1 during March and April 2025

	Volume (kgal)	Carbon Tetrachloride (kg)	Trichloro-ethylene (kg)	Chromium (kg)	Nitrogen in NO ₃ (kg)*	Nitrate (kg)*	Technetium-99 (Ci)	Iodine-129 (Ci)*	Cyanide (kg)
March	130,110	177.82	1.11	14.6	14,321	63,399	0.101	3.36x10 ⁻⁴	1.40
April	120,466	174.32	1.11	14.2	13,357	59,130	0.962	3.14x10 ⁻⁴	1.40

Note - numbers shown are estimates; actual numbers are reported in the annual P&T reports.

* Removed from the aquifer, but not treated before injection into the 200 West aquifer with the 200 West P&T treated effluent

Cumulative values of the volume of groundwater treated and mass of constituents extracted from 200-ZP-1

	Volume (kgal)	Carbon Tetrachloride (kg)	Trichloro-ethylene (kg)	Chromium (kg)	Nitrogen in NO ₃ (kg)*	Nitrate (kg)*	Technetium-99 (Ci)	Iodine-129 (Ci)*	Cyanide (kg)
Cumulative (2019 to current)	7,000,896	10,417	73.92	758.74	702,747	3,110,877	6.52	1.87x10 ⁻²	51.8
Cumulative CY2025	491,845	669.06	4.90	54.78	53,897	238,588	0.383	1.26x10 ⁻³	4.54
Cumulative CY2024	1,241,104	1,620	12.58	129.79	125,249	554,445	1.01	3.25x10 ⁻³	6.78
Cumulative CY2023	1,064,562	1,117	9.11	107.52	99,911	442,278	0.92	2.94x10 ⁻³	5.93
Cumulative CY2022	1,055,841	1,416	10.24	110.55	104,375	462,045	0.96	2.84x10 ⁻³	8.15
Cumulative CY2021	1,059,652	1,546	10.83	114.29	103,750	459,276	1.09	2.67x10 ⁻³	8.79
Cumulative CY2020	909,138	1,898	12.11	114.98	100,008	442,709	1.04	2.47x10 ⁻³	8.06
Cumulative CY2019	886,306	1,929	12.00	100.88	89,061	394,253	0.91	2.55x10 ⁻³	8.45

Note - numbers shown are estimates; actual numbers are reported in the annual P&T reports.

Note- Interpolated method used to calculate mass of extracted contaminants. Note – values include available data from extraction before 200W Pump & Treat operation.

* Removed from the aquifer, but not treated before injection into the 200 West aquifer with the 200 West P&T treated effluent

**Nitrate treatment ceased for 200-ZP-1 OSP

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Regulatory Agency Comments: None

200 West Pump & Treat Facility

EPA Lead

HFO –Patrick Brice, CPCCo – Ryan Carter

- Pumping continued at the 200 West P&T and flows currently average 3,262gpm.
- The installation of the third air stripper is ongoing with the tower install complete.
- BP-5/PO-1 Tc-99 IX Train: The IX trains were installed in 289TA. Currently the BP-5/PO-1 wells and pumping system in 200E area are pending completion. The installation of mechanical and electrical systems will continue in the future.

The volume of groundwater treated, and mass of constituents removed by the 200 West P&T Facility during –March - April 2025

Month	Volume k(gal)	Carbon Tetrachloride (kg)	Trichloroethylene (kg)	Chromium (kg)	Tc-99 (Ci)	Cyanide** (kg)	Uranium (kg)
March	146,980	179.04	1.17	0.27	1.35E-01	3.48	7.54
April	138,377	175.60	1.18	0.30	1.38E-01	3.62	7.28

Note - numbers shown are estimates; actual numbers are reported in the annual P&T reports and annual groundwater reports.

Note – I-129 not included because not removed by the 200W Pump & Treat facility.

Cumulative values of the volume of groundwater treated and mass of constituents removed by the 200 West P&T Facility

	Volume (kgal)	Carbon Tetra-chloride (kg)	Trichloro-ethylene (kg)	Chromium (kg)	Nitrogen in NO3 (kg)*	Nitrate (kg)*	Tc-99 (Ci)	Cyanide (kg)	Uranium (kg)
Cumulative (2019 to current)	8,291,450	10,006	67.46	111.8	351,299	348,684	11.97	293.0	577.71
Cumulative FY2025	974,041	1,179	7.72	1.75	NA	NA	0.94	23.47	51.01
Cumulative FY2024	1,440,388	1,191	9.49	3.42	NA	NA	1.69	37.08	78.83
Cumulative FY2023	1,254,061	1,124	7.98	3.82	NA	NA	1.70	41.38	100.47
Cumulative FY2022	1,250,338	1,427	9.18	5.42	NA	NA	1.76	45.97	94.70
Cumulative FY2021	1,256,238	1,559	9.83	4.99	NA	NA	2.04	52.50	98.43
Cumulative FY2020	1,098,780	1,923	11.52	87.58	NA	NA	1.90	27.32	75.87
Cumulative FY2019	1,094,762	1,953	11.64	99.44	351,299	1,555,133	1.93	57.64	85.09

Note – numbers shown are estimates; actual numbers are reported in the annual P&T reports. Note- Interpolated method used to calculate mass of treated contaminants.

Note – I-129 not included because not removed by the 200W Pump & Treat facility.

Note– While Tritium is a COC it is not tracked specifically for removal through the P&T like other COCs.


* Nitrate treatment was suspended in October 2019 for the 200-ZP-1 OU Optimization Study Chromium treatment was reduced as well.

**Cyanide is tracked but not treated in the 200W Pump & Treat facility, reported values are extracted concentrations.

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

2W EXTRACTION WELLS AVERAGE DAILY FLOW RATES
Current GPM = 3,261 Capacity = 3,261 / 3,500 = 93%
7d Average GPM = 3,262 Capacity = 3,262 / 3,500 = 93%
30d Average GPM = 3,203 Aves: 100% Avail;

Data validated thru last completed month; current month is not yet validated.

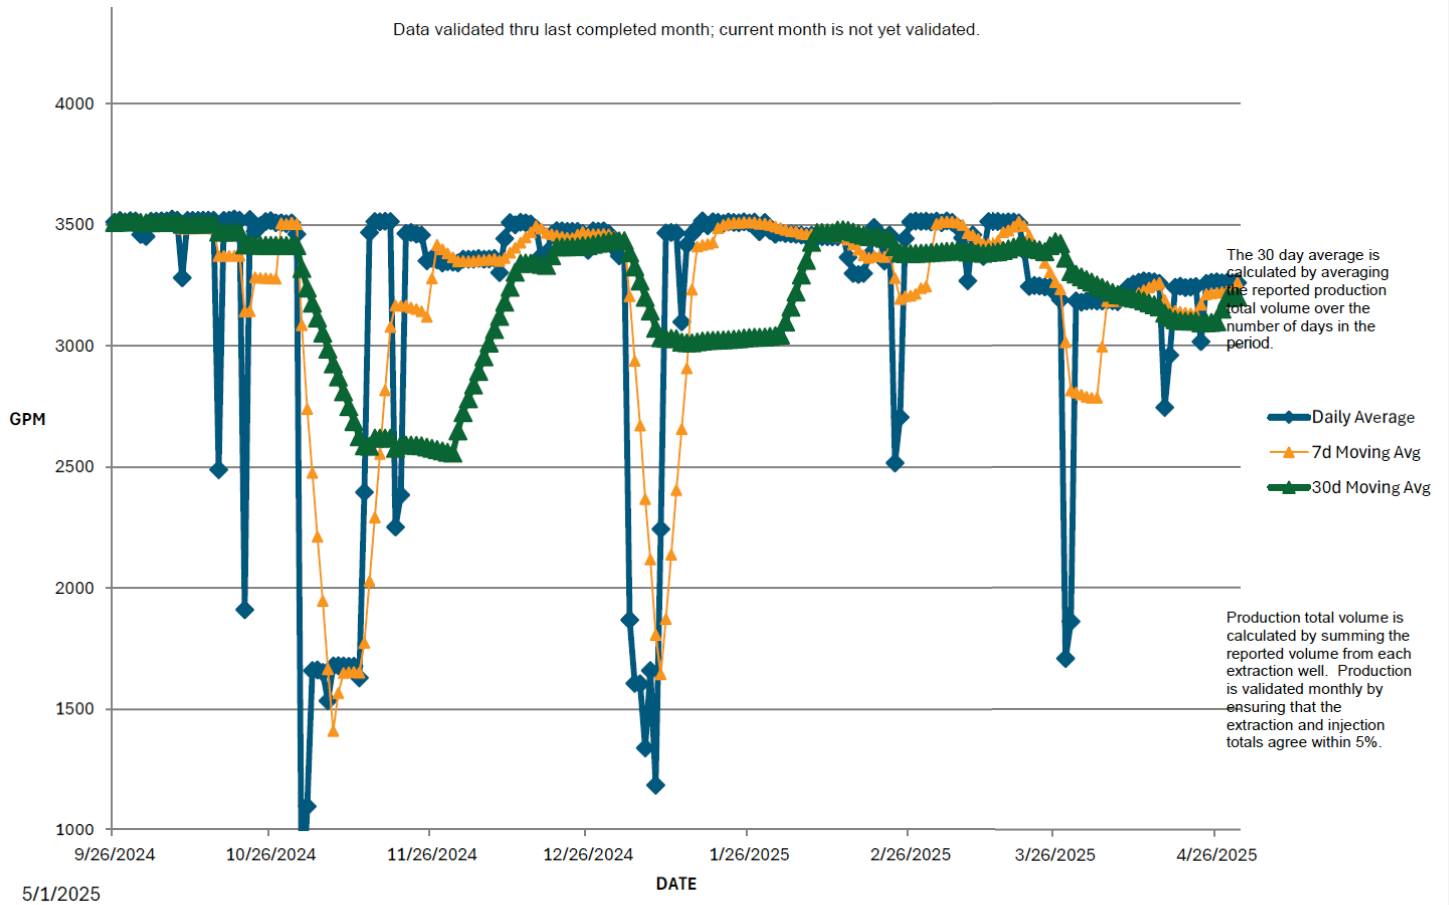

Regulatory Agency Comments: None

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

M-024 Well Installation

Ecology Lead

HFO – Kaitlyn Nelson, CPCCo - Jennifer Richart

Milestone M-024-75: *Complete the Construction of All Well Listed for CY24 and Before.*

- Due Date 12/31/2024, Status: Completed 12/04/2024 (reference letter [24-SGD-0065](#)).

Target Date M-024-76-T01: *Conclude Discussion of Well Commitments Initiated Under M-024-58.*

- Due date 08/01/2025, Status: On Schedule.

Milestone M-024-76: *Complete the Construction of All Well Listed for CY25 and Before.*

- Due Date 12/31/2025, Status: On Schedule
 - Four wells including 199-B4-19 (D0146), 199-B4-20 (D0396), 299-W12-6 (D0473), and 299-W11-116 (D0474) are complete.
 - One well 299-W14-35 (D0316) is in progress.

Target Date M-024-77-T01: *Conclude Discussion of Well Commitments Initiated Under M-024-58.*

- Due date 08/01/2026, Status: On Schedule.

Milestone M-024-77: *Complete the Construction of All Well Listed for CY26 and Before.*

- Due Date 12/31/2026, Status: On Schedule

Target Date M-024-78-T01: *Conclude Discussion of Well Commitments Initiated Under M-024-58.*

- Due date 08/01/2027, Status: On Schedule.


Milestone M-024-78: *Complete the Construction of All Well Listed for CY27 and Before.*

- Due Date 12/31/2027, Status: On Schedule

Regulatory Agency Comments: ECY requests clarification on locations for wells listed as “TBD”.

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

Hanford Annual Groundwater Sampling Program Performance
HFO - TBD, CPCCo – C. Arola

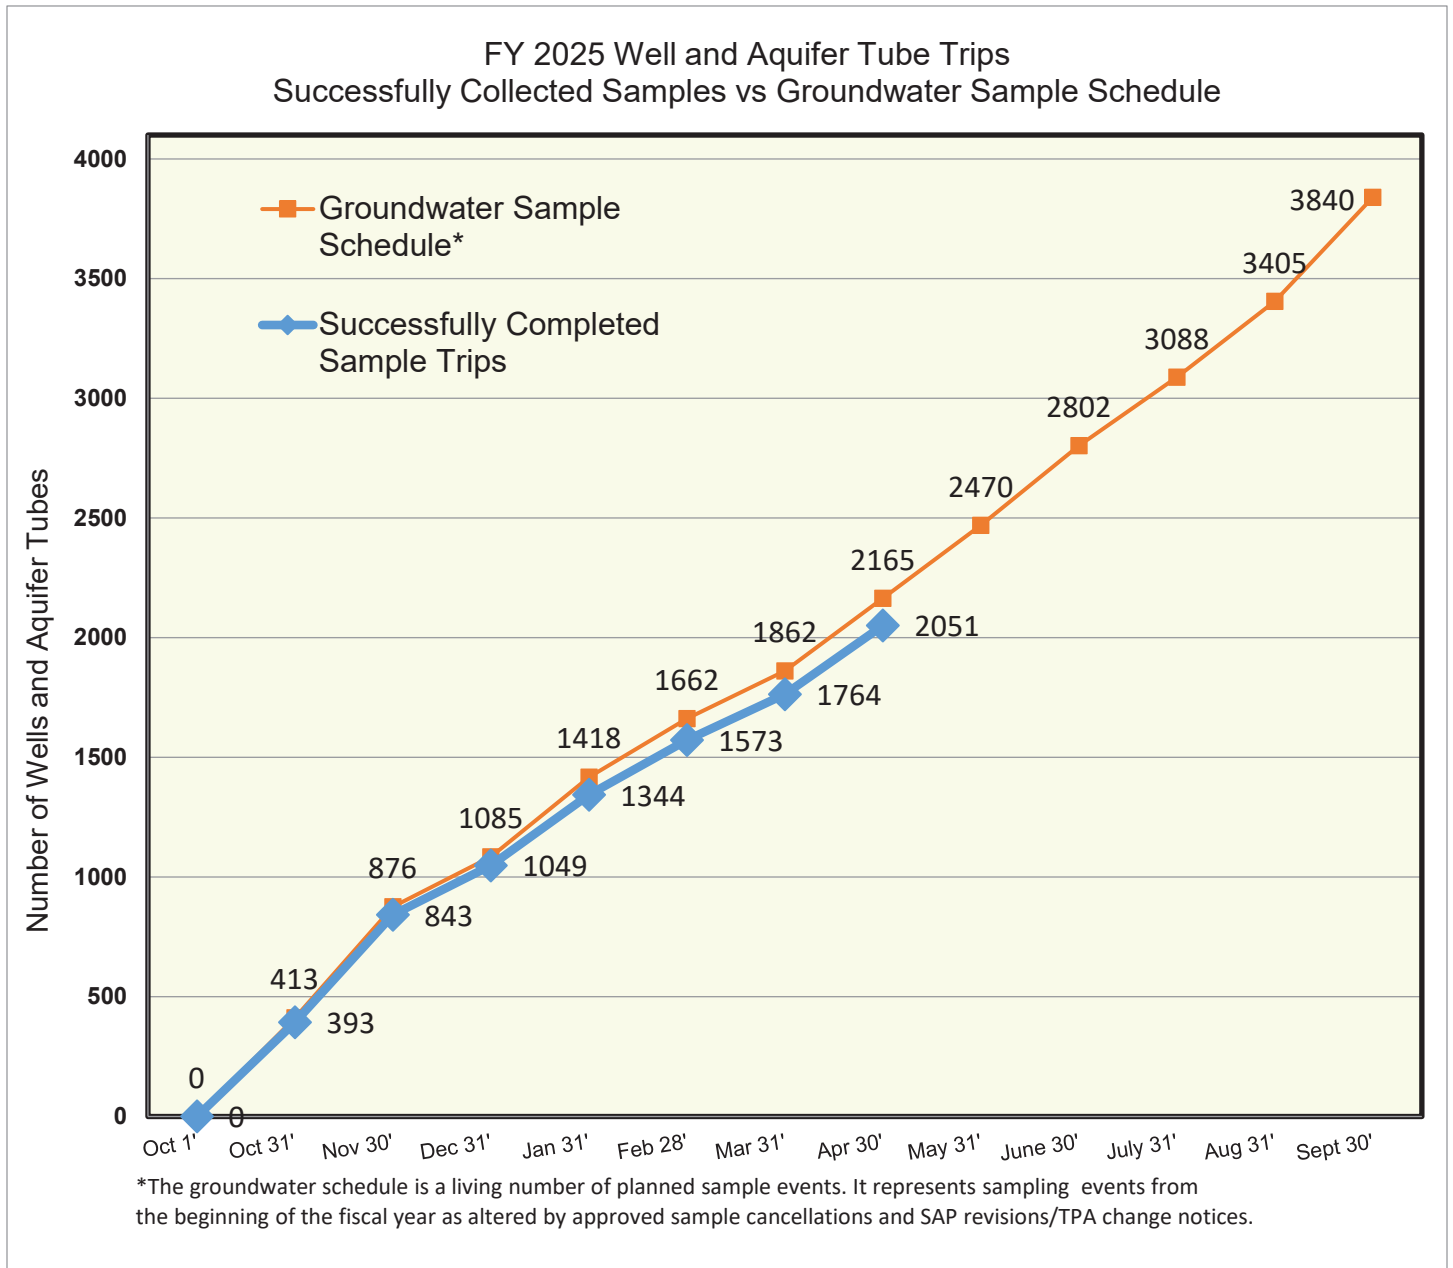

*The groundwater schedule is a living number of planned sample events. It represents sampling events from the beginning of the fiscal year as altered by approved sample cancellations and SAP revisions/TPA change notices.

Regulatory Agency Comments: None

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

Central Plateau Milestone Status

MS#	Title	Due Date
Fiscal Year 2018		
M-015-93C	Initiate Characterization Field Work for the 200-SW-2 OU Landfills	9/30/2018 In Abeyance
Fiscal Year 2019		
M-015-98	Complete Remedial Investigation of U Plant Related Waste Sites located in 200-WA-1 in accordance with the WA-1 RI/FS Work Plan	6/30/2019 In Abeyance
M-085-70	Submit to Ecology a RI/FS Work Plan for 200-CB-1	9/30/2019 In Abeyance
Fiscal Year 2020		
M-015-99	Complete Remedial Investigation of PFP Related Waste Sites located in 200-WA-1 in accordance with the 200-WA-1 and 200-BC-1 RI/FS Work Plan.	12/31/2019 In Abeyance
Fiscal Year 2021		
M-015-112	Submit Draft B 200-IS-1 RFI/CMS/RI/FS Work Plan to Ecology with Schedule Dates	11/30/2020 In Abeyance
Fiscal Year 2022		
M-015-84	Complete RI of 200-WA-1 and 200-BC-1 Waste Sites in Accordance with RI/FS Work Plan	12/31/2021 In Abeyance
Fiscal Year 2023		
M-015-92B	Submit RFI/CMS, RI/FS Study report and Proposed CAD/PP for 200-EA-1	11/30/2022 In Abeyance
M-037-20	Submit Coordinated Closure Proposal for the 4 Specified TSDs if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-92B
M-015-93B	Submit RFI/CMS & RI/FS Report and Proposed CAD/PP for 200-SW-2 OU	1/31/2023 In Abeyance
M-037-26	Submit Coordinated Closure Proposal for Green Island TSDs in LLBG if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-93B
M-015-92C	Submit RFI/CMS & RI/FS Report and PCAD/PP for 200-IS-1 OU to Ecology	3/31/2023 In Abeyance
M-037-25	Submit Coordinated Closure Proposal for Inactive SST Components Outside WMAs if Requesting Alternative Closure Requirements	Submit concurrently with M-015-92C
M-015-38B	Submit FS/PP for 200-CW-1, 200-CW-3 and 200-OA-1 OUs	7/31/2023 In Abeyance
M-037-22	Submit Coordinated Closure Proposal for the 2 Specified TSDs if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-38B
M-015-91B	Submit FS/PP for the 200-BC-1 and 200-WA-1 OUs to EPA	7/31/2023 In Abeyance
M-015-110B	Submit CMS & FS and PCAD/PP for 200-DV-1 OU	9/30/2023 In Abeyance
Fiscal Year 2024		
M-015-91D	Submit Draft CCF to Establish Schedule for Activities in the 200-WA-1 & 200-BC-1 OUs RI/FS Work Plan	01/31/2025 In Abeyance
M-015-92E	Submit Draft CCF to Establish Schedule for Activities in the 200-EA-1 OU RFI/CMS/RI/FS Work Plan	01/31/2025 In Abeyance

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

MS#	Title	Due Date
M-085-84C	Complete Infrastructure Upgrades to Support Demolition Preparation of the PUREX Complex	01/31/2025 In Abeyance
Fiscal Years 2025 and Beyond		
M-024-75	Complete the Construction of All Wells Listed for CY24 and Before	12/31/2024 Completed 12/04/2024
M-085-86	Submit a Modification to the PUREX RAWP a Schedule for White Powder Removal	3/30/2025 In Abeyance
M-085-76	Initiate response actions for the B Plant geographic area	9/30/2025 In Abeyance
M-085-84	Initiate response actions for the PUREX Operable Unit	9/30/2025 In Abeyance
M-085-84D	Initiate Utility System Isolations for the PUREX Complex	9/30/2025 In Abeyance
M-015-92F	Submit Draft CCF with Date for Milestone M-015-112 for Submittal of 200-IS-1 OU RFI/CMS/RI/FS WP	Due date is 7 days after approval of the 200-EA-1 OU WP, Rev 0 In Abeyance
M-085-01	Submit change package to establish a date for Major Milestone M-085-00	6/30/2026 On Schedule
M-015-00	Complete the RI/FS (or RFI/CMS) Process for All Non-Tank Farm Operable Units	6/30/2026 At Risk
M-024-77-T01	Conclude discussions of well commitments initiated under M-024-58	8/01/2026 On Schedule
M-016-210	Submit PMR with 90% Design for Final Landfill Cover, Including Closure Schedule for NRDWL and SWL	8/31/2026 On Schedule
M-016-211	Submit PMR with Updated Post-Closure Pan, Including Groundwater Monitoring Plan for NRDWL and SWL	180 days after Ecology's approval of the 90% cover design submitted in Milestone M-016-210 On Schedule
M-085-90	Submit Remedial Investigation/Feasibility Study Work Plan for 200-CR-1 to EPA	9/30/2026 At Risk
M-024-77	Complete the Construction of All Wells Listed for CY26 and Before	12/31/2026 On Schedule
M-026-07E	Evaluation of Tritium Treatment Technology to EPA & Ecology	3/31/2027 On Schedule
M-024-78-T01	Conclude discussions of well commitments initiated under M-024-58	8/01/2027 On Schedule
M-016-200B	Complete U Plant (221 U Facility) barrier construction	9/30/2027 In Abeyance
M-024-78	Complete the Construction of All Wells Listed for CY27 and Before	12/31/2027 On Schedule

**Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025**

Documents Submitted to the Administrative Record

Document Number	Title	Signature Date	Referencing Document Number	Referencing Document Title
<u>D4-PUREX-005</u>	Facility Status Change Form for 203A	3/19/2025	N/A	N/A
<u>D4-PUREX-006</u>	Facility Status Change Form for 205A	3/19/2025	N/A	N/A
<u>D4-PUREX-007</u>	Facility Status Change Form for 211A	3/18/2025	N/A	N/A
<u>DOE/HFO-2024-45, Rev. 0</u>	Final Status Baseline/Background Data Summary for the Liquid Effluent Retention Facility and 200 Area Effluent Treatment Facility	01/08/2025	N/A	N/A
<u>ECF-200PO1-24-0072, Rev. 0</u>	FY24 Remedial Process Optimization Modeling Analysis for WMA C/A-AX 200-PO-1	3/11/2025	N/A	N/A
<u>ECF-HANFORD-25-0020, Rev. 0</u>	Calculation of Critical Means for use in Calendar Year 2025 RCRA Groundwater Monitoring	4/08/2025	N/A	N/A
<u>CPC-2500852</u>	200 AREA PROJECT MANAGERS MEETING (PMM) JANUARY 17, 2025	03/10/2025	N/A	N/A

Regulatory Agency Comments: None

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Milestones and O.U. Status
March - April 2025 Data
May 15, 2025

Approved TPA Change Notices

Number	Signature Date	Document Title	Description of Change

Regulatory Agency Comments: None

Monthly Performance Report Assessment

The HFO Project Managers have identified no outstanding issues with the preceding month's Environmental Performance Report for this scope.

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Action Items List, May 15, 2025

OPEN ACTION ITEM TRACKING

Action #	Action/Subject	Assigned To	Owed To	Assigned Date	Original Due Date	Adjusted Due Date	Status
----------	----------------	-------------	---------	---------------	-------------------	-------------------	--------
