Waste Tank Summary Report for Month Ending March 31, 2001



EDMC

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

CH2MHILL Hanford Group, Inc.

Richland, Washington

Contractor for the U.S. Department of Energy
Office of River Protection under Contract DE-AC06-99RL14047

LEGAL DISCHARMEN	•

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

This report has been reproduced from the best available copy. Available in paper copy and microfiche.

Available electronically at http://www.doc.gov/bridge. Available for a processing fee to the U.S. Department of Energy and its contractors, in paper, from: U.S. Department of Energy Office of Scientific and Technical Information P.O. Box 62 Oak Ridge, TN 37831-0062

Oak Ridge, TN 37831-0062 phone: 865-576-8401 fax: 865-576-5728

email: reports@adonis.osti.gov(423) 576-8401

Available for sale to the public, in paper, from: U.S. Department of Commerce National Technical Information Service 5285 Port Royal Road Springfield, VA 22161

Springfield, VA 22161 Phone: 800-553-6847 fax: 703-605-6900

email: orders@ ntis.fedworld.gov

online ordering:

http://www.ntis.gov/ordering.htm

Printed in the United States of America

ENGINEERING CHANGE NOTICE

Page 1 of ____ Proj. ECN

	1. ECN 668005
į	Proi.

2. ECN Category (mark	one)	3. Originator's Name, Orga	nization, MSIN, and Telephone	No.	4. USQ Required?	5. Date
Supplemental		B. M. Hanlon, Inv	ventory & Flowsheet	Eng.	☐ Yes 🛛 No	04/25/01
Direct Revision	X	R3-72, 373-2053			L 100 L 110	7 0 1, 2 3, 0 1
Change ECN		6. Project Title/No./Work O	rder No.	7. Bldg./Sy	s./Fac. No.	8. Approval Designator
Temporary		Waste Tank Summar]		
1		Month Ending Marc	ch 31, 2001		I/A	N/A_
Standby		Document Numbers Cha sheet no. and rev.)	nged by this ECN (includes	10. Related	ECN No(s).	11. Related PO No.
Supersedure				١ .	- /-	35.45
Cancel/Void		HNF-EP-0182, Rev.		<u> </u>	r/A	N/A
12a. Modification Work		12b. Work Package No.	12c. Modification Work Comp	leted	12d. Restored	I to Original Condition (Temp. by ECNs only)
Yes (fill out Blk. 1	2b)		17/2		J C. CLENG	
No (NA Biks. 12b),	N/A	N/A Design Authority/Cog. Engine	er Signature	& Design Author	N/A ority/Cog. Engineer Signature &
12c, 12a)		<u> </u>	Date Date	Der Orginature	G Deagn Addit	Date Cignature C
13a. Description of Cha	inge	•	13b. Design Baseline Docume	nt? 🗌 Yes	⊠ No	
	•		•			
Complete revis	ion					
Compress 10115						
,						
1						
}						
		1.				
Computer gener	atec	1:				
	m****		11 mm = == 1			
File: \\APUUI\	TWRS	SHAR\SHARE\BETTYH	I/HNE-ED I			
			•			
Size: 6.85MB (7,18	(6,432 bytes)	a A	1		
{			Brill			
Modified: Wedn	esda	ıy, A pril 25, 2001	10:53:46 AM Brill 70:08:56 Am -	22	7. Fac	
(- MAY 2,2001	70:08:32 / 100	Tm). #	
}		may 2.1	2001 8:56 AM -		5-3-01.	
		ا زیمرد میدرد	8. 30 m			
ĺ						
}						
14a, Justification (mark	one)	14b. Justification Details				
Criteria Change	, []	1				
· -		 This ECN is beir	ng generated to upda	ate wast	e tank farm	Summary
Design Improvement	لسا	information.	., journation to apar		o outin Eurin .	- minut 1 J
Environmental					•	
Facility Deactivation		1				
As-Found		i [
Facilitate Const.		.[
Const. Error/Omission	, \sqcap	ł				
Design Error/Omissio		1				
		MCIN and no of conice)				DELEACE CTAND
) 13, distribution (include 	патте	, MSIN, and no. of copies)				RELEASE STAMP
Distribution 1	ist	attached following	a document			
processación 1.			g			
}					E .	<i>/</i>
					DATE:	A HANCOUL
[T HANFORD L
			•		STA: ∠	RELEASE 3 10.
Ì						X — 1
(MAY N	3 2004~
[1	V LUU! —

						1. ECN (use no. from	pg. 1)
	ENGINEERIN	NG CHANGE N	OTICE	i 	Page 2 of _2	668005	
16. Design Verification Required	17. Cost Impact ENGINEERI	NG	COI	NSTRU	UCTION	18. Schedule Impact	(days)
☐ Yes	Additional 🗆 \$		Additional 🔲	s		Improvement 🔲	
⊠ No	Savings		Savings 🔲	\$		Delay	
19. Change Impact Revie	ew: Indicate the related docum i in Block 13. Enter the affects	nents (other than the en	gineering docume	ents ide	entified on Side 1) that	will be affected by	
SDD/DD		Seismic/Stress A				ibration Manual	
Functional Design C	riteria 🗍	Stress/Design Re	•			nysics Procedure	
Operating Specificat		Interface Control				lultiple Unit Listing	
Criticality Specification	_	Calibration Proce	_		•	edures/Specification	
Conceptual Design F		Installation Proce	dure		Compone	•	
Equipment Spec.		Maintenance Pro	cedure		ASME Co		
Const. Spec.		Engineering Prod	edure		Human F	actor Consideration	
Procurement Spec.		Operating Instruc	tion		Computer	r Software	
Vendor Information		Operating Proces	lure		Electric C	ircuit Schedule	
OM Manual		Operational Safe	y Requirement		ICRS Pro	cedure	
FSAR/SAR		1EFD Drawing			Process (Control Manual/Plan	
Safety Equipment Lie		Cell Arrangemen	Drawing		Process F	Flow Chart	
Radiation Work Perm	<u>=</u>	Essential Materia	•		Purchase	Requisition	
Environmental Impac		Fac. Proc. Samp.	Schedule		Tickler Fil	le	
Environmental Repo	_	Inspection Plan		님			
Environmental Permi	it LJ nents: (NOTE: Documents lis	Inventory Adjustn		<u> </u>			
	/A						
21. Approvals	Signature	Date			Signature	Date	
Design Authority			Design Agent	t			
Cog. Eng. B.M. Han	non Bon Harden	4/25/01	PE				
Cog. Mgr. N.W. Kin	rch NWKml	4/30/01	QA				
QA			Safety				
			,				
Safety			Design				
Environ.		-	Environ				
Other			Other				
							
			0504071451				
				a Contr	<u>ENERGY</u> rol Number that tracks t	the .	
			Approval Sign	ia (U/B			
			ADDITIONAL		-		
			ADDITIONAL				

WASTE TANK SUMMARY REPORT FOR MONTH **ENDING MARCH 31, 2001**

BM HANLON

CH2M HILL Hanford Group, Inc. Richland, WA 99352 U.S. Department of Energy Contract DE-AC27-99RL14047

EDT/ECN: ECN~668005

UC:

Cost Center:

Charge Code:

B&R Code:

Total Pages: 90

Key Words: REPORT, WASTE TANK SUMMARY

Abstract: See page iii of document

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-08, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.

ID. а

Approved For Public Release

(1) Document Number **RECORD OF REVISION** HNF-EP-0182 Page _1_ (2) Title WASTE TANK SUMMARY REPORT FOR MONTH ENDING MARCH 31, 2001 Change Control Record Authorized for Release (3) Revision (4) Description of Change - Replace, Add, and Delete Pages (6) Cog. Mgr. (5) Cog. Engr. Date 153 EDT-631372 BM Hanlon JS Garfield RS 156 Bon Henlen BM Hanlon MUKUL NW Kirch Incorporation of ECN-668005

Waste Tank Summary Report for Month Ending March 31, 2001

B. M. Hanion CH2M HILL Hanford Group, Inc.

Date Published May 2001

Prepared for the U.S. Department of Energy Assistant Secretary for Environmental Management

CH2NHILL Hanford Group, Inc.

P. O. Box 1500 Richland, Washington

Contractor for the U.S. Department of Energy Office of River Protection under Contract DE-AC06-99RL14047

Approved for Public Release; Further Dissemination Unlimited

This page intentionally left blank.

WASTE TANK SUMMARY REPORT

B. M. Hanlon

ABSTRACT

(i) This report is the official inventory for radioactive waste stored in underground tanks in the 200 Areas at the Hanford Site. Data that depict the status of stored radioactive waste and tank vessel integrity are contained within the report. This report provides data on each of the existing 177 large underground waste storage tanks and 63 smaller miscellaneous underground storage tanks and special surveillance facilities, and supplemental information regarding tank surveillance anomalies and ongoing investigations. This report is intended to meet the requirement of U. S. Department of Energy-Richland Operations Office Order 435.1 (DOE-RL, July 1999, Radioactive Waste Management, U. S. Department of Energy-Richland Operations Office, Richland, Washington) requiring the reporting of waste inventories and space utilization for Hanford Tank Farm tanks.

This page intentionally left blank.

TABLE OF CONTENTS

	Page
SUMMARY	
I. WASTE TANK STATUS	
II. WASTE TANK INVESTIGATIONS	
III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS	
Appendixes:	
	A 1
A. MONTHLY SUMMARY	A-1
Tables: 1 Monthly Summary	Δ
2 Tank Use Summary	
3 Pumping Record, and Liquid Status and Pumpable Liquid Remaining in Tanks	
4 Inventory Summary by Tank Farm	
5 Inventory and Status by Tank - Double-Shell Tanks	
6 Inventory and Status by Tank - Single-Shell Tanks	
o mitting and backs of rules barget back a rule time.	
B. PERFORMANCE SUMMARY	R-1
Table:	
1 Summary of Waste Transactions in the Double-Shell Tanks	B-2
2 Comparison of Projected Versus Actual Waste Volumes for Hanford Facilities	
C. DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION	J C-1
	· O-1
Tables:	0.4
1 Double-Shell Tank Waste Inventory	
2 Double-Shell Tank Available Space	C-3
Figures: 1 Total Double-Shell Tank Inventory	C 4
1 Total Double-Shell Tank Inventory	C-4
D. WASTE TANK SURVEILLANCE MONITORING TABLES	D 1
Tables:	TD 17
1 Temperature Monitoring in Watch List Tanks	
3 Additions/Deletions to Watch List Tanks by Year	
4 Single-Shell Tank Monitoring Compliance Status	
6 ENRAF Surface Level Gauge Installation and Data Input Methods	D 1/
7 Tank Monitor and Control System (TMACS)	
/ Tank Monitor and Condot System (TMACS)	
	OT A T
E. MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPE	
SURVEILLANCE FACILITIES	E-1
Tables:	
1 Misc. Underground Storage Tanks and Special Surveillance Facilities (Active)	
2 East Area Underground Storage Tanks and Special Surveillance Facilities (Inac	
3 West Area Underground Storage Tanks and Special Surveillance Facilities (Inac	xive)E-4
F. LEAK VOLUME ESTIMATES	E 1
Table: 1 Single-Shell Tank Leak Volume Estimates	TO 6
1 Surgic-Such Tank Teak Annuic Estiliates	

G. SINGLE-SHELL TANKS INTERIM STABILIZATION, AND CONTROLLED,	
CLEAN, AND STABLE (CCS) STATUS	G-1
Tables:	
1 Single-Shell Tanks Interim Stabilization Status	G-2
2 Single-Shell Tank Interim Stabilization Milestones	G-4
3 Single-Shell Tanks Stabilization Status Summary	G-6
H. TANK AND EQUIPMENT CODE AND STATUS DEFINITIONS	H-1
1 Tank and Equipment Code/Status Definitions	H-2
I. TANK FARM CONFIGURATION, STATUS AND FACILITY CHARTS	I -1
1 High-Level Waste Tank Configuration	I-2
2 Double-Shell Tank Instrumentation Configuration	
3 Single-Shell Tank Instrumentation Configuration	
4 Tank Farm Facilities Chart - East Area	I-5
5 Tank Farm Facilities Chart - West Area	I-6

	ETRIC CON	NVERSION CHART			
1 inch = 2.54 centimeters					
I foot	=	= 30.48 centimeters			
1 gallon		= 3.80 liters			
1 ton = 0.90 metric tons					
	°F=	$\left(\frac{9}{5}$ °C $\right)$ +32			
;		930711 E-01 watts ational Table)			

WASTE TANK SUMMARY REPORT For Month Ending March 31, 2001

Note: Changes from the previous month are in bold print.

I. WASTE TANK STATUS

Category	Quantity	Date of Last Change
Double-Shell Tanks ^b	28 double-shell	10/86
Single-Shell Tanks	149 single-shell	1966
Assumed Leaker Tanks	67 single-shell	07/93
Sound Tanks	28 double-shell 82 single-shell	1986 07/93
Interim Stabilized Tanks	128 single-shell	03/01
Not Interim Stabilized ^c	21 single-shell	03/01
Intrusion Prevention Completed	108 single-shell	09/96
Controlled, Clean, and Stable ^f	36 single-shell	09/96
Watch List Tanks ^{de}	19 single-shell 5 double-shell	09/00 01/01
Total	24 tanks	

Of the 128 tanks classified as Interim Stabilized, 65 are listed as Assumed Leakers. (See Table G-1)

II WASTE TANK INVESTIGATIONS

This section includes all single- or double-shell tanks or catch tanks which are showing surface level or interstitial liquid level (ILL) decreases, or drywell radiation level increases in excess of established criteria.

^b Five double-shell tanks (SY-101 was removed from the list in January 2001) are currently included on the Hydrogen Watch List and are thus prohibited from receiving waste in accordance with "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the National Defense Authorization Act for Fiscal Year 1991, November 5, 1990, Public Law 101-510.

^c Two of these tanks are Assumed Leakers (BY-105, BY-106). (See Table F-1)

^d See Appendix D for more information on Watch List Tanks.

Dates for the Watch List tanks are "officially added to or removed from the Watch List" dates. Eighteen tanks were removed from the Organic Watch List in December 1998; the last two tanks (C-102 and C-103) were removed from the Organic Watch List in August 2000. In December 1999, tank C-106 was removed from the High Heat Load Watch List. In January 2001, DST tank SY-101 was removed from the Hydrogen Watch List. Only the Hydrogen Watch List remains, which contains 19 SSTs and 5 DSTs.

^f The TY tank farm was officially declared Controlled, Clean, and Stable (CCS) in March 1996. The TX tank farm and BX tank farms were declared CCS in September 1996.

A. Assumed Leakers or Assumed Re-leakers: (See Appendix H for definition of "Re-leaker")

This section includes all single- or double-shell tanks or catch tanks for which an off-normal or unusual occurrence report has been issued, or for which a waste tank investigation is in progress, for assumed leaks or re-leaks. Tanks/catch tanks will remain on this list until either a) completion of Interim Stabilization, b) the updated occurrence report indicates that the tank/catch tank is not an assumed leaker, or c) the investigation is completed.

Catch Tank 241-AX-152 - This catch tank was declared an "assumed leaker" on March 23, 2001 by the Plant Review Committee, after an evaluation by the Leak Assessment Team. The water used as test solution was pumped to a double-shell tank on March 1, 2001, after the tank was identified as a potential leaking tank. (Also see item #7, Occurrence Report RP-CHG-Tankfarm-2001-0014).

B. Tanks with increases indicating possible intrusions:

This section includes all single-shell tanks and related receiver tanks for which the surveillance data show that the surface level or ILL has met or exceeded the increase criteria, or are still being investigated.

Candidate Intrusion List: Increase criteria in the following tanks indicate possible intrusions.

Tank 241-B-202 Tank 241-BX-101 Tank 241-BX-103

Tank 241-BY-103

The surveillance data was last reviewed on the tanks listed as having probable liquid intrusions: Memo 74B20-99-045, dated November 22, 1999.

III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS

1. Single-Shell Tank Interim Stabilization - (See Appendix G, page G-4 for further information)

<u>Tank 241-U-105</u> - This tank was Interim Stabilized on March 29, 2001, due to major equipment failure. Total Waste: 353.0 Kgallons; Supernate: none; DIL and DLR: 44.0 Kgallons; PLR: 39.7 Kgallons; Saltcake: 321.0 Kgallons; Sludge: 32.0 Kgallons. Total Pumped 87.5 Kgallons.

<u>Tank 241-U-106</u> - This tank was Interim Stabilized on March 9, 2001. Total Waste: 171.9 Kgallons; Supernate: 1.7 Kgallons; DIL and DLR: 35.8 Kgallons; PLR: 30.2 Kgallons; Saltcake: 170.2 Kgal; no Sludge. Total Pumped: 39.1 Kgal.

2. Single-Shell Tanks Saltwell Jet Pumping (See Table A-6 footnotes for further information)

Tank 241-A-101 - Pumping began May 6, 2000. No pumping since August 2000; a total of 14.1 Kgallons has been pumped from this tank since start of pumping in May 2000.

Tank 241-AX-101 - Pumping began July 29, 2000. No pumping since August 2000; pumping began again on March 22, 2001. In March 2001, a total of 9.8 Kgallons was pumped from this tank; a total of 18.2 Kgallons has been pumped since the start of pumping in July 2000.

Tank 241-S-102 - Pumping problems forced many shutdowns. The pump was replaced and pumping resumed on February 19, 2000. Problems with the new pump forced a shutdown on March 23, 2000. Pumping was interrupted in early June 2000; due to the flushing involved in trying to return to pumping, June pumping resulted in a net addition to the tank. No pumping since June 2000; a total of 56.8 Kgallons has been pumped from this tank since start of pumping in March 1999.

Tank 241-S-109 - Pumping began September 23, 2000. The pumping rate dropped below 0.05 GPM and the pump was shut down on January 27, 2001. The tank is now being evaluated to determine if it can be Interim Stabilized. A total of 145.2 Kgallons has been pumped from this tank (111.0 Kgallons were pumped in 1979 [primary stabilization], and partial isolation in 1982).

Tank 241-SX-101 - Pumping began November 22, 2000. In December 2000, a total of 6.9 Kgallons was pumped; a total of 19.2 Kgallons has been pumped from this tank. The pump failed on December 9, 2000. No pumping since December 2000.

Tank 241-SX-103 - Pumping began October 26, 2000. In March 2001, a total of 3.1 Kgallons was pumped; a total of 113.1 Kgallons has been pumped from this tank since start of pumping in October 2000.

Tank 241-SX-105 - Pumping began August 8, 2000. In March 2001, there was no net removal of tank waste; a total of 151.1 Kgallons has been pumped since start of pumping in August 2000.

Tank 241-U-102 - Pumping began January 20, 2000. During March 2001, a total of 1.8 Kgallons was pumped; a total of 75.8 Kgallons has been pumped from this tank since start of pumping in January 2000.

Tank 241-U-109 - Pumping began March 11, 2000. The saltwell pump was replaced following pump failure in December 2000, and pumping was restarted March 30, 2001. In March 2001, there was no net waste removal from this tank; a total of 65.9 Kgallons has been pumped from this tank since start of pumping in March 2000.

3. 242-A Evaporator Campaign 01-1

More than 800,000 gallons of double-shell tank waste was processed through the 242-A Evaporation facility resulting in the elimination of approximately 640,000 gallons of waste. Campaign 01-1 was completed March 26, 2001. This campaign brings the total to more than 12 million gallons of waste water removed from the tank farms since the restart of the Evaporator in 1994. This evaporation from the double-shell tanks means that more space is made available for the storage of liquid removed from the single-shell tanks. The next 242-Evaporator campaign is scheduled for FY2002.

4. Tank BX-102 Vadose Zone Project Activities Completed

The SST Vadose Zone Project drilling and testing activities near Tank BX-102 were completed in March 2001. A borehole (299-E33-45) was drilled through the postulated uranium plume resulting from the 1951 Tank BX-102 overfill event to confirm the presence of uranium, define its present depth, and survey other contaminants of interest such as Tc-99. Thirty-five split-spoon samples were collected for laboratory analyses. This borehole was decommissioned after collection and analysis of groundwater samples.

5. RP-CHG-TANKFARM-2001-0004, Occurrence Report, "Corrosion Observed in DST Tank 241-AY-101 During Video Inspection of the Annulus Section," Off-Normal Occurrence, Latest Update: March 26, 2001.

Corrosion of the primary and secondary liners of DST AY-101 was observed during video inspections of the tank annulus region in 1999 and 2000. Follow-up video inspections that were completed on January 29, 2001, show more extensive corrosion in localized regions of the primary and secondary liners when viewed from the annulus region.

In addition, ultrasonic testing data collected during March 2001 and evaluated on March 22, 2001, shows localized thinning of approximately 19.4 percent, versus a reporting limit of 20 percent, of a small area on the inside of the primary liner at the previous wasteair interface approximately 343 inches above the bottom of the tank. Thus, corrosion has occurred on both the outside and the inside of the primary liner, and on the inside of the secondary liner. There are no visual or radiological indications of waste leakage from the tank.

An operational restriction has been imposed to limit the waste level in this tank to less than 80 inches until further evaluation can be performed.

An Update or Final report will be submitted no later than May 31, 2001.

6. RP-CHG-TANKFARM-2001-0006, Occurrence Report, "Flammable Gas Level Exceeds Lower Flammability Limit (LFL) at 241-C-101 Riser 1," Off-Normal Occurrence, Latest Update: March 23, 2001.

While performing the required initial flammable gas monitoring at C-101 Riser 1, the flammable gas level was found to be greater than 25% LFL. Upon opening Riser #1, the flammable and toxic gas monitoring detected levels in excess of 100% LFL. The riser was immediately secured in a safe condition. This work activity was in preparation for installation of a buoyancy type (ENRAF) tank liquid-level measuring device.

All work was stopped per the work instruction. Additional flammable gas monitoring samples taken at the C-101 Breather Filter and Manual Tape access points indicated 0% LFL. A grab sample was taken for additional analysis. Entry restrictions were put in place.

An alternate riser was identified that provided direct access to the dome space and dome space monitoring was performed, resulting in 5% LFL in the tank dome space, which is consistent with previous sampling in this tank.

Cause: The engineering drawings identified Riser #1 as a spare and available for use. The work crews discovered the presence of an unknown object in the riser. The configuration is indicative of a possible temperature probe well. The ENRAF liquid level gauge will be installed in a different riser.

No further action is required.

7. RP-CHG-TANKFARM-2001-0014, Occurrence Report, "Catch Tank AX-152 was Identified as a Potential Leaking Tank," Off-Normal Occurrence, Notification Date: March 5, 2001, Latest Update: March 23, 2001.

Based on an engineering evaluation, this catch tank was identified as a potential leaking tank. On March 23, 2001, the Plant Review Committee determined, based on information and a recommendation by the Leak Assessment Team, to declare catch tank AX-152 an "assumed leaker." The water used as a test solution was pumped to a double-shell tank on March 1, 2001, as an immediate action.

8. RP-CHG-TANKFARM-2001-0016, Occurrence Report, "Tank 241-C-107 Dome Surface Indication," Off-Normal Occurrence, Notification Date: March 12, 2001.

During sampling of Single-Shell Tank 241-C-107 by the Characterization Project on March 6, 2001, a video camera was in use to film the dome area of the tank. An indication was observed in the dome or the dome coating that must be further evaluated to determine if it could be a crack.

An investigation of the anomaly inside the top of tank C-107 was completed, and it was concluded the anomaly is not a crack but a shadow cast by features on the surface of the

tank's dome, or ceiling which was caused by a ridge of irregular concrete which protruded between the construction forms when the tank was being built in 1943.

This Occurrence Report will be cancelled.

APPENDIX A MONTHLY SUMMARY

TABLE A-1. MONTHLY SUMMARY TANK STATUS

March 31, 2001

	200	200	
	EAST AREA	WEST AREA	TOTAL
IN SERVICE	25	03	28 (1)
OUT OF SERVICE	66	83	149
SOUND	59	51	110
ASSUMED LEAKER	32	35	67
INTERIM STABILIZED	60	68	128
ISOLATED			
PARTIAL INTERIM	11	30	41
INTRUSION PREVENTION COMPLETE	55	53	108
CONTROLLED, CLEAN, AND STABLE	12	24	36

		WASTE VOLUM	MES (Kgallons))	 .,		-
		200	200		SST	DST	
		EAST AREA	WEST AREA	TOTAL	TANKS	TANKS	TOTAL
SUPERN	ATANT						
AW	Aging waste	1770	0	1770	0	1770	1770
cc	Complexant concentrate waste	3169	1263	4432	0	4432	4432
CP	Concentrated phosphate waste	1088	0	1088	0	1088	1088
DC	Dilute complexed waste	1714	850	2564	1	2563	2564
DN	Dilute non-complexed waste	894	0	894	0	894	894
PD	PUREX/TRUsolids	648	0	648	0	648	648
NCPLX	Non-complexed waste	164	151	315	315	0	315
DSSF	Double-shell slurry feed	5847	168	6015	1039	4976	6015
TOTAL	L SUPERNATANT	15294	2432	17726	1355	16371	17726
SOLIDS							
Sludg	e (includes liquids)	6459	5648	12107	1105 9	1048	12107
Salto	ake (includes liquids)	8106	15910	24016	20808	3208	24016
TOTA	L SOLIDS	14565	21558	36123	31867	4256	36123
TC	ITAL WASTE	29859	23990	53849	33222	20627	53849
AVAILA	BLE SPACE IN TANKS	9882	787	10669	0	10669	10669
DRAINA	BLE INTERSTITIAL LIQUID (2)	1425	2035	3460	3460	(2)	3460
DRAINA	BLE LIQUID REMAINING (2)	2462	2353	4815	4815	(2)	4815

⁽¹⁾ Includes five double-shell tanks on Hydrogen Watch List not currently allowed to receive waste, AN-103, AN-104, AN-105, AW-101, and SY-103. SY-101 was removed from the Hydrogen Watch List in January 2001and will return to service later in the year.

⁽²⁾ Drainable Interstitial Liquid and Drainable Liquid Remaining for single-shell tanks only; not applicable for double-shell tanks

HNF-EP-0182, Rev. 156

TABLE A-2. TANK USE SUMMARY March 31, 2001

					ISOLATED TAN	NKS	
TANK	TANKS AVAILABLE TO RECEIVE		ASSUMED	PARTIAL INTERIM	INTRUSION PREVENTION	CONTROLLED CLEAN, AND	INTERIM STABILIZED
<u>FARMS</u>	WASTE TRANSERS	<u>SOUND</u>	<u>LEAKER</u>	ISOLATED	COMPLETED	STABLE	TANKS
EAST							
Α	0	3	3	2	4	0	5
AN	7 (1)	7	0	0	0	0	0
AP	8	8	0	0	0	0	0
AW	6 (1)	6	0	0	0	0	0
ΑX	0	2	2	1	3	0	3
AY	2	2	0	0	0	0	0
ΑZ	2	2	0	0	0	0	0
В	0	6	10	0	16	0	16
BX	0 -	7	5	0	12	12	12
BY	0	7	5	5	7	0	10
С	0	9	7	3	13	0	14
Total	25	59	32	11	55	12	60
WEST							
S	0	11	1	10	2	0	6
SX	0	5	10	6	9	Ō	11
SY	3 (1)	3	0	0	0	Ō	0
Т	0	9	7	5	11	0	16
TX	0	10	8	0	18	18	18
TY	0	1	5	0	6	6	6
U	0	12	4	9	7	0	11
Total	3	51	35	30	53	24	68
TOTAL	28	110	67	41	108	36	128

⁽¹⁾ Five Double-Shell Tanks on the Hydrogen Watch List are not currently receiving waste transfers (AN-103, 104, 105, AW-101, and SY-103). SY-101 was removed from the Hydrogen Watch List in January 2001 and will return to service later in the year.

TABLE A-3. PUMPING RECORD, LIQUID STATUS AND PUMPABLE LIQUID REMAINING IN TANK FARMS

March 31, 2001

	_	<u>-</u>	Waste Vo	olumes (Kgallons)			-	1
			CUMULATIVE		DRAINABLE	DRAINABLE	PUMPABLE	
TANK	PUMPED	PUMPED FY	TOTAL PUMPED	SUPERNATANT	INTERSTITIAL	LIQUID	SST LIQUID	1
<i>EARMS</i>	<u>THIS MONTH</u>	TO DATE	<u> 1979 TO DATE</u>	LIQUID	LIQUID	<u>REMAINING</u>	<u>REMAINING</u>	-
EAST								
A	0.0	0.0	164.6	503	161	665	622	1
AN	N/A	N/A	N/A	3769	N/A	N/A	N/A	
AP	N/A	N/A	N/A	6276	N/A	N/A	N/A	- [
AW	N/A	N/A	N/A	1864	N/A	N/A	N/A	
AX	9.8	9.8	31.1	368	105	473	447	
AY	N/A	N/A	N/A	579	N/A	N/A	N/A	-1
ΑZ	N/A	N/A	N/A	1770	N/A	N/A	N/A	
В	0.0	0.0	0.0	15	262	277	203	ļ
BX	N/A	0.0	200.2	24	127	N/A	N/A	-
BY	0.0	0.0	1567.8	0	581	581	498	
С	0.0	0.0	103.0	126	189	315	207	
Total	9.8	9.8	2066.7	15294	1425	2311	1977	
WEST								Ì
S	0.0	21.7	1075.1	76	636	712	578	
SX	3.1	204.6	662.2	134	323	457	384	1
SY	N/A	N/A	N/A	2113	N/A	N/A	N/A	
Т	0.0	0.0	245.7	29	218	246	168	
ΤX	N/A	0.0	1205.7	9	297	N/A	N/A	
TY	N/A	0.0	29.9	0	53	N/A	N/A	
U	1.8	33.1	367.2	71	508	579	493	- [
Total	4.9	259,4	3585.8	2432	2035	1994	1823	
TOTAL	14.7	269.2	5652.5	17726	3460	4305	3600	

N/A = Not applicable for Double-Shell Tank Farms, and Single-Shell Tank Farms which have been declared Controlled, Clean and Stable (BX, TX, TY).

					SUPERN	ATANT	LIQUIL	VOL	UMES (Kgallo		SOLIE	S VOLUI	ME_
TANK	TOTAL	AVAIL			-					<u></u>			SALT	
EARM	WASTE	SPACE	_AW	CC	CP	DC	DN	<u>PD</u>	NCPLX	DSSE	TOTAL	SLUDGE	CAKE	TOTAL
EAST												}]
Α	1479	0	0	0	0	0	0	0	0	503	503	574	402	976
AN	5517	2463	0	1780	0	0	247	0	0	1742	3769	0	1748	1748
AP	6365	2755	0	1389	1088	1604	37	0	0	2158	6276	0	89	89
AW	3357	3483	0	0	0	0	140	648	0	1076	1864	571	922	1493
AX	816	0	0	0	0	0	0	0	0	368	368	26	422	448
AY	828	1132	0	0	0	109	470	o	0	0	579	249	0	249
AZ	1927	49	1770	0	0	0	٥	0	0	0	1770	157	0	157
В	1909	0	0	0	0	0	0	0	15	0	15	1211	683	1894
BX	1490	0	0	0	0	0	0	0	24	0	24	1259	207	1466
BY	4387	0	0	0	0	0	0	0	0	0	٥	754	3633	4387
С	1784	0	0	0	0	1	0	0	125	0	126	1658	0	1658
Total	29859	9882	1770	3189	1088	1714	894	848	184	5847	15294	8459	8106	14585
WEST		!									ł			
S	5056	0	0	0	٥	0	0	0	75	1	76	1184	3796	4980
sx	3731	0	0	0	0	0	0	0	0	134	134	927	2673	3600
SY	2633	787	0	1263	0	850	0	0	o	0	2113	71	449	520
Т	1877	0	0	0	0	0	0	0	29	0	29	1703	145	1848
TX	6810	0	0	0	0	0	0	0	9	О	9	697	6104	6801
ΤΥ	639	0	0	0	0	0	0	0	o	o	0	529	110	639
U	3244	0	0	0	0	0	0	0	38	33	71	537	2633	3170
Yotel	23990	787	0	1263	۵	850	0	0	151	168	2432	5848	15910	21558
TOTAL	53840	10669	1770	4432	1089	2584	894	648	315	8015	17726	12107	24016	36123

TABLE A-5. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

March 31, 2001

		TANK	STATUS						SOLID	S VOLUME			PHOTOS/	VIDEOS	
									SLUDGE	· -	SALTCAKE	-			SEE
				EQUIVA-		AVAIL.	SUPER-	SLUDGE	LIQUID	SALTCAKE	LIQUID				FOOTNOT
				LENT	TOTAL	SPACE	NATANT	(includes	(15%	(includes	(25%	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	TANK	WASTE	WASTE	(1)	LIQUID	liquid)	porosity)	liquid)	porosity)	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MATL	STATUS	USE	INCHES	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
												<u></u>			
								ANK FARI	M STATU	<u>s</u>	•		1		
AN-101	DN	SOUND	DRCVR	89.8	247	893	247	0	0	0	0	06/30/99			l
AN-102	CC	SOUND	CWHT	383.6	1055	85	966	0	0	89	22	06/30/99			
AN-103	DSS	SOUND	CWHT	348.0	957	183	500	0	0	457	114	06/30/99	10/29/87		1
AN-104	DSSF	SOUND	CWHT	362.5	1052	88	603	0	0	449	112	06/30/99	08/19/88		
AN-105	DSSF	SOUND	CWHT	410.2	1128	12	639	0	0	469	122	06/30/99	01/26/88		1
AN-106	CC	SOUND	CWHT	13,8	38	1102	21	0	0	17	4	06/30/99			
AN-107	CC	SOUND	CWHT	378.2	1040	100	793	0	0	247	62	06/30/99	09/01/88		
									 - <u>-</u> -						
7 DOUBL	-SHELL 1	ANKS		TOTALS	5517	2463	3769	0	0	1748	436	L			<u></u>
							AD T	ANE EAD	M STATU	2					
AP-101	DSSF	SOUND	DRCVR	404.7	1113	27	1113	0	<u>vistatu.</u> O	2 0	0	05/01/89			1
AP-102	CP	SOUND	DRCVR		1088	52	1088	0	0	0	0	07/11/89			1
AP-103	CC	SOUND	DRCVR		281	859	281	۱ ٥	o	0	0	05/31/96			1
AP-103	CC	SOUND	DRCVR		1108	32	1108	l ő	o	0	0	10/13/88			
AP-105	DSSF	SOUND	CWHT	412.4	1134	6	1045	ة ا	0	89	22	06/30/99		09/27/98	
AP-106	DC	SOUND	DRCVR		622	518	622	١ ٥	0	0	0	10/13/88		03/27/30	Ί
					982	158	982	lő	0	0	0				
AP-107	DC	SOUND	DRCVR		37	1103	37	"	0	0	0	10/13/88			
AP-108	DN	SOUND	DRCVR	13.5	3/	1103	3'	ľ	U	U	U	10/13/88			1
8 DOUBL	E-SHELL T	ANKS		TOTALS	6365	2755	6276	0	0	89	22	<u> </u>			
			·												
						<u>A</u>	W TANK	FARM ST	<u>ATUS</u>						
AW-101	DSSF	SOUND	CWHT	409.5	1126	14	751	0	o	375	94	10/31/00	03/17/88		1
AW-102	DN	SOUND	EVFD	30.9	85	1055	55	0	0	30	8	01/31/01	02/02/83		
AW-103	PD	SOUND	DRCVR	305.5	840	300	477	316	79	47	12	06/30/99			1
AW-104	DN	SOUND	DRCVR	114.9	316	824	85	0	0	231	58	06/30/99	02/02/83		1
AW-105	PD	SOUND	DRCVR	154,9	426	714	171	255	38	0	0	06/30/99	, , , , ,		
AW-106	DSSF	SOUND	SRCVR		564	576	325	0	О	239	60	06/30/99	02/02/83		
															<u> </u>
6 DOUBL	E-SHELL	TANKS		TOTALS	3357	3483	1864	571	117	922	232	i			

TABLE A-5. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

March 31, 2001

		TANK	STATUS										PHOTO	S/VIDEOS	[
									SLUDGE		SALTCAKE				SEE
				EQUIVA-		AVAIL.	SUPER-	SLUDGE	LIQUID	SALTCAKE	LIQUID				FOOTNO1
				LENT	TOTAL	SPACE	NATANT	(includes	(15%	(includes	(25%	SOLIDS	LAST	LAST	FOR
	WASTE			WASTE	WASTE	(1)	LIQUID	liquid)	porosity)	liquid)	porosity)	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MATL	STATUS	USE	INCHES	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGE
							AY TA	NK FARM	STATUS						
AY-101	DC	SOUND	DRCVR	67.3	185	796	109	76	11	0	0	06/30/99	12/28/82		1
AY-102	DN	SOUND	DRCVR	233.8	643	337	470	173	26	o	0	10/31/00	04/28/81		1
2 DOUBL	E-SHELL 1	TANKS		TOTALS	828	1132	579	249	39	0	0			<u></u>	<u> </u>
							AZ TA	NK FARM	STATUS						
AZ-101	AW	SOUND	CWHT	338.5	931	49	879	52		0	0	06/30/98	08/18/83		1
AZ-102	AW	SOUND	DRCVR	362.2	996	0	891	105	16	0	0	06/30/99	10/24/84		
2 DOUBL	E-SHELL 1	TANKS		TOTALS	1927	49	1770	157	24	0	0				<u> </u>
							SY TA	NK FARM	STATUS						
SY-101	CC	SOUND	CWHT	352.7	970	170	887	0	0	83	21	06/30/99	04/12/89		1
SY-102	DC	SOUND	DRCVR	334.9	921	219	850	71	11	0	0	06/30/99	04/29/81		ł
SY-103	CC	SOUND	CWHT	269.8	742	398	376	0	0	366	92	06/30/99	10/01/85		
DOUBL	E-SHELL 1	TANKS		TOTALS	2633	787	2113	71	11	449	113				
	OTAL				20627	10669	16371	1048	191	3208	B03		ļ		<u> </u>

Note: +/- 1 Kgal differences are the result of computer rounding

Available Space C	<u>alculations Used in this Documer</u>	nt
Tank Farms	(Most Conservative)	
AN, AP, AW, SY	1,140,000 gal (414.5 in.)	1,140 Kgal
AY, AZ (Aging Waste)	980,000 gal (356,4 in.)	980 Kgal

NOTE: Supernate + Sludge (includes liquid) + Saltcake (includes liquid) = Total Waste

⁽¹⁾ Available Space volumes include restricted space, - see Appendix C tables for allocation of these restrictions.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
March 31, 2001

		These	volumes a	ne the re	sult of	engineer	000000000000000000000000000000000000000	iletions s	900000000000000000000000000000000000000	nd serve	with ei	rfore le	vel mesun	emente		
<u> </u>	TANK S		<u> </u>	Andrew of State		odece – <u>vinneiseli</u> obei		UID VOLU				VOLUME	4	PHOTOS/	VIDEOS	Ī
	TANK O	TATO			 	DRAIN-	Eid	OID VOLO	DRAIN-	PUMP-	SOLIDS	VOLUME		11101037	VIDEOG	SEE
					SUPER-	ABLE	PUMPED		ABLE	ABLE						FOOTNOT
			STABIL/	TOTAL	NATE	INTER-	THIS	TOTAL	LIQUID	LIQUID		SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION		LIQUID	STIT.	MONTH	PUMPED	REMAIN		SLUDGE		VOLUME	IN-TANK	IN-TANK	
TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)		(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
			_		4			NK FARM						1		
A-101	DSSF	SOUND	/PI	877	494	95	0.0	14.1	590	574	3	380	09/30/99			(9)
A-102	DSSF	SOUND	IS/PI	41	4	8	0.0	39.5	12	4	15	22	07/27/89			ĺ
A-103	DSSF	ASMD LKR	IS/IP	371	5	45	0.0	111.0	50	43	366	0	06/03/88	12/28/88		
A-104	NCPLX	ASMD LKR	IS/IP	28	0	4	0.0	0.0	4	0	28	0	01/27/78	06/25/86		Į.
A-105	NCPLX	ASMD LKR	IS/IP	37	٥	0	0.0	0.0	0	0	37	0	10/31/00	08/20/86		
A-106	СР	SOUND	IS/IP	1 25	0	9	0.0	0.0	9	1	125	0	09/07/82	08/19/86		
6 SINGL	E-SHELL T	ANKS	TOTALS	1479	503	161	0.0	164.6	665	622	574	402				†
		<u> </u>					AV TA	NK FARM	PATTIC						_	
AX-101	DesE	SOUND	/PI	666	368	74	9.8	18.1	442	436] з	295	09/30/99	08/18/87		1
AX-101		ASMD LKR	IS/IP	30	0	7	0.0	13.0	7	430	7	23	06/30/99	06/05/89		(h)
_		SOUND	IS/IP		Ö	23		0.0	23	11-	8		1			ነ
AX-103		ASMD LKR	IS/IP	112	٥	1	0.0 0.0	0.0	23 1	0	8		06/30/99	08/13/87		
AX-104	NUTLA	ASMD LKN	(3/IF	8	١	•	0.0	0.0	•	U	ľ	0	06/30/99	08/18/87]
4 SINGL	E-SHELL T	ANKS	TOTALS:	816	368	105	9.8	31.1	473	447	26	422				
							B_TAN	K FARM	STATUS							
B-101	NCPLX	ASMD LKR	IS/IP	113	0	24	0.0	0.0	24	17	0	113	06/30/99	05/19/83		İ
B-102	NCPLX	SOUND	IS/IP	32	4	7	0.0	0.0	11	4	lo	28	06/30/99	08/22/86		l
B-103	NCPLX	ASMD LKR	IS/IP	59	0	11	0.0	0.0	11	3	0	59	06/30/99	10/13/86		
B-104	NCPLX	SOUND	IS/IP	371	1	45	0.0	0.0	46	42	309	61	06/30/99	10/13/88		
B-105	NCPLX	ASMD LKR	IS/IP	158	0	20	0.0	0.0	20	16	28	130	06/30/99	05/19/88		
B-106	NCPLX	SOUND	IS/IP	117	1	25	0.0	0.0	26	19	0	116	02/29/00	02/28/85		1
B-107	NCPLX	ASMD LKR	IS/IP	165	1	22	0.0	0.0	23	19	93	71	06/30/99	02/28/85		
B-108	NCPLX	SOUND	IS/IP	94	0	15	0.0	0.0	15	11	53	41	06/30/99	05/10/85		!
B-109	NCPLX	SOUND	IS/IP	127	0	21	0.0	0.0	21	17	63	64	06/30/99	04/02/85		1
B-110	NCPLX	ASMD LKR	(S/IP	246	1	27	0.0	0.0	28	20	245	0	02/28/85	03/17/88		1
B-111	NCPLX	ASMD LKR	IS/IP	237	1	23	0.0	0.0	24	29	236	ō	06/28/85	06/26/85		1
B-112	NCPLX	ASMD LKR	IS/IP	33	3	4	0.0	0.0	7	3	30	o	05/31/85	05/29/85		[
B-201	NCPLX	ASMD LKR	IS/IP	29	1	4	0.0	0.0	5	1	28		04/28/82		06/23/95	
B-202	NCPLX	SOUND	IS/IP	27	o	4	0.0	0.0	4	o	27	o	05/31/85		06/15/95	
B-203	NCPLX	ASMD LKR	IS/IP	51	1	5	0.0	0.0	6	1	50	0	05/31/85	11/13/86	,10,00	1
B-204	NCPLX	ASMD LKR	IS/IP	50	i	5	0.0	0.0	6	1	49	0	05/31/84	10/22/87		Į
														,		L
16 SING	LE-SHELL	TANKS	TOTALS	1909	15	262	0.0	0.0	277	203	1211	683	Ì			

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
March 31, 2001

1000000000	(2000) 2000 (2000) (2000) (2000) (2000)		8835.00098889859860098	000000000000000000000000000000000000000	MARCO SERVICIO DE COMPANSO DE	X00000000000000		11CH 31, 2	~~~	-224460000000000000000	Negativa a a a a a a a a a a a a a a a a a a	99000000000000000000000000000000000000				
			volumes a	re the re	sult of e	ngineer	ing calci	ilations a	ind may i	rot agree	with su	rface le	zei measo	rements		
	TANK :	STATUS					LIO	UID VOLU	ME		SOLIDS	VOLUME		PHOTOS	VIDEOS	
						DRAIN-			DRAIN-	PUMP-			[SEE
					{	ABLE	PUMPED		ABLE	ABLE	Ì		ł	}		FOOTNOT
			STABIL/	TOTAL	SUPER-	INTER-	THIS	TOTAL	LIQUID	LIQUID	ļ	SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION	WASTE	NATE	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
							BX_TA	NK FARM	STATUS							•
BX-10	NCPLX	ASMD LKR	IS/IP/CCS	43	1 1	4	0.0	0.0	5	1	42	0	04/28/82	11/24/88	11/10/94	.[
BX-10	2 NCPLX	ASMD LKR	IS/IP/CCS	96	0	0	0.0	0.0	0	0	96	0	04/28/82	09/18/85		{
BX-10	NCPLX	SOUND	IS/IP/CCS	71	9	4	0.0	0.0	13	9	62	0	11/29/83	10/31/86	10/27/94	.]
BX-104	NCPLX	COUND	IS/IP/CCS	93	3	4	0.0	17.4	7	3	90	0	02/29/00	09/21/89		Ì
BX-10	NCPLX	SOUND	IS/IP/CCS	51	5	4	0.0	15.0	9	5	46	0	06/30/99	10/23/86		[
BX-10	NCPLX	SOUND	IS/IP/CCS	38	0	4	0.0	14.0	4	0	38	0	08/01/95	05/19/88	07/17/95	:[
BX-10	7 NCPLX	SOUND	IS/IP/CCS	345	1 1	36	0.0	23.1	37	33	344	0	09/18/90	09/11/90		
BX-10	B NCPLX	ASMD LKR	IS/IP/CCS	26	0	4	0.0	0.0	4	0	26	0	07/31/79	05/05/94		
BX-10	NCPLX	SOUND	IS/IP/CCS	193	0	25	0.0	8.2	25	20	193	0	09/17/90	09/11/90		
BX-110	NCPLX	ASMD LKR	IS/IP/CCS	207	3	28	0.0	1.5	31	26	133	71	06/30/99	07/15/94	10/13/94	1
BX-11	NCPLX	ASMD LKR	IS/IP/CCS	16 <u>2</u>	1	5	0.0	116.9	6	2	25	136	06/30/99	05/19/94	02/28/95	; \
BX-11:	NCPLX	SOUND	IS/IP/CCS	165	1	. 9	0.0	4.1	10	7	164	0	09/17/90	09/11/90		[
12 SIN	GLE-SHELL	TANKS	TOTALS:	1490	24	127	0.0	200.2	151	106	1259	207	<u> </u>	<u> </u>		
							BY TAI	NK FARM	STATUS						-	
BY-10	NCPLX	SOUND	IS/IP	387	1 0	28	0.0	35.8	28	24	109	278	05/30/84	09/19/89		I
BY-10:	NCPLX	SOUND	IS/PI	277	0	40	0.0	159.0	40	33	ه ا	277	05/01/95	09/11/87	04/11/95	.)
BY-103	NCPLX	ASMD LKR	IS/PI	400	0	58	0.0	95.9	58	53	9	391		09/07/89		1
BY-104	NCPLX	SOUND	IS/IP	326	0	40	0.0	329.5	40	36	150	176	1	04/27/83		}
BY-10	NCPLX	ASMD LKR	/PI	503	0	121	0.0	0.0	121	111	48	455	08/31/99	07/01/86		
BY-106	NCPLX	ASMD LKR	/PI	562	0	132	0.0	63.7	132	119	64	478	12/31/98	11/04/82		1
BY-10	NCPLX	ASMD LKR	IS/IP	266	0	39	0.0	56.4	39	35	40	226	06/30/99	10/15/86		
BY-108	NCPLX	ASMD LKR	IS/IP	228	0	33	0.0	27.5	33	26	154	74	04/28/82	10/15/86		l l
BY-109	NCPLX	SOUND	IS/PI	290	0	31	0.0	157.1	31	26	57	233		06/18/97		
BY-110	NCPLX	SOUND	IS/IP	398	0	21	0.0	213.3	21	17	103	295		07/26/84		}
BY-111	NCPLX	SOUND	IS/IP	459	0	14	0.0	313.2	14	6	0	459	06/30/99	10/31/86		1
BY-112	NCPLX	SOUND	IS/IP	291	0	24	0.0	116.4	24	12	0	291	1	04/14/88		1
12 CIN	GLE-SHELL	TANKS	TOTALS:	4387	-	 581	0.0	1567.8	581	498	75.		 	 		
12 JIN	OLL OI IELL	ININO	TOTALS.	4307	<u> </u>	901	V.U	1907.6	201	490	754	3633	<u> </u>	<u> </u>		1

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
March 31, 2001

		These	e volumes a	re the n	esult of	engineci	800000000000000000000000000000000000000	alen 51, ulations :	70000000000000000	not agree	with s	ırface le	vel measo	rements		
2	TANK	STATUS						UID VOLU				VOLUME				***************************************
						DRAIN-			DRAIN-	PUMP-						SEE
					1	ABLE	PUMPED		ABLE	ABLE	1		<u>'</u>			FOOTNOTES
			STABIL/	TOTAL	SUPER-	INTER-	THIS	TOTAL	LIQUID	LIQUID	1	SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION	WASTE	NATE	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
TAN	K MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
							C TAI	NK FARM	STATUS				· · · · · · · · · · · · · · · · · · ·			
C-10	1 NCPLX	ASMD LKR	IS/IP	88	0	4	0.0	0.0	4	0	88	0	11/29/83	11/17/87		1
C-10	2 DC	SOUND	IS/IP	316	0	62	0.0	46.7	62	55	316	0	09/30/95	05/18/76	08/24/95	
C-10	3 NCPLX	SOUND	/PI	198	79	18	0.0	0.0	97	83	119	0	12/31/98	07/28/87		
C-10	4 CC	SOUND	IS/IP	263	0	0	0.0	0.0	0	0	263	0	02/01/00	07/25/90		
C-10	5 NCPLX	SOUND	IS/PI	132	0	20	0.0	0.0	20	0	132	o	02/29/00	08/05/94	08/30/95	
C-10	6 NCPLX	SOUND	/PI	48	42	0	0.0	0.0	42	9	6	0	10/31/99	08/05/94	08/08/94	j
C-10	7 DC	SOUND	IS/IP	257	0	30	0.0	40.8	30	25	257	o	06/30/99	00/00/00		
C-10	8 NCPLX	SOUND	IS/IP	66	0	4	0.0	0.0	4	0	66	0	02/24/84	12/05/74	11/17/94	
C-10	9 NCPLX	SOUND	IS/IP	66	4	4	0.0	0.0	8	4	62	0	11/29/83	01/30/76		Į
C-11	O DC	ASMD LKR	IS/IP	178	1	37	0.0	15.5	38	30	177	0	06/14/95	08/12/86	05/23/95	
C-11	1 NCPLX	ASMD LKR	IS/IP	57	0	4	0.0	0.0	4	0	57	0	04/28/82	02/25/70	02/02/95	
C-11	2 NCPLX	SOUND	IS/IP	104	0	6	0.0	0.0	6	1	104	0	09/18/90	09/18/90		1
C-20	1 NCPLX	ASMD LKR	IS/IP	2	0	0	0.0	0.0	0	0	2	0	03/31/82	1 2/02/86		
C-20		ASMD LKR	IS/IP	1	0	0	0.0	0.0	0	0	[1	0	01/19/79	12/09/86		
C-20		ASMD LKR	IS/IP	5	0	0	0.0	0.0	0	0	5	0	04/28/82	12/09/86		
C-20	4 NCPLX	ASMD LKR	IS/IP	3	0	O	0.0	0.0	o	0	3	0	04/28/82	12/09/86		
16 S	INGLE-SHEL	L TANKS	TOTALS:	1784	126	189	0.0	103.0	315	207	1658	0				
					_		S TAI	NK FARM	STATUS				_	_		
S-10	1 NCPLX	SOUND	/PI	427	12	83	0.0	0.0	95	80	211	204	12/31/98	03/18/88		
S-10	2 DSSF	SOUND	/PI	492	0	93	0.0	56.8	93	89	105	387	05/31/00	03/18/88		(c)
S-10	3 DSSF	SOUND	IS/PI	237	1	45	0.0	23.9	46	39	9	227	04/30/00	06/01/89	01/28/00	
S-10	4 NCPLX	ASMD LKR	IS/IP	294	1	34	0.0	0.0	35	31	293	0	12/20/84	12/12/84		
S-10	5 NCPLX	SOUND	IS/IP	456	0	42	0.0	114.3	42	33	1 2	454	09/26/88	04/12/89		
S-10	6 NCPLX	SOUND	IS/PI	455	0	26	0.0	203.6	26	2	0	455	02/28/01	03/17/89	01/28/00	(a)
S-10	7 NCPLX	SOUND	/PI	376	14	61	0.0	0.0	75	61	293	69	06/30/99	03/12/87		
S-10		SOUND	IS/PI	432	0	0	0.0	199.B	0	0	5	427	10/01/99	03/12/87	12/03/96	
S-10		SOUND	/PI	473	0	59	0.0	145.2	59	49	13	460	12/31/00	12/31/98		(i)
S-11		SOUND	IS/PI	390	0	30	0.0	203.1	30	27	131	259	05/14/92	03/12/87	12/11/96	1
S-11		SOUND	/PI	501	48	82	0.0	3.3	130	97	116	337	09/30/99	08/10/89		
S-11	2 NCPLX	SOUND	/Pt	523	0	81	0.0	125.1	81	70	6	517	12/31/98	03/24/87		
12 S	INGLE-SHEL	L TANKS	TOTALS:	5056	76	636	0.0	1075.1	712	578	1184	3796				

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
March 31, 2001

*********	980988889989999	555555522003034444444	>>>>>>>>	300300000000000000000000000000000000000	000000000000000000000000000000000000000	000000000000000000000000000000000000000	1 VI 2	uch 31, 2	ZUU 1	*****		national description		Anna i marana and an anna an an a		
			volumes a	re the re	solt of	engineer				ot agree				rements		
	TANK S	TATUS					LIC	MID VOLU	ME		SOLIDS	VOLUME				
					ł	DRAIN-			DRAIN-	PUMP-	ł					SEE
						ABLE	PUMPED		ABLE	ABLE						FOOTNOTE
			STABIL/		SUPER-	INTER-	THIS	TOTAL	LIQUID	LIQUID		SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION		NATE	STIT.	MONTH	PUMPED	REMAIN		SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
							SX TAI	NK FARM	STATUS							
SX-101	DC	SOUND	/PI	429	0	93	0.0	19.2	93	80	1 0	429	12/31/00	03/10/89		1 0
SX-102	DSSF	SOUND	/PI	514	134	95	0.0	0.0	229	216		380	04/30/00			"
SX-103	NCPLX	SOUND	/PI	521	0	34	3.1	113.1	34	19	115	406	03/31/01	12/17/87		(k)
SX-104	DSSF	ASMD LKR	IS/PI	446	0	48	0.0	231.3	48	44	136	310	04/30/00		02/04/98	1
SX-105	DSSF	SOUND	/Pi	486	0	2	0.0	151.1	2	-10	65	421	01/31/01	06/15/88	02,0,00	(f)
SX-106	NCPLX	SOUND	IS/PI	397	0	37	0.0	147.5	37	31	0	397	05/31/99	06/01/89		{ ``'
SX-107	NCPLX	ASMD LKR	IS/IP	102	0	0	0.0	0.0	0	0	85	17	10/31/00			1
SX-108	NCPLX	ASMD LKR	IS/IP	87	0	0	0.0	0.0	0	0	87	0	12/31/93			
SX-109	NCPLX	ASMD LKR	IS/IP	249	6	0	0.0	0.0	0	0	60	189	10/31/00			1
SX-110	NCPLX	ASMD LKR	IS/IP	62	o	0	0.0	0.0	0	0	62	0	10/06/76			
SX-111	NCPLX	ASMD LKR	IS/IP	122	0	8	0.0	0.0	8	3	122	0	06/30/99			
SX-112	NCPLX	ASMD LKR	IS/IP	108	0	6	0.0	0.0	6	1	108	0	06/30/99	03/10/87		(
SX-113	NCPLX	ASMD LKR	IS/IP	31	0	0	0.0	0.0	0	0	31	0	06/30/99	03/18/88		
SX-114	NCPLX	ASMD LKR	IS/IP	165	0	0	0.0	0.0	O	0	44	121	10/31/00	02/26/87		J
SX-115	NCPLX	ASMD LKR	IS/IP	12	0	0	0.0	0.0	0	0	12	0	04/28/82	03/31/88		
15 SING	LE-SHELL	TANKS	TOTALS:	3731	134	323	3.1	662.2	457	384	927	2670				
	•						T TAN	K FARM	STATUS							
T-101	NCPLX	ASMD LKR	IS/PI	102	1 1	20	0.0	25.3	21	16	37	64	06/30/99	04/07/93		1
T-102	NCPLX	SOUND	IS/IP	32	13	3	0.0	0.0	16	11	19	0	08/31/84	06/28/89		
T-103	NCPLX	ASMD LKR	IS/IP	27	4	3	0.0	0.0	7	3	23	0	11/29/83	07/03/84		
T-104	NCPLX	SOUND	IS/PI	317	0	31	0.0	149.5	31	27	317	0	12/31/99	06/29/89	10/07/99	Ì
T-105	NCPLX	SOUND	IS/IP	98	0	5	0.0	0.0	5	0	98	o	05/29/87	05/14/87	,,00	ſ
T-106	NCPLX	ASMD LKR	IS/IP	21	2	0	0.0	0.0	2	2	19	o	04/28/82	06/29/89		
T-107	NCPLX	ASMD LKR	IS/PI	173	0	34	0.0	11.0	34	20	173	o	05/31/96		05/09/96]
T-108	NCPLX	ASMD LKR	IS/IP	44	0	5	0.0	0.0	5	0	21	23		07/17/84	,,00	
							- • -		•	•			1 - 4,00,00			

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

March 31, 2001 These volumes are the result of engineering calculations and may not agree with surface level measurements TANK STATUS LIQUID VOLUME SOLIDS VOLUME DRAIN-DRAIN-PUMP-SEE ABLE **PUMPED** ABLE ABLE FOOTNOTES STABIL/ TOTAL SUPER-INTER-THIS TOTAL LIQUID LIQUID SALT SOLIDS LAST LAST FOR WASTE TANK ISOLATION WASTE NATE STIT. MONTH **PUMPED** REMAIN REMAIN SLUDGE CAKE VOLUME IN-TANK IN-TANK THESE INTEGRITY STATUS TANK MAT'L. (Kgal) (Kgal) (Kgal) (Kgal) (Kgal) (Kgal) (Kgal) (Kgal) UPDATE **PHOTO** VIDEO CHANGES (Kgal) T-109 NCPLX ASMD LKR IS/IP 56 0 10 0.0 0.0 10 3 0 58 06/30/99 02/25/93 NCPLX SOUND IS/PI 369 43 T-110 1 48 0.0 50.3 48 368 0 01/31/00 07/12/84 10/07/99 T-111 NCPLX ASMD LKR IS/PI 446 35 04/18/94 04/13/94 02/13/95 0 38 0.0 9.6 38 446 0 T-112 NCPLX SOUND IS/IP 67 7 4 0.0 0.0 11 7 60 0 04/28/82 08/01/84 NCPLX SOUND T-201 IS/IP 29 1 4 0.0 0.0 5 28 0 05/31/78 04/15/86 NCPLX SOUND 21 T-202 IS/IP 0 3 0.0 0 0.0 3 21 0 07/12/81 07/06/89 T-203 NCPLX SOUND IS/IP 35 0 5 0.0 0.0 5 0 35 01/31/78 08/03/89 0 T-204 NCPLX SOUND IS/IP 38 0 0.0 5 0.0 5 38 0 07/22/81 08/03/89 16 SINGLE-SHELL TANKS TOTALS: 1877 29 218 0.0 245.7 246 168 1703 145 TX TANK FARM STATUS TX-101 NCPLX SOUND 87 IS/IP/CCS 3 8 0.0 0.0 11 7 74 10 06/30/99 10/24/85 TX-102 NCPLX SOUND IS/IP/CCS 217 0 27 0.0 94.4 27 16 217 08/31/84 0 10/31/85 TX-103 NCPLX SOUND IS/IP/CCS 157 0 18 0.0 68.3 18 11 0 157 06/30/99 10/31/85 TX-104 NCPLX SOUND IS/IP/CCS 65 5 0.0 37 06/30/99 9 3.6 14 9 23 10/16/84 TX-105 NCPLX ASMD LKR IS/IP/CCS 609 0 25 0.0 121.5 25 14 0 609 08/22/77 10/24/89 TX-106 NCPLX SOUND IS/IP/CCS 341 0 37 0.0 37 30 0 341 134.6 06/30/99 10/31/85 TX-107 NCPLX ASMD LKR IS/IP/CCS 36 1 6 0.0 0.0 7 8 27 06/30/99 10/31/85 TX-108 NCPLX SOUND IS/IP/CCS 134 0 0.0 06/30/99 8 13.7 B 1 6 128 09/12/89 TX-109 NCPLX SOUND IS/IP/CCS 384 0 6 0.0 72.3 6 2 384 0 06/30/99 10/24/89 TX-110 NCPLX ASMD LKR IS/IP/CCS 462 0 14 0.0 115.1 14 10 37 425 06/30/99 10/24/89 TX-111 NCPLX SOUND IS/IP/CCS 370 0 6 10 0.0 98.4 10 43 327 06/30/99 09/12/89 SOUND IS/IP/CCS TX-112 NCPLX 649 0 26 0.0 94.0 26 21 0 649 05/30/83 11/19/87 TX-113 NCPLX ASMD LKR IS/IP/CCS 653 0 30 0.0 30 19.2 0 0 653 10/31/00 04/11/83 09/23/94 TX-114 NCPLX ASMD LKR IS/IP/CCS 535 0 17 0.0 104.3 17 11 4 531 06/30/99 04/11/83 02/17/95 ASMD LKR TX-115 NCPLX IS/IP/CCS 568 0 25 0.0 99.1 25 15 0 06/30/99 06/15/88 568

ASMD LKR

ASMD LKR

SOUND

IS/IP/CCS

IS/IP/CCS

IS/IP/CCS

TOTALS:

631

626

286

6810

0

0

0

9

21

10

0

297

0.0

0.0

0.0

0.0

23.8

54.3

89.1

1205.7

21

10

306

0

17

0

176

68

29

21

697

563

597

265

6104

06/30/99

06/30/99

02/01/00

10/17/89

04/11/83

12/19/79

TX-116 NCPLX

TX-117 NCPLX

TX-118 NCPLX

18 SINGLE-SHELL TANKS

HNF-EP-0182, Rev. 156

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
March 31, 2001

	5000000000000000	10001000000000000000	x2000000000000000000000000000000000000	950000000000000 000 0000	8585586666666666	000000000000000000000000000000000000000	5555555557457455655		11CH 31, 2		nananantiktäätänana	AND THE STATE OF T		******	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,		
			These	volumes a	re the re	sult of	engineer	ing calci	lations a	nd nay r	not agree	with su	rface le	vel measu	rements		
		TANK S	TATUS					LIQ	NID VOLUI	ME		SOLIDS	VOLUME		PHOTOS/	/IDEOS	
							DRAIN-			DRAIN-	PUMP-						SEE
						SUPER-	ABLE	PUMPED		ABLE	ABLE	Į]			FOOTNOTES
				STABIL/	TOTAL	NATE	INTER-	THIS	TOTAL	LIQUID	LIQUID	1	SALT	SOLIDS	LAST	LAST	FOR
		WASTE	TANK	ISOLATION	WASTE	rianid	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
	TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
								TV TA	NK FARM	STATUS							
	TY-101	NCPLX	ASMD LKR	IS/IP/CCS	118	1 0	2	0.0	8.2	2	o	72	46	06/30/99	08/22/89		1
	TY-102		SOUND	IS/IP/CCS	64	ه ا	12	0.0	6.6	12	5	6	64	06/28/82			
	TY-103		ASMD LKR	IS/IP/CCS	162	0	20	0.0	11.5	20	16	162	0	07/09/82			1
	TY-104		ASMD LKR	IS/IP/CCS	43	١٠	4	0.0	0.0	4	0	43	0	06/27/90			Į
	TY-105	NCPLX	ASMD LKR	IS/IP/CCS	231	0	12	0.0	3.6	12	10	231	0	04/28/82			
	TY-106	NCPLX	ASMD LKR	IS/IP/CCS	21	0	3	0.0	0.0	3	0	21	0	06/30/99			
						<u> </u>											
	6 SINGL	E-SHELL 1	ANKS	TOTALS:	639	0	53	0.0	29.9	53	31	529	110				
1								II TAN	K FARM	OVER A VERTICE							
w	U-101	NCPLX	ASMD LKR	IS/IP	25	3	3	0.0	0.0	6 BIAIUS		۰.	•	1	004070		1
	U-102	NCPLX	SOUND	/PI	25 299	0	27	1.8	75.8		2 17	22	0	04/28/82			l
	U-103	NCPLX	SOUND	IS/PI	418	1	33	0.0	98.9	27 34	28	43	256	03/31/01	06/08/89		(e)
	U-103	NCPLX	ASMD LKR	IS/IP	122	,	0	0.0	0.0	0	26 0	13	404	05/31/00			Ī
	U-105	NCPLX	SOUND	JS/PI	353	٥	44	0.0	87.5	44	32	79	43 321	06/30/99 03/31/01			1
	U-106	NCPLX	SOUND	IS/PI	172	2	36	0.0	39.1	38	30	0	170	03/31/01	07/07/88		(b)
	U-107	DSSF	SOUND	/PI	408	33	92	0.0	0.0	125	115	15	360	12/31/98			(1)
	U-108	NCPLX	SOUND	/PI	468	24	108	0.0	0.0	132	124	29	415	12/31/98			
	U-109	NCPLX	SOUND	/P1	399	0	61	0.0	65.9	61	52	35	364	12/31/90			(d)
	U-110	NCPLX	ASMD LKR	IS/PI	186	٥	18	0.0	0.0	18	14	186	0	12/31/00			(4)
	U-111	DSSF	SOUND	/Pf	329	ا ا	80	0.0	0.0	80	71	26	303	12/31/98			
	U-112	NCPLX	ASMD LKR	IS/IP	49	4	4	0.0	0.0	8	4	45	0	02/10/84			
	U-201	NCPLX	SOUND	IS/IP	5	1	1	0.0	0.0	2	1	4	o	08/15/79			
	U-202	NCPLX	SOUND	IS/IP	5	1	1	0.0	0.0	2	1	1 4	0	08/15/79			J
	U-203	NCPLX	SOUND	IS/IP	3	1	0	0.0	0.0	1	1	2	0	0B/15/79			
	U-204	NCPLX	SOUND	IS/IP	3		0	0.0	0.0	1	1	2	0	08/15/79			
				- <u></u>											. =,, -		
	16 SING	LE-SHELL	TANKS	TOTALS:	3244	_71	_ 508	1.8	367.2	579	493	537	2636				
	654N/5	TOTAL			0000	1055	2155										
	GRAND	IUIAL			33222	1355	3460	14.7	5652.5	4815	3913	11059	20808				<u>i</u>

A-14

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS March 31, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENTS FOOTNOTES:

Total Waste is calculated as the sum of Sludge and Saltcake plus Supernate. The category "Interim Isolated (II) was changed to Intrusion Prevention (IP) in June 1993. Stabilization information from WHC-SD-RE-TI-178 SST STABILIZATION RECORD, latest revision, or SST Stabilization or Cognizant Engineer

Porosity values are 25% for saltcake and 15% for sludge, per HNF-2978, Rev. 1, "Updated Pumpable Liquid Volume Estimates and Jet Pump Durations for Interim Stabilization of Remaining Single-Shell Tanks," September 1999, with the exception of those tanks which have been interim stabilized and the porosities recalculated.

(a) S-106 This tank was declared interim Stabilized on February 1, 2001, DOE concurred on February 12, 2001,

(b) U-105 This tank was declared interim Stabilized on March 29, 2001, due to major equipment failure.

Total Waste: 353.0 Kgal Supernate: 0.0 Kgal

Drainable Interstitial Liquid: 44.0 Kgal

Pumped this Month: 0.0 Kgall Total Pumped: 87.5 Kgall

Drainable Liquid Remaining: 44.0 Kgal Pumpable Liquid Remaining: 39.7 Kgal

Sludge: 32,0 Kgal Saltcake: 321.0 Kgal

(c) S-102 Following information from Cognizant Engineer:

Pumping commenced March 18, 1999. Many pumping problems occurred over the following months, and the pump has been replaced several times. Pumping was interrupted again in June 2000. No pumping since June 2000.

HNP-EP-0182, Rev. 156

(d) U-109 Following information from Cognizant Engineer

Pumping began March 11, 2000. Saftcake volume is adjusted to correspond to current waste removal. Remaining volumes based on HNF-2978, Rev. 2.

Pumping was shut down on December 3, 2000, due to jet pump failure. Attempts to restart the pump have been unsuccessful; the pump was replaced and restarted March 30, 2001.

During March 2001, a total of 1,025 gal of fluid was removed and a total of 1,079 gal of water was added for pump priming/equipment flushes.

There was no net waste removal in March and 54 gal of flush water must still be removed. In addition, 284 gal of water was used as dilution and 1,010 gal of water was used for transfer line flushes.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

March 31, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENT FOOTNOTES:

(e) U-102 Following Information from Cognizant Engineer

Pumping began in this tank on January 20, 2000. Saltcake volume is adjusted to correspond to current waste removal. Remaining volumes are based on HNF-2978, Rev. 2.

Total Waste: 299.2 Kgal Supernate: 0.0 Kgal

Drainable Interstitial Liquid: 27.2 Kgal Pumped this Month: 1.8 Kgal Total Pumped: 75.8 Kgal

Drainable Liquid Remaining: 27.1 Kgal Pumpable Liquid Remaining: 17.2 Kgal

Siudge: 43.0 Kgal Saltcake: 256.2 Kgal

During March 2001, a total of 2,548 gal of fluid was removed with 707 gal of water added by pump priming/equipment flushes, for a net removal of 1,841 gal of waste. In addition, 3,314 gal of water were used as dilution and 4,837 gal of water were used for transfer line flushes.

(f) SX-105 Following information from Cognizant Engineer:

Saltwell pumping began August 8, 2000. Remaining volumes are based on HNF-2978, Rev. 2.

Tank Waste: 485.9 Kgal Supernate: 0.0 Kgal

A-15

Drainable interstial Liquid: 1.9 Kgal Pumped this month: 0.0 Kgal Total Pumped: 15.1 Kgal

Drainable Liquid Remaining: 1.9 Kgal
Pumpable Liquid Remaining: -10.1 Kgal (*)

Sludge: 65.0 Kgal Saltcake: 420.9 Kgal

In March 2001, a total of 67 gal of fluid was removed with 421 gal of water added by pump priming and system flushes. There was no net waste removal; 354 gal of flush waster must be removed next month. In addition, 16 gal of dilution water and 405 gal of water for transfer lines flushes were used.

(*) Minus 1,097 gal estimate for PLR because there is more pumpable liquid in the tank than originally estimated. This is due to the fact that approximately 118,000 gal of supernate was in the tank at the start of pumping.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

March 31, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENT FOOTNOTES:

(g) A-101 Following information from Cognizant Engineer

Pumping began on May 6, 2000. No pumping since August 2000. Remaining volumes are based on the original estimated volumes in HNF-2978, Rev. 1.

(h) AX-101 Following Informtion from Cognizant Engineer

Pumping began July 29, 2000; shutdown in August 2000, and resumed March 22, 2001. Remaining volumes are based on the original estimated volumes in HNF-2978, Rev. 1.

Total Waste: 665.8 Kgal Supernate: 367.8 Kgal

Drainable Interstitial: 73.7 Kgal Pumped this month: 9.8 Kgal Total Pumped: 18.2 Kgal

Drainable Liquid Remaing: 442.0 Kgal Pumpable Liquid Remaining: 425.8 Kgal

Sludge: 3.0 Kgal Saltcake: 295.0 Kgal

In March, 2001, a total of 10,346 gal of fluid was removed with 546 gal of water added for pump priming/equipment, for a net removal of 9,800 gal of waste. In addition, 9,753 gal of water was used as dilution and 1,656 gal of water was used for transfer line flushes.

(i) U-106 This tank was declared Interim Stabilization on March 9, 20001.

Total Waste: 171, 9 Kgal Supernate: 1.7 Kgal

Drainable Interetitial: 35.8 Kgal Pumped this month: 0.0 Kgal Total Pumped: 39.1 Kgal

Drainable Liquid Remaing: 35.8 Kgal Pumpable Liquid Remaining: 30.2 Kgal

Sludge: 0.0 Kgal Saltcake: 170.2 Kgal

A-17

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

March 31, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENTS FOOTNOTES:

(j) S-109 Following information from Cognizant Engineer:

Pumping began September 23, 2000.

Remaining volumes are based on HNF-2978, Rev. 2,

The pumping rate dropped below .05 gpm and the pump was shut down on January 27, 2001. The tank is now being evaluated to determine if it can be interim stabilized,

(k) SX-103 Following information from Cognizant Engineer:

Pumping began October 26, 2000.

Remaining volumes are based on HNF-2978, Rev. 2.

Total Waste: 520.9 Kgal Supernate: 0.0 Kgal

Drainable Interstitial Liquid: 33.9 Kgal Pumped this month: 3.1 Kgal

Total Pumped: 113.1 Kgal

Drainable Liquid Remaining: 33.9 Kgal Pumpable Liquid Remaining: 18.9 Kal

Studge: 115,0 Kgal Sattcake: 405,9 Kgal

In March 2001, a total of 3,398 gal of fluid was removed with a total of 292 gal of water added by pump priming/equipment flushes, for a net removal of 3,106 gal of waste. In addition, 4,430 gal of water were used as dilution and 787 gal of water were used for transfer line flushes.

(I) SX-101 Following information from Cognizant Engineer:

Pumping began November 22, 2000. No pumping since December 2000.

Remaining volumes are based on HNF-2978. Rev 2. Saltcake volume is adjusted to correspond to current waste removal.

APPENDIX B PERFORMANCE SUMMARY

TABLE B-1. SUMMARY OF WASTE TRANSACTIONS IN THE DOUBLE-SHELL TANK (DST) SYSTEM March 31, 2001

All volumes in Kilo-Gallons

- The DST system received waste additions from SST pumping, campaign 01-01,152-AX & 151-AZ in March.
- There was a net change of -580,000 gallons in the DST system for March.
- The total DST inventory as of March 31, 2001 was 20.627 million gallons.
- There were ~22 Kgals of Saltwell Liquid (SWL) (10 SWL + 12 H2O) pumped to the East Area DSTs (101-AN) in March.
- There were ~22 Kgals of SWL (5 Kgals SWL + 17 Kgals H2O) pumped to the West Area DSTs (102-SY) in March.
- The SWL numbers are preliminary and are subject to change once cognizant engineers do a validation, the volumes reported contain actual waste volume plus any water added for dilution and transfer line flushes.
- The Cold Run (training and testing) for evaporator 242A campaign 01-01 contributed ~19,000 gallons of water to the tank farms prior to the campaign Hot Run, which commenced on March 13th and was completed on March 27th.
- As supplied by evaporator engineering, the Waste Volume Reduction (WVR) for campaign 01-01 was ~682,000 gallons (pre evaporator flush and pot dump) and/or ~645,000 gallons (post flush and pot dump).
- ~37,000 gallons of water was added to the Tank Farms after completion of campaign 01-01 (evaporator flush and pot dump).
- Single-Shell Tank 105-U was declared Interim Stabilized in March; although all stabilization criteria had not been met the tank was declared stabilized due to "major equipment failure". Final adjusted waste volumes for this tank are 282,000 gallons sattcake (SC) + 27,000 gallons sludge (SL) + 44,000 gallons interstitial liquid (IL) = 353,000 gallons
- Also, Single-Shell Tank 106-U was declared Interim Stabilized in March. Final adjusted waste volume for Tank 106-U are: 134,000 gallons saltcake (SC) + 36,000 gallons interstitial liquid (IL) + 2,000 supernatant (DN) = 172,000 gallons.

	GENERATIONS	OTHER GAINS ASS	OCIATED WITH	OTHER LOSSES ASS	OCIATED WITH
SWL (West)	+22 Kgal (2SY)	SLURRY	+3 Kgal	SLURRY	-2 Kgal
SWL (East)	+22 Kgal (1AN)	CONDENSATE	+9 Kgal	CONDENSATE	-4 Kgal
vap. Training & Flush	+56 Kgal (2AW, 6AW)	INSTRUMENTATION	+0 Kgal	INSTRUMENTATION	-0 Kgal
TOTAL	+100 Kgai	UNKNOWN	+1 Kgal	UNKNOWN	-5 Kgal

	PROJECTED VERSUS ACTUAL WASTE VOLUMES								
	ACTUAL DST WASTE RECEIPTS	PROJECTED DST WASTE RECEIPTS (1)	MISC. DST CHANGES (+/-)	PROJECTED WVR (1)	NET DST CHANGE	TOTAL DST VOLUME			
ОСТ00	222	155	-24	0	198	20653			
NOV00	261	262	-14	O	247	20900			
DEC00	139	300	-1	Ö	138	21038			
JAN01	113	397	-25	0	88	21126			
FEB01	100	303	-19	0	B1	21207			
MAR01	100	-283	2	-684	-580	20627			
APR01		321		0					
MAY01		302		0					
JUN01		334		0					
JUL01		296		0					
AUG01		289		0					
SEP01		282		0		i			

(1): The "PROJECTED DST WASTE RECEIPTS" and "WVR" numbers were updated in November 2000, the projected volumes will be updated as new and/or more accurate information is obtained. The projected volumes reported are the most current available, as supplied by cognizant engineers.

242-A	Evaporator Waste Volume Re	duction
Campaign 94-1	(04/15/94 - 06/13/94)	-2417
Campaign 94-2	(09/22/94 - 11/18/94)	-2787
Campaign 95-1	(06/09/95 - 07/26/95)	-2161
Campaign 96-1	(05/07/96 - 05/25/96)	-1117
Campaign 97-1	(03/24/97 - 04/02/97)	-351
Campaign 97-2	(09/16/97 - 09/30/97)	-653
Campaign 99-1	(07/24/99 - 08/15/99)	-818
Campaign 00-1	(04/20/00 - 05/05/00)	-682
Campaign 01-1	(03/13/01 - 03/27/01)	-682
	uction (WVR) since restart on 4/15/94	-11668

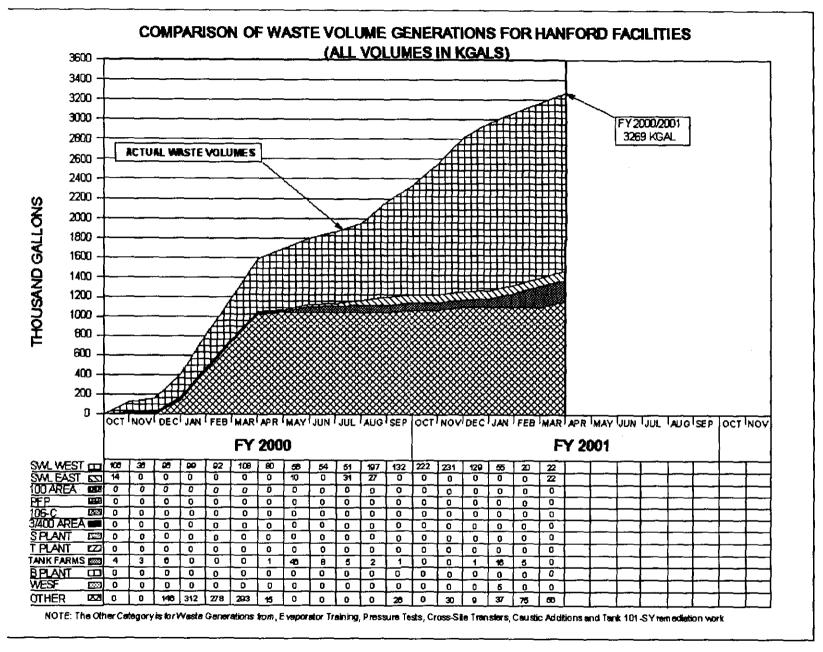


Figure B-1. Comparison of Projected Versus Actual Waste Volumes for Hanford Facilities

APPENDIX C

DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION

Table C-1. Double-Shell Tank Waste Inventory - March 31, 2001

TOTAL AVAILAB	LE DST SPACE
NON-AGING =	27380
AGING =	3920
	TOTAL 31280

MONTHLY INVENTO	RY CHANGE
02/00 TOTAL	21207
03/01 TOTAL	20627
CHÁNG	5 ♥0

TANK NAME	WASTE TYPE	TOTAL INVENTORY (1)	TOTAL SUPERNATE	TOTAL SOLIDS (3)	SALTCAKE (2)	SALTCAKE	SLUDGE (2)	SLUDGE LIQUID	REMAINING UNUSED TANK SPAC
241-AN-101	DN	247	247	0	0	0	0	0	893
241-AN-102	cc	1055	986	89	89	22		0	85
241-AN-103	055	957	500	457	457	114		0 '	183
241-AN-104	OSSF	1052	803	449	449	112		ā	88
241-AN-105	DSSF	1126	639	489	489	122	0	ō.	12
241-AN-106	cc	36	21	17	17	4	a l		1102
241-AN-107	ec	1040	793	247	247	62	0	0	100
241-AP-101	DSSF	1113	1113	0	0	0	0	Ö .	27
241-AP-102	CP	1088	1068	0	0	0	0	0	52
241-AP-103	cc	281	281	0	. 0	0	0	o l	859
241-AP-104	oc	1108	1108	0	٥	0	0	0	32
241-AP-105	DSSF	1134	1045	80	80	22	0	0	6
241-AP-108	DC .	622	622	0	. 0	0	0	0	518
241-AP-107	i oc	P42	982	. 0		٥	. 0	0	158
241-AP-108	DN_	37	37	0	0	LO_ j		0	1103
241-AW-101	DSSF	1126	751	375	375	94	0	0	14
241-AW-102	DN	86	55	30	30		0	0	1065
241-AW-103	DESFACRW	840	477	363	47	12	316	70	300
241-AW-104	DN	316	85	231	231	58	0	0	824
241-AW-105	NORW	426	171	255	0	0	255	38	714
241-AW-106	DSSF	584	325	239	239	<u>80</u>	0		576
241-AY-101	OC	185	108	76	0	0	76	- 11	795
241-AY-102	DN	643	470	173	_ 0	_ 0	173	26	337
241-AZ-101	NCAW	931	879	52	0	0	52	8	49
241-AZ-102	NCAW	995	891	105	0	. 0	105	16	0
241-SY-101	CC	970	887	83	83	21	D	0	170
241-SY-102	DC	921	850	71	0	Q	71	11	219
241-SY-103	œ	742	376	366	388	92	0	o	398
		建筑的	16371	4264		CONTRACTOR OF MARKETINE	1044	SOCIETATION : PROCESSOR	Belleville of the state

NOTE: Ail Volumes in Kilo-Galions (Kgals)

- (1) Total Inventory = (Total Supernate + Total Solids)
 (2) Saltcake Includes Saltcake Liquids; Sludge Includes Sludge Liquid
 (3) Total Solids = (Saltcake + Sludge)

EMERGENCY SPACE LAW of HLW RETURN REMAINING SPACE

2678

Tank Space Usage	inventory Calculation	by Waste Type:
TANK SPACE CHANGE	1	
02/01 TANK SPACE 10089	1	COMPLEXED SUPERNATE (DCICC)
23/01 TANK SPACE 10669	DILUTE SUPERNATE (DN)	AN-102= 966
CHANGE= 580	AN-101= 247	AN-108= 21
	AP-108= 37	AN-107= 793
OPERATIONAL SPACE	AW-102= 56	AP-103= 281
W-101= 803	AW-104= 85	AP-104= 1108
V2-108= 1103	AW-105- 171	AP-106= 622
\W-102= 1055	AY-102= 470	AP-107= 982
W-105= 714	TOTAL DN= 1085	AY-101= 109
W-106= 578	TOTAL SOLIDS- 589	5Y-101= 887
TY-102= 219	10, 212, 11.1.1.1.2.2.2.2.2.2.2.2.2.2.2.2.2.2.2.	5Y-102= 850
TOTAL. 4580	SLURRY SUPERNATE (DSS/DSSF	SY-103= 376
	AN-103= 500	TOTAL DC/CC= 8895
DESTRICTED PRINCE		
RESTRICTED SPACE		TOTAL SOLIDS 949
N-102= 85		
W+107= 100	AP-101= 1113	AGING SUPERNATE (AW)
/P-102= 52	AP-108= 1048	AZ-101= 879
Z-101= 49	AW-101= 751	AZ-102= 691
Z-102= 0	AW-103= 477	TOTAL AW- 1770
5Y-101= 170	AW-106= 325	TOTAL SOLIDS 157
TOTAL® 456	TOTAL DSS/D\$S 5453	
	TOTAL SOLIDS# 2461	PHOSPHATE SUPERNATE (CP)
WATCH LIST SPACE		TOTAL CP# 1088
W-103= 183		
N-104= 88	DST SLUDGE /	SALTCAKE LIQUID
W-105= 12	AN-102* 22	AVV-104= 58
W-101= 14	AN-103= 114	AW-105* 38
Y-103= 398	AN-104= 112	AW-106= 60
TOTAL= 696	AN-105# 122	AY-101= 11
	AN-108× 4	AY-102≈ 26
NON-ALLOCATED SPACE	AN-107= 62	AZ-101= 8
N-108= 1102	AP-106= 22	AZ-102* 16
(P-101± 27 V-103= 859	AW-101= 94	SY-101= 21 SY-102= 11
P-103= 859 P-104= 32	AW-102* 8 AW-103* 91	SY-102= 11 SY-103= 92
P-106= 6	7.7.	SALTCAKE LIQUID* 901
U-106= 518		
	GPANO	TOTALS
- 131		
W-103= 300	DILUTE SUPERNATE (DN/DC)	
W-104= 824	SLURRY (DSS/DSSF)=	5453
Y-101= 795	CONCENTRATED COMPLEXED	
Y-102= 337	CONCENTRATED PHOSPHATE	
OTAL 4968	AGING SUPERNATE (AW)=	<u>1770</u>
MERGENCY SPACE -1140	DST SOLIDS (NO LIQUID)=	3265
	DST SLUDGE / SALTCAKE LIQ	JID= 991
AW of HLW RETURN -1140	DOT SCOOL OF CHARLES	91 <u>0 - </u>

20627

TOTAL*

Table C-2. Double-Shell Tank Waste Inventory - March 31, 2001

TOTAL AVAILABLE TANK SPACE	AS OF MAR	RCH 31, 2001 =	10689 KGALS
WATCH LIST TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE
Unusable DST Headspace - Due to Special Restrictions	AN-103	— - -	183 KGALS
Placed on the Tanks, as Stated in the "Wyden Bill"	AN-104	DSSF	88 KGALS
	AN-105	DSSF	12 KGALS
	AW-101		14 KGALS
	SY-103	CC	398 KGALS
		TOTAL=	695 KGALS
		AVAILABLE TANK SPACE=	10669 KGALS
TOTAL AVAILABLE SPACE AFTER WA		NUS WATCH LIST SPACE=	-695 KGALS 9974 KGALS
IVALAIALABLE STACE A 1-1 III		or not because	277 NOALS
RESTRICTED TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE
OST Headspace Available to Store Only Specific Waste Ty	P AN-102	CC	85 KGALS
•	AN-107	CC	100 KGALS
	AP-102	CP	52 KGALS
	AZ-101	= :	49 KGALS
	AZ-102	AW	0 KGALS
	SY-101		170 KGALS
	0	TOTAL*	456 KGALS
AVAILABLE SPACE AFTER WA	TCH LIST S	SPACE DEDUCTIONS=	9974 KGALS
AVAIDABLE OF NOT TER TAX		S RESTRICED SPACE=	-456 KGALS
TOTAL AVAILABLE SPACE AFTER RES		V	9518 KGALS
OPERATIONAL TANK SPACE	TANK	WASTE TYPE	AVAILABLE SPACE
OST Headspace Available For Facility Generated	AN-101	DN	893 KGALS
Vaste and 242-A Evaporator Operations	AP-108	DN	1103 KGALS
	AW-102	DN	1055 KGALS
	AW-105	NCRW	714 KGALS
	AW-106	DSSF	576 KGALS
	SY-102	DC	219 KGALS
		TOTAL*	4580 KGALS
AVAILABLE SPACE AFTER RES	TRICTED S	SPACE DEDUCTIONS=	9518 KGALS
	MINUS	OPERATIONAL SPACE=	-4560 KGALS
TOTAL AVAILABLE SPACE AFTER OPE	RATIONAL	SPACE DEDUCTIONS*	4958 KGALS
NON-ALLOCATED TANK SPACE	_ TANK_	WASTE TYPE	AVAILABLE SPACE
ion-Alloctated DST Headspace	AN-106	CC	1102 KGALS
•	AP-101	DSSF	27 KGALS
	AP-103		859 KGALS
	AP-104		32 KGALS
	AP-105		6 KGALS
	AP-106		518 KGALS
	AP-107		158 KGALS
		DSSF/NCRW	300 KGALS
	AW-104		824 KGALS
	AY-101	-	795 KGALS
	AY-102		337 KGALS
TOTAL	NON-ALLC	OCATED TANK SPACE=	4968 KGALB
EMERGEN	NCY TANK	SPACE	-1140 KGALS
EMEKGE!			
LAW or H	LW RETUE	RN SPACE:	-1140 KGALS

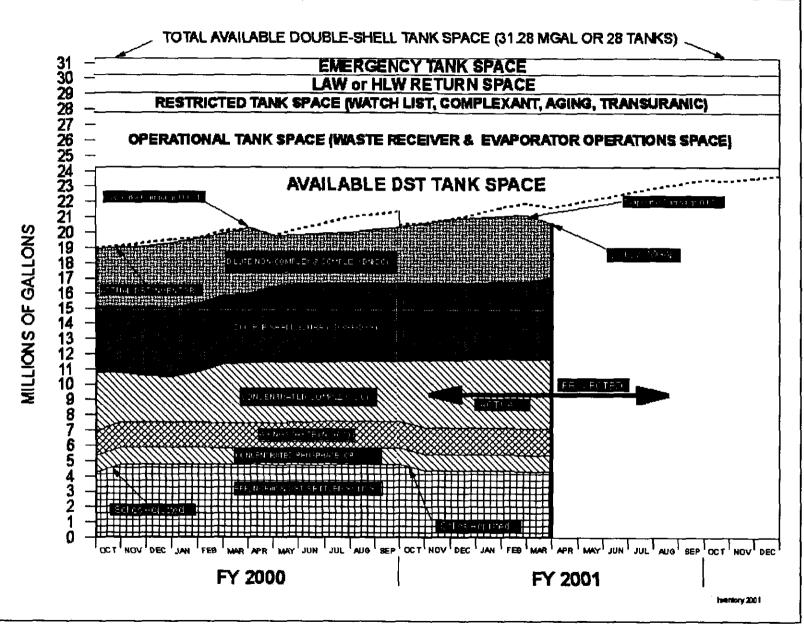


Figure C-1. Total Double-Shell Tank Inventory

APPENDIX D

WASTE TANK SURVEILLANCE MONITORING TABLES

TABLE D-1. TEMPERATURE MONITORING IN WATCH LIST TANKS (Sheet 1 of 2) March 31, 2001

These tanks have been identified as Watch List Tanks in accordance with Public Law 101-510, Section 3137, "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," (1990), because they "... may have a serious potential for release of high-level waste due to uncontrolled increases in temperature or presssure."

All Watch List tanks are reviewed for increasing temperature trends. Temperatures in these tanks are monitored by the Tank Monitor And Control System (TMACS), unless indicated otherwise.

Temperatures are taken in the waste unless in-waste thermocouples are out of service. Temperatures below are the highest temperatures recorded in these tanks during this month.

Temperatures in Degrees F.

		HYDROGEN (FI	LAMMABLE C	GAS)	
Single-Shell Tanks			Double-Shell Tanks		
		Officially Added to	}	Off	icially Added to
Tank No.	Temp.	Watch List	Tank No.	Temp.	Watch List
A-101	144	1/91	AN-103	102	1/91
AX-101	128	1/91	AN-104	104	1/91
AX-103	105	1/91	AN-105	101	1/91
S-102	100	1/91	AW-101	98	6/93
S-111	89	1/91	SY-103	94	1/91
S-112	83	1/91	5 DST*		
SX-101	127	1/91			
SX-102	139	1/91			
SX-103	153	1/91			
SX-104	137	1/91	ļ		
SX-105	157	1/91			
SX-106	97	1/91	}		
SX-109 (1)	132	1/91		19 Single-She	il Tanks
T-110	63	1/91	1	5 Double-She	ll Tanks
U-103	86	1/91	Į.	24 Tanks on 1	Watch List
U-105	87	1/91			
U-107	78	12/93	1		
U-108	86	1/92	}		
U-109	84	1/91			
19 5578					

All tanks were removed from the Ferrocyanide Watch List and 18 tanks from the Organics Watch List. Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999. The remaining two tanks (C-102 and C-103) were removed from the Organics Watch List in August 2000. DST SY-101 was removed from the Hydrogen Watch list on January 11, 2001.

TABLE D-1. TEMPERATURE MONITORING IN WATCH LIST TANKS (sheet 2 of 2)

Notes:

Unreviewed Safety Question (USQ):

When a USQ is declared, special controls are required, and work in the tanks is limited. There are currently no USQs on any tanks.

Hydrogen/Flammable Gas:

These tanks are suspected of having a significant potential for hydrogen/flammable gas generation, entrapment, and episodic release. The USQ associated with these tanks was closed in September 1998. Twenty-four tanks (19 SST and 5 DST) remain on the Hydrogen Watch List.

High Heat:

These tanks contain heat generating strontium-rich sludge and require drainable liquid to be maintained in the tank to promote cooling. There are currently nine tanks on the High Heat Load List but no tanks on the High Heat Load Watch List.

Active ventilation:

There are 15 single-shell tanks on active ventilation (seven are on the Watch List as indicated by an asterisk):

C-105	SX-107
C-106 (2)	SX-108
SX-101 *	SX-109 * (1)
SX-102 *	SX-110
SX-103 *	SX-111
SX-104 *	SX-112
SX-105 *	SX-114
SX-106 *	

Footnotes:

- (1) Tank SX-109 is on the Hydrogen Watch List as it has the potential for flammable gas accumulation only because other SX tanks vent through it.
- (2) Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999.

TABLE D-2. TEMPERATURE MONITORING IN NON-WATCH LIST TANKS March 31, 2001

SINGLE-SHELL TANKS WITH HIGH HEAT LOADS (>26,000 Btu/hr)

Nine tanks have high heat loads for which temperature surveillance requirements are established by HNF-SD-WM-TSR-006, Rev 1, Tank Waste Remediation System Technical Safety Requirements, December 1999.

In an analysis, WHC-SD-WM-SARR-010, Rev 1, Heat Removal Characteristics of Waste Storage Tanks, Kummerer, 1995, it was estimated that nine tanks have heat sources >26,000 Btu/hr, which is the new parameter for determining high heat load tanks. See also document HNF-SD-WM-BIO-001, Rev 1, Tank Waste Remediation System Basis for Interim Operation, Noorani, 1998.

Temperatures in these tanks did not exceed the Technical Safety Requirements (TSR) for this month, and are monitored by the Tank Monitoring and Control System (TMACS), unless indicated otherwise.

All high heat load tanks are on active ventilation.

Tank No.	Temperatu	re (F.)
C-106 (1)	61	(Riser #8)
SX-103	153	
SX-107	162	
SX-108	179	
SX-109 (2)	132	
\$X-110	161	
SX-111	179	
SX-112	144	
SX-114	172	
9 Tenke		

Notes:

- (1) C-106 was removed from the High Heat Load Watch List on December 16, 1999. The final thermal analysis report, RPP-6463, Rev. 0, "Thermal Analysis for Tanks 241-AY-102 and C-106," was issued August 9, 2000. The report concluded that the best estimate heat load for C-106 is between 7,000 and 11,000 Btu/hr. Although it no longer meets the criteria for a high heat load tank, an AB amendment is required to revise the temperature control limits and monitoring frequency. The AB Amendment request is pending review by ORP, and is expected to be approved in April 2001.
- (2) SX-109 is on the Hydrogen Watch List as it has the potential for flammable gas accumulation only because the other SX tanks vent through it.

SINGLE-SHELL TANKS WITH LOW HEAT LOADS (<26,000 Btu/hr)

There are 114 low heat load non-watch list tanks. Temperatures in tanks connected to TMACS are monitored by TMACS; temperatures in those tanks not yet connected to TMACS are manually taken semiannually in January and July. Temperatures obtained semiannually have been within historical ranges for the applicable tank.

No temperatures have been obtained for several years in the tanks listed below. Most of these tanks have no thermocouple tree.

	Tank Numbers	
BX-104	SX-115	TX-110
BY-102	T-102	TX-114
BY-109	T-105	TX-116
C-204	TX-101	TX-117
		U-104

TABLE D-3. ADDITIONS/DELETIONS TO WATCH LISTS BY YEAR March 31, 2001

Added/Deleted dates may differ from dates that tanks were officially added to the Watch Lists. (See Table D-1).

							arika
	Ferrocyanide	Hydrogen	Organics 8	High Heat		ST D	ST Total
1/81 Original List Response to Public Lew 101-8. Added 2/91 (revision to Original List)	23 1 T-107	23			200	_1]_	1
Tats) - December 3), 1991 Added 8/92	24	23 1 AW-101	8)		48	6 63 1 1
Total - Devember 31, 1982	25	24	8	1		40	6 54
Added 3/83 Deleted 7/93	-4 (BX-110)		1 U-111	ĺ		-4	
	(BX-111) (BY-101)		l	Ì			
Added 12/93	(T-101)	1 (U-107)	}			٥	
Total « December 31, 1993	20	26		1		4	6 51
Added 2/94 Added 5/94			1 T-111 10 A-101	j		4	
			AX-102 C-102			-	
			S-111 SX-103				
(TY-104 U-103			- [- (
Ì		}	U-105 U-203			ł	
			บ-203 บ-204				}
Deleted 11/94	-2 (BX-102) (BX-106)					-2	
Total - December 31, 1395 Deleted 6/96	18 -4 (C-108)	25	20			48	6 54
Deligited 0/80	(C-109)						
	(C-111) (C-112)						
Deleted 9/96	-14 (BY-103) (BY-104)		j			-12	
}	(BY-105) (BY-106)					-	1
	(BY-107) (BY-108)					- }	
	(BY-110)						
	(BY-111) (BY-112)						
[(T-107) (TX-118)					- (
1	(TY-101) (TY-103)		ı			- {	1 1
Deleted 12/98	(TY-104)		-18 (A-101)			10	
Deleted 12/30			(AX-102)			"	
			(B-103) (S-102)]	
	;		(S-111) (SX-103)			ļ	
{	I		(\$X-106) (T-111)	ľ		ſ	
			(TX-105) (TX-118)	1		Ì	1
}			(TY-104)			}	} }
]			(U-103) (U-105)				
]) I	(U-106) (U-107)				
			(U-111) (U-203)				
		N.	(U-204)			2009/2 2000	
Total - December 31, 1998 Deleted 12/99	0	26	2	-1 (C-106)		22 -1	6 28
Deleted 08/00			-1 (C-102) -1 (C-103)		Ŧ	7	\dashv
Deleted 01/01		-1 (SY-101)			533 SAX		-1
Total - March 31, 2001	0	24	0	0	**	19	5 24

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS 149 TANKS (Sheet 1 of 6) March 31, 2001

The following table indicates whether Single-Shell tank monitoring was in compliance with the requirements as specified in the applicable documents as of the last day of the applicable month:

NOTE:

All Watch List and High Heat tank temperature monitoring is in compliance. (4)

All Dome Elevation Survey monitoring is in compliance

Psychrometrics monitoring is on "as needed" basis (2).

Drywell monitoring no longer required (5). In-tank photos/videos are taken "as needed"

LEGEND:	
(Shaded)	= in compliance with all applicable documentation
N/C	= noncompliance with applicable documentation
O/S	= Out of Service
Neutron	 LOW readings taken by Neutron probe
POP	= Plant Operating Procedure, TO-040-650
MT/FIC/ ENRAF	= Surface level measurement devices
OSD	= Operating Spec. Doc., OST-T-151-00013, 00030, 00031
N/A	 Not applicable (not monitored, or no monitoring schedule)
None	 Applicable equipment not installed
FSAR/TSR	 Final Safety Analysis Report/Technical Safety Requirements

		Category	Temperature	Primary Leak	Surf	ace Level Read (OSD)	ings (1)	LOW Readings
Tank	Watch	High	Readings	Detection		(OSD)(5,7)		
Number	List	Heat	(4)	Source (5)	MT	FIC	ENRAF	Neutron
A-101	X			LOW	None	None		
A-102				None	None		None	None
A-103				FOM	None	None		
A-104				None	None	None		None
A-105				None		None	None	None
A-106				None	None	None		None
AX-101				LOW	None	None		(9)
AX-102				None	None	None		None
AX-103	X			None	Hone	None		None
AX-104				None	None	None		None
B-101				None	None	None		None
B-102				ENRAF	None	None		None
3-103				None	None	None		0/6
B-104				LOW	None	None		
B-105				LOW	None	None		
B-106				ENRAF	None	None		None
B-107				None	None	None		None
B-108				None	None	None		None
B-109				None	None	None		None
B-110				LOW	None	Nane		
3-111				LOW	None	None		
B-112				ENRAF	Nore	None		None
3-201				ENRAF	None	None		None
3-202				ENRAF	None	Name		None
3-203				ENRAF	None	None		None
3-204				ENRAF	None	None		None
3X-101				ENRAF	None	None	(13)	None
3X-102				None	lione	None		None
3X-103				ENRAF	None	None	(13)	None
BX-104			None	ENRAF	None	None	(13)	Note
3X-105				None	None	None		None
3X-106				ENRAF	fione	None		None
3X-107				ENRAF	Nene	None	(13)	None

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS
149 TANKS (Sheet 2 of 6)

	Tank	Category	Temperature	Primary Leak	Surfa	LOW Readings		
Tank	Watch High		Readings	Detection	1	(OSD)(5,7)		
Number	List	Heat	(4)	Source (5)	MI	FIC	ENRAF	Neutron
BX-108				None	None	None		None
BX-109				None	Norre	None		None
BX-110				None	None	Norte		Name
BX-111				LOW	None	Nune		
BX-112				ENRAF	None	None	(13)	None
BY-101				LOW		None	None	
BY-102			NOTE	LOW	None	None		
BY-103				LOW	None	None		
BY-104				LOW		None	None	
BY-105				LOW		None	None	
BY-106				LOW		None	None	
BY-107				LOW		None	None	
BY-108				None		None	None	None
BY-109			None	LOW	None	0/6	None	
BY-110	_			LOW	None	None		
BY-111				LOW	None	None		
BY-112				LOW		None	None	
C-101				None		None	None	None
C-102 (10)				None	None		None	None
C-103 (10)				ENRAF	None	None		None
C-104				None	None	None		None
C-105				None	None	None		None
C-106 (3)	_	X		ENRAF	None	None		None
C-107	_			ENRAF	None	None		None
C-10B				None		None	None	None
C-109				None		None	None	None
C-110	_			MT		None None	None None	None
C-111	_			None		None	19(07)#	None
C-112				None	None	None		None
C-201				None			None	None
C-202	_			None None		None	None None	None
C-203			None	None		None	None	None
C-204 S-101			2	ENRAF	None	None	iesiie	140/12
S-102	Х			LOW	None	None		
S-102				ENRAF	None	None		
S-103				LOW	None	None		
S-105	-			LOW	None	None		
S-106				LOW	None	None		
S-107				ENRAF	None	None		None
S-107				LOW	None	None		
S-109				LOW	None	None		
S-110				LOW	None	None		
S-111	Х			ENRAF	None	None		
S-112	Х			LOW	None	None		
SX-101	Х			LOW	None	None		
SX-102	X			LOW	None	None		
SX-103	X	Х		LOW	None	None		
SX-104	Х			LOW	None	None		
SX-105	X			LOW	None	None		Q/\$ (111)
SX-106	×			LOW	None	None		
SX-107		Х		None	None	None		None
\$X-108		×		None	Ngne	None		None

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS 149 TANKS (Sheet 3 of 6)

	Tank Ca	stegory	Temperature	Primary Loak	Surf	ngs (1)	LOW Readings	
Tank	Watch High		Readings	Detection	1	(OSD)(5,7)		
Number	List	Heat	(4)	Source (5)	Mi	FIC	ENRAF	Neutron
SX-109	X	Х		None	None	None		None
SX-110		X		None	None	Mone		None
SX-111		,		None	None	None		Vicina
SX-112		Х		None	None	None		None
SX-113				None	None	None		None
SX-114				None	None	None		None
SX-115			None	None	None	None		None
T-101				None	None	None		None
T-102			None	ENRAF	None	None		None
T-103				None	None	None		None
T-104				LOW	None	None		***
T-106 T-106			None	None None	None None	None None		None
T-107				ENRAF	None	None		None
T-107				ENRAF	None	None		None
T-109				None	None	None		None
T-110	×			LOW	None	None		- ALUINO
T-111				LOW	None	None		
T-112				ENRAF	None	None		None
T-201				MT		None	None	None
T-202				MT		Bione	None	None
T-203				None		None	None	None
T-204	_			MT		None	None	None
TX-101			None	ENRAF	None	None		None
TX-102				LOW	None	None		
TX-103				None	None	None		None
TX-104				None	None	None		None
TX-105				None	None	None		None (B)
TX-106				LOW	None	None		
TX-107				Nane	None	None		None
TX-108				None	None	None		None
TX-109				LOW	Nema	Bones		
TX-110			None	LOW	Nove	None		
TX-111				LOW	None	None		
TX-112				LOW	None	None		
TX-113				LOW	None	None		
TX-114			None	LOW	None	None		
TX-115				LOW	None	None		
TX-116			None	None	None	None		Reite
TX-117			None	LOW	None	None		
TX-118				LOW	None	None		
TY-101				None	None	None		None
TY-102				ENRAF	None	None		None
TY-103				LOW	None	None		
TY-104				ENRAF	None	None		None
TY-105				None	None	None		None
TY-106				None	None	None		None
U-101	_			MT		None	None	Pione
U-102	-			LOW	None	None		
U-103	Х		None		None	Acres None	None	None
U-104	х		NUID	LOW	None	None), -), -), -), -), -), -), -), -	17.11
U-105 U-106	•			LOW	None	None		

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS 149 TANKS (Sheet 4 of 6)

	Tank Category		Temperature	Primary Leak	Suri	Surface Level Readings (1)					
Tank	Watch	High	Readings	Detection	1	(OSD)					
Number	List	Heat	(4)	Source (5)	МТ	FIC	ENRAF	(OSD)(5,7) Neutron			
U-107	×			ENRAF	None	Name					
U-108	X			LOW	None	None					
U-109	×			LOW	None	None					
U-110				None	None	None		None			
U-111				LOW	Noise	None					
U-112				None		None	None	None			
U-201				MT		None	None	None			
U-202				MT		None	None	None			
U-203				None	None	None		None			
U-204				ENRAF	None	None		None			
Catch Tanks a	nd Special Su	naillence Fe	cilities								
A-302-A	N/A	N/A	N/A	(6)	None	None		None			
A-302-B	N/A	N/A	N/A	(6)		None	None	None			
ER-311	N/A	N/A	N/A	(6)	None	None		None			
AX-152	N/A	N/A	N/A	(6)(12)		None	None	None			
AZ-151	N/A	N/A	N/A	(6)	Name		None	None			
AZ-154	N/A	N/A	N/A	(6)		None	Name	None			
BX-TK/SMP	N/A	N/A	N/A	(6)		None	None	None			
A-244 TK/SMP	N/A	N/A	N/A	(6)	None	None	None	None			
AR-204	N/A	N/A	N/A	(6)	None	None	None	None			
A-417	N/A	N/A	N/A	(6)	Norm	None	None	None			
A-350	N/A	N/A	N/A	(6)	None	None	None	None			
CR-003	N/A	N/A	17.	(8)	None	Norse	None	None			
Vent Sta.	N/A	NIA	N/A	(6)		None	None	None			
244-S TK/SMP	N/A	N/A	N/A	(6)	None	None	None	None			
S-302	N/A	N/A	N/A	(6)	None	None		None			
S-304	N/A	N/A	N/A	(6)	None	None		None			
TX-244 TK/SMP	N/A	N/A	N/A	(6)		None	None	None			
ТХ-302-В	N/A	N/A	N/A	(0)		None	None	None			
TX-302-C	N/A	N/A	N/A	(6)	None	None		None			
U-301-B	N/A	N/A	N/A	(6)	None	None		Name			
UX-302-A	N/A	N/A	N/A	(8)	None	None		None			
S-141	N/A	N/A	N/A	(6)	0/\$	None	Norse	None			
S-142	N/A	N/A	N/A	(6)	0/5	None	None	None			
Totals:	19	9	N/C: 0		N/C: O	N/C: 0	N/C: 0	N/C: 0			
149 tenks	Hydrogen Watch List Tanks	High Heat Tanks (non- Watch List)									

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS -149 TANKS (Sheet 5 of 6)

Footnotes:

1. All SSTs have either manual tape, FIC, or ENRAF surface level measuring devices. Some also have zip cords.

ENRAF gauges are being installed to replace FICs (or sometimes manual tapes). The ENRAF gauges are being connected to TMACS, but many are currently being read manually from the field. See Table D-6 for list of ENRAF installations.

2. High heat tanks have active exhausters; psychrometrics can be taken in the high heat tanks. Psychrometric readings are not required by OSD, but can be taken on an "as needed" basis.

Psychrometric readings are taken annually in SX-farm.

- 3. Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999.
- 4. Temperature readings may be regulated by OSD, POP, or FSAR (FSAR only regulates high heat load tanks). Temperatures cannot be obtained in 13 low heat load tanks (see Table D-2). The OSD does not require readings or repair of out-of-service thermocouples for the low heat load (<26,000 Btu/h) tanks. However, the POP requires that attempts are to be made semiannually in January and July to obtain readings for these tanks.

Temperatures in some tanks cannot be taken in the waste because the waste level is lower than the lowest thermocouple in these trees.

Temperatures for many tanks are monitored continuously by TMACS; see Table D-7, TMACS Monitoring Status.

5. Document OSD-T-151-00031, "Operating Specifications for Tank Farm Leak Detection," Rev. D-2, December 7, 2000, requires that single-shell tanks with the surface level measurement device contacting liquid, partial liquid, or floating crust surface, will be monitored for leak detection on a daily basis. Tanks with a solid surface will be monitored for leak detection on a weekly basis by taking neutron scan data from a Liquid Observation Well (LOW), if an LOW is present. Tanks with a solid surface but without LOWs will not be monitored for leak detection until an LOW is installed. The OSD specifies what leak detection methods are to be used for each tank, and the requirements if the readings are not taken on the required frequency or if equipment is out of service.

This OSD revision does not require drywell surveys to be taken; drywell scans will only be taken by special request, since any scans would have to be subcontracted. The contractor no longer has drywell scanning equipment.

6. Leak detection for the catch tanks is performed by monitoring for the buildup of liquid in the secondary containment (for most tanks with secondary containment) or for decrease in the liquid level for those tanks without secondary containment or Catch tank 241-S-302 is monitored for intrusions only, and is not subject to leak detection monitoring requirements until liquid is present above the intrusion level.

Weight Factor is the surface level measuring device currently used in A-417, A-350, 244-A Tank/Sump, and 244-S Tank/Sump. Double-Shell Receiver Tank (DCRT) CR-003 is inactive and measured in gallons. 204-AR is also measured in gallons.

7. Document SD-WM-TI-605, REV. 0, dated January 1994, describes the rationale for Liquid Observation Well (LOW) installation priority. This priority is based on tank leak status, tank surface condition, and tank stabilization status. Also included is a listing of tanks with the waste level being below two feet, which have no priority assigned because no effort will be made to install LOWs in the near future. LOW probes are unable to accurately monitor interstitial liquid levels less than two feet high.

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS - 149 TANKS (Sheet 6 of 6)

Tanks which will not receive LOWs:

A-102	BX-101	C-201	T-106
A-104	BX-103	C-202	T-108
A-105	BX-105	C-203	T-109
AX-102	BX-106	C-204	TX-107
AX-104	BX-108	SX-110	TY-102
B-102	C-108	SX-113	TY-104
B-103	C-109	SX-115	TY-106
B-112	C-111	T-102	U-101
		T-103	U-112

Total - 34 Tanks

- 8. Tank TX-105 the LOW was in riser 8; the riser has been removed and the LOW has not been monitored since January 1987. Liquid levels are being taken in riser 9 by ENRAF and recorded in TMACS.
- 9. Tank AX-101 LOW readings are taken by gamma sensors.
- 10. Tanks C-102 and C-103 were removed from the Organics Salts Watch List on August 23, 2000
- 11. Tank SX-105 LOW scan not taken for week ending August 28, 2000. LOW is primary leak detection device; ENRAF is backup and monitored daily in TMACS. LOW has failed structurally, and will be replaced. Work Package 2H0005040. Fabrication shop has finished making the LOW. (Tank is currently being saltwell pumped).
- 12. Catch Tank AX-152 has been declared an "assumed leaker," per Occurrence Report RP-CHG-TANKFARM- 2001-0014, based on an engineering evaluation. The remaining liquid (water which was being used to perform a leak test of the catch tank) has been pumped to a double-shell tank.
- 13. BX farm is in power outage lasting about 2 weeks and putting the liquid level gauges in O/S condition. Power off as of March 30, 2001; no readings in BX-101, -103, -104, -107, and -112, which are daily requirements with no backup device specified. OSD-00031 states the gauges must be repaired in 14 days; if no readings are obtained by April 13, 2001, an OSD violation will occur. Discrepancy Report 01-890 was issued on April 2, 2001.

TABLE D-5. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS 28 TANKS (Sheet 1 of 2) March 31, 2001

specified in the applicable documents as of the last day of the applicable month.

The following table indicates whether Double-Shell tank monitoring was in compliance with the requirements as

NOTE:

Dome Elevation Surveys are not required for DSTs.

Psychrometrics and in-tenk photos/videos are taken "as needed" (2)

LEGEND: (Shaded) = In compliance with all applicable documentation N/C = Noncompliance with applicable documentation FIC/ENRAF = Surface level measurement devices M.T. OSD = OSD-T-151-0007, OSD-T-151-00031 None = no M.T., FIC or ENRAF installed 0/\$ - Out of Service W.F. = Weight Factor N/A = Not Applicable (not monitored or no monitoring schedule) Rad. = Radiation

						R	adiation Reading	js
Tank		Temperature Readings (3) (OSD)	Sur	face Level Rea (OSD)	dings (1)	Leak Det	Annulus	
Number	Watch List		M.T.	FIC	ENRAF	W.F.	Rad. (6)	(OSD)
AN-101				None			N/A	
AN-102				None			N/A	
AN-103	X			None			N/A	
AN-104	X		0/6	None			N/A	
AN-105			0/5	None			N/A	
AN-106				Name			N/A	
AN-107				None		6 7/8	N/A	
AP-101			0/8	None		0/5 (7)	N/A	0/8
AP-102				None		0/5 (7)	N/A	
AP-103				None		0/6 (7)	N/A	
AP-104			0/8	None		0/5 (7)	N/A	
AP-105				None		0/5 (7)	N/A	0/8
AP-106				None		0/5 (7)	N/A	
AP-107				None		0/6 (7)	N/A	0/\$
AP-108				None		0/5 (7)	N/A	
AW-101	7		0/8	None			N/A	
AW-102					(6)		N/A	
AW-103				None			N/A	
AW-104				None			N/A	
AW-105				None			N/A	
AW-106				None			N/A	
AY-101				None		0/8	N/A	0/\$
AY-102			0/5	None			N/A	0/5
AZ-101				None			N/A	0/8
AZ-102					None		N/A	0/5
SY-101	(10)		None	None		0/8 (9)	N/A	
SY-102			0/5 (6)	None			N/A	
SY-103	×		0/6 (8)	None		0/6 (9)	N/A	
Totals: 28 tanks	5 Watch List Tanks	N/C: 0	N/C: 0	N/C: 0	N/C: 0	N/C: 0	N/C: 0	N/C: 0

TABLE D-5. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS - 28 TANKS (Sheet 2 of 2)

Footnotes:

- Some double-shell tanks have both FIC and manual tape which is used when the FIC is out of service.
 Noncompliance (N/C) will be shown when no readings are obtained. ENRAF gauges are being installed to replace FICs. The ENRAF gauges are being connected to TMACS, but some are currently being read manually.
- 2. Psychrometric readings are taken on an "as needed" basis. No psychrometric readings are currently being taken in the double-shell tanks.
- 3. OSD specifies double-shell tank temperature limits, gradients, etc.
- 4. Applicable OSD and HNF-IP-0842, latest revisions, are used as guidelines for monitoring Leak Detection Pits. See also (6) and (7) below.
- 5. AW-102 has ENRAF, FIC and M.T. At some point the FIC will be removed.
- 6. USQ TF-97-0038, dated April 28, 1997, specifies discontinuing the use of leak detection pit radiation monitoring equipment in all double-shell tank farms where the leak detection pits are used as tertiary leak detection. This applies to all double-shell tank farms.
- Leak Detection Pit weekly readings are being obtained by Instrument Technicians in these tanks: AP-103C (for tanks AP-101 - 104) AP-105C (for tanks AP-105 - 108)
- SY-102 Manual Tape has sporadic readings. ENRAF is primary device.
 SY-103 Manual Tape has sporadic readings. ENRAF is primary device.
- SY-101 LDP readings are above normal range. EDL #S0007 to repair it.
 SY-103 LDP readings are above normal range. EDL #241-SY-95-5 to repair it.
- 10. SY-101 was removed from the Hydrogen Watch List on January 11, 2001.

TABLE D-6. ENRAF SURFACE LEVEL GAUGE INSTALLATION AND DATA INPUT METHODS

March 31, 2001

LEGEND

SACS TMACS = Surveillance Analysis Computer System

Auto

= Tank Monitor and Control System

= Automatically entered into TMACS and electronically transmitted to SACS

Manual

= Manually entered directly into SACS by surveillance personnel, from Field Data sheets

EAST /			2000					WEST			2002		,	
Tank	Installed	Input		Tank	Installed	Input		Tank	Installed	Input		Tank	Installed	Input
No	Date	Method		No.	Date	Method		No.	Date	Method		No.	Date_	Method
A-101	09/95	Auto		B-201	07/00	Auto		S-101	02/95	Auto		TX-101	11/95	Auto
A-102				B-202	07/00	Auto		S-102	05/95	Auto		TX-102	05/96	Auto
A-103	07/96	Auto		B-203	06/00	Auto	***	S-103	05/94	Auto	***	TX-103	12/95	Auto
A-104	05/96	Manual	200	B-204	06/00	Auto		S-104	05/99	Auto		TX-104	03/96	Auto
A-105			***	8X-101	04/96	Auto		S-105	07/95	Auto	***	TX-105	04/96	Auto
A-106	01/96	Auto		BX-102	06/96	Auto	***	S-106	06/94	Auto	200	TX-106	04/96	Auto
AN-101	08/96	Auto	***	BX-103	04/96	Auto		S-107	06/94	Auto	***	TX-107	04/96	Auto
AN-102	05/00	Auto	***	BX-104	05/96	Auto		S-108	07/95	Auto		TX-108	04/96	Auto
AN-103	08/95	Auto		BX-105	03/96	Auto		S-109	08/95	Auto	***	TX-109	11/95	Auto
AN-104	08/95	Auto	*	BX-106	07/94	Auto		S-110	08/95	Auto		TX-110	05/96	Auto
AN-105	08/95	Auto		BX-107	06/96	Auto		S-111	08/94	Auto		TX-111	05/96	Auto
AN-106	05/00	Auto		BX-108	05/96	Auto		S-112	05/95	Auto		TX-112	05/96	Auto
AN-107	04/00	Auto	***	BX-109	08/95	Auto		SX-101	04/95	Auto		TX-113	05/96	Auto
AP-101	06/99	Auto		BX-110	06/96	Auto		SX-102	04/95	Auto		TX-114	05/96	Auto
AP-102	08/99	Auto	***	BX-111	05/96	Auto	*	SX-103	04/95	Auto	***	TX-115	05/96	Auto
AP-103	08/99	Auto		BX-112	03/96	Auto		SX-104	05/95	Auto		TX-116	05/96	Auto
AP-104	07/99	Auto		BY-101				SX-105	05/95	Auto		TX-117	06/96	Auto
AP-105	08/99	Auto		BY-102	09/99	Auto	*	SX-106	08/94	Auto	**	TX-118	03/96	Auto
AP-106	08/99	Auto		BY-103	12/96	Auto	*	SX-107	09/99	Auto		TY-101	07/95	Auto
AP-107	08/99	Auto		BY-104			*	SX-108	09/99	Auto		TY-102	09/95	Auto
AP-108	08/99	Auto	***	BY-105				SX-109	09/98	Auto	***	TY-103	09/95	Auto
AW-101	08/95	Aute	***	BY-106			8	SX-110	09/99	Auto	88	TY-104	06/95	Auto
AW-102	05/96	Auto	~	BY-107				SX-111	09/99	Auto		TY-105	12/95	Auto
AW-103	05/96	Auto	***	BY-108				SX-112	09/99	Auto		TY-106	12/95	Auto
AW-104	01/96	Auto		BY-109				SX-113	09/99	Auto	8	U-101		
AW-105	06/96	Auto		BY-110	02/97	Manual		SX-114	09/99	Auto		U-102	01/96	Manual
AW-106	06/96	Auto	***	BY-111	02/99	Manuai		SX-115	09/99	Manuai	*	U-103	07/94	Auto
AX-101	09/95	Auto		BY-112				SY-101	07/94	Auto		U-104		
AX-102	09/98	Auto	**	C-101			*	SY-102	06/94	Auto	***	U-105	07/94	Auto
AX-103	09/95	Auto	*	C-102				SY-103	07/94	Auto		U-106	08/94	Auto
AX-104	10/96	Auto	*	C-103	08/94	Auto		T-101	05/95	Manual	*	U-107	08/94	Auto
AY-101	03/96	Auto	**	C-104	04/99	Manual		T-102	06/94	Auto	8	U-108	05/95	Auto
AY-102	01/98	Auto	*	C-105	05/96	Manual		T-103	07/95	Manual	***	U-109	07/94	Auto
AZ-101	08/96	Manual	▩	C-106	02/96	Auto		T-104	12/95	Manual		U-110	01/96	Manuai
AZ-102	11/00	Manual		C-107	04/95	Auto		T-105	07/95	Manusi		U-111	01/96	Manual
8-101	07/00	Auto	*	C-108			**	T-106	07/95	Manual		U-112		
3-102	02/95	Auto		C-109			8	T-107	06/94	Auto	**	U-201		
3-103	07/00	Auto	***	C-110			***	T-108	10/95	Manuai		U-202		
B-104	06/00	Auto	***	C-111			88	T-109	09/94	Manual		U-203	09/98	Manuai
3-105	08/00	Auto		C-112	03/96	Manuai		T-110	05/95	Auto	*	U-204	06/98	Manual
B-106	07/00	Auto	***	C-201				T-111	07/95	Manual				
3-107	06/00	Auto		C-202				T-112	09/95	Manual	***			
B-108	07/00	Auto		C-203			×	T-201			*			
B-109	08/00	Auto	*	C-204				T-202						
B-110	07/00	Auto						T-203			*			
B-111	07/00	Auto						T-204						
B-112	03/95	Auto	**								***			
	t Area: 71							Total W	est Area: 77					
				41 11		14400 00	288		ntered into S/		_		.	

148 ENRAFs installed: 125 automatically entered into TMACS, 23 manually entered into SACS

TABLE D-7. TANK MONITOR AND CONTROL SYSTEM (TMACS) March 31, 2001

Note: Indicated below are the number of tanks having at least one operating sensor monitored by TMACS.

Some tanks have more than one sensor: multiple sensors of the same type in a tank are not shown in the table (for example: 10 tanks in BY-Farm have at least one operating TC sensor and 3 tanks in BY-Farm have at least one operating RTD sensor).

Acceptance Testing Completed: Sensors Automatically Monitored by TMACS

	Temper				T .	Γ
[Resistance	ĺ	1		[
EAST AREA	Thermocouple	Thermal	ENRAF	ľ	ł	Gas
	Tree	Device	Level	Pressure	Hydrogen	Sample
Tank Farm	(TC)	(RTD)	Gauge	(b)	(c)	Flow
A-Farm (6 Tanks)	1	,	3	<u> </u>	1	1
AN-Farm (7 Tanks)	7		7	7	3	3
AP-Farm (8 Tanks)			8		 	
AW-Farm (6 Tanks)	6		6		1	1
AX-Farm (4 Tanks)	3		4		1	
AY-Farm (2 Tanks)			2		T	
AZ-Farm (2 Tanks)					f	
B-Farm (16 Tanks)	1		16	1		
BX-Farm (12 Tanks)	11		12			
BY-Farm (12 Tanks)	10	3	2			
C-Farm (16 Tanks)	15 (f)	1	3	1		
TOTAL EAST AREA				[
(91 Tanks)	54	4	63	8_	6	5
WEST AREA		!				
S-Farm (12 Tanks)	12		12	1	3	1 (e)
SX-Farm (15 Tanks)	14		14	1	7	5 (e)
SY-Farm (3 Tanks) (a)	3		3	1	2	2
T-Farm (16 Tanks)	14	1	3 (d)		1	(e)
TX-Farm (18 Tanks)	13		18			
TY-Farm (6 Tanks)	6	3	6			
U-Farm (16 Tanks)	15		6	4	6	6
TOTAL WEST AREA]]	J	J
(86 Tanks)	77	4	62	7	19	19
TOTALS (177 Tanks)	131	8	125	15	25	24

- (a) Tank SY-101 has 2 gas sample flow sensors plus 2 vent flow sensors, and 2 ENRAFs.
- (b) Each tank has two sensors (high and low range).
- (c) Each tank has two sensors (high and low range).
- (d) T-107 Auto ENRAF O/S, manual readings taken daily
- (e) S, SX, and T-Farms five gas sample flow sensors have been unhooked or removed. Will eventually use SHMS equipment on other tanks but none scheduled yet.
- (f) C-105 acromag needs replacing. Manual readings are taken weekly.

APPENDIX E

MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPECIAL SURVEILLANCE FACILITIES

TABLE E-1. EAST AND WEST AREA MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPECIAL SURVEILLANCE FACILITIES

ACTIVE - still running transfers through the associated diversion boxes or pipeline encasements March 31, 2001

EACILITY	LOCATION	PURPOSE (receives waste from:)	(Gallons)	MONITORED BY	REMARKS
EAST AREA					
241-A-302-A	A Farm	A-151 DB	673	SACS/ENRAF/Manually	Pumped to AW-105 7/00
241-ER-311	B Plant	ER-151, ER-152 DB	8708	SACS/ENRAF/Manually	
241-AX-152	AX Farm	AX-152 DB	0	SACS/MT	Declared Assumed Leaker; pumped to AY-102 3/1/01
241-AZ-151	AZ Farm	AZ-702 condensate	2710	SACS/ENRAF/TMACS	Volume changes daily - pumped to AZ-101 or AZ-102 as needed
241-AZ-154	AZ Farm		25	SACS/MT	
244-BX-TK/SMP	BX Complex	DCRT - Receives from several farms	18594	SACS/MT	Using Manual Tape for tank/sump, pumped 10/16/99 to 66.0 in. Sump 0/S 2/5/01
244-A-TK/SMP	A Complex	DCRT - Receives from several farms	6801	MCS/SACS/WTF	WTF- pumped 3/99 to AP-108
A-350	A Farm	Collects drainage	290	MCS/SACS/WTF	WTF (uncorrected) pumped as needed
AR-204	AY Farm	Tanker trucks from various facilities	240	DIP TUBE	Alarms on SACS-pumped to AP-108, 7/00
A-417	A Farm		12344	SACS/WTF	WTF (uncorrected) pumped 4/98
CR-003-TK/SUMP	C Farm	DCRT	3007	MT/ZIP CORD	Zip cord in sump O/S 3/11/96, water intrusion, 1/98
WEST AREA					
241-TX-302-C	TX Farm	TX-154 DB	155	SACS/ENRAF/Manually	
241-U-301-B	U Farm	U-151, U-152, U-153, U-252 DB	8022	SACS/ENRAF/Manually	Returned to service 12/30/93
241-UX-302-A	U Plant	UX-154 DB	3182	SACS/ENRAF/Manually	
241-S-304	\$ Farm	S-151 DB	128	SACS/ENRAF/Manually	Replaced S-302-A, 10/91; ENRAF installed 7/98
					Sump not alarming.
244-S-TK/SMP	S Ferm	From original tanks to SY-102	14195	SACS/Manually	WTF (uncorrected)
244-TX-TK/SMP	TX Farm	From original tanks to SY-102	11590	SACS/Manually	MT - pumped PFP 241-Z tank D-5 to 244-TX DCRT on 11/22/00, level now 56.50"
Vent Station Catch 1	Γenk	Cross Country Transfer Line	374	SACS/Manually	MT

Total Active Facilities 18

LEGEND: DE - Diversion Box

DCRT - Double-Contained Receiver Tank

TK - Tank

SMP - Sump

FIC - Food instrument Corporation measurement device

MT - Matural Tape

Zip Cord - surface level measurement device

WTF - Weight Time Factor - can be recorded as WTF,

CWF (corrected), and Uncorrected WTF

SACS - Surveillance Automated Control System

MCS - Monitor and Control System

Manually - Not connected to any automated system

O/S - Out of Service

ENRAF - Surface Level Measuring Device

R - Usually denotes replacement NM - Not Monitored

TABLE E-2. EAST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES INACTIVE - no longer receiving waste transfers

March 31, 2001

				MONITOR	RED
EACILITY	LOCATION	RECEIVED WASTE FROM:	(Gallons)	<u>BY</u>	REMARKS
216-BY-201	BY Farm	TBP Waste Line	Unknown	NM	(216-BY)
241-A-302-B	A Farm	A-152 DB	5759	SACS/MT	Isolated 1985, Project B-138 Interim Stabilized 1990, Rain intrusion
241-AX-151	N of PUREX	PUREX	Unknown	NM	Isolated 1985
241-B-301-B	B Farm	B-151, B-152, B-153, B-252 DB	22250	NM	Isolated 1985 (1)
241-B-302-B	B Farm	B-154 DB	4930	NM	Isolated 1985 (1)
241-BX-302-A	BX Farm	BR-152, BX-153, BXR-152, BYR-152 DB	840	NM	Isolated 1985 (1)
241-BX-302-B	BX Farm	BX-154 DB	1040	NM	Isolated 1985 (1)
241-BX-302-C	BX Farm	BX-155 DB	870	NM	Isolated 1985 (1)
241-C-301-C	C Farm	C-151, C-152, C-153, C-252 DB	10470	NM	Isolated 1985 (1)
241-CX-70	Hot Semi-	Transfer lines	Unknown	NM	Isolated, Decommission Project,
241-CX-72	Works	Transfer lines	650	NM	See Dwg H-2-95-501, 2/5/87
241-ER-311A	SW B Plant	ER-151 DB	Unknown	NM	Isolated
244-AR VAULT	A Complex	Between farms & B-Plant	Unknown	NM	Not actively being used. Systems activated for final clean-out.
244-BXR-TK/SMP-001	BX Farm	Transfer lines	7200	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-002	BX Farm	Transfer lines	2180	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-003	BX Farm	Transfer lines	1810	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-011	BX Farm	Transfer lines	7100	NM	Interim Stabilization 1985 (1)
361-B-TANK	B Plant	Drainage from B-Plant	Unknown	NM	Interim Stabilization 1985 (1)
		Total East Area inactive facilities	18	LEGEND:	DS - Diversion Box.
					DCRT - Double-Contained Receiver Tank MT - Manual Tape
					BACS - Surveillance Automated Control System TK - Tank

244-TXR-TK/SMP-003 TX Farm

SE of U Plant

T Plant

U Plant

270-W

361-T-TANK

361-U-TANK

TABLE E-3. WEST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES

INACTIVE - no longer receiving waste transfers March 31, 2001

Unknown

Unknown

Unknown

Unknown

MONITORED

NM

NM

NM

NM

<u>EACILITY</u>	<u>LOCATION</u>	<u>RECEIVED WASTE FROM:</u>	<u>(Gallons)</u>	<u>BY</u>	<u>REMARKS</u>
216-TY-201	E. of TY Farm	Supernate from T-112	Unknown	NM	Isolated
231-W-151-001	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
231-W-151-002	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
241-S-302	S Farm	240-S-151 DB	8376	SACS/ENRAF	Assumed Leaker EPDA 85-04
241-S-302-A	S Farm	241-S-151 DB	0		Assumed Leaker TF-EFS-90-042
Partially	filled with grout 2/91,	determined still assumed leaker after lea	k test. Manual F	C readings are un	obtainable due to dry grouted surface

Partially fill	ed with grout 2/91.	determined still assumed leaker after leak t	test. Manual F	IC readings are w	nobteinable due to dry grouted euréeae
CASS mon	itoring system retire	ed 2/23/99; intrusion readings discontinued	. S-304 replac	ed S-302-A	montainable das to di A Bionted antiscs.
241-S-302-B	S Farm	S Encasements	Unknown	NM	Isolated 1985 (1)
241-SX-302	SX Farm	SX-151 DB, 151 TB	Unknown	NM	Isolated 1987
241-SX-304	SX Farm	SX-152 Transfer Box, SX-151 DB	Unknown	NM	Isolated 1985 (1)
241-T-301	T Farm	DB T-151, -151, -153, -252	Unknown	NM	Isolated 1985 (241-T-301B)
241-TX-302	TX Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TX-302-X-B	TX Farm	TX Encasements	Unknown	NM	Isolated 1985 (1)
241-TX-302-B	TX Farm	TX-155 DB	1600	SACS/MT	New MT installed 7/16/93
241-TX-302-B(R)	E. of TX Farm	TX-155 DB	Unknown	NM	Isolated
241-TY-302-A	TY Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TY-302-B	TY Farm	TY Encasements	Unknown	NM	Isolated 1985 (1)
241-Z-8	E. of Z Plant	Recupiex waste	Unknown	NM	Isolated, 1974, 1975
242-T-135	T Evaporator	T Evaporator	Unknown	NM	Isolated
242-TA-R1	T Evaporator	Z Plant waste	Unknown	NM	Isolated
243-S-TK-1	N. of S Farm	Pers. Decon. Facility	Unknown	NM	Isolated
244-U-TK/SMP	U Farm	DCRT - Receives from several farms	Unknown	NM	Not yet in use
244-TXR VAULT	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-001	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-002	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
AAA TVD TV (CNAD AAA	TV C	T			_ ,,

Total West Area inactive facilities 14 LEGEND: DB - Diversion Box, TB - Transfer Box DCRT - Double-Contained Receiver Tank TK - Tank SMP - Sumo R - Usually denotes replacement FIC - Surface Level Monitoring Device MT - Manual Tops O/S - Out of Service SACS - Surveillance Automated Control System NM - Not Monitored **ENRAF** - Surface Level Monitoring Device

Isolated 1970

Isolated 1985 (1)

Interim Stabilized, MT removed 1984 (1)

Interim Stabilzed, MT removed 1984 (1)

HNF-EP-0182, Rev. 156

(1) SOURCE: WASTE STORAGE TANK STATUS & LEAK DETECTION CRITERIA document

Transfer lines

Condensate from U-221

Drainage from T-Plant

Drainage from U-Plant

APPENDIX F LEAK VOLUME ESTIMATES

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 1 of 5) March 31, 2001

Tark Number			Date Declared Confirmed or	Associated KiloCuries	Interim Stabilized	Leak Estimate			
241-A-104 1975 500 to 2500	Tank Number		Assumed Leaker (3)	Gallons (2)		137 cs (10)	Date (11)	Updated	Reference
241-A-104 (11) 1968 (1900) (18) (18) (18) (18) (18) (18) (18) (18	241-A-103	•	1987	5500	(8)		06/88	1987	(j)
241-AX-102 1988 3000 (8) 09/88 1989 (b) 1942 - (6) 09/81 1989 (c) 241-B-101 1974 - (6) 03/81 1989 (c) 241-B-101 1974 - (6) 03/81 1989 (c) 241-B-105 1978 - (6) 03/81 1989 (c) 241-B-105 1978 - (6) 03/81 1989 (c) 241-B-107 1980 8000 (8) 03/85 1986 (d) 241-B-107 1980 8000 (8) 03/85 1986 (d) 241-B-101 1981 10000 (8) 03/85 1986 (d) 241-B-110 1981 10000 (8) 05/85 1989 (c) 241-B-111 1976 20 (6) 06/85 1989 (c) 241-B-112 1976 20 (6) 06/85 1989 (c) 241-B-112 1976 20 (6) 06/85 1989 (c) 241-B-12 1976 10000 (8) 06/85 1989 (c) 241-B-12 1976 10000 (8) 06/85 1989 (c) 241-B-12 1976 10000 (8) 06/84 1986 (d) 241-B-204 1984 400 (8) 06/84 1986 (d) 241-B-204 1984 400 (8) 06/84 1986 (d) 241-B-204 1984 400 (8) 06/84 1986 (d) 241-B-204 1984 (d) 241-B-204 (d) 1988		/43		500 to 2500			09/78		(a)(q)
241-AX-102 1988 3000 (8) 09/88 1989 (h) 241-AX-104 1977(6) 09/81 1989 (g) 241-B-103 1974(6) 02/81 1989 (g) 241-B-103 1976(6) 02/81 1989 (g) 241-B-103 1976(6) 02/81 1989 (g) 241-B-105 1980 000 (8) 02/85 1989 (g) 241-B-105 1980 000 (8) 02/85 1986 (g) 241-B-110 1980 000 (8) 02/85 1986 (g) 241-B-111 1978 2(6) 06/85 1986 (g) 241-B-111 1978 2(6) 06/85 1989 (g) 241-B-111 1978 2(6) 06/85 1989 (g) 241-B-112 1978 2000 0.5/85 1989 (g) 241-B-201 1980 1200 (8) 08/81 1989 (g) 241-B-101 1972(6) 08/81 1989 (g) 241-B-102 1971 70000 000 0.5 (f) 07/79 1986 (d) 241-B-110 1974 2500 0.5 (f) 07/79 1986 (d) 241-B-110 1984 113(6) 08/85 1989 (g) 241-B-110 1984 113(6) 08/85 1989 (g) 241-B-110 1984 1510 (6) 07/79 1989 (g) 241-B-110 1984 2000 0.5 (f) 07/79 1989 (g) 241-B-110 1988 8500 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.5 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.5 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.5 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.5 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.0 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.0 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.0 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.0 (g) 0.0 (g) 1189 (g) 241-C-101 1984 2000 0.0 (g) 0.0	241-A-105	11)	1303	277000		(0) 00 (0)	07/79	ופפו	(D)(C)
241-B-101 1974 (6) 0.3/81 1989 (g) 241-B-103 1978 (6) 0.2/85 1989 (g) 241-B-105 1978 3 (6) 0.2/85 1989 (g) 241-B-105 1978 3 (6) 0.3/81 1989 (g) 241-B-107 1981 10000 0.3/85 1989 (g) 241-B-107 1981 10000 0.3/85 1989 (g) 241-B-112 1978 2000 0.6/85 1989 (g) 241-B-201 1980 1200 (g) 0.6/85 1989 (g) 241-B-203 1980 1200 (g) 0.6/85 1989 (g) 241-B-203 1984 400 (g) 0.6/84 1986 (g) 241-B-204 1984 400 (g) 0.6/84 1986 (g) 241-B-204 1984 400 (g) 0.6/84 1986 (g) 241-B-204 1984 400 (g) 0.6/84 1989 (g) 241-B-101 1976 0.50 (g) 0.5/78 1989 (g) 241-B-101 1984 (13) 0.6(6) 0.5/85 1989 (g) 241-B-101 1984 130 0.6(6) 0.3/95 1993 (g) 241-B-101 1984 0.5/88 0.				3000		 			
241-B-103									
241-B-105 1978									
241-B-110									(g)
241-B-111									
241-B-201 1980 1200 (8) 06/81 1984 (e)[ff] 241-B-204 1984 400 (8) 06/84 1985 (g) 241-B-204 1984 400 (8) 06/84 1985 (g) 241-BX-102 1971 70000 50 (f) 11/78 1986 (d) 241-BX-108 1974 2500 0.5 (f) 11/78 1986 (d) 241-BX-108 1974 2500 0.5 (f) 11/78 1986 (d) 241-BX-108 1974 2500 0.5 (f) 07/79 1986 (d) 241-BX-101 1984 (13) - (6) 03/85 1993 (g) 241-BX-102 1971 70000 11/78 1986 (d) 241-BX-103 1974 2500 (f) 11/78 1986 (d) 241-BX-103 1974 2500 (f) 11/78 1986 (d) 241-BX-103 1974 2500 (f) 11/78 1983 (g) 241-BX-103 1984 15100 (8) 07/79 1983 (g) 241-BX-108 1984 2500 0.2/85 1983 (g) 241-BX-108 1984 2000 0.8/110 11/78 1989 (g) 241-BX-108 1972 25000 0.8/110 11/78 1989 (g) 241-BX-108 1972 25000 0.8/110 11/78 1989 (g) 241-C-101 1980 20000 (8)(10) 11/78 1989 (g) 241-C-110 1984 2000 0.5/85 1989 (g) 241-C-202 (4) 1988 5500 (8) 03/84 1989 (g) 241-C-203 (4) 1988 5500 (8) 03/84 1989 (g) 241-C-203 (4) 1988 460 (8) 03/81 1987 (f) 241-C-203 (4) 1988 6000 (8) 03/81 1987 (f) 241-SX-104 1988 6000 (8) 03/81 1989 (g) 241-SX-104 1988 6000 (8) 03/81 1989 (g) 241-SX-104 1989 0000 0.8/11 1989 (g) 241-SX-111 (14) 1969 0000 0.8/11 1989 (g) 241-SX-113 1962 15000 17 to 140 08/79 1989 (g) 241-SX-114 1972 6000 0.8/11 1989 (g) 241-SX-115 1969 0000 0.8/11 1988 (d) 241-SX-115 1969 0000 0.8/11 1988 (d) 241-SX-115 1979 1984 (10) 0000 0.8/11 1988 (d) 241-SX-116 1979 1974 <1000 (8) 0000 0.8/11 1989 (g) 241-TX-105 1974 <1000 (8) 0000 0.8/11 1989 (g) 241-TX-105 1977 6000 1977 1986 (d) 241-TX-105 1977 6000 1977 1986 (d) 241-TX-105 1977 6000 1977 1986 (d) 241-TX-106 1978 1974 <1000 (8) 0000 0.7 (d) 02/83 1989 (g) 241-TX-106 1973 1974 <1000 (8) 0000 0.7 (d) 02/83 1989 (g) 241-TX-106 1973 1974 (1000 (8) 0000 0.7 (d) 02/83 1989 (g) 241-TX-106 1973 1980 0.0 (d) 0000 0.7 (d) 02/83 1989 (g) 241-TX-106 1973 1974 (1000 0.0 (8) 0000 0.7 (d) 02/83 1989 (g) 241-TX-106 1973 1974 (10	241-B-111		1978				06/85	1989	
241-B203 1983 300 (8) 06/84 1986 (d) 241-B204 1984 400 (8) 06/84 1988 (g) 241-B204 1984 (d) (8) 06/84 1989 (g) 241-BX-101 1972 (6) 09/78 1989 (d) 241-BX-102 1971 70000 50 (f) 17/79 1986 (d) 241-BX-103 1974 2500 0.5 (f) 07/79 1986 (d) 241-BX-110 1974 2500 0.5 (f) 07/79 1986 (d) 241-BX-110 1974 30 (6) 08/85 1989 (g) 241-BX-110 1984 (13) (6) 08/85 1989 (g) 241-BX-103 1973 <- 5000 11/87 1983 (g) 241-BX-105 1984 (6) N/A 1989 (g) 241-BX-105 1984 4 (6) N/A 1989 (g) 241-BX-106 1984 1510 (g) N/A 1989 (g) 241-BX-106 1984 1510 (g) N/A 1989 (g) 241-BX-106 1984 1510 (g) N/A 1989 (g) 241-BX-108 1972 <- 5000 0.2/85 1983 (e) 241-C-101 1980 2000 (8) 100 11/83 1986 (d) 241-C-101 1980 2000 (8) 0.2/85 1983 (e) 241-C-101 1984 2000 (8) 0.3/84 1989 (g) 241-C-202 (4) 1988 5500 (g) 0.3/82 1987 (f) 241-C-203 (4) 1988 400 (g) 0.3/82 1987 (f) 241-C-203 (4) 1988 3500 (g) 0.3/82 1987 (f) 241-C-203 (4) 1988 350 (g) 0.3/82 1986 (d) 241-C-203 (4) 1988 350 (g) 0.3/82 1986 (d) 241-SX-104 1988 6000 (g) 0.3/82 1987 (f) 241-SX-104 1988 6000 (g) 0.6 0.4/84 1989 (g) 241-SX-107 1984 (5000 10/79 1983 (e) 241-SX-107 1984 (5000 10/79 1984 (c) 241-SX-107 1984 (5000 10/79 1983 (e) 241-SX-107 1984 (5000 10/79 1983 (e) 241-SX-107 1984 (5000 10/79 1984 (c) 241-SX-107 1984 (5000 10/79 1983 (e) 241-SX-107 1984 (5000 10/79 1983 (e) 241-SX-107 1984 (5000 10/79 1984 (c) 241-SX-107 1989 (c) 241-SX-107 1989 (c) 241-SX-107					(0)				(g)
241-BX-101									
241-8X-102 1971 70000 50 (i) 11/78 1986 (d) 241-8X-110 1976 2500 0.5 (i) 0.779 1986 (d) 241-8X-110 1976 - (6) 0.5 (i) 0.785 1989 (g) 241-8X-111 1984 (13) - (6) 0.5 (i) 0.785 1989 (g) 241-8X-110 1984 (13) - (6) 0.5 (ii) 0.785 1983 (g) 241-8Y-105 1984 - (6) 0.6 (iii)						-			
241-BX-108					(6)	50 (1)			(g) (d)
241-BX-111							07/79	1986	
241-BY-105						•		1989	(g)
241-BY-105					(0)				
241-BY-106		•			(6)		N/A		
241-BY-108									(g)
241-C-101					(8)				
241-C-111					(8)(10	0)	11/83		(d)
241-C-201 (4) 1988 550 03/82 1987 (i) 241-C-203 1984 400 (8) 03/82 1987 (i) 241-C-203 1984 400 (8) 03/82 1987 (i) 241-C-203 1988 350 09/82 1987 (i) 241-C-204 (4) 1988 350 09/82 1987 (i) 241-S-104 1968 24000 (8) 12/84 1989 (g) 241-SX-104 1988 6000 (8) 04/00 1988 (k) 241-SX-107 1964 < 5000 10/79 1983 (a) 241-SX-108 (5)(14) 1962 2400 to 17 to 140 08/79 1991 (m)(q)(t) 241-SX-108 (5)(14) 1965 < 100000 < 40 (n)(t) 05/81 1992 (g) (m)(q)(t) 241-SX-110 1976 5500 (8) 08/79 1999 (g) 241-SX-111 (14) 1974 500 to 2000 40 (l)(t) 05/81 1992 (g) 241-SX-112 (14) 1969 30000 40 (l)(t) 07/79 1986 (d)(t) 241-SX-113 1982 15000 (8) 11/78 1986 (d)(t) 241-SX-114 1972 - (6) 07/79 1986 (d)(t) 241-SX-115 1965 50000 (8) 04/93 1992 (g) 241-T-103 1974 < 1000 (8) 11/78 1986 (d) 241-T-105 1979 1974 < 1000 (8) 11/78 1986 (d) 241-T-107 1984 - (6) 05/96 1989 (g) 241-T-109 1974 < 1000 (8) 11/78 1980 (g) 241-T-109 1974 < 1000 (8) 11/78 1980 (g) 241-T-109 1974 < 1000 (8) 12/84 1989 (g) 241-T-109 1974 < 1000 (8) 12/84 1989 (g) 241-T-109 1974 < 1000 (8) 12/84 1989 (g) 241-T-109 1977 - (6) 04/83 1989 (g) 241-T-109 1977 - (6) 04/83 1989 (g) 241-TX-110 1979 1984 (12) < 1000 (8) 02/95 1994 (f) (17/97 1986 (d) 241-TX-110 1977 - (6) 04/83 1989 (g) 241-TX-110 1977 - (6) 04/83 1989 (g) 241-TX-116 1977 - (6) 04/83 198					(6)				(g)
241-C-202 (4) 1988		(4)			(8)				(g) (i)
241-C-204	241-C-202		1988	450			08/81	1987	(i)
241-S-104		<i>(4</i>)			(8)				
241-SX-104		1.7			(8)				
241-SX-108 (5)(14) 1962 2400 to 35000 (m)(q)(t) (1)(q)(t) (241-SX-109 (5)(14) 1976 5500 (8) (0)(q)(t) (1)(q)(t)			1988	6000					
241-SX-109 (5)(14)		(F) (A A)				47 4. 440			(a)
241-SX-109 (5)(14) 1976 5500 (8)	241-5X-108	(5)(14)	1962				08//9	1991	(m)(q)(t)
241-SX-111 (14) 1974 500 to 2000 0.6 to 2.4 (l)(q)(t) 07/79 1986 (d)(q)(t) 241-SX-112 (14) 1969 30000 40 (l)(t) 07/79 1986 (d)(t) 241-SX-113 1962 15000 8 (l) 11/78 1986 (d) 241-SX-114 1972 (6) 07/79 1989 (g) 241-SX-115 1965 50000 21 (o) 09/78 1992 (o) 241-T-101 1992 7500 (8) 04/93 1992 (o) 241-T-103 1974 <1000 (8) 11/83 1989 (g) 241-T-108 1973 115000 (8) 11/83 1989 (g) 241-T-107 1984 (6) 05/96 1989 (g) 241-T-109 1974 <1000 (8) 11/83 1989 (g) 241-T-109 1974 <1000 (8) 11/83 1989 (g) 241-T-109 1974 <1000 (8) 11/8 1980 (f) 241-T-109 1974 <1000 (8) 11/78 1980 (f) 241-T-111 1979, 1994 (12) <1000 (8) 02/95 1994 (f)(r) 241-TX-105 1977 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 04/83 1989 (g) 241-TX-116 1973 3000 0.7 (l) 02/83 1986 (d) 241-TY-104 1981 1400 (8) 11/83 1986 (d) 241-TY-105 1980 35000 4 (l) 02/83 1986 (d) 241-TY-106 1959 30000 0.7 (l) 02/83 1986 (d) 241-TY-106 1959 30000 0.9 (l) 11/78 1986 (d) 241-TY-106 1959 30000 0.9 (l) 11/78 1986 (d) 241-TY-106 1959 30000 0.0 (l) 09/79 1986 (d) 241-U-101 1980 8500 (l) 09/79 1986 (d) 241-U-101 1980 8500 (l) 09/79 1986 (d) 241-U-101 1980 8500 (l) 09/79 1986 (d)		(5)(14)		<10000	(0)				
241-SX-112 (14) 1969 30000 40 (I)(t) 07/79 1986 (d)(t) 241-SX-113 1962 15000 8 (I) 11/78 1986 (d)(t) 241-SX-114 1972 (6) 07/79 1989 (g) 241-SX-115 1965 50000 21 (o) 09/78 1992 (o) 241-T-101 1992 7500 (8) 04/93 1992 (p) 241-T-103 1974 < 1000 (8) 11/83 1989 (g) 241-T-106 1973 11500 (8) 40 (I) 08/81 1986 (d) 241-T-107 1984 (6) 05/96 1989 (g) 241-T-108 1974 < 1000 (8) 11/78 1980 (f) 241-T-109 1974 < 1000 (8) 11/78 1980 (f) 241-T-111 1979, 1984 (12) < 1000 (8) 02/95 1994 (f)(r) 241-TX-105 1977 (6) 04/83 1989 (g) 241-TX-107 (5) 1984 2500 10/79 1986 (d) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 04/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 04/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 04/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 04/83 1989 (g) 241-TX-116 1973 < 1000 (8) 04/83 1989 (g) 241-TY-101 1973 < 1000 (8) 04/83 1989 (g) 241-TY-101 1973 < 1000 (8) 04/83 1989 (g) 241-TY-101 1973 S000 0.7 (I) 02/83 1986 (d) 241-TY-105 1960 35000 4 (I) 02/83 1986 (d) 241-TY-106 1960 35000 2 (II) 11/78 1986 (d) 241-TY-106 1960 35000 0.09 (I) 11/78 1986 (d) 241-U-101 1959 30000 0.09 (I) 11/78 1986 (d) 241-U-104 1961 55000 0.09 (I) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)		(1.4)			(8)	0 6 to 2 4 (1)(a)(t)			
241-5X-113									
241-SX-115 1965 50000 21 (o) 09/78 1992 (ö) 241-T-101 1992 7500 (8) 04/93 1992 (p) 241-T-103 1974 <1000 (8)	241-SX-113				101	8 (1)	11/78		(d)
241-T-101 1992 7500 (8) 04/93 1992 (p) 241-T-103 1974 <1000 (8)					(0)	21 (o)			(g) (o)
241-T-103		;			(8)				
241-T-107 1984 (6) 05/96 1989 (g) 241-T-108 1974 <1000 (8)	241-T-103			<1000	(8)	40 (0			(g)
241-T-108 1974 <1000 (8)				115000	(6)	40 (1)			(a)
241-T-111 1979, 1994 (12) < 1000 (8) 02/95 1994 (f)(r) 241-TX-105 1977 (6) 04/83 1989 (g) 241-TX-107 (5) 1984 2500 10/79 1986 (d) 241-TX-110 1977 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 03/83 1989 (g) 241-TY-101 1973 <1000 (8)	241-T-108		1974	<1000	(8)		11/78	1980	(f)
241-TX-105 1977 (6) 04/83 1989 (g) 241-TX-107 (5) 1984 2500 10/79 1986 (d) 241-TX-110 1977 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TY-101 1977 (6) 04/83 1989 (g) 241-TY-101 1973 <1000							12/84 02/95		(g) (f)(r)
241-TX-107 (5) 1984 2500 10/79 1986 (d) 241-TX-110 1977 (6) 04/83 1989 (g) 241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TY-101 1977 (6) 03/83 1989 (g) 241-TY-101 1973 <1000							04/83		
241-TX-113 1974 (6) 04/83 1989 (g) 241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 03/83 1989 (g) 241-TY-101 1973 <1000 (8)	241-TX-107	(5)			16/	•			(d)
241-TX-114 1974 (6) 04/83 1989 (g) 241-TX-115 1977 (6) 09/83 1989 (g) 241-TX-116 1977 (6) 04/83 1989 (g) 241-TX-117 1977 (6) 03/83 1989 (g) 241-TY-101 1973 <1000 (8)									(g)
241-TX-116 1977 - (6) 04/83 1989 (g) 241-TX-117 1977 - (6) 03/83 1989 (g) 241-TY-101 1973 <1000 (8)	241-TX-114		1974		(6)		04/83	1989	(g)
241-TX-117 1977 (6) 03/83 1989 (g) 241-TY-101 1973 <1000 (8)									(g)
241-TY-103 1973 3000 0.7 (l) 02/83 1986 (d) 241-TY-104 1981 1400 (8) 11/83 1986 (d) 241-TY-105 1960 35000 4 (l) 02/83 1986 (d) 241-TY-106 1959 20000 2 (l) 11/78 1986 (d) 241-U-101 1959 30000 20 (l) 09/79 1986 (d) 241-U-104 1961 55000 0.09 (l) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)	241-TX-117		1977		(6)		03/83	1989	(g)
241-TY-104 1981 1400 (8) 11/83 1986 (d) 241-TY-105 1960 35000 4 (l) 02/83 1986 (d) 241-TY-106 1959 20000 2 (l) 11/78 1986 (d) 241-U-101 1959 30000 20 (l) 09/79 1986 (d) 241-U-104 1961 55000 0.09 (l) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)					(8)	0.7 (1)			
241-TY-106 1959 20000 2 (I) 11/78 1986 (d) 241-U-101 1959 30000 20 (I) 09/79 1986 (d) 241-U-104 1961 55000 0.09 (I) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)			1981	1400	(8)		11/83	1986	(d)
241-U-101 1959 30000 20 (I) 09/79 1986 (d) 241-U-104 1961 55000 0.09 (I) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)	241-TY-105								
241-U-104 1961 55000 0.09 (l) 10/78 1986 (d) 241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)									
241-U-110 1975 5000 to 8100 (8) 0.05 (q) 12/84 1986 (d)(q) 241-U-112 1980 8500 (8) 09/79 1986 (d)				55000		0.09 (1)	10/78	1986	(d)
	241-U-110					0.05 (q)			
	nnecesconere en		1360		00000000000	60 (F)	<u> </u>	1300	(0)

N/A = not applicable (not yet interim stabilized)

TABLE F-1. SINGLE-SHELL LEAK VOLUME ESTIMATES (Sheet 2 of 6)

Footnotes:

- (1) Current estimates [see reference(b)] are that 610 Kgallons of cooling water was added to Tank 241-A-105 from November 1970 to December 1978 to aid in evaporative cooling. In accordance with <u>Dangerous Waste Regulations</u> [Washington Administrative Code 173-303-070 (2)(a)(ii), as amended, Washington State Department of Ecology, 1990, Olympia, Washington], any of this cooling water that has been added and subsequently leaked from the tank must be classified as a waste and should be included in the total leak volume. In August 1991, the leak volume estimate for this tank was updated in accordance with the WAC regulations. Previous estimates excluded the cooling water leaks from the total leak volume estimates because the waste content (concentration) in the cooling water which leaked should be much less than the original liquid waste in the tank (the sludge is relatively insoluble). The total leak volume estimate in this report (10 Kgallons to 277 Kgallons) is based on the following (see References):
 - Reference (b) contains an estimate of 5 Kgallons to 15 Kgallons for the initial leak prior to August 1968.
 - 2. Reference (b) contains an estimate of 5 Kgallons to 30 Kgallons for the leak while the tank was being sluiced from August 1968 to November 1970.
 - 3. Reference (b) contains an estimate of 610 Kgallons of cooling water added to the tank from November 1970 to December 1978 but it was estimated that the leakage was small during this period. This reference contains the statement "Sufficient heat was generated in the tank to evaporate most, and perhaps nearly all, of this water." This results in a low estimate of zero gallons leakage from November 1970 to December 1978.
 - 4. Reference (c) contains an estimate the 378 to 410 Kgallons evaporated out of the tank from November 1970 to December 1978. Subtracting the minimum evaporation estimate from the cooling water added estimate provides a range from 0 to 232 Kgallons of cooling water leakage from November 1970 to December 1978.

	Low Estimate	High Estimate
Prior to August 1968	5,000	15,000
August 1968 to November 1970	5,000	30,000
November 1970 to December 1978	0	232,000
Totals	10,000	277,000

- These leak volume estimates do not include (with some exceptions), such things as: (a) cooling/raw water leaks, (b) intrusions (rain infiltration) and subsequent leaks, (c) leaks inside the tank farm but not through the tank liner (surface leaks, pipeline leaks, leaks at the joint for the overflow or fill lines, etc.), and (d) leaks from catch tanks, diversion boxes, encasements, etc.
- In many cases, a leak was suspected long before it was identified or confirmed. For example, reference (d) shows that Tank 241-U-104 was suspected of leaking in 1956. The leak was "confirmed" in 1961. This report lists the "assumed leaker" date of 1961. Using <u>present</u> standards, Tank 241-U-104 would have been declared an assumed leaker in 1956. In 1984, the criteria designations of "suspected leaker," "questionable integrity," "confirmed leaker," "declared leaker," "borderline" and "dormant," were merged into one category now reported as "assumed leaker." See reference (f) for explanation of when, how long, and how fast some of the tanks leaked. It is highly likely that there have been undetected leaks from single-shell tanks because of the nature of their design and instrumentation.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 3 of 6)

- (4) The leak volume estimate date for these tanks is before the "declared leaker" date because the tank was in a "suspected leaker" or "questionable integrity" status; however, a leak volume had been estimated prior to the tank being reclassified.
- (5) The increasing radiation levels in drywells and laterals associated with these three tanks could be indicating continuing leak or movement of existing radionuclides in the soil. There is no conclusive way to confirm these observations.
- (6) Methods were used to estimate the leak volumes from these 19 tanks based on the <u>assumption</u> that their cumulative leakage is approximately the same as for 18 of the 24 tanks identified in footnote (9). For more details see reference (g). The total leak volume estimate for these tanks is 150 Kgallons (rounded to the nearest Kgallons), for an average of approximately 8 Kgallons for each of 19 tanks.
- (7) The total has been rounded to the nearest 50 Kgallons. Upper bound values were used in many cases in developing these estimates. It is likely that some of these tanks have not actually leaked.
- (8) Leak volume estimate is based solely on observed liquid level decreases in these tanks. This is considered to be the most accurate method for estimating leak volumes.
- (9) The curie content shown is as listed in the reference document and is <u>not</u> decayed to a consistent date: therefore, a cumulative total is inappropriate.
- (10) Tank 241-C-101 experienced a liquid level decrease in the late 1960s and was taken out of service and pumped to a "minimum heel" in December 1969. In 1970, the tank was classified as a "questionable integrity" tank. Liquid level data show decreases in level throughout the 1970s and the tank was saltwell pumped during the 1970s, ending in April 1979. The tank was reclassified as a "confirmed leaker" in January 1980. See references (q) and (r); refer to reference (s) for information on the potential for there to have been leaks from other C-farm tanks (specifically, C-102, C-103, and C-109).
- (11) These dates indicate when the tanks were declared to be interim stabilized. In some cases, the official interim stabilization documents were issued at a later date. Also, in some cases, the field work associated with interim stabilization was completed at an earlier date.
- (12) Tank T-111 was declared an assumed re-leaker on February 28, 1994, due to a decreasing trend in surface level measurement. This tank was pumped, and interim stabilization completed on February 22, 1995.
- (13) Tank BX-111 was declared an assumed re-leaker in April 1993. Preparations for pumping were delayed, following an administrative hold placed on all tank farm operations in August 1993. Pumping resumed and the tank was declared interim stabilized on March 15, 1995.
- (14) The leak volume and curie release estimates on SX-108, SX-109, SX-111, and SX-112 have been reevaluated using a Historical Leak Model [see reference (t)]. In general, the model estimates are much higher
 than the values listed in the table, both for volume and curies released. The values listed in the table do not
 reflect this revised estimate because, "In particular, it is worth emphasizing that this report was never meant to
 be a definitive update for the leak baseline at the Hanford Site. It was rather meant to be an attempt to view the
 issue of leak inventories with a new and different methodology." (This quote is from the first page of the
 referenced report).
- In July 1998, the Washington State Department of Ecology (Ecology) directed the U. S. Department of Energy (DOE) to develop corrective action plans for eight single-shell tank farms (B/BX/BY/S/SX/T/TX/TY) where groundwater contamination likely originated from tank farm operations. A Tri-Party Agreement milestone (M-45 series) was developed that established a formalized approach for evaluating impacts on groundwater quality of losses of tank wastes to the vadose zone underlying these tank farms. Planning documents have been

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 4 of 6)

completed for the S, SX, B, BX, and BY tank farms and will be completed shortly for the T, TX, and TY farms. The phase 1 field investigation is near completion in the S and SX tank farms and has begun in the B, BX, and BY farms. Field work is anticipated in FY-02 for the T, TX, and TY tank farms. The remaining four single-shell tank farms are expected to be included in corrective action plans in the near future.

All of the information included in this appendix is currently under review and significant revisions are anticipated. Recently, major tank farm vadose zone investigation efforts (such as the baseline spectral gammaray logging of all drywells in all single-shell tank farms, as well as drilling and sampling in the SX tank farm) were completed. This appendix will be revised as a better understanding of past tank leak events is developed.

SST Vadose Zone Project drilling and testing activities near tank BX-102 were completed March 2001. A borehole (299-E33-45) was drilled through the postulated uranium plume resulting from the 1951 tank BX-102 overfill event to confirm the presence of uranium, define its present depth, and survey other contaminants of interest such as Tc-99. Thirty-five split-spoon samples were collected for laboratory analyses. This borehole was decommissioned after collection and analysis of groundwater samples.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 5 of 6)

References:

- (a) Murthy, K.S., et al, June 1983, Assessment of Single-Shell Tank Residual Liquid Issues at Hanford Site, Washington, PNL-4688, Pacific Northwest Laboratory, Richland, Washington.
- (b) WHC, 1991a, Tank 241-A-105 Leak Assessment, WHC-MR-0264, Westinghouse Hanford Company, Richland, Washington.
- (c) WHC, 1991b, Tank 241-A-105 Evaporation Estimate 1970 Through 1978, WHC-EP-0410, Westinghouse Hanford Company, Richland, Washington.
- (d) Smith, D. A., January 1986, Single-Shell Tank Isolation Safety Analysis Report, SD-WM-SAR-006, Rev. 1, Westinghouse Hanford Company, Richland, Washington.
- (e) McCann, D. C., and T. S. Vail, September 1984, Waste Status Summary, RHO-RE-SR-14, Rockwell Hanford Operations, Richland, Washington.
- (f) Catlin, R. J., March 1980, Assessment of the Surveillance Program of the High-Level Waste Storage Tanks at Hanford, Hanford Engineering Development Laboratory, Richland, Washington.
- (g) Baumhardt, R. J., May 15, 1989, Letter to R. E. Gerton, U.S. Department of Energy-Richland Operations Office, Single-Shell Tank Leak Volumes, 8901832B R1, Westinghouse Hanford Company, Richland, Washington.
- (h) WHC, 1990a, Occurrence Report, Surface Level Measurement Decrease in Single-Shell Tank 241-AX-102, WHC-UO-89-023-TF-05, Westinghouse Hanford Company, Richland, Washington.
- (i) Groth, D. R., July 1, 1987, Internal Memorandum to R. J. Baumhardt, Liquid Level Losses in Tanks 241-C-201, -202 and -204, 65950-87-517, Westinghouse Hanford Company, Richland, Washington.
- (j) Groth, D. R. and G. C. Owens, May 15, 1987, Internal Memorandum to J. H. Roecker, *Tank 103-A Integrity Evaluation*, Westinghouse Hanford Company, Richland, Washington.
- (k) Dunford, G. L., July 8, 1988, Internal Memorandum to R. K. Welty, Engineering Investigation: Interstitial Liquid Level Decrease in Tank 241-SX-104, 13331-88-416, Westinghouse Hanford Company, Richland, Washington.
- (1) ERDA, 1975, Final Environmental Statement Waste Management Operations, Hanford Reservation, Richland, Washington, ERDA-1538, 2 vols., U.S. Energy Research and Development Administration, Washington, D.C.
- (m) WHC, 1992a, Tank 241-SX-108 Leak Assessment, WHC-MR-0300, Westinghouse Hanford Company, Richland, Washington.
- (n) WHC, 1992b, Tank 241-SX-109 Leak Assessment, WHC-MR-0301, Westinghouse Hanford Company, Richland, Washington.
- (0) WHC, 1992c, Tank 241-SX-115 Leak Assessment, WHC-MR-0302, Westinghouse Hanford Company, Richland, Washington.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 6 of 6)

- (p) WHC, 1992d, Occurrence Report, Apparent Decrease in Liquid Level in Single Shell Underground Storage Tank 241-T-101, Leak Suspected; Investigation Continuing, RL-WHC-TANKFARM-1992-0073, Westinghouse Hanford Company, Richland, Washington.
- (q) WHC,1990b, A History of the 200 Area Tank Farms, WHC-MR-0132, Westinghouse Hanford Company, Richland, Washington.
- (r) WHC, 1993a, Assessment of Unsaturated Zone Radionuclide Contamination Around Single-Shell Tanks 241-C-105 and 241-C-106, WHC-SD-EN-TI-185, REV OA, Westinghouse Hanford Company, Richland, Washington.
- (s) WHC, 1994, Occurrence Report, Apparent Liquid Level Decrease in Single Shell Underground Storage Tank 241-T-111; Declared an Assumed Re-Leaker, RL-WHC-TANKFARM-1994-0009, Westinghouse Hanford Company, Richland, Washington.
- (t) HNF, 1998, Agnew, S. F. and R. A. Corbin, August 1998, Analysis of SX Farm Leak Histories Historical Leak Model, (HLM), HNF-3233, Rev. 0, Los Alamos National Laboratory, Los Alamos, New Mexico

APPENDIX G

SINGLE-SHELL TANKS INTERIM STABILIZATION, AND CONTROLLED, CLEAN AND STABLE (CCS) STATUS

TABLE G -1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (Sheet 1 of 3) March 31, 2001

		Interim	<u> </u>	***			Interim		**			Interim	(
Tank	Tank	Stabil.	Stabil.		Tank	Tank	Stabil.	Stabil.		Tank	Tank	Stabil.	Stabil.
					Number	Integrity	Date (1)	Method		Number	Integrity	Date (1)	Method
Number	integrity	<u>Date (1)</u> N/A	Method		C-101	ASMD LKR	11/83	AR	8	T-108	ASMD LKR	11/78	AR
A-101 A-102	SOUND	08/89	SN	2000 2000	C-102	SOUND	09/95	JET	****	T-109	ASMD LKR	12/84	AR
A-103	ASMD LKR	06/88	AR	***	C-103	SOUND	N/A		**	T-110	SOUND	01/00 (5)	JET
A-104	ASMD LKR	09/78	AR	88	C-104	SOUND	09/89	SN	***	T-111	ASMD LKR	02/95	JET
A-105	ASMD LKR	07/79	AR	3200	C-105	SOUND	10/95	AR	~	T-112	SOUND	03/81	AR(2)(3)
A-106	SOUND	08/82	AR	8	C-106	SOUND	N/A		**	T-201	SOUND	04/81	AR (3)
AX-101	SOUND	N/A			C-107	SOUND	09/95	JET		T-202	SOUND	08/81	AR
AX-102	ASMD LKR	09/88	SN	***	C-108	SOUND	03/84	AR		T-203	SOUND	04/81	AR
AX-103	SOUND	08/87	AR		C-109	SOUND	11/83	AR	*	T-204	SOUND	08/81	AR
AX-104	ASMD LKR	08/81	AR		C-110	ASMD LKR	05/95	JET	***	TX-101	SOUND	02/84	AR
B-101	ASMD IKR	03/81	SN	889	C-111	ASMD LKR	03/84	SN	888	TX-102	SOUND	04/83	JET
B-102	SOUND	08/65	SN	***	C-112	SOUND	09/90	AR		TX-103	SOUND	08/83	JET
B-103	ASMD IKR	02/85	SN		C-201	ASMD LKR	03/82	AR		TX-104	SOUND	09/79	SN
B-104	SOUND	06/85	SN		C-202	ASMD LKR	08/81	AR		TX-106	ASMD LKR	04/83	JET
B-105	ASMD IKR	12/84	AR	***	C-203	ASMD LKR	03/82	AR		TX-106	SOUND	06/83	JET
B-106	SOUND	03/85	SN		C-204	ASMD LKR	09/82	AR		TX-107	ASMD LKR	10/79	AR
B-107	ASMD LKR	03/85	SN	***	S-101	SOUND	N/A			TX-108	SOUND	03/83	JET
B-108	SOUND	05/85	SN		S-102	SOUND	N/A			TX-109	SOUND	04/83	JET
B-109	SOUND	04/85	SN	8	S-103	SOUND	04/00	JET (6)		TX-110	ASMD LKR	04/83	JET
8-110	ASMD LKR	12/84	AR		S-104	ASMD LKR	12/84	AR	***	TX-111	SOUND	04/83	JET
B-111	ASMD LKR	06/85	SN	***	S-105	SOUND	09/88	JET (10)	888 888	TX-112	SOUND ASMD LKR	04/83	JET
B-112	ASMD LKR	05/85	SN	888	S-106	SOUND	02/01	JE1 (10)	888	TX-113 TX-114	ASMD LKR	04/83	JET
B-201	ASMD LKR	08/81	AR (3)	200	5-107	SOUND	N/A 12/96	JET	8888 1883	TX-115	ASMD LKR	09/83	JET
B-202	SOUND	05/85	AR(2)		S-108 S-109	SOUND	N/A	JEI	***	TX-116	ASMD LKR	04/83	JET
B-203	ASMD LKR	06/84	AR AR	3888 5888	S-109 S-110	SOUND	01/97	JET	2866 8558	TX-117	ASMD LKR	03/83	JET
B-204	ASMD LKR	06/84	AR	888	S-110	SOUND	N/A	- JL 1	8000 8000	TX-118	SOUND	04/83	JET
BX-101 BX-102	ASMD LKR	11/78	AR	30000	S-112	SOUND	N/A		***	TY-101	ASMD LKR	04/83	JET
BX-102	SOUND	11/83	AR(2)	888 888	SX-101	SOUND	N/A		***	TY-102	SOUND	09/79	ÄR
BX-103	SOUND	09/89	SN	**** ****	SX-102	SOUND	N/A			TY-103	ASMD LKR	02/83	JET
BX-105	SOUND	03/81	SN	8	SX-103	SOUND	N/A		***	TY-104	ASMD LKR	11/83	AR
BX-106	SOUND	07/95	SN	***	5X-104	ASMD LKR	04/00	JET (7)	***	TY-105	ASMD LKR	02/83	JET
BX-107	SOUND	09/90	JET		SX-105	SOUND	N/A			TY-106	ASMD LKR	11/78	AR
BX-108	ASMD LKR	07/79	SN		SX-106	SOUND	05/00	JET (8)		U-101	ASMD LKR	09/79	AR
BX-109	SOUND	09/90	JET		SX-107	ASMD LKR	10/79	AR		U-102	SOUND	N/A	
BX-110	ASMD LKR	08/85	SN	888	SX-108	ASMD LKR	08/79	AR		U-103	SOUND	09/00	JET (9)
BX-111	ASMD LKR	03/95	JET		SX-109	ASMO LKR	05/81	AR		U-104	ASMD LKR	10/78	AR
BX-112	SOUND	09/90	JET	**	SX-110	ASMD LKR	08/79	AR		U-105	SOUND	03/01	JET (11)
BY-101	SOUND	05/84	JET		SX-111	ASMD LKR	07/79	SN	**	U-106	SOUND	03/01	JET (12)
BY-102	SOUND	04/95	JET		SX-112	ASMD LKR	07/79	AR	*	U-107	SOUND	N/A	
BY-103	ASMD LKR	11/97	JET		SX-113	ASMD LKR	11/78	AR	8	U-108	SOUND	N/A	
BY-104	SOUND	01/85	JET	***	SX-114	ASMD LKR	07/79	AR		U-109	SOUND	N/A	
BY-105	ASMD LKR	N/A			SX-115	ASMD LKR	09/78	AR		U-110	ASMD LKR	12/84	AR
BY-106	ASMD LKR	N/A		***	T-101	ASMD LKR	04/83	SN	***	U-111	SOUND	N/A	
BY-107	ASMD LKR	07/79	JET	***	T-102	SOUND	03/81	AR(2)(3)		U-112	ASMD LKR	09/79	AR
BY-108	ASMD LKR	02/85	JET		T-103	ASMD LKR	11/83	AR		U-201	SOUND	08/79	AR
BY-109	SOUND	07/97	JET		T-104	SOUND	11/99 (4)	JET		U-202	SOUND	08/79	SN
BY-110	SOUND	01/85	JET_		T-105	SOUND	06/87	AR		U-203	SOUND	08/79	AR
BY-111	SOUND	01/85	JET		T-108	ASMD LKR	08/81	AR		U-204	SOUND	08/78	SN
8Y-112	SOUND	06/84	JET_		T-107	ASMD LKR	05/96	JET	L				
LEGEND: AR = Administratively interim stabilized JET = Saltwell jet pumped to remove drainable interstitial liquid					Interim Stabilized Tanks 128 Not Yet Interim Stabilized 21								
SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized ASMD LKR = Assumed Leaker					Total Single-Shell Tanks 149								

TABLE G-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (sheet 2 of 3)

Footnotes:

- (1) These dates indicate when the tanks were actually interim stabilized. In some cases, the official interim stabilization documents were issued at a later date.
- (2) Although tanks, BX-103, T-102 and T-112 met the interim stabilization administrative procedure at the time they were stabilized, they no longer meet the recently updated administrative procedure. The tanks were reevaluated in 1996 and memo 9654456, J. H. Wicks to Dr. J. K. McClusky, DOE-RL, dated September 1996, was issued which recommended that no further pumping be performed on these tanks, based on an economic evaluation.

Document RPP-5556, Rev. 0, "Updated Drainable Interstitial Liquid Volume Estimates for 119 Single-Shell Tanks Declared Stabilized," J. G. Field, February 7, 2000, states that five tanks no longer meet the stabilization criteria (BX-103, T-102, and T-112 exceed the supernate criteria, and BY-103 and C-102 exceed the DIL criteria).

An intrusion investigation was completed on tank B-202 in 1996 because of a detected increase in surface level. As a result of this investigation, it was determined that this tank no longer meets the recently updated administrative procedure for 200 series tanks.

- Original Interim Stabilization data are missing on four tanks: B-201, T-102, T-112, and T-201. Document HNF-SD-RE-TI-178, Rev. 7, dated February 9, 2001, added three additional tanks to those missing stabilization data: A-104, BX-101, and SX-115.
- (4) Tank 241-T-104 was Interim Stabilized on November 19, 1999. In-tank video taken October 7, 1999, shows the surface is clearly sludge-type waste with no saltcake present. No visible water on surface. Waste surface appears level across tank with numerous cracks. There is a minimal collapsed area around the saltwell screen, with no visible bottom.
- (5) Tank 241-T-110 was Interim Stabilized on January 5, 2000, due to major equipment failure. An in-tank video taken October 7, 1999 (pumping was discontinued on August 12, 1999), showed the surface of this tank as smooth, brown-tinted sludge with visible cracks,
- (6) Tank 241-S-103 was declared Interim Stabilized April 18, 2000. The surface is a rough, black and brown-colored waste with yellow patches of saltcake visible throughout. The surface appears to be damp but not saturated, and shows irregular cracking typically seen with surfaces beginning to dry out. A pool of supernatant liquid (10 feet in diameter, 5 feet deep, 1.0 Kgallons) is visible from video observations.
- (7) Tank 241-SX-104 was declared Interim Stabilized April 26, 2000, due to major equipment failure. The surface is a rough, yellowish gray saltcake waste with an irregular surface of visible cracks and shelves that were created as the surface dried out. The waste surface appears to be dry and shows no standing water within the tank.
- (8) Tank 241-SX-106 was declared Interim Stabilized May 5, 2000. The surface is a smooth, white-colored saltcake waste. The surface level slopes slightly from the tank sidewall down to a large depression in the center of the tank. A second depression surrounds both saltwell screens and an abandoned LOW. The waste surfaces appear dry and show no standing water within the tank.

TABLE G-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (sheet 3 of 3)

- (9) Tank 241-U-103 was declared Interim Stabilized September 11, 2000. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 30% of the waste surface is covered by the salt formations. The surface level slopes slightly from the tank sidewall down to the first of two depressions in the center of the tank. The waste surface appears dry and shows signs of drying and cracking due to saltwell pumping. LOW readings indicate an average adjusted ILL of 60.2 inches. There is a small pool of supernatant liquid estimated to be 500 gallons.
- (10) Tank 241-S-106 was declared Interim Stabilized on February 1, 2001. The surface is a rough, brown and yellow-colored saltcake waste with an irregular surface of mounds and saltcake crystals that were created as the surface was dried out. The waste surface appears to be dry and shows no standing water within the tank. There is no evidence of supernatant liquid from video observations. The waste surface slopes gradually from the tank sidewall to the depression in the center of the tank. The depression surrounds both of the saltwell screens, but does not extend around the temperature probe and ENRAF devices.
- (11) Tank 241-U-105 was declared Interim Stabilized on March 29, 2001, due to major equipment failure. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 15% of the surface is covered by the salt formations. The surface level slopes to the first of two depressions in the center of the tank; the first depression is cone shaped and estimated to be 22 feet in diameter. The second depression, inside the first, is cylindrically shaped and has a diameter of approximately 10 feet. Both depressions are centered on the saltwell screen. The waste surface appears dry and shows signs of cracking due to saltwell pumping. There is no visible liquid in the tank.
- (12) Tank 241-U-106 was declared Interim Stabilized on March 9, 2001. The surface is a dark brown/yellow colored waste that is covered with many stalagmite-type crystals growing on the surface. The crystals cover approximately 75% of the waste surface. The waste surface is irregular, appears dry, and shows only minimal signs of cracking due to saltwell pumping. The supernatant pool is estimated to be 13.3 feet in diameter based on the visible portion of the saltwell screen. The pool is centered on the saltwell screen.

TABLE G-2. SINGLE-SHELL TANK INTERIM STABILIZATION MILESTONES March 31, 2001 (sheet 1 of 2)

New single-shell tank interim stabilization milestones were negotiated in 1999 and are identified in the "Consent Decree." The Consent Decree was approved on August 16, 1999.

CONSENT DECREE Attachments A-1 and A-2

Following is the schedule for pumping liquid waste from the remaining twenty-nine (29) single-shell tanks. This schedule is enforceable pursuant to the terms of the Decree except for the "Project Pumping Completion Dates," which are estimates only and not enforceable. (Note: Schedule does not include C-106)

Tank		Projected Pumping	Actual Pumping	Projected Pumping	Interim Stabilization
Designation		Start Date	Start Date	Completion Date	Date
1.	T-104	Already initiated	March 24, 1996	May 30, 1999	November 19, 1999
2.	T-110	Already initiated	May 12, 1997	May 30, 1999	Јапиагу 5, 2000
3.	SX-104	Already initiated	September 26, 1997	December 30, 2000	April 26, 2000
4.	SX-106	Already initiated	October 6, 1998	December 30, 2000	May 5, 2000
5.	S-102	July 31, 1999	March 18, 1999	March 30, 2001	
6.	S-106	July 31, 1999	April 16, 1999	March 30, 2001	February 1, 2001
7.	S-103	July 31, 1999	June 4, 1999	March 30, 2001	April 18, 2000
8.	U-103*	June 15, 2000	September 26, 1999	April 15, 2002	September 11, 2000
9.	U-105*	June 15, 2000	December 10, 1999	April 15, 2002	March 29, 2001
10.	U-102*	June 15, 2000	January 20, 2000	April 15, 2002	
11.	U-109*	June 15, 2000	March 11, 2000	April 15, 2002	
12.	A-101	October 30, 2000	May 6, 2000	September 30, 2003	
13.	AX-101	October 30, 2000	July 29, 2000	September 30, 2003	
14.	SX-105	March 15, 2001	August 8, 2000	February 28, 2003	
15.	SX-103	March 15, 2001	October 26, 2000	February 28, 2003	
16.	SX-101	March 15, 2001	November 22, 2000	February 28, 2003	
17.	U-106*	March 15, 2001	August 24, 2000	February 28, 2003	March 9, 2001
18.	BY-106	July 15, 2001		June 30, 2003	
19.	BY-105	July 15, 2001		June 30, 2003	
20.	U-108	December 30, 2001	•	August 30, 2003	
21.	U-107	December 30, 2001		August 30, 2003	
22.	S-111	December 30, 2001		August 30, 2003	
23.	SX-102	December 30, 2001		August 30, 2003	
24.	U-111	November 30, 2002		September 30, 2003	
25.	S-109	November 30, 2002	September 23, 2000	September 30, 2003	
26.	S-112	November 30, 2002		September 30, 2003	
27.	S-101	November 30, 2002		September 30, 2003	
28.	S-107	November 30, 2002		September 30, 2003	

No later than December 30, 2000, DOE will determine whether the organic layer and pumpable liquida will be pumped from this tank together or separately, and will establish a deadline for initiating pumping of this tank. The parties will incorporate the initiation deadline into this schedule as provided in Section VI of the Decree.

ORP issued a letter to WDOE on December 22, 2000, meeting the requirements of this milestone.

^{*} Tanks containing organic complexants.

TABLE G-2. SINGLE-SHELL TANK INTERIM STABILIZATION MILESTONES (sheet 2 of 2)

<u>Completion of Interim Stabilization</u>. DOE will complete interim stabilization of all 29 single-shell tanks listed above by September 30, 2004.

Percentage of Pumpable Liquid Remaining to be Removed:

93% of Total Liquid	9/30/1999 (1)
38% of Organic Complexed Pumpable Liquids	9/30/2000 (2)
5% of Organic Complexed Pumpable Liquids	9/30/2001
18% of Total Liquid	9/30/2002
2% of Total Liquid	9/30/2003

The "percentage of pumpable liquid remaining to be removed" is calculated by dividing the volume of pumpable liquid remaining to be removed from tanks not yet interim stabilized by the sum of the total amount of liquid that has been pumped and the pumpable liquid that remains to be pumped from all tanks.

- (1) The Pumpable Liquid Remaining was reduced to 88%, by 9/30/99, exceeding this milestone. Reference LMHC-9957926 R1, D. I. Allen, LHMC RPP to D. C. Bryson, DOE-OPP, dated October 26, 1999
- (2) The Complexed Pumpable Liquid Remaining was reduced to 38%, by 9/15/00. Reference CHG-0004752, R. F. Wood, CHG, to J. J. Short, DOE-RPP, dated September 13, 2000.

APPENDIX H

TANKS AND EQUIPMENT CODE AND STATUS DEFINITIONS

TABLE H - 1. TANK AND EQUIPMENT CODE/STATUS DEFINITIONS March 31, 2001

1. TANK STATUS CODES

WASTE TYPE (also see definitions, section 2 below)

AW	Aging Waste (Neutralized Current Acid Waste [NCAW])
CC	Complexant Concentrate Waste
CP	Concentrated Phosphate Waste
DC	Dilute Complexed Waste
DN	Dilute Non-Complexed Waste
DSS	Double-Shell Slurry
DSSF	Double-Shell Slurry Feed
NCPLX	Non-Complexed Waste
PD	Plutonium-Uranium Extraction (PUREX) Neutralized Cladding

Removal Waste (NCRW), transuranic waste (TRU)

TANK USE (DOUBLE-SHELL TANKS ONLY)

CWHT	Concentrated Waste Holding Tank
DRCVR	Dilute Receiver Tank
EVFD	Evaporate Feed Tank
SRCVR	Slurry Receiver Tank

2. DEFINITIONS

WASTE TANKS - GENERAL

Waste Tank Safety Issue

A potentially unsafe condition in the handling of waste material in underground storage tanks that requires corrective action to reduce or eliminate the unsafe condition.

Watch List Tank

An underground storage tank containing waste that requires special safety precautions because it may have a serious potential for release of high level radioactive waste because of uncontrolled increases in temperature or pressure. Special restrictions have been placed on these tanks by "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the *National Defense Authorization Act for Fiscal Year 1991*, November 5, 1990, Public Law 101-510, (also known as the Wyden Amendment).

Characterization

Characterization is understanding the Hanford tank waste chemical, physical, and radiological properties to the extent necessary to insure safe storage and interim operation, and ultimate disposition of the waste.

WASTE TYPES

Aging Waste (AW)

High level, first cycle solvent extraction waste from the PUREX plant (NCAW)

Concentrated Complexant (CC)

Concentrated product from the evaporation of dilute complexed waste.

Concentrated Phosphate Waste (CP)

Waste originating from the decontamination of the N Reactor in the 100 N Area. Concentration of this waste produces concentrated phosphate waste.

Dilute Complexed Waste (DC)

Characterized by a high content of organic carbon including organic complexants: ethylenediaminetetraacetic acid (EDTA), citric acid, and hydroxyethyl-ethylenediaminetriacetic acid (HEDTA), being the major complexants used. Main sources of DC waste in the DST system are saltwell liquid inventory (from SSTs).

Dilute Non-Complexed Waste (DN)

Low activity liquid waste originating from T and S Plants, the 300 and 400 Areas, PUREX facility (decladding supernatant and miscellaneous wastes), 100 N Area (sulfate waste), B Plant, saltwells, and PFP (supernate).

Double-Shell Slurry (DSS)

Waste that exceeds the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. For reporting purposes, DSS is considered a solid.

Double-Shell Slurry Feed (DSSF)

Waste concentrated just before reaching the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. This form is not as concentrated as DSS.

Non-complexed (NCPLX)

General waste term applied to all Hanford Site (NCPLX) liquors not identified as complexed.

PUREX Decladding (PD)

PUREX Neutralized Cladding Removal Waste (NCRW) is the solids portion of the PUREX plant neutralized cladding removal waste stream; received in Tank Farms as a slurry. NCRW solids are classified as transuranic (TRU) waste.

Drainable Interstitial Liquid (DIL)

Interstitial liquid that is not held in place by capillary forces, and will therefore migrate or move by gravity. (See also Section 4 below)

Supernate

The liquid above the solids or in large liquid pools covered by floating solids in waste storage tanks. (See also Section 4 below)

Ferrocyanide

A compound of iron and cyanide commonly expressed as FeCN. The actual formula for the ferrocyanide anion is $[Fe(CN)_6]^{-4}$.

INTERIM STABILIZATION (Single-Shell Tanks only)

Interim Stabilized (IS)

A tank which contains less than 50 Kgallons of drainable interstitial liquid and less than 5 Kgallons of supernatant liquid. If the tank was jet pumped to achieve interim stabilization, then the jet pump flow or saltwell screen inflow must also have been at or below 0.05 gpm before interim stabilization criteria is met.

Jet Pump

The jet pump system includes 1) a jet assembly with foot valve mounted to the base of two pipes that extend from the top of the well to near the bottom of the well casing inside the saltwell screen, 2) a centrifugal pump to supply power fluid to the down-hole jet assembly, 3) flexible or rigid transfer jumpers, 4) a flush line, and 5) a flowmeter. The jumpers contain piping, valves, and pressure and limit switches.

The centrifugal pump and jet assembly are needed to pump the interstitial liquid from the saltwell screen into the pump pit, nominally a 40-foot elevation rise. The power fluid passes through a nozzle in the jet assembly and acts to convert fluid pressure head to velocity head, thereby reducing the pressure in the jet assembly chamber. The reduction in pressure allows the interstitial liquid to enter the jet assembly chamber and mix with the power fluid. Velocity head is converted to pressure head above the nozzle, lifting power fluid, and interstitial liquid to the pump pit. Pumping rates vary from 0.05 gallons to about 4 gpm.

Saltwell Screen

The saltwell system is a 10-inch diameter saltwell casing consisting of a stainless steel saltwell screen welded to a Schedule 40 carbon steel pipe. The casing and screen are to be inserted into the 12-inch tank riser located in the pump pit. The stainless steel screen portion of the system will extend through the tank waste to near the bottom of the tank. The saltwell screen portion of the casing is an approximately 10-foot length of 300 Series, 10-inch diameter, stainless steel pipe with screen openings (slots) of 0.05 inches.

Emergency Pumping Trailer

A 45-foot tractor-type trailer is equipped to provide storage space and service facilities for emergency pumping equipment: this consists of two dedicated jet pump jumpers and two jet pumps, piping and dip tubes for each, two submersible pumps and attached piping, and a skid-mounted Weight Factor Instrument Enclosure (WFIE) with an air compressor and electronic recording instruments. The skid also contains a power control station for the pumps, pump pit leak detection, and instrumentation. A rack for over 100 feet of overground double-contained piping is also in the trailer.

INTRUSION PREVENTION (ISOLATION) Single-Shell Tanks only

Partially Interim Isolated (PI)

The administrative designation reflecting the completion of the physical effort required for Interim Isolation except for isolation of risers and piping that is required for jet pumping or for other methods of stabilization.

Interim Isolated (II)

The administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. In June 1993, Interim Isolation was replaced by Intrusion Prevention.

Intrusion Prevention (IP)

Intrusion Prevention is the administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. Under no circumstances are electrical or instrumentation devices disconnected or disabled during the intrusion prevention process (with the exception of the electrical pump).

Controlled, Clean, and Stable (CCS)

Controlled, Clean, and Stable reflects the completion of several objectives: "Controlled" - provide remote monitoring for required instrumentation and implement controls required in the TWRS Authorization Basis; "Clean" - remove surface soil contamination and downpost the Tank Farms to RBA/URMA/RA radiological control status, remove abandoned equipment, and place reusuable equipment in compliant storage; and "Stable" - remove pumpable liquids from the SSTs and IMUSTs and isolate the tanks.

TANK INTEGRITY

Sound

The integrity classification of a waste storage tank for which surveillance data indicate no loss of liquid attributed to a breach of integrity.

Assumed Leaker

The integrity classification of a waste storage tank for which surveillance data indicate a loss of liquid attributed to a breach of integrity.

Assumed Re-Leaker

A condition that exists after a tank has been declared as an "assumed leaker" and then the surveillance data indicates a <u>new</u> loss of liquid attributed to a breach of integrity.

TANK INVESTIGATION

Intrusion

A term used to describe the infiltration of liquid into a waste tank.

SURVEILLANCE INSTRUMENTATION

Drywells

Historically, the drywells were monitored with gross logging tools as part of a secondary leak monitoring system. In some cases, neutron-moisture sensors were used to monitor moisture in the soil as a function of well depth, which could be indicative of tank leakage. The routine gross gamma logging data were stored electronically from 1974 through 1994. The routine gross gamma logging program ended in 1994. A program was initiated in 1995 to log each of the available drywells in each tank farm with a spectral gamma logging system. The spectral gamma logging system provides quantitative values for gamma-emitting radionuclides. The baseline spectral gamma logging database is available electronically.

Repeat spectral drywell scans are not part of the established Tank Farm leak detection program, but can be run on request if special needs arise. A select subset of drywells is routinely monitored by the Vadose Zone Characterization Project to assess movement of gamma-emitting radionuclides in the subsurface.

Laterals

Laterals are horizontal drywells positioned under single-shell waste storage tanks to detect radionuclides in the soil which could be indicative of tank leakage. These drywells can be monitored by radiation detection probes. Laterals are 4-inch inside diameter steel pipes located 8 to 10 feet below the tank's concrete base. There are three laterals per tank. Laterals are located only in A and SX farms. There are currently no functioning laterals and no plan to prepare them for use.

Surface Levels

The surface level measurements in all waste storage tanks are monitored by manual or automatic conductivity probes, and recorded and transmitted or entered into the Surveillance Analysis Computer System (SACS).

Automatic FIC

An automatic waste surface level measurement device is manufactured by the Food Instrument Company (FIC). The instrument consists of a conductivity electrode (plummet) connected to a calibrated steel tape, a steel tape reel housing and a controller that automatically raises and lowers the plummet to obtain a waste surface level reading. The controller can provide a digital display of the data and until February 1999, the majority of the FICs transmitted readings to the CASS. Since CASS retirement, all FIC gauges are read manually. FICs are being replaced by ENRAF detectors (see below).

ENRAF 854 ATG Level Detector

FICs and some manual tapes are in the process of being replaced by the ENRAF ATG 854 level detector. The ENRAF gauge, fabricated by ENRAF Incorporated, determines waste level by detecting variations in the weight of a displacer suspended in the tank waste. The displacer is connected to a wire wound onto a precision measuring drum. A level causes a change in the weight of the displacer which will be detected by the force transducer. Electronics within the gauge causes the servo motor to adjust the position of the displacer and compute the tank level based on the new position of the displacer drum. The gauge displays the level in decimal inches. The first few ENRAFs that received remote reading capability transmit liquid level data via analog output to the Tank Monitor and Control System (TMACS). The remaining ENRAFs and future installations will transmit digital level data to TMACS via an ENRAF Computer Interface Unit (CIU). The CIU allows fully remote communication with the gauge, minimizing tank farm entry.

Annulus

The annulus is the space between the inner and outer shells on DSTs only. Drain channels in the insulating and/or supporting concrete carry any leakage to the annulus space where conductivity probes are installed. The annulus conductivity probes and radiation detectors are the primary means of leak detection for all DSTs.

Liquid Observation Well (LOW)

In-tank liquid observation wells are used for monitoring the interstitial liquid level (ILL) in single-shell waste storage tanks. The wells are usually constructed of fiberglass or TEFZEL-reinforced epoxy-polyester resin (TEFZEL, a trademark of E. I. du Pont de Nemours & Company). There are a few LOWs constructed of steel. LOWs are sized to extend to within 1 inch of the bottom of the waste tank, are sealed at their bottom ends and have a nominal outside diameter of 3.5 inches. Two probes are used to monitor changes in the ILL; gamma and neutron, which can indicate intrusions or leakage by increases or decreases in the ILL. There are 65 LOWs (64 are in operation) installed in SSTs that contain or are capable of containing greater than 50 Kgallons of drainable interstitial liquid, and in two DSTs only. The LOWs installed in two DSTs, (SY-102 and AW-103 tanks), are used for special, rather than routine, surveillance purposes only.

Thermocouple (TC)

A thermocouple is a thermoelectric device used to measure temperature. More than one thermocouple on a device (probe) is called a thermocouple tree. In DSTs there may be one or more thermocouple trees in risers in the primary tank. In addition, in DSTs only, there are thermocouple elements installed in the insulating concrete, the lower primary tank knuckle, the secondary tank concrete foundation, and in the outer structural concrete.

These monitor temperature gradients within the concrete walls, bottom of the tank, and the domes. In SSTs, one or more thermocouples may be installed directly in a tank, although some SSTs do not have any trees installed. A single thermocouple (probe) may be installed in a riser, or lowered down an existing riser or LOW. There are also four thermocouple laterals beneath Tank 105-A in which temperature readings are taken in 34 thermocouples.

In-tank Photographs and Videos

In-tank photographs and videos may be taken to aid in resolving in-tank measurement anomalies and determine tank integrity. Photographs and videos help determine sludge and liquid levels by visual examination.

TERMS/ACRONYMS

CCS Controlled, Clean and Stable (tank farms)

FSAR Final Safety Analysis Report (replaces BIOS, effective October 18, 1999)

II Interim Isolated

IP Intrusion Prevention Completed

IS Interim Stabilized

MT/FIC/ENRAF Manual Tape, Food Instrument Corporation, ENRAF Corporation (surface level

measurement devices)

OSD Operating Specifications Document

PI Partial Interim Isolated

SAR Safety Analysis Reports

SHMS Standard Hydrogen Monitoring System

TMACS Tank Monitor and Control System

TPA Hanford Federal Facility Consent and Compliance Order, "Washington State Department of

Ecology, U. S. Environmental Protection Agency, and U. S. Department of Energy," Fourth

Amendment, 1994 (Tri-Party Agreement)

TSR Technical Safety Requirements

USQ Unreviewed Safety Question

<u>Wyden Amendment</u> "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the <u>National Defense Authorization Act for Fiscal Year 1991</u>, November 5, 1990, Public Law 101-510.

3. <u>INVENTORY AND STATUS BY TANK - COLUMN VOLUME CALCULATIONS AND DEFINITIONS FOR TABLE A-6 (SINGLE-SHELL TANKS)</u>

COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS
Total Waste	Solids volume plus Supernatant liquid. Solids include sludge and saltcake (see definitions below).
Supernate (1)	May be either measured or estimated. Supernate is either the estimated or measured liquid floating on the surface of the waste or under a floating solids crust. In-tank photographs or videos are useful in estimating the liquid volumes; liquid floating on solids and core sample data are useful in estimating large liquid pools under a floating crust.
Drainable Interstitial Liquid (DIL) (1)	This is initially calculated. Drainable interstitial liquid is calculated based on the saltcake and sludge volumes, using calculated porosity values from past pumping or actual data for each tank. Interstitial liquid is liquid that fills the interstitial spaces of the solids waste. The sum of the interstitial liquid contained in saltcake and sludge minus an adjustment for capillary height is the initial volume of drainable interstitial liquid.

COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS
Pumped This Month	Net total gallons of liquid pumped from the tank during the month. If supernate is present, pump production is first subtracted from the supernatant volume. The remainder is then subtracted from the drainable interstitial liquid volume.
Total Pumped (1)	Cumulative net total gallons of liquid pumped from 1979 to date.
Drainable Liquid Remaining (DLR) (1)	Supernate plus Drainable Interstitial Liquid. The total Drainable Liquid Remaining is the sum of drainable interstitial liquid and supernate.
Pumpable Liquid Remaining (PLR) (1)	<u>Drainable Liquid Remaining minus unpumpable volume</u> . Not all drainable interstitial liquid is pumpable.
Sludge	Solids formed during sodium hydroxide additions to waste. Sludge usually was in the form of suspended solids when the waste was originally received in the tank from the waste generator. In-tank photographs or videos may be used to estimate the volume.
Saltcake	Results from crystallization and precipitation after concentration of liquid waste, usually in an evaporator. If saltcake is layered over sludge, it is only possible to measure total solids volume. In-tank photographs or videos may be used to estimate the saltcake volume.
Solids Volume Update	Indicates the latest update of any change in the solids volume.
Solids Update Source - See Footnote	Indicates the source or basis of the latest solids volume update.
Last In-tank Photo	Date of last in-tank photographs taken.
Last In-tank Video	Date of last in-tank video taken.
See Footnotes for These Changes	Indicates any change made the previous month. A footnote explanation for the change follows the Inventory and Status by Tank Appendix (Table E-6).

(1) As pumping continues, supernate, DIL, DLR, PLR, and total gallons pumped are adjusted accordingly based on actual pump volumes.

APPENDIX I

TANK FARM CONFIGURATION, STATUS AND FACILITIES CHARTS

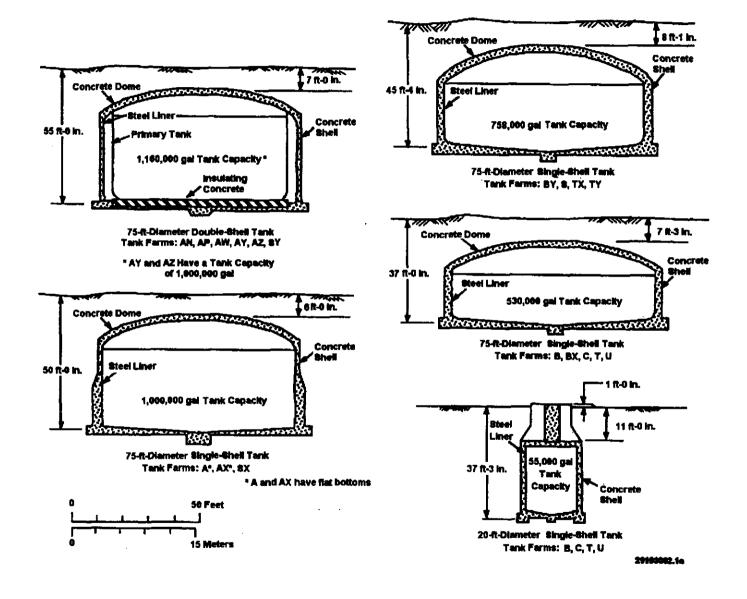


Figure I-1. High-Level Waste Tank Configuration

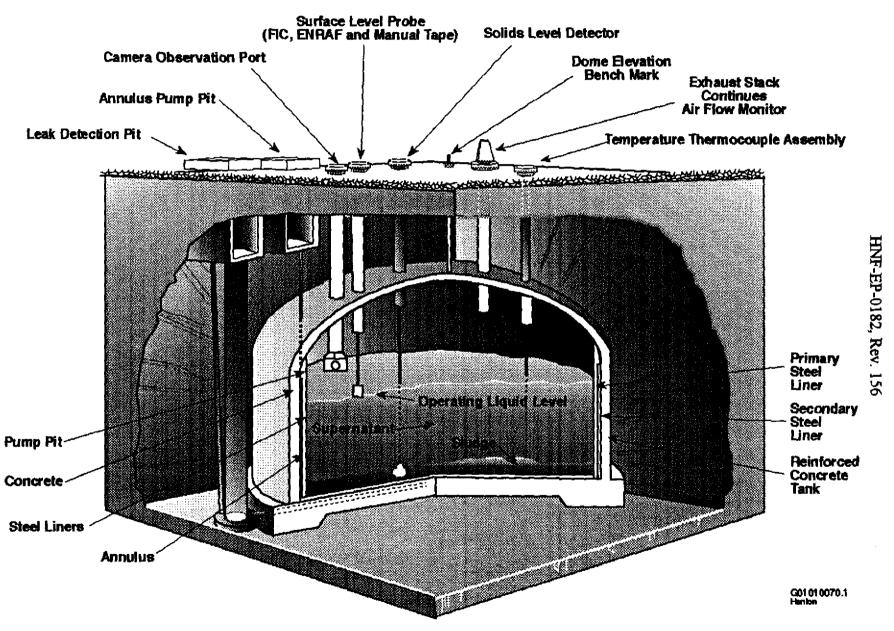


Figure I-2. Double-Shell Tank Instrumentation Configuration



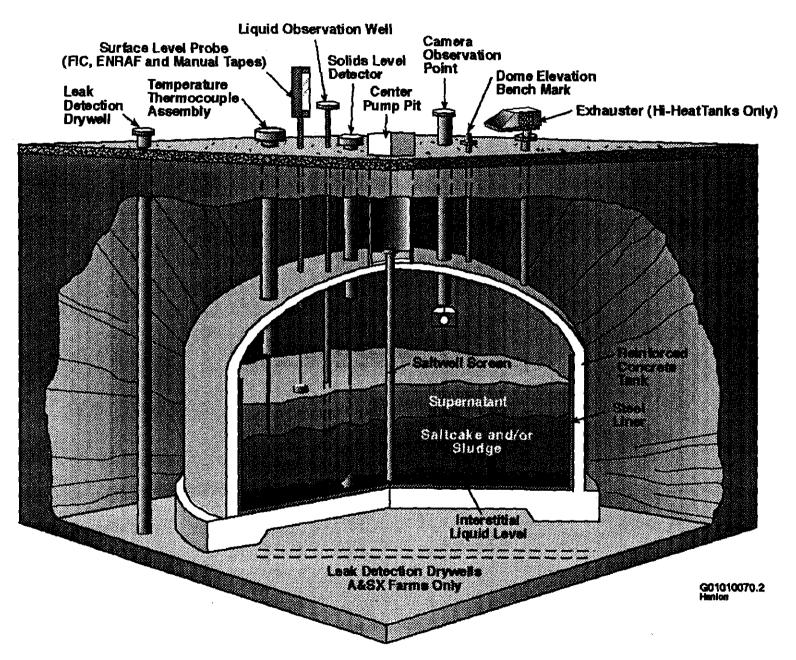


Figure I-3. Single-Shell Tank Instrumentation Configuration

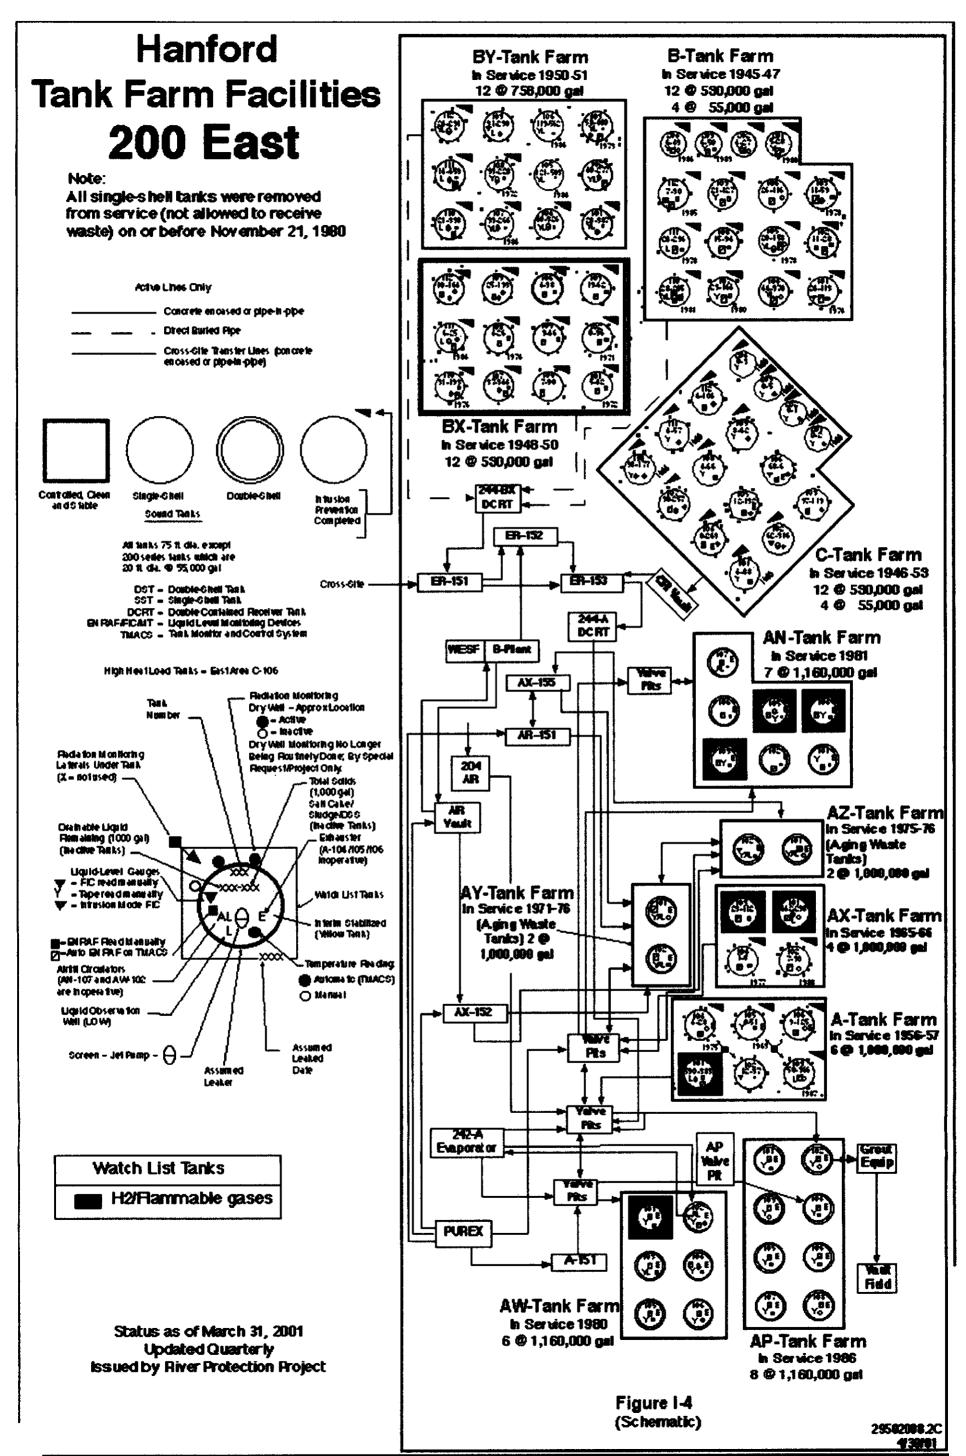

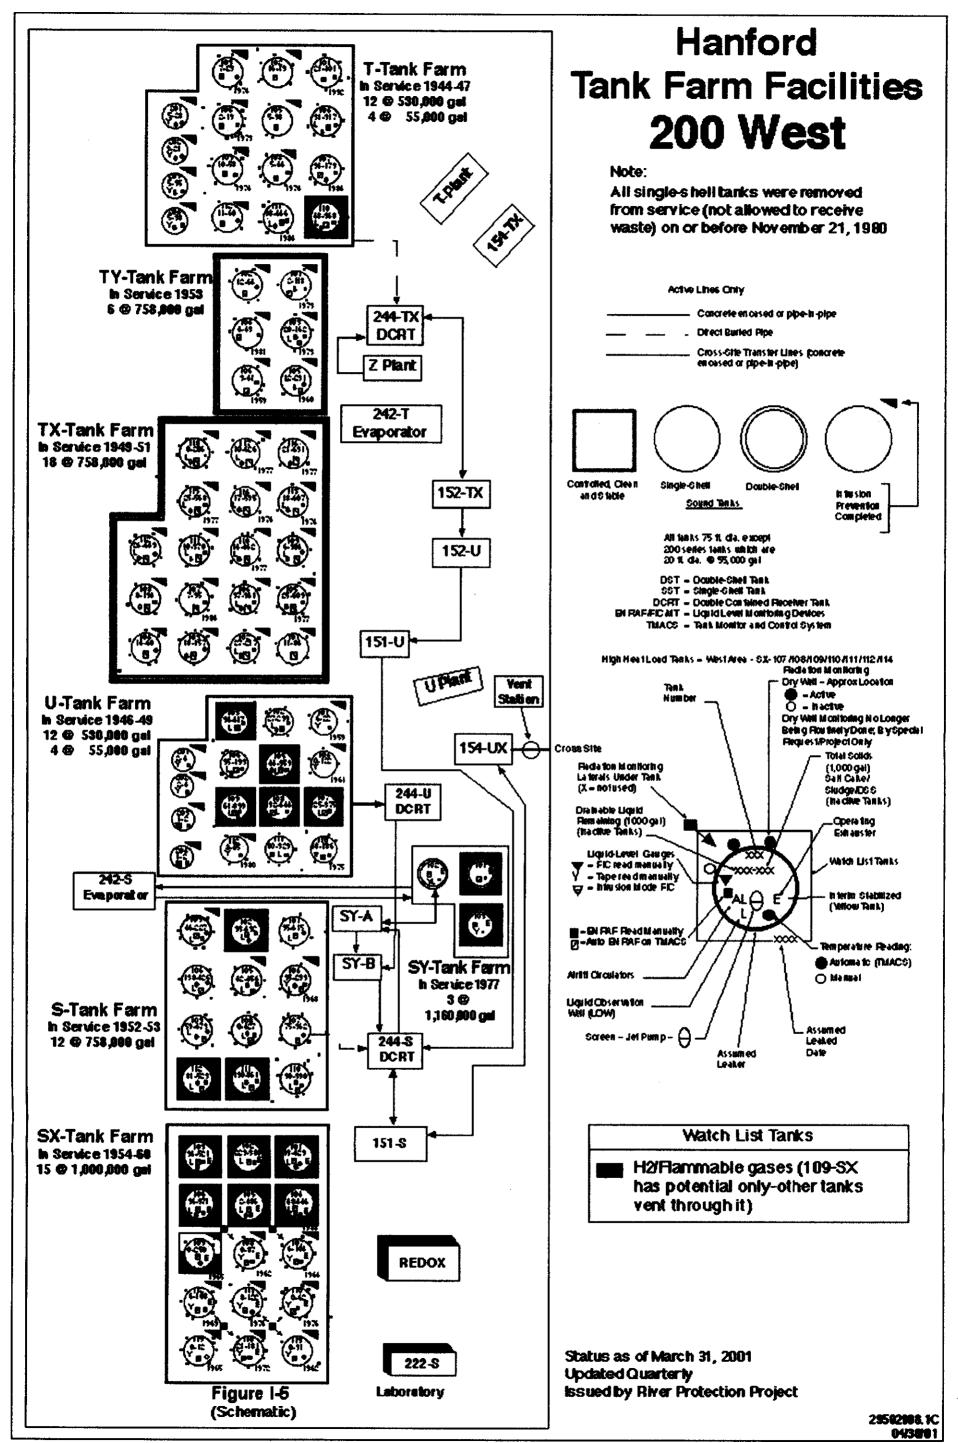

DISTRIBUTION

Number of copies

OFFSITE - USA

2 Congress of the United States

U. S. Senate

717 Hart Senate Building Washington D.C. 20510

Senator Ron Wyden

U. S. House of Representatives 1323 Longworth House Office Building Washington D. C. 20515

Congressman Richard "Doc" Hastings, 4th District Atten: Jeff Markey

U. S. Department of Energy-Headquarters 4

> 1000 Independence Avenue, SW Washington, D. C. 20585

H. Calley

EM-38 Cloverleaf Bldg.

Willam M. Levitan

EM-1 FORS/5A-014

U. S. Department of Energy-Headquarters

19901 Germantown Rd Germantown, MD 20874

Kurt Juroff

EM-44

Ralph Lightener

EM-44

1 U. S. Nuclear Regulatory Commission

Division of Fuel Cycle, Safeguards & Security Mail Stop T8-A33 Washington, DC 20555

Robert Pierson, Chief FSPB/FCSS (ADDRESSEE ONLY)

2 Washington State Department of Ecology

> Nuclear & Mixed Waste Management Program P.O. Box 47600

Olympia, WA 98504-7600

Library

Washington State Department of Ecology

Nuclear Waste Program 300 Desmond Drive Lacey, WA 98504

R. Stanley

1 Washington State Department of Health

Radiation Protection 7171 Cleanwater Lane P. O. Box 47827 Olympia, WA 98504-7827

Allen W. Conklin

1 Oregon State Department of Energy

625 Marion St. NE, Suite 1

Salem, OR 97301

Dirk Dunning

Do not remove from distribution without permission from ODOE

1 Oak Ridge National Laboratory

P. O. Box 2008

Oak Ridge, TN 37831-6180

C. Forsberg

MS-6180

Donald T. Oakley 9612 Hall Road

Potomac, MD 20854

1 Foster-Miller, Inc.

Power Systems Technology Group

350 Second Avenue

Waltham, MA 02451-1196

Maureen Williams

1 MACTEC

8310 Centerbrook Place Alexandra, VA 22308

Stanley Blacker, Vice President

1 Framatome Advanced Nuclear Power

3315 Old Forrest Rd Lynchburg, VA 24506

Brian Butler

TRI-CITIES:

1 ARES Corporation

636 Jadwin Ave., Suite B Richland, WA 99352

1 Babad Technical Services

2540 Cordoba Court Richland, WA 99352

1	Wastren Inc. 1050 Gilmore Ave, Suite C Richland, WA 99352	
	Gary Dunford	
<u>ONSITE</u>		
1 .	BAT R. T. Winward	H6-60
1	MACTEC - ERS J. F. Bertsch	B1-42
1	General Accounting Office C. R. Abraham	A1-80
1	Washington State Departme Library	ent of Ecology B5-18
1	U. S. Environmental Protect D. R. Sherwood	ion Agency B5-01
7	U. S. Department of Energy	<u>:</u>
	D. C. Bryson	H6-60
	Wen-Shou Liou	H6-60
	J. Polehn	H6-60
	M. J. Royack	H6-60
	A. B. Sidpara	H6-60
	D. J. Williams	H6-60
	Reading Room	H2-53
2	Pacific National Northwest 1	<u>aboratories</u>
	J. L. Huckaby	K7-15
	B. E. Opitz	K6-75
86	CH2M Hill (CHG), and Affiliated Co	<u>mpanies</u>
	D. I. Allen	S5-07
	J. C. Allen-Floyd	H6-06
	K. M. Bowen	R2-12
	V. C. Boyles	R2-11
	D. L. Carlile	T4-07
	R. J. Cash	R1-44
	C. Defigh-Price	T4-08
	M. P. Delozier	H6-08
	M. L. Dexter (12)	R1-51
	R. A. Dodd	S5-07
	A. F. Erhart	R3-73
	S. D. Estey	R2-11
	J. G. Field	R2-12

L. A. Fort

K. D. Fowler

G. T. Frater

J. R. Freeman-Pollard

R2-12

R2-11

T4-08

R1-57

B. C. Gooding	T4-07
B. M. Hanlon (8)	R3-72
D.C. Hedengren	R3-73
C. C. Hendersen	B2-05
B. A. Higley	R3-73
S. W. Hildreth	T4-07
K. M. Hodgson	R2-14
T. M. Hohl	R3-73
B. A. Johnson	S7-02
G. D. Johnson	R1-44
T. E. Jones	HO-22
J. Kalia	R1-43
M. R. Kembel	S7-03
R. A. Kirkbride	R3-73
P. F. Kison	T4-07
N. W. Kirch	R2-11
J. S. Konyu	S7-64
G. M. Koreski	R2-11
J. G. Kristofzski	R2-50
J. A. Lechelt	R2-11
P. Ohl	H4-01
T. May	R2-11
	H6-63
M. A. Payne R. E. Pohto	R2-84
	T4-08
R. E. Raymond (2)	
W. E. Ross	S7-83
N. J. Scott-Proctor	S5-00 R2-50
P. P. Sederburg	
J. N. Strode	R3-76
D. D. Taylor	H6-64
R. R. Thompson D. T. Vladimiroff	T4-08
	S7-20
A. E. Young (10)	R1-10
Central Files	B1-07
200 West Shift Office	T4-00
200 East Shift Office	S5-04
Environmental	
Data Mgmt Center (2)	H6-08
Unified Dose Assessment	110 00
Center (UDAC)	A0-20
Document Processing Center	A3-94
Dooming I Loopsanik Court	113 77
