Waste Tank Summary Report for Month Ending April 30, 2001

B. M. Hanlon CH2M HILL Hanford Group, Inc.

RECEIVED 1 9 2001

EDMC

Date Published May 2001

Prepared for the U.S. Department of Energy Assistant Secretary for Environmental Management

CH2MHILL

Hanford Group, Inc.

P. O. Box 1500 Richland, Washington

Contractor for the U.S. Department of Energy Office of River Protection under Contract DE-AC06-99RL14047

Approved for Public Release; Further Dissemination Unlimited

This page intentionally left blank.

ENGINEERING CHANGE NOTICE

Page 1 of ______

1. ECN	66	87	52	
*********		*****		

Proj. ECN

	<u>.</u>				
2. ECN Category (mark one)	3. Originator's Name, Orga	inization, MSIN, and Telephone	No.	4. USQ Required?	5. Date
Supplemental	1	ventory & Flowsheet	Eng.	☐ Yes ⊠ No	05/14/01
Direct Revision	R3-72, 373-2053		To 04- (0-		1
Change ECN	6. Project Title/No./Work O		7. Bldg./Sys	S/PEC. NO.	8. Approval Designator
Change ECN	Waste Tank Summa: Month Ending Apr:		,	I/A	N/A
Standby		inged by this ECN (includes		I ECN No(s).	11. Related PO No.
Supersedure	sheet no. and rev.)		1		
Cancel/Void	HNF-EP-0182, Rev	. 156	N	r/a	N/A
12a. Modification Work	12b. Work Package No.	12c. Modification Work Comp	leted	12d. Restored	to Original Condition (Temp. by ECNs only)
Yes (fill out Bik. 12b)		N/A		01 044,144	N/A
No (NA Biks. 12b, 12c, 12d)	N/A	Design Authority/Cog. Engin	eer Signature	& Design Autho	rity/Cog. Engineer Signature & Date
13a Description of Change		13b. Design Baseline Docum	2 17 Vac	⊠ No	Date
13a. Description of Change		i iyo. Design paseiine Docum	BIILE L 148	REM LAG	
Complete revision					
Computer generate	d:				
File: \\AP001\TWF	SSHAR\SHARE\BETTYH	1 \HNF-EP 1		. 17	
Size: 5-03M9-16-9	10-264 huses)	11 mp (5,344,736) 7 mb (4,381,1846)	(sutes)	rule	
DIZE. 3.33MD (0,2	4.1	7 mb (4,381, 1846	YTES)		
Modified: Monday,	May 14, 2001 1:04	:10 PM	•		
Thurs	MAY 24, 2001 H.	49:04 AM Brill			
Tuesda	- and 30 7	141129 pm			
· care	7, may = 1,2001	3:21:55 pm d.7:	\ 4/		
	-	5 30	-01		
d to helifortion (made and)	14b. Justification Details	<u> </u>			
14a. Justification (mark one)	14b. Sedireston Deale		•		
		ng generated to upd	ate wast	e tank farm s	ummarv
Design Improvement L Environmental	information.	., ,			
	31				
, , u, , , , , , , , , , , , , , ,	3 3				
}	-				
,]]	•			
	41				
Design Error/Omission L 15. Distribution (include name	A MRIN and no of content				RELEASE STAMP
19. Discirration (History Call	e, mont, and no. or copies)				THE COURT OF LAND
Distribution list	attached followin	g document			
				1.	/
				DATE:	К нанголо
				STA	4 RELEADE 12
			•		10
				MAY 2	7004~
				11000	COUL

				-			1. ECN (use	no. from pg. 1)
	ENGINEER	ING CHANGE NO	OTICE			Page 2 of 2	668	752
ENGINEERING CHANGE NOTICE		Impact (days)						
Required	1	RING		CON	ISTRI	JCTION	10. 0000	(42,5)
☐ Yes	Additional 🗆 \$	A	Additional	□ \$	·		Improvement	-
⊠ No	Savings 🔲 \$	s	Savings i	□ \$	·		Delay	D
	w: Indicate the related docu	uments (other than the eng	gineering do	cume	nts ide	entified on Side 1) that	will be affected	by
_	I IN Block 13. Enter the affect				_			_
			•					
1		_	•		_		··•	·
, ,			•			•	•	
1					_		•	ication \Box
l	·····		_			•		
1 '' '								
,								ration 🔲
Į.						•		
		. •						
· ·		•	y Requirem	ent			-	
,		_						
• • •		•	•			·		
			•	on	_		•	
		•	Schedule			FICKIET F	ile	
	_	•	D	_4	_			
	_	• •	•		_		Abadaba alaala	
organization has been	n notified of other affected do	ocuments listed below.	rices by and		, –,	MIGIGA DEIGH RIGHER	THE CONTRACTOR	•
0.80.177								
_							nent Number/Re	vision
Document	Number/Revision						nent Number/Re	vision
Document	Number/Revision						nent Number/Re	evi s lon
Document	Number/Revision						nent Number/Re	evision
Document N	Number/Revision	Document N				Docum	nent Number/Re	
Document N	Number/Revision	Document N				Docum	nent Number/Re	
Document N. 21. Approvals Design Authority	Number/Revision /A Signature	Document N	lumber/Revi	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority	Number/Revision /A Signature	Document N	Design	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hai	Number/Revision /A Signature	Date 5/14/01	Design PE	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hall Cog. Mgr. N.W. K1	Number/Revision /A Signature	Date 5/14/01	Design PE QA	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety	ision		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety	Agent		Docum	nent Number/Re	
Document N. 21. Approvals Design Authority Cog. Eng. B.M. Hat Cog. Mgr. N.W. K1	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design	Agent		Docum	nent Number/Re	
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ	Agent		Docum	nent Number/Re	
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ	Agent		Docum	nent Number/Re	
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other	Agent		Signature	nent Number/Re	
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other	Agent	TOF	Signature		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other	Agent	IT OF	Signature ENERGY Trol Number that tracks		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other	Agent	IT OF	Signature ENERGY Trol Number that tracks		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other	Agent TMEN Tre or and Sign	IT OF	Signature ENERGY Trol Number that tracks		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other DEPAR Signatu Approve	Agent TMEN Tre or and Sign	IT OF	Signature ENERGY Trol Number that tracks		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other DEPAR Signatu Approve	Agent TMEN Tre or and Sign	IT OF	Signature ENERGY Trol Number that tracks		
Document N 21. Approvals Design Authority Cog. Eng. B.M. Hai Cog. Mgr. N.W. K1 QA Safety Environ.	Number/Revision /A Signature	Date 5/14/01	Design PE QA Safety Design Environ Other DEPAR Signatu Approve	Agent TMEN Tre or and Sign	IT OF	Signature ENERGY Trol Number that tracks		

WASTE TANK SUMMARY REPORT FOR MONTH **ENDING APRIL 30, 2001**

BM HANLON

CH2M HILL Hanford Group, Inc. Richland, WA 99352

U.S. Department of Energy Contract DE-AC27-99RL14047

EDT/ECN: ECN-668752

UC:

Cost Center:

Charge Code:

B&R Code:


Total Pages: 88

Key Words: REPORT, WASTE TANK SUMMARY

Abstract: See page iii of document

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailetop H6-08, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.



Approved For Public Release

THIS PAGE INTENTIONALLY LEFT BLANK

RECORD OF REVISION

(1) Document Number HNF-EP-0182

Page 1

(2) Title

WASTE TANK SUMMARY REPORT FOR MONTH ENDING APRIL 30, 2001

	Change Control Record (3) Revision (4) Description of Change - Replace, Add, and Delete Pages (5) Cog. Engr. (6) Cog. Mgr. Date (7)							
		Author	zed for Release					
(3) Revision	<u></u>	(5) Cog. Engr.	(6) Cog. Mgr. Date					
153	(7) EDT~631372	BM Hanlon	JS Garfield					
157 RS	Incorporation of ECN-668752	BM Hanlon	NW Kirch 5/24					

THIS PAGE INTENTIONALLY LEFT BLANK

WASTE TANK SUMMARY REPORT

B. M. Hanlon

ABSTRACT

This report is the official inventory for radioactive waste stored in underground tanks in the 200 Areas at the Hanford Site. Data that depict the status of stored radioactive waste and tank vessel integrity are contained within the report. This report provides data on each of the existing 177 large underground waste storage tanks and 63 smaller miscellaneous underground storage tanks and special surveillance facilities, and supplemental information regarding tank surveillance anomalies and ongoing investigations. This report is intended to meet the requirement of U. S. Department of Energy-Richland Operations Office Order 435.1 (DOE-RL, July 1999, Radioactive Waste Management, U. S. Department of Energy-Richland Operations Office, Richland, Washington) requiring the reporting of waste inventories and space utilization for Hanford Tank Farm tanks.

This page intentionally left blank.

TABLE OF CONTENTS

· ·	Page
SUMMARY	
I WASTE TANK STATUS	
II. WASTE TANK INVESTIGATIONS	
III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS	
III. DOILVERENT TO THE WILL STILL ST	
Appendixes:	
A. MONTHLY SUMMARY	A-
Tables:	
1 Monthly Summary	
2 Tank Use Summary	
3 Pumping Record, and Liquid Status and Pumpable Liquid Remaining in Tanks	
4 Inventory Summary by Tank Farm	A
6 Inventory and Status by Tank - Double-Shell Tanks	
o inventory and status by Tank - Single-Shell Tanks	
B. PERFORMANCE SUMMARY	B- 1
Table:	
1 Summary of Waste Transactions in the Double-Shell Tanks	B-2
2 Comparison of Projected Versus Actual Waste Volumes for Hanford Facilities	B-2
C. DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION	C- 1
Tables:	-
1 Double-Shell Tank Waste Inventory	C-0
2 Double-Shell Tank Available Space	
Figures:	
1 Total Double-Shell Tank Inventory	
· · · · · · · · · · · · · · · · · · ·	
D. WASTE TANK SURVEILLANCE MONITORING TABLES	D- 1
Tables:	
1 Temperature Monitoring in Watch List Tanks	D-2
2 Temperature Monitoring in Non-Watch List Tanks	D-4
3 Additions/Deletions to Watch List Tanks by Year	D-:
4 Single-Shell Tanks Monitoring Compliance Status	
5 Double-Shell Tanks Monitoring Compliance Status	D-12
6 ENRAF Surface Level Gauge Installation and Data Input Methods	
7 Tank Monitor and Control System (TMACS)	D-15
E. MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPEC	TAT
SURVEILLANCE FACILITIES	E-1
Tables:	and to see the second
1 Miscellaneous Underground Storage Tanks and Special Surveillance Facilities (A	Euve)E-2
2 East Area Underground Storage Tanks and Special Surveillance Facilities (Inactiv	c)B-1
3 West Area Underground Storage Tanks and Special Surveillance Facilities (Inactive	vc)E-
F. LEAK VOLUME ESTIMATES	 -1
Table:	
1 Single-Shell Tank Leak Volume Estimates	F-:

G. SINGLE-SHELL TANKS INTERIM STABILIZATION AND CONTROLLED,	
CLEAN, AND STABLE (CCS) STATUS	G-1
Tables:	
1 Single-Shell Tanks Interim Stabilization Status	G-2
2 Single-Shell Tanks Interim Stabilization Milestones	G-4
3 Single-Shell Tanks Stabilization Status Summary	G-6
H. TANK AND EQUIPMENT CODE AND STATUS DEFINITIONS 1 Tank and Equipment Code/Status Definitions	H-1
I. TANK FARM CONFIGURATION, STATUS, AND FACILITY CHARTS	
1 High-Level Waste Tank Configuration	1-2
2 Double-Shell Tank Instrumentation Configuration	I-3
3 Single-Shell Tank Instrumentation Configuration	I-4

	METRIC CONV	ERSION CHART
l inch	=	2.54 centimeters
l foot	=	30.48 centimeters
l gallon		3.79 liters
l ton	=	0.91 metric tons
7/ 3	$^{\circ}F = \left(\frac{9}{5}\right)$	<i>)</i>
	1 Btu/h = 0 (Internatio	

WASTE TANK SUMMARY REPORT For Month Ending April 30, 2001

Note: Changes from the previous month are in bold print.

I. WASTE TANK STATUS

Quantity	Date of Last Change
28 double-shell	10/86
149 single-shell	1966
67 single-shell	07/93
28 double-shell 82 single-shell	1986 07/93
128 single-shell	03/01
21 single-shell	03/01
108 single-shell	09/96
36 single-shell	09/96
19 single-shell 5 double-shell	09/00 01/01
	28 double-shell 149 single-shell 67 single-shell 28 double-shell 82 single-shell 128 single-shell 21 single-shell 108 single-shell 36 single-shell

Of the 128 tanks classified as Interim Stabilized, 65 are listed as Assumed Leakers. (See Table G-1)

II. WASTE TANK INVESTIGATIONS

This section includes all single- or double-shell tanks or catch tanks which are showing surface level or interstitial liquid level (ILL) decreases, or drywell radiation level increases in excess of established criteria.

^{*} Five double-shell tanks (SY-101 was removed from the list in January 2001) are currently included on the Hydrogen Watch List and are thus prohibited from receiving waste in accordance with "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the National Defense Authorization Act for Fiscal Year 1991, Public Law 101-510, November 5, 1990.

^{&#}x27;Two of these tanks are Assumed Leakers (BY-105, BY-106). (See Table F-1)

⁴ See Appendix D for more information on Watch List Tanks.

Dates for the Watch List tanks are "officially added to or removed from the Watch List" dates. Eighteen tanks were removed from the Organic Watch List in December 1998; the last two tanks (C-102 and C-103) were removed from the Organic Watch List in August 2000. In December 1999, tank C-106 was removed from the High Heat Load Watch List. In January 2001, DST tank SY-101 was removed from the Hydrogen Watch List. Only the Hydrogen Watch List remains, which contains 19 SSTs and 5 DSTs.

^f The TY tank farm was officially declared Controlled, Clean, and Stable (CCS) in March 1996. The TX tank farm and BX tank farms were declared CCS in September 1996.

A. <u>Assumed Leakers or Assumed Re-leakers</u>: (See Appendix H for definition of "Re-leaker")

This section includes all single- or double-shell tanks or catch tanks for which an off-normal or unusual occurrence report has been issued, or for which a waste tank investigation is in progress, for assumed leaks or re-leaks. Tanks/catch tanks will remain on this list until either a) completion of Interim Stabilization, b) the updated occurrence report indicates that the tank/catch tank is not an assumed leaker, or c) the investigation is completed.

Catch Tank 241-AX-152 - This catch tank was declared an "assumed leaker" on March 23, 2001, by the Plant Review Committee, after an evaluation by the Leak Assessment Team. The water used as test solution was pumped to a double-shell tank on March 1, 2001, after the tank was identified as a potential leaking tank. (Also see item #3, Occurrence Report RP-CHG-Tankfarm-2001-0014).

B. Tanks with increases indicating possible intrusion:

This section includes all single-shell tanks and related receiver tanks for which the surveillance data show that the surface level or ILL has met or exceeded the increase criteria, or are still being investigated.

Candidate Intrusion List: Increase criteria in the following tanks indicate possible intrusions.

Tank 241-B-202 Tank 241-BX-101 Tank 241-BX-103 Tank 241-BY-103

The surveillance data was last reviewed on the tanks listed as having probable liquid intrusions: Memo 74B20-99-045, dated November 22, 1999.

III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS

A. <u>Single-Shell Tanks Saltwell Jet Pumping (See Table A-6 footnotes for further information)</u>

Tank 241-A-101 - Pumping began May 6, 2000. No pumping has occurred since August 2000; a total of 14.1 Kgallons has been pumped from this tank since the start of pumping in May 2000.

Tank 241-AX-101 - Pumping began July 29, 2000. No pumping since August 2000; pumping began again on March 22, 2001. In April 2001, a total of 3.6 Kgallons was pumped from this tank; a total of 21.7 Kgallons has been pumped since the start of pumping in July 2000.

Tank 241-S-102 - Pumping problems forced many shutdowns. The pump was replaced and pumping resumed on February 19, 2000. Problems with the new pump forced a shutdown on March 23, 2000. Pumping was interrupted in early June 2000. The flushing involved in trying to resume pumping in June resulted in a net addition to the tank. No pumping has occurred since June 2000; a total of 56.8 Kgallons has been pumped from this tank since start of pumping in March 1999.

Tank 241-S-109 - Pumping began September 23, 2000. The pumping rate dropped below 0.05 GPM and the pump was shut down on January 27, 2001. The tank is now being evaluated to determine if it can be Interim Stabilized. A total of 145.2 Kgallons has been pumped from this tank (111.0 Kgallons were pumped in 1979 [primary stabilization], and partial isolation was completed in 1982).

Tank 241-SX-101 - Pumping began November 22, 2000. The pump failed on December 9, 2000. No pumping since December 2000. A total of 19.2 Kgallons has been pumped from this tank.

Tank 241-SX-103 - Pumping began October 26, 2000. In April 2001, a total of 3.2 Kgallons was pumped; a total of 116.3 Kgallons has been pumped from this tank since start of pumping in October 2000.

Tank 241-SX-105 - Pumping began August 8, 2000. In April 2001, a total of 1.5 Kgallons was pumped; a total of 152.6 Kgallons has been pumped since start of pumping in August 2000.

Tank 241-U-102 - Pumping began January 20, 2000. During April 2001, a total of 3.9 Kgallons was pumped; a total of 79.7 Kgallons has been pumped from this tank since the start of pumping in January 2000.

Tank 241-U-109 - Pumping began March 11, 2000. The saltwell pump was replaced following its failure in December 2000, and pumping was restarted March 30, 2001. In April 2001, a total of 2.4 Kgallons was pumped; a total of 68.3 Kgallons has been pumped from this tank since start the of pumping in March 2000.

B. RP-CHG-TANKFARM-2001-0004, Occurrence Report, "Corrosion Observed in DST Tank 241-AY-101 During Video Inspection of the Annulus Section," Off-Normal Occurrence, Latest Update: May 2, 2001.

Corrosion of the primary and secondary liners of DST AY-101 was observed during video inspections of the tank annulus region in 1999 and 2000. Follow-up video inspections that were completed on January 29, 2001, show more extensive corrosion in localized regions of the primary and secondary liners when viewed from the annulus region.

In addition, ultrasonic testing data collected during March 2001 and evaluated on March 22, 2001, show localized thinning of approximately 19.4 percent, versus a reporting limit of 20 percent, of a small area on the inside of the primary liner at the previous waste-air interface approximately 343 inches above the bottom of the tank. Thus, corrosion has occurred on both

the outside and the inside of the primary liner, and on the inside of the secondary liner. There are no visual or radiological indications of waste leakage from the tank.

An operational restriction has been imposed to limit the waste level in this tank to less than 80 inches until further evaluation can be performed.

Internal tank videos have revealed two stained areas on the primary side of the internal tank wall. Preliminary evaluation by corrosion engineers indicates the stains potentially denote past leakage of known water intrusion from the annulus to the interior of the tank. Further evaluation will be necessary to assess the potential for penetration of the primary tank wall. The potential penetration points are approximately 22 feet above the waste surface, which is being controlled at 80 inches above the floor of the tank. There is no known evidence of any leakage from the tank to the annulus space, or any evidence of structural damage to the tank.

Testing and evaluation procedures are being discussed by tank and corrosion specialists from across the U.S. Department of Energy complex and the private sector.

An Update or a Final Report will be submitted no later than May 31, 2001.

C. RP-CHG-TANKFARM-2001-0014, Occurrence Report, "Catch Tank AX-152 was Identified as a Potential Leaking Tank," Off-Normal Occurrence, Notification Date: March 5, 2001, Latest Update: April 12, 2001.

Based on an engineering evaluation, this catch tank was identified as a potential leaking tank. On March 23, 2001, the Plant Review Committee determined, based on information and a recommendation by the Leak Assessment Team, to declare catch tank AX-152 an "assumed leaker." The water used as a test solution was pumped to a double-shell tank on March 1, 2001, as an immediate action.

This update is being submitted to provide additional time for Deficiency Evaluation and cause analysis.

An Update or a Final report will be submitted no later than May 17, 2001.

APPENDIX A MONTHLY SUMMARY

TABLE A-1. MONTHLY SUMMARY

Tank Status April 30, 2001

	200	200	
	EAST AREA	WEST AREA	TOTAL
IN SERVICE	25	03	28 (1)
OUT OF SERVICE	66	83	149
SOUND	59	51	110
ASSUMED LEAKER	32	35	67
INTERIM STABILIZED	60	68	128
ISOLATED			
PARTIAL INTERIM	11	30	41
INTRUSION PREVENTION COMPLETE	55	53	108
CONTROLLED, CLEAN, AND STABLE	12	24	36

		WASTE VOLU	MES (Kgallons))			
		200	200		SST	DST	
		EAST AREA	WEST AREA	TOTAL	TANKS	TANKS	TOTAL
SUPERN	ATANT						
AW	Aging waste	1775	0	1 77 5	0	1775	1775
CC	Complexant concentrate waste	3168	1066	4234	0	4234	4234
CP	Concentrated phosphate waste	1088	G	1088	0	1088	1088
DC	Dilute complexed waste	1680	913	2593	1	2592	2593
DN	Dilute non-complexed waste	894	0	894	0	894	894
PD	PUREX/TRUsolids	960	0	960	0	960	960
NCPLX	Non-complexed waste	164	151	315	315	0	315
DSSF	Double-shell slurry feed	5559	168	57 27	1035	4692	5727
TOTA	LSUPERNATANT	15288	2298	17586	1351	16235	17586
SOLIDS						*****************************	
Sludg	j ë	6555	5648	12203	11059	1144	12203
Salto	ake	8009	16097	24106	20797	3309	24106
TOTA	AL SOLIDS	14564	21745	36309	31856	4453	36309
TC	TAL WASTE	29852	24043	53895	33207	20688	53895
AVAILA	BLE SPACE IN TANKS	9885	723	10608	0	10608	10608
DRAINA	BLE INTERSTITIAL LIQUID (2)	1425	2024	3449	3449	(2)	3449
DRAINA	BLE LIQUID REMAINING (2)	2458	2342	4800	4800	(2)	4800

⁽¹⁾ Includes five double-shell tanks on the Hydrogen Watch List which are prohibited from receiving additional waste (AN-103, AN-104, AN-105, AW-101, and SY-103) by Public Law 101-510. SY-101 was removed from the Hydrogen Watch List in January 2001 and will return to service later in fiscal year 2001.

⁽²⁾ Drainable Interstitial Liquid and Drainable Liquid Remaining for single-shell tanks only; not applicable for double-shell tanks

TABLE A-2. TANK USE SUMMARY April 30, 2001

					ISOLATED TAI			
	TANKS AVAILABLE			PARTIAL	INTRUSION	CONTROLLED	- INTERIM	
TANK	TO RECEIVE		ASSUMED	INTERIM	PREVENTION	CLEAN, AND	STABILIZED	
<u>FARMS</u>	WASTE TRANSERS	<u>SOUND</u>	<u>LEAKER</u>	ISOLATED	COMPLETED	STABLE	<u>TANKS</u>	
EAST								
A	 O	3	3	2	4	0	5	
AN	7 (1)	7	0	0	0	0	0	
AP	8	8	0	0	0	0	0	
AW	6 (1)	6	0	0	0	0	0	1
AX	0	2	2	1	3	0	. 3	
AY	2	2	0	0	0	0	0	
ΑZ	2	2	0	0	0	0	0	
B	0	6	- 10	0	16	0	16	
BX	0	7	5	0	12	12	12	
BY	0	7	5	5	7	0	10	
С	0	9	7	3	13	0	14	
Total	25	59	32	11	55	12	60	
WEST								
S	0	11	1	10	2	0	6	
SX	0	5	10	6	9	0	11	
SY	3 (1)	3	0	0	0	0	0	
T	0	9	7	5	11	0	16	
TX	0	10	8	0	18	18	18	
TY	0	1	5	0	6	6	6	
U	0	12	4	9	7	0	11	
Total	3	51	35	30	53	24	68	
TOTAL	28	110	67	41	108	36	128	

⁽¹⁾ Five Double-Shell Tanks on the Hydrogen Watch List ere prohibited from receiving additional waste (AN-103, 104, 105, AW-101, and SY-103) by Public Law 101-510. SY-101 was removed from the Hydrogen Watch List in January 2001 and will return to service later in fiscal year 2001.

TABLE A-3. PUMPING RECORD, LIQUID STATUS, AND PUMPABLE LIQUID REMAINING IN TANK FARMS

April 30, 2001

			Waste Vo	lumes (Kgallons)			
<i>TANK <u>FARMS</u></i> EAST	PUMPED THIS MONTH	PUMPED FY H 10 DATE	CUMULATIVE TOTAL PUMPED 1979 TO DATE	SUPERNATANT LIQUID	DRAINABLE INTERSTITIAL LIQUID	DRAINABLE LIQUID REMAINING	PUMPABLE SST LIQUID REMAINING
A	0.0	0.0	164.6	503	161	665	622
AN	N/A	N/A	N/A	3770	N/A	N/A	N/A
AP	N/A	N/A	N/A	6274	N/A	N/A	N/A
AW	N/A	N/A	N/A	1906	N/A	N/A	N/A
AX	3.6	14.0	34.7	364	105	469	433
AY	N/A	N/A	N/A	531	N/A	N/A	N/A
AZ	N/A	N/A	N/A	1775	N/A	N/A	N/A
В	0.0	0.0	0.0	15	262	277	203
BX	N/A	0.0	200.2	24	127	N/A	N/A
BY	0.0	0.0	1567.8	0	581	581	498
С	0.0	0.0	103.0	126	189	315	207
Total	3.6	14.0	2070.3	15288	1425	2307	1963
WEST							
S	0.0	21.7	1075.1	76	636	712	578
SX	4.7	209.3	666.9	134	318	452	378 379
SY	N/A	N/A	N/A	1979	N/A	N/A	N/A
T	0.0	0.0	245.7	29	218	246	168
TΧ	N/A	0.0	1205.7	9	297	N/A	N/A
TY	N/A	0.0	29.9	Ō	53	N/A	N/A
U	6.3	39.4	373.5	71	502	573	487
Total	11.0	270.4	3596.8	2298	2024	1983	1812
TOTAL	14.6	284.4	5667.1	17586	3449	4290	3575

N/A = Not applicable for Double-Shell Tank Farms, and Single-Shell Tank Farms which have been declared Controlled, Clean and Stable (BX, TX, TY).

					SUPERA	IATANT	LIQUIL	VOL	UMES	Kgallo		SOLIE	S VOLUM	ME
TANK	TOTAL	AVAIL											SALT	
FARM	WASTE	SPACE	_AW	CC	CP	DC	<u>DN</u>	PD	NCPLX	DSSF	_TOTAL	SLUDGE	_CAKE	LATOL
EAST														
A	1479	0	0	0	0	0	0	0	0	503	503	574	402	976
AN	5519	2461	0	1779	0	0	253	0	0	1738	3770	0	1749	1749
AP	6363	2757	0	1389	1088	1603	37	0	0	2157	6274	0	89	89
AW	3354	3486	0	0	0	0	149	960	0	797	1906	624	824	1448
AX	812	0	0	0	0	0	0	0	0	364	364	26	422	448
AY	823	1137	. 0	0	0	76	455	0	0	0	531	292	0	292
AZ	1932	44	1775	0	0	0	0	0	0	0	1775	157	0	157
В	1909	0	0	0	0	0	0	0	15	0	15	1211	683	1894
BX	1490	0	0	0	0	0	0	0	24	σ	24	1259	207	1466
BY	4387	0	0	0	0	0	0	0	0	0	0	754	3633	4387
С	1784	0	0	0	0	1	0	0	125	0	126	1658	0	1658
Total	29852	9485	1775	3166	1088	1880	294	985	184	9559	15228	8555	8009	14564
WEST														
S	5056	0	0	0	0	0	0	0	75	1	76	1184	3796	4980
sx	3726	٥	0	0	0	0	0	0	0	134	134	927	2665	3592
SY	2697	723	0	1066	0	913	0	0	0	О	1979	71	647	718
T	1877	0	0	0	0	0	0	0	29	0	29	1703	145	1848
TX	6810	0	0	0	0	0	0	0	9	0	9	697	6104	6801
ΤΥ	639	0	0	0	0	0	0	0	0	0	0	529	110	639
U	3238	0	0	0	0	0	0	0	38	33	71	537	2630	3167
Total	24043	723	ō.	1986	O	913	O	Ð	151	168	2288	5548	18097	2174
TOTAL	53945	10808	1775	4234	1088	2599	894	960	315	6727	17586	12203	24108	36300

TABLE A-5. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

April 30, 2001

		TANK S	TATUS					SOLID	S VOLUME		PHOTOS/	VIDEOS	
				EQUIVA-		AVAIL.	SUPER-			401 P.F			SEE FOOTNOT
	_			LENT	TOTAL	SPACE	NATANT			SOLIDS	LAST	LAST	FOR
T A D 14'	WASTE	TANK STATUS	TANK USE	WASTE	WASTE	(1) (Yanali	LIQUID	SLUDGE (Kgal)	SALTCAKE (Kgal)	VOLUME	IN-TANK PHOTO	IN-TANK VIDEO	THESE
TANK	MATL	SIAIUS	USE.	MUNES	(Kgal)	(Kgal)	(Kgal)	(right)	(VBar)	DIDATE	THOTO	VIDEO	TOTANGE
						AN	TANK FAI	RM STATUS					
AN-101	DN	SOUND	DRÇVR	92.0	253	887	253	0	0	06/30/99			
AN-102	CC	SOUND	CWHT	383.3	1054	86	965	0	89	06/30/99			
AN-103	DSS	SOUND	CWHT	347.6	956	184	497	0	459	06/30/99	10/29/87		į.
AN-104	DSSF	SOUND	CWHT	382.2	1051	89	606	0	445	06/30/99	06/19/88		
AN-105	DSSF	SOUND	CWHT	409.8	1127	13	635	0	492	06/30/99	01/26/88		
AN-106	CC	SOUND	CWHT	13.8	38	1102	21	0	17	06/30/99			
AN-107	CC	SOUND	CWHT	378.2	1040	100	793	0	247	06/30/99	09/01/88		
DOUBLE	E-SHELL T	ANKS		TOTALS:	5519	2461	3770	0	1749				
_						AD	TANK PAR	RM STATUS	- · · · · · ·				
AP-101	DSSF	SOUND	DRCVR	404.7	1113	27	1113	0	0	05/01/89	l		1
AP-102	CP CP	SOUND	DRCVR	395.6	1088	52	1088	ő	ő	07/11/89			1
AP-103	CC	SOUND	DRCVR	102.2	281	859	281	o	o	05/31/96			1
AP-103	CC	SOUND	DRCVR	402.9	1108	32	1108	ő	o	10/13/88			ŀ
AP-105	DSSF	SOUND	CWHT	412.0	1133	7	1044	ő	89	06/30/99		09/27/95	.
AP-105	DC	SOUND	DRCVR	226.2	622	518	622	ő	0	10/13/88		03,2,,5	1
	DC	SOUND	DRCVR	356.7	981	159	981	l ő	ő	10/13/88			
AP-107 AP-108	DN	SOUND	DRCVR	13.5	37	1103	37	ő	0	10/13/88			
e coulei	E-SHELL T	ANKS		TOTALS:	6363	2757	6274	0	89	<u> </u>		· · · · · ·	-
O DOODE	L-OI ILLEC 1			1017.120.	0000		<u> </u>			-v.			
								RM STATUS					
AW-101	DSSF	SOUND	CWHT	409.5	1126		738	0	388	10/31/00	03/17/88		I
AW-102	DN	SOUND	EVFD	31.3	86		56	30	0	01/31/01	02/02/83		
AW-103	PD	SOUND	DRCVR	400.7	1102	38	789	273	40	06/30/99	Į		Į.
AW-104	DN	SOUND	DRÇVR	114.9	316	824	93	66	157	06/30/99	02/02/83		
AW-105	PD	SOUND	DRCVR	154.9	426	714	171	255	0	06/30/99			
AW-106	DSSF	SOUND	SRCVR	108.4	298	842	59	٥	239	06/30/99	02/02/83		
6 DOUBL	E-SHELL T	ANKS		TOTALS:	3354	3486	1906	624	824				

TABLE A-5. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

April 30, 2001

		TANK	STATUS					SOLIC	S VOLUME		PHOTO	S/VIDEOS	
TANK	WASTE MATL	TANK STATUS	TANK USE	EQUIVA- LENT WASTE INCHES	TOTAL WASTE (Kgal)	AVAIL. SPACE (1) (Kgall	SUPER- NATANT LIQUID (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO	SEE FOOTNOT FOR THESE CHANGES
		-				AY	TANK FAI	RM STATUS					
AY-101	DC	SOUND	DRCVR	66,9	184	796	76	108	0	06/30/99	12/26/82		l
AY-102	DN	SOUND	DRCVR	232,4	639	341	465	184	0	10/31/00	04/28/81		
2 DOUBL	E-SHELL	TANKS		TOTALS	823	1137	531	292	0				
						ΑZ	TANKFAI	rm status					
AZ-101	AW	SOUND	CWHT	340.4	936	44	684	52	0	06/30/98	08/18/83		1
AZ-102	AW	SOUND	DACVR	362.2	998	O	99 1	105	0	06/30/99	10/24/64]
2 DOUBL	E-SHELL	TANKS		TOTALS	1932	44	1775	157	0				
		<u> </u>				SY	TANK PAI	RM STATUS	·				
SY-101	CC	SOUND	CWHT	352.7	970	170	695	1 0	275	06/30/99	04/12/89		1
SY-102	DC	SOUND	DRCVR	357.8	984	156	913	71	0	06/30/99	04/29/B1		1
SY-103	cc	SOUND	CWHT	270.2	743	397	371	0	372	06/30/99	10/01/85		{
3 DOUBL	LE-SHELL	TANKS		TOTALS	2697	723	1979	71	847				
GRAND	TOTAL				20688	10608	16235	1144	3309	<u> </u>			┼

Note: +/- 1 Kgal differences are the result of computer rounding

Available Space Calcu	lations Used in this Docum	<u>nent</u>
Tank Ferms	(Most Conservative	
AN, AP, AW, SY	1,140,000 gel (414.5	i 1,140 Kgal
AY, AZ (Aging Westel	980,000 gal (358.4	i 980 Kgal

NOTE: Supernate + Sludge (Includes liquid) + Saltcake (Includes liquid) = Total Waste

⁽¹⁾ Available Space volumes include restricted space, - see Appendix C tables for allocation of these restrictions.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
April 30, 2001

XXXXXXXXXX							$a_{000000000000000000000000000000000000$	pru 30, 2	H0000000000000000000000000000000000000	*********	:::::::::::::::::::::::::::::::::::::::	200 000 0000000	000000000000000000000000000000000000000	William Commence		
			volumes a	e lle r	sult of	engineer				KK BEICE	with si	nisce le	rei measu	emenis		
	TANK S	TATUS					LIQ	NID VOLU	ME		SOLIDS	VOLUME		PHOTOS/	VIDEOS	
						DRAIN-			DRAIN-	PUMP-	l			_		SEE
					SUPER-	ABLE	PUMPED		ABLE	ABLE						FOOTNOT
			STABIL/	TOTAL	NATE	INTER-	THIS	TOTAL	FIGUID	LIQUID	i	SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION	WASTE	LIQUID	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE		VOLUME	IN-TANK	IN-TANK	THESE
TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kpal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGE
							A TAN	K FARM	STATUS							
A-101	DSSF	SOUND	/PI	877	494	95	0.0	14.1	590	574	з	380	09/30/99	06/21/85		(h)
A-102	DSSF	SOUND	IS/PI	41	4	8	0.0	39.5	12	4	15	22	07/27/89	07/20/89		,
A-103	DSSF	ASMD LKR	IS/IP	371	5	45	0.0	111.0	50	43	366	0	06/03/68	12/26/68		
A-104	NCPLX	ASMD LKR	IS/IP	28	١٥	4	0.0	0.0	4	0	28	0	01/27/78	06/25/86		ł
A-105	NCPLX	ASMD LKR	IS/IP	37	0	0	0.0	0.0	0	0	37	0	10/31/00	08/20/86		i
A-106	CP	SOUND	IS/IP	125	0	9	0.0	0.0	9	1	125	0	09/07/82	08/19/86		•
e chici	E-SHELL 1	TANKS	TOTALS	1479	503	161	0.0	164.6	665	622	574	402				├ ─
0 34101	E-SHIELL	AIRS	IOIALS	14/8	_ 603		0.0	104.0		022	1 8/4	402		<u> </u>		Ц
							AX TA	<u>NK FARM</u>	<u>STATUS</u>							_
AX-101	DSSF	SOUND	/PI	662	364	74	3.6	21.7	438	422	3	295	09/30/99	08/18/87		(1)
AX-102		ASMD LKR	IS/IP	30	0	7	0.0	13.0	7	0	7	23	06/30/99	06/05/89		
AX-103		SOUND	IS/IP	112	0	23	0.0	0.0	23	11	8	104	06/30/99	08/13/87		
AX-104	NCPLX	ASMD LKR	IS/IP	8	0	1	0.0	0.0	1	0	8	0	06/30/99	08/18/87		
4 SINGL	E-SHELL 1	ANKS	TOTALS:	612	364	105	3.6	34.7	469	433	28	422				
							D TAN	K FARM	CTATTIC				' -		·	
B-101	NCPLX	ASMD LKR	IS/IP	113	هٔ ا	24	0.0	0.0	<u>24</u>	17	ه ا	113	06/30/99	05/19/83		ı
B-102	NCPLX	SOUND	IS/IP	32	,	7	0.0	0.0	11	4	ة ا	28	06/30/99	08/22/85		
B-103	NCPLX	ASMD LKR	IS/IP	59		11	0.0	0.0	11	3	ŏ	59	06/30/99	10/13/88		
B-104	NCPLX	SOUND	IS/IP	371	Ĭ	45	0.0	0.0	46	42	309	61	06/30/99	10/13/88		
B-105	NCPLX	ASMD LKR	IS/IP	158	ه ا	20	0.0	0.0	20	16	28	130	06/30/99	05/19/88]
B-106	NCPLX	SOUND	IS/IP	117	ľ	25	0.0	0.0	26	19	ة ا	116	02/29/00	02/28/85		. *
B-107	NCPLX	ASMD LKR	IS/IP	165		22	0.0	0.0	23	19	93	71	06/30/99	02/28/85		
B-108	NCPLX	SOUND	IS/IP	94	ه ا	15	0.0	0.0	15	11	53	41	06/30/99	05/10/85		
B-109	NCPLX	SOUND	IS/IP	127	0	21	0.0	0.0	21	17	63	64	06/30/99	04/02/85		
B-110	NCPLX	ASMO LKR	IS/IP	246	1	27	0.0	0.0	28	20	245	0	02/28/86	03/17/88		i
B-111	NCPLX	ASMD LKR	IS/IP	237	1	23	0.0	0.0	24	29	236	0	06/28/85	06/26/85		
B-112	NCPLX	ASMD LKR	IS/IP	33	3	4	0.0	0.0	7	3	30	ō	05/31/85	05/29/85		
8-201	NCPLX	ASMD LKR	IS/IP	29	1	4	0.0	0.0	5	1	28	0	04/28/82		06/23/95	
B-202	NCPLX	SOUND	IS/IP	27	0	4	0.0	0.0	4	0	27	0	05/31/85	-	06/15/95	4
B-203	NCPLX	ASMD LKR	IS/IP	51	1	5	0.0	0.0	6	1	50	0	05/31/84	11/13/86		
B-204	NCPLX	ASMD LKR	IS/IP	50	1	5	0.0	0.0	6	1	49	o	05/31/84	10/22/87		1
10 0010	I E CUE''	TANKE	TOTALE	1909	 _						4055					
10 SING	BLE-SHELL	IMNE	TOTALS	1809	15	262	0.0	0.0	277	203	1211	683				

HNF-EP-0182, Rev. 157

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
April 30, 2001

		****************		*********		06:2:24000000000	4 2 9	P111 JO, 2	************		(Onnoncorrocoton	**********	***************************************	******		****
			volumes a	te lite re	anii o e	o di besi	10,615	il divines j	iii saya			14:-1		nem zest		
	TANK S	TATUS					1,10	UID VOLU	ME		SOLIDS	VOLUME		PHOTOS	VIDEOS	
				-	l -	DRAIN-			DRAIN-	PUMP-	[SEE
						ABLE	PUMPED		ABLE	ABLE	ľ					FOOTNOT
			STABIL	TOTAL	SUPER-	INTER-	THIS	TOTAL	LIQUID	FIGUID	1	SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION		NATE	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MATL.	INTEGRITY	STATUS	(Kgal)	(Kgafi	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGE
							BX TA	NK FARM	STATUS			_				
BX-101	NCPLX	ASMD LKR	IS/IP/CCS	43	1	4	0.0	0.0	- 5	t	42	0	04/28/82	11/24/88	11/10/94	1
BX-102	NCPŁX	ASMO LKR	IS/IP/CCS	96] 0	0	0.0	0.0	0	0	96	0	04/28/82	09/18/85		Ì
BX-103	NCPLX	SOUND	IS/IP/CCS	71	9	4	0.0	0.0	13	9	62	0	11/29/63	10/31/86	10/27/94	{
BX-104	NCPLX	SOUND	IS/IP/CCS	93] 3	4	0.0	17.4	7	3	90	0	02/29/00	09/21/89		
BX-105	NCPLX	SOUND	IS/IP/CCS	51	5	4	0.0	15.0	9	5	46	0	06/30/99	10/23/86		l
8X-106	NCPLX	SOUND	IS/IP/CCS	38	Jo	4	0.0	14.0	4	0	38	0	06/01/95	05/19/88	07/17/95	
BX-107	NCPLX	SOUND	IS/IP/CCS	345	1	36	0.0	23.1	37	33	344	0	09/18/90	09/11/90		l
BX-108	NCPLX	ASMD LKR	IS/IP/CCS	26	0	4	0.0	0.0	4	0	26	0	07/31/79	05/05/94		
BX-109	NCPLX	SOUND	IS/IP/CCS	193	0	25	0.0	8.2	26	20	193	O	09/17/90	09/11/90		}
BX-110	NCPLX	ASMD LKR	IS/IP/CCS	207	3	28	0.0	1.5	31	26	133	71	06/30/99	07/15/94	10/13/94	
BX-111	NCPLX	ASMO LKR	IS/IP/CCS	162	1	5	0.0	116.9	6	2	25	136	06/30/99	05/19/94	02/28/95	ļ
BX-112	NCPLX	SOUND	IS/IP/CCS	165	1	9	0.0	4.1	10	7	164	0	09/17/90	09/11/90		İ
12 SING	BLE-SHELL	TANKS	TOTALS:	1490	24	127	0.0	200.2	151	106	1259	207				
		<u></u>	<u> </u>				BY TAI	NK FARM	STATUS							
BY-101	NCPLX	SOUND	IS/IP	387	1 0	28	0.0	35.8	28	24	1 109	278	05/30/84	09/19/89		1
BY-102	NCPLX	SOUND	IS/PI	277	0	40	0.0	159.0	40	33	0	277	05/01/95		04/11/95	ł
BY-103	NCPLX	ASMD LKR	IS/PI	400	0	58	0.0	95.9	58	53	9	391	06/30/99		02/24/97	1
BY-104	NCPLX	SOUND	1S/IP	326	[0	40	0.0	329,5	40	36	150	176		04/27/83		1
BY-105	NCPLX	ASMD LKR	/Pi	503) 0	121	0.0	0.0	121	111	48	455	l .	07/01/86		1
BY-106	NCPLX	ASMD LKR	/PI	562	٥	132	0.0	63.7	132	119	84	478	12/31/98	11/04/82		ł
BY-107	NCPLX	ASMD LKR	IS/IP	266	٥	39	0.0	56.4	39	35	40	226	06/30/99	1		•
BY-108	NCPLX	ASMD LKR	IS/IP	228	0	33	0.0	27.5	33	26	154	74	04/28/82	10/15/86		Į.
BY-109	NCPLX	SOUND	IS/PI	290	j o	31	0.0	157.1	-31	26	. 57	233		06/18/97		
BY-110	NCPLX	SOUND	IS/IP	398	0	21	0.0	213.3	21	17	103	295	1	07/26/84		ł
BY-111	NCPLX	SOUND	IS/IP	459) 0	14	0.0	313.2	14	6	0	459	1	10/31/86		1
BY-112	NCPLX	COUND	IS/IP	291	0	24	0,0	116,4	24	12	0	291	;	04/14/88		1
10 6897	DIE SUELI	TANKS	TOTAL S:	4387	-	581	0.0	1567,8	581	498	75.4	2022	 	 		
IZ SHIC	BLE-SHELL	. IAUV2	TOTALS:	436/	<u>. </u>	50 (0.0	1507.8	501	498	754	3633	<u> </u>			1

HNF-EP-0182, Rev. 157

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

			These	volumes a	re the n	endt of	engineer	800000000000000000000000000000000000000	ulations	357555555555555555	not agree	with s	rface le	vel mean	rements		
		TANK S							UID VOLU				VOLUME				
							DRAIN-			DRAIN-	PUMP-						SEE
							ABLE	PUMPED		ABLE	ABLE						FOOTNOTES
				STABIL/	TOTAL	SUPER-	INTER-	THIS	TOTAL	LIQUID	LIQUID		SALT	SOLIDS	LAST	LAST	FOR
		WASTE	TANK	ISOLATION	WASTE	NATE	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
	TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
				. -	-			C TAI	NK FARM	STATUS			-		-		
	C-101	NCPLX	ASMD LKR	IS/IP	88	0	4	0.0	0.0	4	0	88	0	11/29/83	11/17/87		
	C-102	DC	SOUND	IS/IP	316	0	62	0,0	46.7	62	55	316	0	09/30/95	05/18/76	08/24/95	
	C-103	NCPLX	SOUND	/PI	198	79	18	0.0	0.0	97	83	119	0	12/31/98	07/28/87		
	C-104	CC	SOUND	IS/IP	263	0	0	0.0	0.0	0	0	263	0	02/01/00	07/25/90		
	C-105	NCPLX	SOUND	IS/PI	132	0	20	0.0	0.0	20	0	132	0	02/29/00	08/05/94	08/30/95	
	C-106	NCPLX	SOUND	/Pf	48	42	0	0.0	0.0	42	9	6	0	10/31/99	08/05/94	08/08/94	İ
	C-107	DC	SOUND	IS/IP	257	0	30	0.0	40.B	30	25	257	0	06/30/99	00/00/00		
	C-108	NCPLX	SOUND	IS/IP	66	0	4	0.0	0.0	4	0	66	0	02/24/84	12/05/74	11/17/94	Į.
	C-109	NCPLX	SOUND	IS/IP	66	4	4	0.0	0.0	8	4	62	0	11/29/83	01/30/76		
	C-110	DC	ASMO LKR	IS/IP	178	1	37	0.0	15.5	38	30	177	0	06/14/95	08/12/86	05/23/95	
	C-111	NCPLX	ASMD LKR	IS/IP	57	0	4	0.0	0.0	4	0	57	0	04/28/82	02/25/70	02/02/95	
•	C-112	NCPLX	SOUND	IS/IP	104	0	6	0.0	0.0	6	1	104	0	09/18/90	09/18/90		1
5	C-201	NCPLX	ASMD LKR	IS/IP	2	0	0	0.0	0.0	0	0	2	0	03/31/82	12/02/86		
	C-202	EMPTY	ASMID LKR	IS/IP	1	0	0	0.0	0.0	0	0	1	0	01/19/79	12/09/86		Ī
	C-203	NCPLX	ASMD LKR	IS/IP	5	0	0	0.0	0.0	0	0	5	0	04/28/82	12/09/86		ļ
	C-204	NCPLX	ASMD LKR	IS/IP	3	0	0	0.0	0.0	0	0	3	0	04/28/82	12/09/86		Ì
	16 SING	OLE-SHELL	TANKS	TOTALS:	1784	126	189	0.0	103.0	315	207	1658	0				
					1				IK FARM			•					
	S-101	NCPLX	SOUND	/Pt	427	12	83	0.0	0.0	95	80	211	204	12/31/98	03/18/88		
	S-102	DSSF	SOUND	/PI	492	0	93	0.0	56.8	93	89	105	387	05/31/00	03/18/88		(c)
	S-103	DSSF	SOUND	IS/PI	237	1	45	0.0	23.9	46	39	9	227	04/30/00		01/28/00	•
	S-104	NCPLX	ASMD LKR	IS/IP	294	1	34	0.0	0.0	35	31	293	0	1 2/20/84	12/12/84		
	S-105	NCPLX	SOUND	IS/IP	456	0	42	0.0	114.3	42	33	2	454	09/26/88	04/12/89		i
	S-106	NCPLX	SOUND	IS/PI	455	0	26	0.0	203.6	26	2	٥	455	02/28/01	03/17/89	01/28/00	I
	S-107	NCPLX	SOUND	/PI	376	14	61	0.0	0.0	75	61	293	69	06/30/99	03/12/87		
	S-108	NCPLX	SOUND	IS/PI	432	0	0	0.0	199.6	0	0	5	427	10/01/99	03/12/87	12/03/96	
	S-109	NCPLX	SOUND	/PI	473	0	59	0.0	145.2	59	49	13	460	12/31/00	12/31/98		(e)
	S-110	NCPLX	SOUND	IS/PI	390	0	30	0.0	203.1	30	27	131,	259	05/14/92	03/12/87	12/11/96	1
	S-111	NCPLX	SOUND	/PI	501	48	82	0.0	3.3	130	97	116	337	09/30/99	08/10/89		
	S-112	NCPLX	SOUND	/PI	523	0	B 1	0.0	125.1	81	70	6	517	12/31/98	03/24/87		!
	12 SING	SLE-SHELL	TANKS	TOTALS:	5056	76	636	0.0	1075.1	712	578	1184	3796				·
						_						<u> </u>					<u> </u>

<u>A-1</u>

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

	Anna ann an Anna Anna Anna Anna					***********		ли ж, д		dankti. Wasanini						
			volumes a	n the re	solt of	agineer	ujy (calcu	1 (16 (1.)	nd may	a karee				ements		
	TANK S	TATUS					LIQ	UID VOLU	ME		SOLIDS	VOLUME				
					1	DRAIN-			DRAIN-	PUMP-						SEE
						ABLE	PUMPED		ABLE	ABLE						FOOTNOT
			STABIL/	TOTAL	SUPER-	INTER-	THIS	TOTAL	LIQUID	LIQUID	l	SALT	SOLIDS	LAST	LAST	FOR
	WASTE	TANK	ISOLATION		NATE	STIT.	MONTH	PUMPED	REMAIN		SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	THESE
TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgel)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
			-				SX TAI	NK PARM	STATUS							
SX-101	DC	SOUND	/PI	429	0	93	0.0	19.2	93	80	1 0	429	12/31/00	03/10/89		(e)
SX-102	DSSF	SOUND	/P1	514	. 134	95	0.0	0.0	229	216	0	380	04/30/00		•	'='
SX-103	NCPLX	SOUND	/PI	518	o	31	3.2	116.3	31	16	115	403	04/30/01	12/17/87		(k)
SX-104	DSSF	ASMD LKR	IS/PI	446	0	48	0.0	231.3	. 48	44	136	310	04/30/00	09/08/98	02/04/98	
SX-106	DSSF	SOUND	/PI	484	0	0	1.5	152.6	0	-12	65	419	04/30/01	06/15/8B		(g)
SX-106	NCPLX	SOUND	15/PI	397	0	37	0.0	147.5	37	31	0	397	05/31/99	06/01/89		
SX-107	NCPLX	ASMD LKR	IS/IP	102	0	0	0.0	0.0	0	0	85	17	10/31/00	03/06/87		J
5X-108	NCPLX	ASMD LKR	IS/IP	87	0	0	0.0	0.0	0	0	87	0	12/31/93	03/06/87		
SX-109	NCPLX	ASMD LKR	IS/IP	249	0	0	0.0	0.0	0	0	60	189	10/31/00	05/21/86		
8X-110	NCPLX	ASMD LKR	IS/IP	62	0	0	0.0	0.0	0	0	62	0	10/06/76	02/20/87		İ
6X-111	NCPLX	ASMD LKR	IS/IP	122	0	8	0.0	0.0	8	3	122	0	06/30/99	06/09/94		ľ
SX-112	NCPLX	ASMD LKR	IS/IP	108	0	6	0.0	0.0	6	1	108	0	06/30/99	03/10/67		
SX-113	NCPLX	ASMD LKR	IS/IP	31	0	0	0.0	0.0	0	0	31	0	06/30/99	03/16/88		Ì
SX-114	NCPLX	ASMD LKR	IS/IP	165	0	0	0.0	0.0	0	0	44	121	10/31/00	02/26/87		J
SX-115	NCPLX	ASMD LKR	IS/IP	12	0	0	0.0	0.0	0	0	12	0	04/28/82	03/31/88		ļ
5 SING	LE-SHELL	TANKS	TOTALS:	3726	134	318	4.7	666.9	452	379	927	2665				
							T TAN	K FARM	STATUS							
T-101	NCPLX	ASMD LKR	IS/PI	102	1	20	0.0	25.3	21	16	37	64	06/30/99	04/07/93		1
T-102	NCPLX	SOUND	IS/IP	32	13	3	0.0	0.0	16	11	19	0	08/31/84	06/28/89		ļ
T-103	NCPLX	ASMD LKR	IS/IP	27	4	3	0.0	0.0	7	3	23	0	11/29/83	07/03/84		
T-104	NCPLX	SOUND	15/PI	317	0	31	0.0	149.5	31	27	317	0	12/31/99	06/29/89	10/07/99	ı l
T-105	NCPLX	SOUND	IS/IP	98	0	5	0.0	0.0	. 5	0	98	0	05/29/87	05/14/87		ļ
T-106	NCPLX	ASMO LKR	IS/IP	21	2	0	0.0	0.0	2	2	19	0	04/28/82	06/29/89		1
T-107	NCPLX	ASMD LKR	15/PI	173	0	34	0.0	11.0	34	20	173	0	05/31/96	07/12/84	05/09/96	1
T-108	NCPLX	ASMD LKR	IS/IP	44	0	5	0.0	0.0	5	0	21	23	06/30/99	07/17/84		1

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

·····	TANK S		volumes a	engainemakhi		monimum.		UID VOLU		سمد الشمد		VOLUME			<u> </u>	****
	WASTE	TANK	STABIL/		SUPER-	ORAIN- ABLE INTER- STIT.	PUMPED THIS MONTH	TOTAL PUMPED	DRAIN- ABLE LIQUID REMAIN	PUMP- ABLE LIQUID REMAIN	SUIDGE	SALT	SOLIDS VOLUME	LAST IN-TANK	LAST IN-TANK	SEE FOOTNOTE FOR
TANK	MATL.	INTEGRITY	STATUS	-	(Kgel)	(Kgal)		(Kgel)	(Kgal)		(Kgal)	(Kgal)	UPDATE	PHOTO	VIDEO	CHANGES
					<u>-</u> -											•
-109	NCPLX	ASMD LKR	IS/IP	58	0	10	0.0	0.0	10	3	٥	58	06/30/99			1
-110	NCPLX	SOUND	IS/PI	369	1	48	0.0	50.3	48	43	368	0	01/31/00	07/12/B4		
-111	NCPLX	ASMD LKR	IS/PI	446	•	38	0.0	9.6	38	35	446	0	04/18/94	04/13/94	02/13/95	i
-112	NCPLX	SOUND	IS/IP	67	7	4	0.0	0.0	11	7	60	0	04/28/82	08/01/84		
-201	NCPLX	SOUND	IS/IP	29	1 1	4	0.0	0.0	5	1	28	0	05/31/78	04/15/86		ľ
-202	NCPLX	SOUND	IS/IP	21	0	3	0.0	0.0	3	0	21	0	07/12/81	07/06/89		
-203	NCPLX	SOUND	IS/IP	35	0	5	0.0	0.0	5	0	35	0	01/31/78	08/03/89		
-204	NCPLX	SOUND	ts/IP	38	0	5	0.0	0.0	5	0	38	0.	07/22/81	08/03/89		
6 SING	3LE-SHELL	TANKS	TOTALS:	1877	29	218	0,0	245.7	246	168	1703	145				1
							THE TAI	NK FARM			<u> </u>			<u> </u>		<u> </u>
FY.101	NCPLX	SOUND	IS/IP/CCS	87	1 3	8	0.0	0.0	11	7	74	10	06/30/99	10/24/85		ī
	NCPLX	SOUND	IS/IP/CCS	217	ا آ	27	0.0	94.4	27	16	6	217	08/31/84	10/31/85		
	NCPLX	SOUND	IS/IP/CCS	157	١،	18	0.0	68.3	18	11		157	06/30/99	10/31/85		
	NCPLX	SOUND	IS/IP/CCS	65	5	9	0.0	3.6	14	9	23	37	06/30/99	10/16/84		
	NCPLX	ASMD LKR	IS/IP/CCS	609	ه ا	25	0.0	121.5	25	14	23	609	08/22/77	10/24/89		1
	NCPLX	SOUND	IS/IP/CCS	341	Ö	37	0.0	134.6	37	30	Ιŏ	341	06/30/99	10/31/85		l
	NCPLX	ASMD LKR	IS/IP/CCS	36	Ĭ	6	0.0	0.0	7	1	8	27	06/30/99	10/31/85		
	NCPLX	SOUND	IS/IP/CCS	134	6	8	0.0	13.7	6	1	6	128	06/30/99	09/12/89		
	NCPLX	SOUND	IS/IP/CCS	384	ة ا	6	0.0	72.3	6	2	384	0	06/30/99	10/24/89		İ
	NCPLX	ASMD LKR	IS/IP/CCS	462	ة ا	14	0.0	115.1	14	10	37	425	06/30/99			
	NCPLX	SOUND	IS/IP/CCS	370	ľ	10	0.0	98.4	10	6	43	327	06/30/99	09/12/89		
	NCPLX	SOUND	IS/IP/CCS	649	0	26	0.0	94.0	26	21	0	649	05/30/83	11/19/87		· ·
	NCPLX	ASMD LKR	IS/IP/CCS	653	ا	30	0.0	19.2	30	0	ő	653	10/31/00	04/11/83	00/22/04	1
	NCPLX	ASMD LKR	IS/IP/CCS	535	١ ٥	17	0.0	104.3	17	11	4	631	06/30/99	04/11/83		1
	NCPLX	ASMD LKR	IS/IP/CCS	568	l ő	25	0.0	99.1	25	15		568	06/30/99	06/15/88	02/17/90	Ï
	NCPLX	ASMD LKR	IS/IP/CCS	631	l ő	25	0.0	23.8	21	17	68	563	06/30/99	10/17/89		
	NCPLX	ASMD LKR	IS/IP/CCS	626	"	10	0.0	54.3	10	5	29	503 597	06/30/99	04/11/83		1
	NCPLX	SOUND	IS/IP/CCS	286		0	0.0	54.3 89.1	0	0	29	265	02/01/00			
											<u> </u>		32,3.,00			<u> </u>
8 SIN	GLE-SHELL	TANKS	TOTALS:	6810	9	297	0.0	1205.7	306	176	697	6104				1

HNF-EP-0182, Rev. 157

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS
April 30, 2001

						*************		AĮ	oru 30, 2	VUI						****	
			These	volumes a	o lie re	ault of	51/4H 14/1	ing calci	lations 9	0.05%	of agree	with su	ire (yo energy	0.002005		
		TANK S	TATUS					FIO	NID AOFR	ME		SOLIDS	VOLUME		PHOTOS/	/IDEOS_	<u> </u>
						j .	DRAIN-			DRAIN-	PUMP-	İ					SEE
						SUPER-	ABLE	PUMPED		ABLE	ABLE	l					FOOTNOTES
				STABIL/	TOTAL	NATE	INTER-	THIS	TOTAL	LIQUID	LIQUID	j	SALT	SOLIDS	LAST	LAST	FOR
		WASTE	TANK	ISOLATION	WASTE	riguid	STIT.	MONTH	PUMPED	REMAIN	REMAIN	SLUDGE	CAKE	VOLUME	IN-TANK	IN-TANK	
	TANK	MAT'L.	INTEGRITY	STATUS	(Kgal)	(Kgal)	(Kgat)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgel)	UPDATE	PHOTO	VIDEO	CHANGES
								TY TA	NK FARM	STATUS							
	TY-101	NCPLX	ASMD LKR	IS/IP/CCS	118	1 0	2	0.0	8.2	2	0	72	48	06/30/99	08/22/89		1
	TY-102	*	SOUND	IS/IP/CCS	64	٥	12	0.0	6.6	12	5	0	64	06/28/82			
	TY-103		ASMD LKR	IS/IP/CCS	162		20	0.0	11.5	20	16	162	0	07/09/82	08/22/89		
	TY-104		ASMD LKR	IS/IP/CCS	43	ا ه	4	0.0	0.0	4	0	43	0	06/27/90	11/03/87		Í
	TY-105		ASMD LKR	IS/IP/CCS	231	١٥	12	0.0	3.6	12	10	231	0	04/28/82	09/07/89		
	TY-106	NCPLX	ASMD LKR	IS/IP/CCS	21	0	3	0.0	0.0	3	0	21	0	06/30/99	08/22/89		
						<u> </u>						Ĺ					
_	6 SINGL	E-SHELL 1	TANKS	TOTALS:	639	<u> </u>	53	0.0	29.9	<u>53</u>	31	529	110	<u> </u>	<u> </u>		<u></u>
A-13								II TAR	K FARM	PITTATO							
ū		wom w	40100 120	10.00					0.0	9 STVI DS	2	۱	0	04/28/82	06/19/79		1
	U-101	NCPLX	ASMD LKR	IS/IP	25 205	3 0	3	0.0 3.9	79.7	23	13	22 43	252	04/30/01	06/06/89		(f)
	U-102	NCPLX NCPLX	SOUND	/PI IS/PI	295 418	1 1	23 33	0.0	98.9	25 34	28	13	404	05/31/00			1 "
	U-103 U-104	NCPLX	ASMD LKR	IS/IP	122		33 0	0.0	0.0	0	0	79	43	06/30/99	08/10/89		Į.
	U-105	NCPLX	SOUND	15/IP 15/P1	353	"	44	0.0	87.5	44	32	32	321	03/31/01	07/07/88		(b)
	U-106	NCPLX	SOUND	IS/PI	172	2	38	0.0	39.1	38	30	0	170	03/31/01	07/07/88		(0)
	U-107	DSSF	SOUND	/PI	408	33	92	0.0	0.0	125	115	15	360	12/31/98] "
	U-108	NCPLX	SOUND	/*I	468	24	108	0.0	0.0	132	124	29	415	12/31/98			ŀ
	U-109	NCPLX	SOUND	/PI	397	6	59	2.4	68.3	59	50	35	362	04/30/01	07/07/88		(d)
	U-110	NCPLX	ASMO LKR	IS/PI	186	ه ا	18	0.0	0.0	18	14	186	0	12/30/84	12/11/84		
	U-111	DSSF	SOUND	/P1	329	o	80	0.0	0.0	80	71	26	303	12/31/98			1
	U-112	NCPLX	ASMD LKR	IS/IP	49	4	4	0.0	0.0	8	4	45	0	02/10/84	08/03/89		Ŀ
	U-201	NCPLX	SOUND	IS/IP	5		1	0.0	0.0	2	1	4	0	08/15/79	06/06/69		
	U-202	NCPLX	SOUND	IS/IP	5	1	1	0.0	0.0	2	1	4	0	08/15/79	06/06/89		İ
	U-203	NCPLX	SOUND	IS/IP	3		o	0.0	0.0	1	1	2	0	08/15/79	06/13/89		
	U-204	NCPLX	SOUND	IS/IP	3	1	0	0.0	0.0	1	1	2	0	06/15/79	06/13/89		
	16 SING	BLE-SHELL	TANKS	TOTALS:	3238	71	502	6.3	373.5	673	487	537	2630	1			
						1											
	GRAND	TOTAL			33207	1351	3449	14.6	5667.1	4800	3888	11059	20797				

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENTS FOOTNOTES:

Total Waste is calculated as the sum of Sludge and Saltcake plus Supernate. The category "Interim Isolated (II)" was changed to Intrusion Prevention (IP) in June 19 Stabilization information from WHC-SD-RE-TI-178 SST STABILIZATION RECORD, latest revision, or SST Stabilization or Cognizant Engineer

Porosity values are 25% for saltcake and 15% for sludge, per HNF-2978, Rev. 1, "Updated Pumpable Liquid Volume Estimates and Jet Pump Durations for Interim Stabilization of Remaining Single-Shell Tanks," September 1999, with the exception of those tanks which have been interim stabilized and the porosities recalculated.

(a) SX-101 Following information from Cognizant Engineer:

Pumping began November 22, 2000. No pumping since December 2000.

Remaining volumes are based on HNF-2978, Rev 2. Saltoske volume is adjusted to correspond to current waste removal.

(b) U-105 This tank was declared interim Stabilized on March 29, 2001, due to major equipment failure.

(c) S-102 Following Information from Cognizant Engineer:

Pumping commenced March 18, 1999. Many pumping problems occurred over the following months, and the pump has been replaced several times. Pumping was interrupted again in June 2000. No pumping since June 2000,

(d) U-109 Following information from Cognizant Engineer

Pumping began March 11, 2000. Satistake volume is adjusted to correspond to current waste removal. Remaining volumes based on HNF-2978, Rev. 2.

Pumping was shut down on December 3, 2000, due to jet pump failure. Attempts to restart the pump have been unsuccessful; the pump was replaced and restarted March 30, 2001.

Tank Waste: 396.7 Kgal Supernate: 0.0 Kgal

Drainable Interstial Liquid: 58.7 Kgal Pumped this month: 2.4 Kgal Total Pumped: 68.3 Kgal

Drainable Liquid Remaining: 58.7 Kgal Pumpable Liquid Remaining: 49.7 Kgal

Słudge: 35.0 Kgał Saltcake: 361.7 Kgal

During April 2001, a total of 5,087 gal of fluid was removed and a total of 2,658 gal of water was added for pump priming/equipment flushes. A total of 54 gal of flush water was carred over from March for a net removal of 2,375 gal of waste.

In addition, 14,762 gal of water was used as dilution and 1,878 gal were used for transfer line flushes.

(e) S-109 Following information from Cognizant Engineer:

Pumping began September 23, 2000.

Remaining volumes are based on HNF-2978, Rev. 2.

The pumping rate dropped below .05 gpm and the pump was shut down on January 27, 2001. The tank is now being evaluated to determine if it can be interim stabilized.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASUREMENT FOOTNOTES:

(f) U-102 Following information from Cognizant Engineer

Pumping began in this tank on January 20, 2000. Saltcake volume is adjusted to correspond to current waste removal. Remaining volumes are based on HNF-2978, Rev. 2.

Total Waste: 295.3 Kgal Supermete: 0.0 Kgal

Drainable Interstitial Liquid: 23.2 Kgal

Pumped this Month: 3.9 Kgal Total Pumped: 79.7 Kgal

Drainable Liquid Remaining: 23.2 Kgal Pumpable Liquid Remaining: 13.3 Kgal

Sludge: 43.0 Kgal Saltcake: 252.3 Kgal

A-15

During April 2001, a total of 4,757 gal of fluid was removed and 846 gal of water added by pump priming/equipment flushes, for a net removal of 3,911 gal of water. In addition, 12,232 gal of water were used as dilution and 3,725 gal of water were used for transfer line flushes.

(a) SX-105 Following information from Cognizant Engineer:

Saltwell pumping began August 8, 2000. Pumping cessed in late April 2001 when the saltwell screen in-flow rate was measured at about 0.02 gpm. Interstitial fluid level is now being allowed to stabilize to determine if the tank can be declared interim Stabilized. An in-tank video will be taken. Remaining volumes are based on HNF-2978, Rev. 2.

Tank Waste: 484.4 Kgal Supernute: 0.0 Kgal

Drainable Interetful Liquid: 0.4 Kgal Pumped this month: 1.5 Kgal Total Pumped: 152.6 Kgal

Drainable Liquid Remaining: 0.4 Kgal Pumpable Liquid Remaining: -11.6 Kgal (*)

Sludge: 65.0 Kgal Saltcake: 419.4 Kgal

In April 2001, a total of 3,157 gal of fluid was removed with 1,303 gal of water added by pump priming/system flushes. A total of 354 gal of flish water was carried over from March for a net removal of 1,500 gal of tank waste. In addition, 6,049 gal of water were used as dilution and 2,485 gal of water were used for line flushes.

(*) Minus 11,597 gal estimate for PLR because there is more pumpable liquid in the tank than originally estimated. This is due to the fact that approximately 118,000 gal of supernate was in the tank at the start of pumping.

(h) A-101 Following information from Cognizant Engineer

Pumping began on May 6, 2000. No pumping since August 2000.

TABLE A-6. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

April 30, 2001

THESE VOLUMES ARE THE RESULT OF ENGINEERING CALCULATIONS AND MAY NOT AGREE WITH SURFACE LEVEL MEASU.

FOOTNOTES:

(i) U-106

(i) AX-101 Following informtion from Cognizant Engineer

> Pumping began July 29, 2000; shutdown in August 2000, and resumed March 22, 2001. Remaining volumes are based on the original estimated volumes in HNF-2978, Rev. 2.

Total Waste: 682.2 Kgal Supernate: 364.2 Kgal Drainable Interstitial: 73,7 Kgal

Pumped this month: 3.6 Kgal Total Pumped: 21.6 Kgal

Drainable Liquid Remaing: 438.4 Kgal Pumpable Liquid Remaining: 422.2 Kgal

Sludge: 3.0 Kgal Saltcake: 295.0 Kgal

in April 2001, a total of 3.645 gal of fluid was removed and 25 gal of water added for pump priming/equipment, for a net removal of 3,620 gal of waste.

in addition, 3,490 gal of water were used as dilution and 245 gal of water were used for transfer line flushes.

(k) SX-103 Following information from Cognizant Engineer:

Pumping began October 26, 2000.

Remaining volumes are based on HNF-2978, Rev. 2.

This tank was declared interim Stabilized on March 9, 2001.

Total Waste: 517.7 Kgal Supernate: 0.0 Kgaf

Drainable Interstitial Liquid: 30.7 Kgal

Pumped this month: 3.2 Kgal Total Pumped: 116,3 Kgal

Drainable Liquid Remaining: 30.7 Kgal

Pumpable Liquid Remaining: 15.7 Kal

Sludge: 115.0 Kgal Sattcake: 402.7 Kgal

in April 2001, a total of 4,393 gal of fluid was removed and a total of 1,148 gal of water added by pump priming/equipment flushes, for a net removal of 3,245 gal of waste. In addition, 5,319 gal of water were used as dilution and 827 gal of water were used for transfer line flushes.

APPENDIX B PERFORMANCE SUMMARY

TABLE B-1. SUMMARY OF WASTE TRANSACTIONS IN THE DOUBLE-SHELL TANK (DST) SYSTEM April 30, 2001

All volumes in Kilo-Gallons

- The DST system received waste additions from SST pumping, 151-AZ, A-350 and Misc. Water in April.
- There was a net change of +61,000 gallons in the DST system for April 2001.
- The total DST inventory as of April 30, 2001 was 20.688 million gallons.
- There were ~8 Kgals of Saltwell Liquid (SWL) (4 SWL + 4 H2O) pumped to the East Area DSTs (101-AN) in April.
- There were ~64 Kgals of SWL (11 Kgals SWL + 53 Kgals H2O) pumped to the West Area DSTs (102-SY) in April.
- The SWL numbers are preliminary and are subject to change once cognizant engineers do a validation, the volumes reported contain actual waste volume plus any water added for dilution and transfer line flushes.
- The solids volumes of the Double-Shell Tanks (DST) were updated this month. The Best Basis Inventory group re-baselined all of the waste tank inventories, and as part of that work the solids in the DST's were re-evaluated by BBI engineers.
- Other changes to the DST inventories that came about as a result of the BBI re-baselining effort, was the elimination of Interstitial Liquid as a unique waste phase for the DST solids, and the addition of a Retained Gas waste phase for the DST solids. Retained Gas constitutes the volume of space taken up by gas trapped in the void section of the solid waste phase.

FACIL	ITY GENERATIONS	OTHER GAINS ASS	OCIATED WITH	OTHER LOSSES ASS	OCIATED WITH
SWL (West)	+64 Kgal (2SY)	SLURRY	+1 Kgal	SLURRY	-5 Kgal
SWL (East)	+8 Kgal (1AN)	CONDENSATE	+4 Kgal	CONDENSATE	-5 Kgal
TANK FARMS	+2 Kgal (2AW, 6AW)	INSTRUMENTATION	+0 Kgal	INSTRUMENTATION	-0 Kgal
101	AL +74 Kgal	UNKNOWN	+1 Kgal	UNKNOWN	-9 Kgal

	was a summary of the state of t						
	ACTUAL DST WASTE RECEIPTS	PROJECTED D8T WASTE RECEIPTS (1)	MISC, DST CHANGES (+/-)	PROJECTED WVR (1)	NET D8T CHANGE	TOTAL DST VOLUME	
OCT00	222	155	-24	0	198	20653	
NOV00	261	262	-14	0	247	20900	
DEC00	139	300	-1	0	138	21038	
JAN01	113	397	-25	0	88	21126	
FEB01	100	303	-19	0	81	21207	
MAR01	100	-283	2	-684	-580	20627	
APR01	74	321	-13	0	61	20688	
MAY01		302		0			
JUN01	·	334		0			
JUL01		296	1	0	 		
AUG01		289		0	········		
SEP01		282		0			

(1): The "PROJECTED DST WASTE RECEIPTS" and "WVR" numbers were updated in November 2000, the projected volumes will be updated as new and/or more accurate information is obtained. The projected volumes reported are the most current available, as supplied by cognizant engineers.

242/A Evaporator Veste Volume	rante le la company
Campaign 94-1 (04/15/94 - 06/13/94)	-2417
Campaign 94-2 (09/22/94 - 11/18/94)	-2787
Campeign 95-1 (06/09/95 - 07/26/95)	-2161
Campaign 96-1 (05/07/96 - 05/25/96)	-1117
Campaign 97-1 (03/24/97 - 04/02/97)	-351
Campaign 97-2 (09/16/97 - 09/30/97)	-653
Campaign 99-1 (07/24/99 - 08/15/99)	-818
Campaign 00-1 (04/20/00 - 05/05/00)	-682
Campaign 01-1 (03/13/01 - 03/27/01)	-682
Total waste reduction (WVR) since restart on 4/15/	-11668

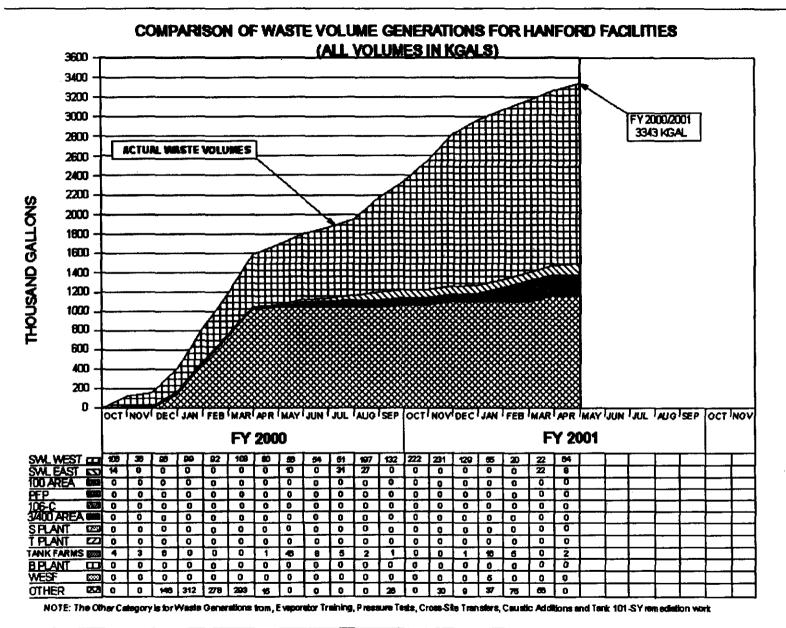


Figure B-1. Comparison of Projected Versus Actual Waste Volumes for Hanford Facilities

This page intentionally blank.

APPENDIX C

DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION

Table C-1. Double-Shell Tank Waste Inventory - April 30, 2001

TYPE HVENTORY (1) SUPERNATE 94 DISS 1064 885 DISS 1064 885 DISS 1064 885 DISS 1064 885 DISS 1064 885 DISS 1064 1127 885 DISS 1066 1127 885 DISS 1127 885 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 885 DISS 1128 1128 885 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128 1128 DISS 1128 1128	TANK		19ACE 27340 27340 2736 2736 27360	1074	TOTAL		MONTH	MONTHLY INVENTORY CHANGE
DEST 100	TANK NAME	WASTE	TOTAL HIVENTORY (1)	TOTAL BUPERNATE	TOTAL SOLIDS (3)	SALTCAKE (2)	SLUDGE (2)	
DESC DE	101-14-175	8 2	186	253	0	. 0	. 0	
DESET 1101 000 445 445 145 177 177 177 177 177 177 177 177 177 17	21-14-18	200	Z j	\$ 8	ŧ	È	0 0	
100 100	101-104		. <u> </u>	22	£	£		
CC 1904 755 267	21.41.00	8]	8 §	2 E	7 8	5 £	• •	
CC CC CC CC CC CC CC C	101 HF-11K	8	1040	75	347	247	• •	
CC 1391 CC 1109 CC 1109 CC 1109 CC 1109 CC 1109 CC 1109 CC 1109 CC 1009 CC 1109 CC 100	201-2-191	Q	Ē	Ē	0	•		- 1
Description 1106 1106 0 0 0 0 0 0 0 0 0	2 - S	8	3	ij	0 1	•	9 <	
Despring 1133 1044 88 88 105	261-45-104	8	108	1	0	•	0.0	
DESTRUCTIVE 120 100 100 100 100 100 100 100 100 100	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	2 E	Ē	Ē	. 2	2	•	
DESCRIPTION OF THE PROPERTY OF	2 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	88		3 8	• •	•		
DESP 1/2d 7/3d 398 3	21-4-12	2	37	77	0	0	٥,	
DESFACENY 1102 788 313 40 788 788 100 100 100 100 100 100 100 100 100 1	341-144-101 141-144-101		8 112	1	.	- 1	ţ o	- 1
HCMW 236 177 256 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	21.44.10	DESTACEN	### ### ### ##########################	3	;	ŧ.	3 1	
CORNEW 171 256 2	101-141-161	2	ĭ	8	B	1 57	8;	
DC (NA 24 100 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	#1.44.18 8	ORT	4 \$	5 3	2 3	į -	· 35	
DE COS 145 191 0 0 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	101-14	8	Į.	2				ı
HCAW 659 891 122 0 0 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	201-77-102	2	2	幸	194	•	Ēŝ	
00 00 00 00 00 00 00 00 00 00 00 00 00	101-24-100	HCMM	2	2	2	8	25	1
CC 743 371 372 372	201-27-182	NCAW		2	į.		3	
00 740 371 372 372	341-57-101	8 8	8		7 7	942		- 1
	241-57-103	8	743	371	372	372	: ه	

NOTE: All Volumes in Kito-Callons (Kgala)
(1) Total Inventory = Total Supermate + Total Solids
(2) Saltsalie Includes Retained Clas; Sludge Includes
(3) Total Belids = Saltsalie + Bludge 0301 YANK SPACE 9401 TANK SPACE CHANGE Tank Space Usage RESTRICTED SPACE OPERATIONAL SPACE - Wiot AH 103-AH 103 PHOSPHATE SUPERNATE (CP) Inventory Calculation by Waste Type: AGING SUPERNATE (AW)

HON-ALLOCATED SPACE

GRAND TOTALS

DILUTE SUPERNATE (DN/DC) =

SLURRY (DSS/DSSF) =

CONCENTRATED COMPLEXED (CC) =

CONCENTRATED PHOSPHATE (CP) =

AGING SUPERNATE (AW) =

DST SOLIDS (SL/SC) =

Table C-2. Double-Shell Tank Waste Inventory - April 30, 2001

			10608 KGALS
NATCH LIST TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE
husable DST Headspace - Due to Special Restrictions	AN-103	- +-	184 KGALS
leced on the Tanks, as Stated in the "Wyden Bill"	AN-104		89 KGALS
	AN-105		13 KGALS
	AW-101		14 KGALS
	SY-103		397 KGALS
		TOTAL*	697 KGALS
		AVAILABLE TANK SPACE=	10608 KGALS
TOTAL AVAILABLE SPACE AFTER WATCH LIST		NUS WATCH LIST SPACE= T TONS =	-697 KGALS 3911 KGALS
			······································
ESTRICTED TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE
ST Headspace Available to Store Only Specific Waste Types	AN-102		86 KGALS
	AN-107	- -	100 KGALS
	AP-102	CP	52 KGALS
	AZ-101		44 KGALS
	AZ-102		0 KGALS
	SY-101		170 KGALS
		TOTAL	452 KGAL8
AVAILABLE SPACE AFTER WATCH LIST			9911 KGALS
TOTAL AVAILABLE SPACE AFTER RESTRICTED		S RESTRICED SPACE= FICHB=	-452 KGALS 9459 Kgal s
PERATIONAL TANK SPACE		WASTE TYPE	AVAILABLE SPACE
ST Headspace Available For Facility Generated	AN-101		887 KGALS
este and 242-A Evaporator Operations	AP-108		1103 KGALS
	AW-102		1054 KGALS
	AW-105		714 KGALS
	AW-106	DSSF	842 KGALS
	SY-102	DC	156 KGALS
		TOTAL*	4766 KGALS
		and Miller and an Artificial State of the Artificial State of the Control of Artificial State of the A	
AVAILABLE SPACE AFTER RESTRICTED	SPACE DEDUC	TIONS=	9459 KGALS
	MINUS	OPERATIONAL SPACE=	-4756 KGALS
AVAILABLE SPACE AFTER OPERATIONAL	MINUS	OPERATIONAL SPACE=	
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	MINUS SPACE DEDUK TANK	OPERATIONAL SPACE= CTIONS= WASTE TYPE	-4756 KGALS 4703 KGALS AVAILABLE SPACE
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	MINUS SPACE DEDUX TANK AN-106	OPERATIONAL SPACE= CTIONS= WASTE TYPE CC	-4756 KGALS 4703 KGALS AVAILABLE SPACE 1102 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	MINUS SPACE DEDUX TANK AN-106 AP-101	OPERATIONAL SPACE= CTIONS= WASTE TYPE CC DSSF	-4756 KGALS 4763 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	MINUS SPACE DEDUX TANK AN-106 AP-101 AP-103	OPERATIONAL SPACE= CTIONS= WASTE TYPE CC DSSF CC	-4756 KGALS 4703 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-106 AP-101 AP-103 AP-104	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC	-4756 KGALS 4703 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-106 AP-101 AP-103 AP-104 AP-105	OPERATIONAL SPACE= TIONS= WASTE TYPE CC DSSF CC CC DSSF	A756 KGALS 4763 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-106 AP-101 AP-103 AP-104 AP-105 AP-106	OPERATIONAL SPACE= TIONS= WASTE TYPE CC DSSF CC CC DSSF DC	AVAILABLE SPACE 1102 KGALS 27 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-108 AP-101 AP-103 AP-104 AP-106 AP-106 AP-107	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC	AVAILABLE SPACE 1102 KGALS 27 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 518 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-108 AP-101 AP-103 AP-104 AP-105 AP-106 AP-107 AW-103	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC DSSF/NCRW	AVAILABLE SPACE 1102 KGALS 27 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 518 KGALS 159 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-108 AP-101 AP-103 AP-104 AP-105 AP-106 AP-107 AW-103 AW-104	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC DSSF/NCRW DN	A756 KGALS 4703 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 518 KGALS 159 KGALS 38 KGALS 38 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE	TANK AN-108 AP-101 AP-103 AP-104 AP-105 AP-106 AP-107 AW-103	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC DSSF/NCRW DN DC	-4756 KGALS 4703 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 518 KGALS 159 KGALS 38 KGALS
	TANK AN-108 AP-101 AP-103 AP-104 AP-105 AP-106 AP-107 AW-103 AW-104 AY-101	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC DSSF/NCRW DN DC DN	4756 KGALS 4763 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 516 KGALS 159 KGALS 38 KGALS 38 KGALS 824 KGALS
TOTAL AVAILABLE SPACE AFTER OPERATIONAL ON-ALLOCATED TANK SPACE on-Allocated DST Headspace	MINUS SPACE DEDUX TANK AN-108 AP-101 AP-103 AP-104 AP-105 AP-106 AP-107 AW-103 AW-104 AY-101 AY-102 OCATED TANK	OPERATIONAL SPACE= TICHS= WASTE TYPE CC DSSF CC CC DSSF DC DC DSSF/NCRW DN DC DN	4765 KGALS 4763 KGALS 4763 KGALS AVAILABLE SPACE 1102 KGALS 27 KGALS 859 KGALS 32 KGALS 7 KGALS 518 KGALS 159 KGALS 38 KGALS 824 KGALS 796 KGALS 341 KGALS

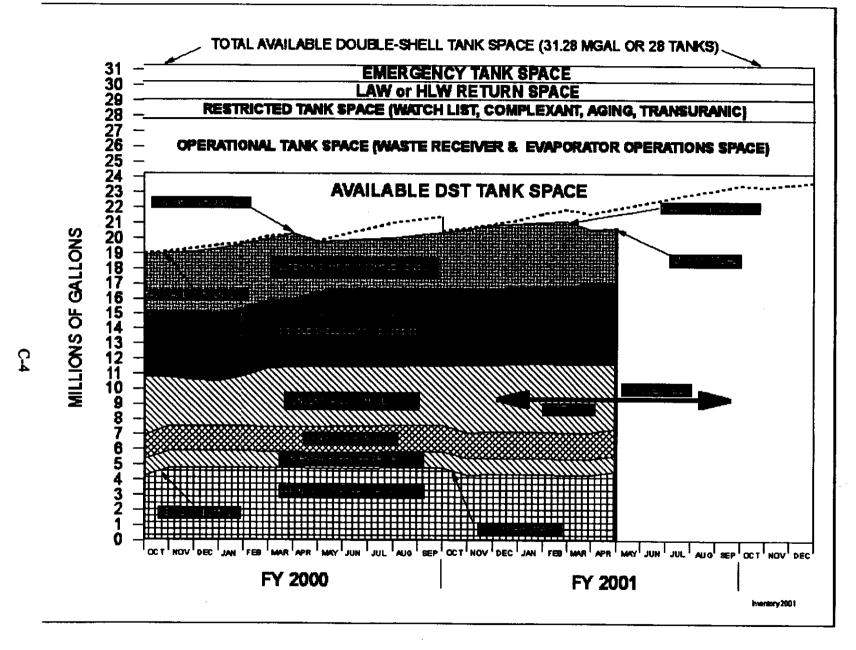


Figure C-1. Total Double-Shell Tank Inventory

APPENDIX D

WASTE TANK SURVEILLANCE MONITORING TABLES

TABLE D-1. TEMPERATURE MONITORING IN WATCH LIST TANKS (Sheet 1 of 2) April 30, 2001

These tanks have been identified as Watch List Tanks in accordance with Public Law 101-510, Section 3137, "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," (1990) because they "... may have a serious potential for release of high-level waste due to uncontrolled increases in temperature or presssure."

All Watch List tanks are reviewed for increasing temperature trends. Temperatures in these tanks are monitored by the Tank Monitor And Control System (TMACS), unless indicated otherwise.

Temperatures are taken in the waste unless in-waste thermocouples are out of service. Temperatures below are the highest temperatures recorded in these tanks during this month.

Temperatures in Degrees F.

		HYDROGEN (F	LAMMABLE (GAS)	
	Single-She	ell Tanks		Double-Sh	ell Tanks
Tank No.	<u>Tamp.</u>	Officially Added to Watch List	Tank No.	Temp.	Officially Added to Watch List
A-101	144	1/91	AN-103	101	1/91
AX-101	126	1/91	AN-104	103	1/91
AX-103	105	1/91	AN-105	100	1/91
S-102	99	1/91	AW-101	96	6/93
S-111	88	1/91	SY-103	94	1/91
S-112	82	1/91	5 DST:		
SX-101	127	1/91			
SX-102	139	1/91			
SX-103	153	1/91			
SX-104	136	1/91			
SX-105	156	1/91			
SX-106	99	1/91			
SX-109 (1)	131	1/91		19 Single-S	hell Tanks
T-110	63	1/91		5 Double-S	
U-103	86	1/91]	24 Tanks o	n Watch List
U-105	87	1/91			
U-107	77	12/93			
U-108	86	1/92			
U-109	84	1/91]		
19 SST:					

All tanks were removed from the Ferrocyanide Watch List and 18 tanks from the Organics Watch List. Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999. The remaining two tanks (C-102 and C-103) were removed from the Organics Watch List in August 2000. DST SY-101 was removed from the Hydrogen Watch list on January 11, 2001.

TABLE D-1. TEMPERATURE MONITORING IN WATCH LIST TANKS (sheet 2 of 2)

Notes:

Unreviewed Safety Ouestion (USO):

When a USQ is declared, special controls are required, and work in the tanks is limited. There are currently no USQs on any tanks.

Hydrogen/Flammable Gas:

These tanks are suspected of having a potential for hydrogen/flammable gas generation, entrapment, and episodic release. The USQ associated with these tanks was closed in September 1998. Twenty-four tanks (19 SST and 5 DST) remain on the Hydrogen Watch List.

High Heat:

These tanks contain heat generating strontium-rich sludge and require drainable liquid to be maintained in the tank to promote cooling. There are currently nine tanks on the High Heat Load List but no tanks on the High Heat Load Watch List.

Active ventilation:

There are 15 single-shell tanks on active ventilation (seven are on the Watch List as indicated by an asterisk):

C-105	SX-107
C-106 (2)	SX-108
SX-101 *	SX-109 * (1)
SX-102 *	SX-110
SX-103 *	SX-111
SX-104 *	SX-112
SX-105 *	SX-114
SX-106 *	

Footnotes:

- (1) Tank SX-109 is on the Hydrogen Watch List as it has the potential for flammable gas accumulation only because other SX tanks vent through it.
- (2) Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999.

TABLE D-2. TEMPERATURE MONITORING IN NON-WATCH LIST TANKS April 30, 2001

SINGLE-SHELL TANKS WITH HIGH HEAT LOADS (>26,000 Btu/hr)

Nine tanks have high heat loads for which temperature surveillance requirements are established by HNF-SD-WM-TSR-006, Rev 2, Tank Waste Remediation System Technical Safety Requirements, December 1999. In an analysis, WHC-SD-WM-SARR-010, Rev 1, Heat Removal Characteristics of Waste Storage Tanks, (Kummerer, 1995) as amended, it was estimated that nine tanks have heat sources >26,000 Btu/hr, which is the new parameter for determining high heat load tanks. See also document HNF-SD-WM-FSAR-067, Rev 2, as amended.

Temperatures in these tanks did not exceed the Technical Safety Requirements (TSR) for this month, and are monitored by the Tank Monitor and Control System (TMACS), unless indicated otherwise. All high heat load tanks are on active ventilation.

Tank No.	Temperatu	re (F.)
C-106 (1)	64	(Riser #8)
SX-103	153	
SX-107	162	
SX-108	179	
SX-109 (2)	131	
SX-110	160	
SX-111	179	
SX-112	144	
SX-114	171	
9 Tanks		

Notes:

- (1) C-106 was removed from the High Heat Load Watch List on December 16, 1999. The final thermal analysis report, RPP-6463, Rev. 0, "Thermal Analysis for Tanks 241-AY-102 and C-106," was issued August 9, 2000. The report concluded that the best estimate heat load for C-106 is between 7,000 and 11,000 Btu/hr. Although it no longer meets the criteria for a high heat load tank, an AB amendment is required to revise the temperature control limits and monitoring frequency. The AB Amendment request is pending review by ORP and is expected to be approved in May 2001.
- (2) SX-109 is on the Hydrogen Watch List since it has the potential for flammable gas accumulation because the other SX tanks vent through it.

SINGLE-SHELL TANKS WITH LOW HEAT LOADS (<26,000 Btu/hr)

There are 114 low heat load non-Watch Lst tanks. Temperatures in tanks connected to TMACS are monitored by TMACS; temperatures in those tanks not yet connected to TMACS are manually taken semiannually in January and July. Temperatures obtained semiannually have been within historical ranges for the applicable tank.

No temperatures have been obtained for several years in the tanks listed below. Most of these tanks have no thermocouple trees.

	Tank Numbers	
BX-104	SX-115	TX-110
BY-102	T-102	TX-114
BY-109	T-105	TX-116
C-204	TX-101	TX-117
		U-104

TABLE D-3. ADDITIONS/DELETIONS TO WATCH LISTS BY YEAR April 30, 2001

Added/Deleted dates may differ from dates that tanks were officially added to the Watch Lists. (See Table D-1).

	Ferrocyanide 23	Hydrogen	Organics #	High Heat	SSTD	SST DST Total	7
Added 2/91 (revision to Original List) Kata (Swemes: 2): 1991 Added 6/92	76 15107	13 AW-101	•				FOF
Total December 31, 1882	10 to Act.	**	11111		8-1	8	Z
	(BY-101) (T-101)	1 46103			7		
Test Consenses 31, 1803	30	***	•		2	0	8
Added 5/94			20 - 1-101 A-7-102 C-102 S-7-103 T-7-104 U-105 U-203 U-204		-		
Deleted 11/84	-2 (BX-102) (BX-106)				7		
Total Desired 6/96 Desired 6/96	18 (C-108) (C-109)	*	94	-	37	•	Ž.
Deleted 9/96	(C1112) -14 (BY-103) (BY-104) (BY-104)				-12		
•	697-109 (697-109) (697-119) (697-119) (77-119) (77-101) (77-101)						
Deleted 12/98			-18 (A-101) (AX-102) (B-103) (S-102) (S-111) (S-103) (SX-103)		01-		
			7-111 77-106) 77-106) 77-106) 77-106) 7-106)				
			(111-3) (111-3) (111-3) (111-3)				
Daletad 12/99			3 [· (C·108)	F	H	
Covers devel		1	1 (5,103)		+	╀	Τ
Deleted 01/01		1 (57-101)					Π
Tetal - April 20, 2001	o	**	0	٥	101	*	Ÿ.

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS

149 TANKS (Sheet 1 of 6) April 30, 2001

The following table indicates whether Single-Shell tank monitoring was in compliance with the requirements as specified in the applicable documents as of the last day of the applicable month:

NOTE:

All Watch List and High Heat tank temperature monitoring is in compliance. (4)
All Dome Elevation Survey monitoring is in compliance

Psychrometrics monitoring is on "as needed" basis (2).

Drywell monitoring no longer required (5). In-tank photos/videos are taken "as needed"

LEGEND:	· · · · · · · · · · · · · · · · · · ·
(Shaded)	= in compliance with all applicable documentation
N/C	= noncompliance with applicable documentation
0/\$	= Out of Service
Neutron	► LOW readings taken by Neutron probe
POP	= Plant Operating Procedure, TO-040-650
MT/FIC/	= Surface level measurement devices
ENRAF	
OSD	= Operating Spec. Doc., OST-T-151-00013, 00030, 00031
N/A	= Not applicable (not monitored, or no monitoring schedule)
None	= Applicable equipment not installed
FSAR/TSR	= Final Safety Analysis Report/Technical Safety
	Requirements

	Tank	Category	Temperature	Primery Leak	Suri	face Level Rea	dings (1)	LOW Readings
Tank	Watch	High	Readings	Detection		(OSD)		(OSD)(5.7)
Number	List	Heat	(4)	Source (5)	MT	FIC	ENRAF	Neutron
A-101	X			LOW	Menu	None		
A-102				None	None		None	None
A-103				LOW	None	None		
A-104				None	Access 1	None		None
A-105				None		None	Nare	None
A-106				None	Horse	None		None
AX-101				LOW	None	None		(9)
AX-102				None	None	None		None
AX-103	X			None	Fore	None		None
AX-104				None	Note	None		None
B-101				None	None	None		None
B-102				ENRAF	Patrice	None		None
B-103				None	Bore	None		
B-104				LOW	None	None		
8-105				LOW	None	None		
B-106				ENRAF	None	None		flone
B-107				None	Nove	None		None
B-108				None	Name:	Mone		None
B-109				None	None	None		None
B-110				LOW	None	None		
B-111				LOW	Nors	None		
B-112				ENRAF	None	None		None
B-201				ENRAF	None	None		None
B-202				ENRAF	None	None		None
B-203				ENRAF	Nere	None		None
B-204				ENRAF	None	None		None
BX-101				ENRAF	Pigne	None	1131	None
BX-102				None	None	None		None
BX-103				ENRAF	Here	None	(12)	None
BX-104			None	ENRAF	None	filterie	(12)	None
BX-105				None	None	None		None
BX-106				ENRAF	Mone	None		None
BX-107				ENRAF	None	None	(12)	None

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS
149 TANKS (Sheet 2 of 6)

	Tank C	Category	Temperature	Primary Leak	Surfa	ce Level Re	edings (1)	LOW Readin	
Tenk	Wetch	High	Readings	Detection		(OSD)		(OSD)(
Number	List	Heat	(4)	Source (5)	MI	FIC	ENR		
BX-108				None	None				
BX-109				None					~~~~
BX-110				None					
8X-111				LOW	None				
BX-112	_			ENRAF	Name		666 (411E)		
BY-101			107	LOW					
BY-1 <i>02</i> BY-103				LOW	None				
8Y-103 8Y-104	100000000000000000000000000000000000000			LOW	Notes		Manager of the second Processor		
BY-105				LOW					
3Y-108	***************************************			LOW					*****
Y-107				LOW	8 10 20 20 20 20 20 20 20 20 20 20 20 20 20				
BY-109				None					***
BY-109			, Comme	LOW	None		**************************************		
9Y-110				FOM	None				******
SY-111				LOW	Diene				
Y-112	***************************************			FOM					
C-101				None			1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	9600	4000
C-102 (10)				None	None			Ness	
C-103 (10)				ENRAF	Notes				
C-104				None	None	*****		0.55	
>105				None	None	***************************************	***************************************		
>106 (3)				ENRAF	None				
>107				ENRAF	None			7000	
C-108				None					
C-109		100		None					
>110				MT					
>111				None					*****
>112				None					
>201				None					
>202				None		***************************************	The second		
>203				None		**************************************	and the second terms of		
204			ALLES AND AND AND AND AND AND AND AND AND AND	None					
-101				ENRAF	teris.	all the same and			<u> </u>
-102				LOW	None				
-103				ENRAF	None				
-104				LOW	1,650				
-106				LOW					
-106				LOW	Neteral	A Comment			
-107				ENRAF) in the			10.0	
-108		Annual Control		FOM	Nore				
-109 -110				LOW	Liste Liste				
-111				ENRAF	3,654				
-112				LOW					
X-101				LOW	A DOME				
X-102				LOW	Reve	e de la companya de l			
X-103	Market Control of the	The Maria Control		LOW	Nesee	CONTESTION COMPANY			
X-104	13.100			LOW		i daesasaanaa kanadaanaa Caradaanaanaa kanadaanaa			
X-106	100 March 100 Ma	400		LOW	Hara			9/8 11	418
X-106	T NO. 3			LOW	157	**************************************			
X-107	************			None	None			None	
X-107				None	Nore			None	_

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS 149 TANKS (Sheet 3 of 6)

		Category	Temperature	Primary Leak	Surf	sce Level Readi	ings (1)	LOW Readings
Tenk Number	Watch List	High Heat	Readings (4)	Detection	MT	(OSD)		(OSD)(5,7)
5X-109	LIST.	X Liest	(-7)	Source (5)	None	FIC	ENRAF	Neutron
5X-110				None	None	None	8	None
SX-111		2		None	Hone	1010		None
SX-112				None	None	None		Hors
SX-113				None	None	Bone		None
SX-114				None	Name	Nore		tione
SX-115			PARTIE	None	None	None		
T-101				None	None	None		None
T-102				ENRAF	None	Bere		1500
T-103				None	2.534	None		Hora
T-104				LOW	Nicote	Siene		
T-105			lises.	None				None
T-106				None	N. Carlo	Berg		6.00
T-107				ENRAF				
T-108				ENRAF				Raid.
T-109				None	Ness	l de		Morie
T-110	X			LOW	None	None		
T-111				LOW	None			
T-112				ENRAF	e de Constantina	No. No. no.		Seco
T-201				MT		None	None	Merce
T-202				MT		Nore	None	Hone
T-203 T-204				None		None	None	None
TX-101				MT		Note	None	None
TX-101	000000000000000000000000000000000000000		Peares	LOW	Nove	None		None
TX-102				None	E. Control	Acres		
TX-104	100000000000000000000000000000000000000			None	None	Hone		Mene
TX-105				None	Non	None		None None (B)
TX-106				LOW	None	None		**************************************
TX-107				None	None	None		bione
TX-108				None	None	Stone		None
TX-109				LOW	None	None		
TX-110			fione	LOW	None	Horse		
TX-111				LOW	None	None		
TX-112				LOW	None	None		
TX-113				LOW	None	None		
TX-114			None	LOW	None	None		
TX-115				LOW	More	2000		
TX-116			None	None				None
TX-117			None.	LOW	None	None		
TX-118				LOW	None	No.		
TY-101				None	Home	Here		No.
TY-102				ENRAF	None	None		Nerve
TY-103				LOW	No.	None		
TY-104				ENRAF		Here		None
TY-105				None				Nena
TY-106				None	None			None
J-101				MT		1,67	1000	Pierre
J-102				LOW				
J-103	ж			LOW		S. Esta		
J-104			NEW YEAR	None		Nerv	None	None
J-105	X			LOW	None	None		
J-106		1		FOM	None	None	1	

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS 149 TANKS (Sheet 4 of 6)

	Tenk Co	ntegory	Temperature	Primary Leak	Sı	Irface Level Read	ings (1)	LOW Readings
Tank	Watch	High	Readings	Detection		(OSD)		(OSD)(5,7)
Number	List	Hest	(4)	Source (5)	МТ	FIC	ENRAF	Neutron
U-107				ENRAF	New			
U-108				LOW		Cont		
U-109				LOW	Home	and the second second		
U-110				None	None	Mane		
U-111				LOW	None	Plane		
U-112				None		Home		
U-201				MT			None	3,550
U-202				MT		. Katu		
U-203				None	34.55	None		
U-204				ENRAF	i de la companya de la companya de la companya de la companya de la companya de la companya de la companya de	None		8. 0. M
Catch Tanks a	end Special Se	urveillence Fa	cilities					
A-302-A	1/4	NIA	WWW.777.	(6)	No.	None		
A-302-B	60 A	17.5						
ER-311	1.0				1.000			
AX-152		10.000.77						
AZ-161	W. U.	N/A	C/A					and the same
AZ-154	3000	12.000 TV NO.	21.0			8.00		8 8 8 8 8 10 7 1 8 8
BX-TK/SMP	NIA	3773	· · · · · · · · · · · · · · · · · · ·				11777	
A-244 TK/SMP	77.50	SW CICS			No.	1694		
AR-204	37.5	**************************************	68 37 T7 W. S. C.					
A-417		216	***************************************		o processor viccourse		an indicated a solventia con-	or received Theresian
A-360	177	1777 Y	777		None	Neve		
CR-003								
Vent Sta.	3/3	NA		(8)				
244-S TK/SMP								
8-302								
S-304			0.000	(6)				
TX-244 TK/8MP							100000000000000000000000000000000000000	
TX-302-B								
TX-302-C	77,5		110), com		
U-301-B	N/A		N/A	(4)		V.Grey		
JX-302-A		17.4		40	Verse	1,000		
5-141		11.0		le i			No.	No.
5-142		11/4				1676	3,000	Hore
Totals:	19	9	N/C: 0		N/C: 0	N/C: O	N/C: 0	N/C: 0
149 tanks	Hydrogen Wetch List Tenks	High Heat Tanks (non- Watch List)						

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS -149 TANKS (Sheet 5 of 6)

Footnotes:

1. All SSTs have either manual tape, FIC, or ENRAF surface level measuring devices. Some also have zip cords.

ENRAF gauges are being installed to replace FICs (or sometimes manual tapes). The ENRAF gauges are being connected to TMACS, but many are currently being read manually from the field. See Table D-6 for list of ENRAF installations.

2. High heat tanks have active exhausters; psychrometrics can be taken in the high heat tanks. Psychrometric readings are not required by OSD, but can be taken on an "as needed" basis.

Psychrometric readings are taken annually in SX-farm.

- 3. Tank C-106 was removed from the High Heat Load Watch List on December 16, 1999.
- 4. Temperature readings may be regulated by OSD, POP, or FSAR (FSAR only regulates high heat load tanks). Temperatures cannot be obtained in 13 low heat load tanks (see Table D-2). The OSD does not require readings or repair of out-of-service thermocouples for the low heat load (<26,000 Btu/h) tanks. However, the POP requires that attempts are to be made semiannually in January and July to obtain readings for these tanks.

Temperatures in some tanks cannot be taken in the waste because the waste level is lower than the lowest thermocouple in these trees.

Temperatures for many tanks are monitored continuously by TMACS; see Table D-7, TMACS Monitoring Status.

5. Document OSD-T-151-00031, "Operating Specifications for Tank Farm Leak Detection," Rev. D-2, December 7, 2000, requires that single-shell tanks with the surface level measurement device contacting liquid, partial liquid, or floating crust surface, will be monitored for leak detection on a daily basis. Tanks with a solid surface will be monitored for leak detection on a weekly basis by taking neutron scan data from a Liquid Observation Well (LOW), if an LOW is present. Tanks with a solid surface but without LOWs will not be monitored for leak detection until an LOW is installed. The OSD specifies what leak detection methods are to be used for each tank, and the requirements if the readings are not taken on the required frequency or if equipment is out of service.

This OSD revision does not require drywell surveys to be taken; drywell scans will only be taken by special request, since any scans would have to be subcontracted. The contractor no longer has drywell scanning equipment.

6. Leak detection for the catch tanks is performed by monitoring for the buildup of liquid in the secondary containment (for most tanks with secondary containment) or for decrease in the liquid level for those tanks without secondary containment or Catch tank 241-S-302 is monitored for intrusions only, and is not subject to leak detection monitoring requirements until liquid is present above the intrusion level.

Weight Factor is the surface level measuring device currently used in A-417, A-350, 244-A Tank/Sump, and 244-S Tank/Sump. Double-Shell Receiver Tank (DCRT) CR-003 is inactive and measured in gallons. 204-AR is also measured in gallons.

7. Document SD-WM-TI-605, REV. 0, dated January 1994, describes the rationale for Liquid Observation Well (LOW) installation priority. This priority is based on tank leak status, tank surface condition, and tank stabilization status. Also included is a listing of tanks with the waste level being below two feet, which have no priority assigned because no effort will be made to install LOWs in the near future. LOW probes are unable to accurately monitor interstitial liquid levels less than two feet high.

TABLE D-4. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS - 149 TANKS (Sheet 6 of 6)

Tanks which will not receive LOWs:

A-102	BX-101	C-201	T-106
A-104	BX-103	C-202	T-108
A-105	BX-105	C-203	T-109
AX-102	BX-106	C-204	TX-107
AX-104	BX-108	SX-110	TY-102
B-102	C-108	SX-113	TY-104
B-103	C-109	SX-115	TY-106
B-112	C-111	T-102	U-101
		T-103	U-112

Total - 34 Tanks

- 8. Tank TX-105 the LOW was in riser 8; the riser has been removed and the LOW has not been monitored since January 1987. Liquid levels are being taken in riser 9 by ENRAF and recorded in TMACS.
- 9. Tank AX-101 LOW readings are taken by gamma sensors.
- 10. Tanks C-102 and C-103 were removed from the Organics Salts Watch List on August 23, 2000
- 11. Tank SX-105 LOW scan not taken for week ending August 28, 2000. LOW is primary leak detection device; ENRAF is backup and monitored daily in TMACS. LOW has failed structurally, and will be replaced. Work Package 2H0005040. Fabrication shop has finished making the LOW. Waiting for schedule of installation. (Tank is currently being saltwell pumped).
- 12. Catch Tank AX-152 has been declared an "assumed leaker," per Occurrence Report RP-CHG-TANKFARM-2001-0014, based on an engineering evaluation. The remaining liquid (water which was being used to perform a leak test of the catch tank) has been pumped to a double-shell tank.
- 13. BX farm is in power outage lasting about 2 weeks and putting the liquid level gauges in O/S condition. Power off as of March 30, 2001; no readings in BX-101, -103, -104, -107, and -112, which are daily requirements with no backup device specified. OSD-00031 states the gauges must be repaired in 14 days; if no readings are obtained by April 13, 2001, an OSD violation will occur. Discrepancy Report 01-890 was issued on April 2, 2001.

Cable from main distribution panel to the ENRAF system is faulty. The OSD was revised with new specifications when an outage/repair cannot be completed in 14 days. An extension letter, memo 7L100-WEB-01-006, was issued April 26, 2001, with a projected completion date of June 22, 2001.

TABLE D-5. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS 28 TANKS (Sheet 1 of 2) April 30, 2001

The following table indicates whether Double-Shell tank monitoring was in compliance with the requirements as specified in the applicable documents as of the last day of the applicable month.

NOTE:

Dome Elevation Surveys are not required for DSTs.

Psychrometrics and in-tank photos/videos are taken "as needed" (2)

LEGEND:	
(Shaded)	= In compliance with all applicable documentation
N/C	 Noncompliance with applicable documentation
FIC/ENRAF	= Surface level measurement devices
M.T.	
OSD	= OSD-T-151-0007, OSD-T-151-00031
None	= no M.T., FIC or ENRAF installed
lo/s	■ Out of Service
W.F.	= Weight Factor
N/A	 Not Applicable (not monitored or no monitoring schedule)
Rad.	= Radiation

		!				R	adiation Reading	8
Tank		Temperatura Readings (3)	Surf	Surface Level Readings (1) (OSD)			sction Pits (4) (OSD)	Annulus
Number	Watch List	(OSD)	M.T.	FIC	ENRAF	W.F.	Rad. (6)	(OSD)
AN-101				(loss)			N/A	
AN-102				None			9/4	
AN-103				Nune			N/A	
AN-104			e e e	(291)			N/A	
AN-105			215	flore			N/A	
AN-106				None			N/A	
AN-107				None		0.6	SEA.	
AP-101			0/6	l Carro		0/3 (7)	WA	
AP-102				None		8807(317)B	37,4	
AP-103				More		0/6 (7)	377.	
AP-104			076	Ners		0,617	N/A	
AP-105				None			N/A	0/8
AP-106				0.07		672.847	N/A	
AP-107				None		(0)(1)(2)	1	
AP-108				None		0/8 (7)	N/A	
AW-101	- X		OR	faces			N/A	
AW-102					65		N/A	
AW-103				None			N/A	
AW-104							N/A	
AW-105				None			N/A	
AW-106				Riona			N/A	
AY-101				None			17/6	C/S
AY-102			0/6	None			B/A	
AZ-101				Papera			WA	0/8
AZ-102					None		N/A	0/8
SY-101			None	None		O/E (9)	N/A	
SY-102			0/6 (8)	None			N/A	
SY-103	*		O/8 #80	None		0/8 (9)	N/A	
Totale:	Б	N/C: 0	N/C: 0	N/C: 0	N/C: O	N/C: 0	N/C: O	N/C: O
28 tanks	Watch List Tanks	!						l .

TABLE D-5. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS - 28 TANKS (Sheet 2 of 2)

Footnotes:

- Some double-shell tanks have both FIC and manual tape which is used when the FIC is out of service.
 Noncompliance (N/C) will be shown when no readings are obtained. ENRAF gauges are being installed to replace FICs. The ENRAF gauges are being connected to TMACS, but some are currently being read manually.
- 2. Psychrometric readings are taken on an "as needed" basis. No psychrometric readings are currently being taken in the double-shell tanks.
- 3. OSD specifies double-shell tank temperature limits, gradients, etc.
- Applicable OSD and HNF-IP-0842, latest revisions, are used as guidelines for monitoring Leak Detection Pits.
 See also (6) and (7) below.
- 5. AW-102 has ENRAF, FIC and M.T. At some point the FIC will be removed.
- 6. USQ TF-97-0038, dated April 28, 1997, specifies discontinuing the use of leak detection pit radiation monitoring equipment in all double-shell tank farms where the leak detection pits are used as tertiary leak detection. This applies to all double-shell tank farms.
- Leak Detection Pit weekly readings are being obtained by Instrument Technicians in these tanks:
 AP-103C (for tanks AP-101 104)
 AP-105C (for tanks AP-105 108)
- SY-102 Manual Tape has sporadic readings. ENRAF is primary device.
 SY-103 Manual Tape has sporadic readings. ENRAF is primary device.
- SY-101 LDP readings are above normal range. EDL #S0007 to repair it.
 SY-103 LDP readings are above normal range. EDL #241-SY-95-5 to repair it.

TABLE D-6. ENRAF SURFACE LEVEL GAUGE INSTALLATION AND **DATA INPUT METHODS**

April 30, 2001

LEGEND

SACS

= Surveillance Analysis Computer System

TMACS = Tank Monitor and Control System

Auto

= Automatically entered into TMACS and electronically transmitted to SACS

Manual

- Manually entered directly into SACS by surveillance personnel, from Field Data sheets

	Manual	= Manua	lly entered (directly into S	ACS by sur	veillance p	ersonnel, fron	n Field Data	she	ets		
EAST	AREA					WEST	AREA					
Tank	Installed	Input	Tank	Installed	Input	Tank	Installed	Input		Tank	installed	Input
No.	Date	Method	No.	Date	Method	No.	Date	Method		No.	Date	Method
A-101	09/95	Auto	B-201	07/00	Auto	S-101	02/95	Auto	888	TX-101	11/95	Auto
A-102			B-202	07/00	Auto	S-102	06/95	Auto	- KEE	TX-102	05/96	Auto
A-103	07/96	Auto	B-203	06/00	Auto	S-103	06/94	Auto	2222	TX-103	12/96	Auto
A-104	06/96	Manual	B-204	06/00	Auto	S-104	05/99	Auto	2000	TX-104	03/96	Auto
A-105			BX-101	04/96	Auto	S-105	07/95	Auto		TX-105	04/96	Auto
A-106	01/96	Auto	BX-102	06/96	Auto	S-106	06/94	Auto		TX-106	04/96	Auto
AN-101	06/96	Auto	8X-103	04/96	Auto	S-107	06/94	Auto	888	TX-107	04/96	Auto
AN-102	06/00	Auto	BX-104	05/96	Auto	S-108	07/95	Auto		TX-108	04/96	Auto
AN-103	08/95	Auto	BX-105	03/96	Auto	S-109	08/95	Auto	***	TX-109	11/95	Auto
AN-104	08/95	Auto	BX-106	07/94	Auto	S-110	08/95	Auto	300	TX-110	05/96	Auto
AN-105	08/95	Auto	BX-107	06/96	Auto	S-111	08/94	Aurto		TX-111	06/96	Auto
AN-106	06/00	Auto	BX-108	06/96	Auto	S-112	06/95	Auto	2.50	TX-112	05/96	Auto
AN-107	04/00	Auto	BX-109	08/95	Auto	SX-101	04/95	Auto		TX-113	05/96	Auto
AP-101	06/99	Auto	BX-110	06/96	Auto	SX-102	04/95	Auto		TX-114	05/96	Auto
AP-102	08/99	Auto	BX-111	05/96	Auto	SX-103	04/95	Auto	256	TX-115	05/96	Auto
AP-103	08/99	Auto	BX-112	03/96	Auto	SX-104	05/95	Auto		TX-116	05/96	Auto
AP-104	07/99	Auto	BY-101			SX-105	05/95	Auto		TX-117	06/96	Auto
AP-105	08/99	Auto	BY-102	09/99	Auto	SX-106	08/94	Auto		TX-118	03/96	Auto
AP-106	08/99	Auto	BY-103	12/96	Auto	SX-107	09/99	Auto	2007 2007	TY-101	07/95	Auto
AP-107	08/99	Auto	BY-104			SX-108	09/99	Auto	20	TY-102	09/95	Auto
AP-108	06/99	Auto	BY-105			SX-109	09/98	Auto	286	TY-103	09/95	Auto
AW-101	08/95	Auto	BY-106			\$X-110	09/99	Auto	2.0	TY-104	06/95	Auto
AW-102	05/96	Auto	BY-107			SX-111	09/99	Auto		TY-105	12/95	Auto
AW-103	06/96	Auto	BY-108			SX-112	09/99	Auto		TY-106	12/95	Auto
AW-104	01/96	Auto	BY-109			SX-113	09/99	Auto		U-101		
AW-105	06/96	Auto	BY-110	02/97	Manual	SX-114	09/99	Auto		U-102	01/96	Menual
AW-106	06/96	Auto	BY-111	02/99	Manual	SX-115	09/99	Manual		U-103	07/94	Auto
AX-101	09/95	Auto	BY-112			8Y-101	07/94	Auto	626	U-104		
AX-102	09/98	Auto	C-101			SY-102	06/94	Auto	88	U-105	07/94	Auto
AX-103	09/95	Auto	C-102			SY-103	07/94	Auto	<i>X</i> :2	U-106	08/94	Auto
AX-104	10/96	Auto	C-103	08/94	Auto	T-101	06/95	Manual	300	U-107	08/94	Auto
AY-101	03/96	Auto	C-104	04/99	Manual	T-102	06/94	Auto		U-10B	05/95	Auto
AY-102	01/98	Auto	C-105	05/96	Manual	T-103	07/95	Manual		U-109	07/94	Auto
AZ-101	08/96	Menuel	C-106	02/96	Auto	T-104	12/95	Menual	#	U-110	01/96	Manual
AZ-102	11/00	Manual	C-107	04/95	Auto	T-105	07/95	Manual		U-111	01/96	Manual
B-101	07/00	Auto	C-108			T-106	07/95	Manual	ä.	U-112		
B-102	02/95	Auto	C-109			T-107	06/94	Auto		U-201		
B-103	07/00	Auto	C-110			T-108	10/95	Manuel		U-202		
B-104	06/00	Auto	C-111			T-109	09/94	Manual	***	U-203	09/98	Menual
B-105	08/00	Auto	C-112	03/96	Manual	T-110	06/95	Auto	XXX	U-204	06/98	Manual
B-106	07/00	Auto	C-201			T-111	07/95	Manual				
B-107	06/00	Auto	C-202			T-112	09/95	Manual				
B-108	07/00	Auto	C-203			T-201						
B-109	08/00	Auto	C-204			T-202						
B-110	07/00	Aurto				T-203			***			
B-111	07/00	Auto	**			T-204						
B-112	03/95	Auto										
	t Area: 71					Total W	est Area: 77					
					<u> </u>							

148 ENRAFs installed: 125 automatically entered into TMACS, 23 manually entered into SACS

TABLE D-7. TANK MONITOR AND CONTROL SYSTEM (TMACS) April 30, 2001

Note: Indicated below are the number of tanks having at least one operating sensor monitored by TMACS.

Some tanks have more than one sensor: multiple sensors of the same type in a tank are not shown in the table (for example: 10 tanks in BY-Farm have at least one operating TC sensor and 3 tanks in BY-Farm have at least one operating RTD sensor).

Acceptance Testing Completed: Sensors Automatically Monitored by TMACS

7,4000	Temper			1	1]
		Resistance			1	
EAST AREA	Thermocouple	Thermal	ENRAF	Ì	1	Gas
	Tree	Device	Level	Pressure	Hydrogen	Sample
Tank Farm	(TC) {	(RTD)	Gauge	(b)	(c)	Flow
A-Farm (6 Tenks)	1		3		1	1
AN-Farm (7 Tanke)	7		7	7	3	3
AP-Ferm (8 Tenks)			8			
AW-Farm (6 Tanks)	6		6		1	1
AX-Farm (4 Tanks)	3		4		1	
AY-Farm (2 Tanks)			2			
AZ-Ferm (2 Tenke)						
B-Farm (16 Tanks)	1		16			
BX-Farm (12 Tanks) (g)	11		12			
BY-Farm (12 Tanks) (g)	10	3	2			
C-Farm (16 Tanks)	15 (f)	1	3	1		
TOTAL EAST AREA	1				1	
(91 Tanks)	54	4	63	88	6	5
WEST AREA						
S-Farm (12 Tanks)	12		12	1	3	1 (e)
SX-Ferm (15 Tenks)	14		14	1	7	5 (e)
SY-Ferm (3 Tanks) (a)	3		3	1	2	2
T-Farm (16 Tanks)	14	1	3 (d)		1	(e)
TX-Ferm (18 Tenks)	13	· · · · · · · · · · · · · · · · · · ·	18			
TY-Ferm (6 Tanks)	6	3	-6			
U-Farm (16 Tanks)	15		6	4	6	6
TOTAL WEST AREA						
(86 Tanks)	77	4	62	. 7	19	19
TOTALS (177 Tanks)	131	8	125	15	25	24

- (a) Tank SY-101 has 2 gas sample flow sensors plus 2 vent flow sensors, and 2 ENRAFs.
- (b) Each tank has two sensors (high and low range).
- (c) Each tank has two sensors (high and low range).
- (d) T-107 Auto ENRAF O/S, manual readings taken daily
- (e) S, SX, and T-Farms five gas sample flow sensors have been unhooked or removed. Will eventually use SHMS equipment on other tanks but none scheduled yet.
- (f) C-105 acromag needs replacing. Manual readings are taken weekly.
- (g) A cable from the main distribution panel is faulty putting BX and BY-farms out of service. Repair and restoration of service is expected by June 22, 2001.

This page intentionally left blank.

APPENDIX E

MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPECIAL SURVEILLANCE FACILITIES

TABLE E-1. EAST AND WEST AREA MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPECIAL SURVEILLANCE FACILITIES

ACTIVE - still running transfers through the associated diversion boxes or pipeline encasements

April 30, 2001

FACILITY	LOCATION	PURPOSE (receives waste from	n:l (Gallons)	MONITORED BY	<u>REMARKS</u>
EAST AREA					
241-A-302-A	A Farm	A-151 D8	673	SACS/ENRAF/Manually	Pumped to AW-105 7/00
241-ER-311	8 Plant	ER-151, ER-152 DB	8837	SACS/ENRAF/Manually	•
241-AX-152	AX Farm	AX-152 DB	0	SACS/MT	Declared Assumed Leaker; pumped to AY-102 3/1/01
241-AZ-151	AZ Farm	AZ-702 condensate	2954	SACS/ENRAF/TMACS	Volume changes daily - pumped to AZ-101 or AZ-102 as needed
241-AZ-154	AZ Farm		25	SACS/MT	
244-BX-TK/SMP	BX Complex	DCRT - Receives from several farms	18594	SACS/MT	Using Manual Tape for tank/sump, pumped 10/16/99 to 66.0 in. Sump O/S 2/5/01
244-A-TK/SMP	A Complex	DCRT - Receives from several farms	7109	MCS/SACS/WTF	WTF- pumped 3/99 to AP-108
A-350	A Farm	Collects drainage	398	MCS/SACS/WTF	WTF (uncorrected) pumped as needed
AR-204	AY Farm	Tanker trucks from various facilities	250	DIP TUBE	Alarms on SACS-pumped to AP-108, 7/00
A-417	A Farm		12932	SACS/WTF	WTF (uncorrected) pumped 4/98
CR-003-TK/SUMP	C Farm	DCRT	2984	MT/ZIP CORD	Zip cord in sump O/S 3/11/96, water intrusion, 1/98
WEST AREA					·
241-TX-302-C	TX Farm	TX-154 DB	156	SACS/ENRAF/Manually	
241-U-301-B	U Farm	U-151, U-152, U-153, U-252 DB	8018	SACS/ENRAF/Manually	Returned to service 12/30/93
241-UX-302-A	U Plant	UX-154 DB	3258	SACS/ENRAF/Manually	
241-S-304	S Farm	S-151 DB	135	SACS/ENRAF/Manually	Replaced S-302-A, 10/91; ENRAF installed 7/98 Sump not alarming.
244-S-TK/SMP	S Farm	From original tanks to SY-102	14195	SACS/Manually	WTF (uncorrected)
244-TX-TK/SMP	TX Farm	From original tanks to SY-102	16604	SACS/Manually	MT - pumped PFP 241-Z tank D-5 to 244-TX DCRT on 4/12/01, level now 76"
Vent Station Catch	Tank	Cross Country Transfer Line	371	SACS/Manually	MT
			l EGENO:	THE CONTRACTOR SOL	

Total Active Facilities 18

LEGEND: DR - Diversion Box

DCRT - Double-Contained Receiver Tank

TX - Tank

SMP - Sump

FIC - Food Instrument Corporation measurement device

MT - Markual Tape

Zip Cord - surface level measurement device

WTF - Weight Time Factor - can be recorded as WTF,

CWF (corrected), and Uncorrected WTF

SACS - Surveillance Automated Control System

MCS - Monitor and Control System

Mensally - Not connected to any externed system

O/S - Out of Service

ENRAF - Surface Level Measuring Devices

TABLE E-2. EAST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES
INACTIVE - no longer receiving waste transfers
April 30, 2001

				MONITORE	ED .
FACILITY	LOCATION	RECEIVED WASTE FROM:	(Gallons)	BY	REMARKS
216-BY-201	BY Farm	TBP Waste Line	Unknown	NM	(216-BY)
241-A-302-B	A Farm	A-152 DB	5759	SACS/MT	Isolated 1985, Project B-138
					Interim Stabilized 1990, Rain Intrusion
241-AX-151	N of PUREX	PUREX	Unknown	NM	Isoleted 1985
241-B-301-B	B Farm	B-151, B-152, B-153, B-252 DB	22250	NM	Isolated 1985 (1)
241-B-302-B	B Farm	B-154 DB	4930	NM	(soleted 1985 (1)
241-BX-302-A	BX Farm	BR-152, BX-153, BXR-152, BYR-152 DB	840	NM	Isolated 1985 (1)
241-BX-302-B	BX Farm	BX-154 DB	1040	NM	solated 1985 (1)
241-BX-302-C	BX Farm	BX-155 DB	870	NM	Isolated 1985 (1)
241-C-301-C	C Farm	C-151, C-152, C-153, C-252 DB	10470	NM	Isolated 1985 (1)
241-CX-70	Hot Semi-	Transfer lines	Unknown	NM	Isolated, Decommission Project,
241-CX-72	Works	Transfer lines	650	NM	See Dwg H-2-95-501, 2/5/87
241-ER-311A	SW B Plant	ER-151 DB	Unknown	NM	Isolated
244-AR VAULT	A Complex	Between farms & B-Plant	Unknown	NM	Not actively being used. Systems activated for final clean-out.
244-BXR-TK/SMP-001	BX Farm	Transfer lines	7200	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-002	BX Ferm	Transfer lines	2180	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-003	BX Farm	Transfer lines	1810	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-011	BX Ferm	Transfer lines	7100	NM	Interim Stabilization 1985 (1)
361-B-TANK	B Plant	Drainage from 8-Plant	Unknown	NM	Interim Stabilization 1985 (1)
				AGT Coproportion control of	

LEGENO: DR - Diversion Box

DCRT - Denials Continued Receiver Tonic

UT - Marcal Tape

BACE - Backliffered Agreemented Control System

TK - Tank

BNF - Burge

R - Denially denotes replacement

MM - Not Monitored

TABLE E-3. WEST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES
INACTIVE - no longer receiving waste transfers
April 30, 2001

MONITORFO	M	α	VIT	n	RF	ת
-----------	---	----------	-----	---	----	---

				INIUIVIIIUKEL	9
<i>FACILITY</i>	LOCATION	RECEIVED WASTE FROM:	(Gallons)	<u>BY</u>	REMARKS
216-TY-201	E. of TY Farm	Supernate from T-112	Unknown	NM	Isolated
231-W-151-001	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
231-W-151-002	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
241-S-302	S Farm	240-S-151 DB	8368	SACS/ENRAF	Assumed Leaker EPDA 85-04
241-S-302-A	S Farm	241-S-151 DB	0		Assumed Leaker TF-EFS-90-042
Partielly	filled with grout 2/91,	determined still assumed leaker after lea	k test. Manual F	IC readings are un	obtainable due to dry grouted surface.
		d 2/23/99; intrusion readings discontinu			
241-S-302-B	S Farm	S Encasements	Unknown	NM	Isolated 1985 (1)
241-SX-302	SX Farm	SX-151 DB, 151 TB	Unknown	NM	isolated 1987
241-SX-304	SX Farm	SX-152 Transfer Box, SX-151 DB	Unknown	NM	Isolated 1985 (1)
241-T-301	T Farm	DB T-151, -151, -153, -252	Unknown	NM	Isolated 1985 (241-T-301B)
241-TX-302	TX Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TX-302-X-B	TX Farm	TX Encasements	Unknown	NM	Isolated 1985 (1)
241-TX-302-B	TX Ferm	TX-155 DB	1600	SACS/MT	New MT installed 7/16/93
241-TX-302-B(R)	E. of TX Farm	TX-155 DB	Unknown	NM	Isolated
241-TY-302-A	TY Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TY-302-B	TY Ferm	TY Encasements	Unknown	NM	lealated 1985 (1)

271-1X-002	INTENNI	17-122 00	OUKUOMU	NM	ISOIATOG 1985 (1)
241-TX-302-X-B	TX Farm	TX Encasements	Unknown	NM	Isolated 1985 (1)
241-TX-302-B	TX Ferm	TX-155 DB	1600	SACS/MT	New MT installed 7/16/93
241-TX-302-B(R)	E. of TX Farm	TX-155 DB	Unknown	NM	Isolated
241-TY-302-A	TY Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TY-302-B	TY Ferm	TY Encasements	Unknown	NM	Isolated 1985 (1)
241-Z-8	E. of Z Plant	Recupiex waste	Unknown	NM	isolated, 1974, 1975
242-T-135	T Evaporator	T Evaporator	Unknown	NM	isolated
242-TA-R1	T Evaporator	Z Plant waste	Unknown	NM	Isolated
243-S-TK-1	N. of S Farm	Pers. Decon. Facility	Unknown	NM	Isolated
244-U-TK/SMP	U Farm	DCRT - Receives from several farms	Unknown	NM	Not vet in use
244-TXR VAULT	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-001	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-002	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-003	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
270-W	SE of U Plant	Condensate from U-221	Unknown	NM	Isolated 1970
361-T-TANK	T Plant	Drainage from T-Plant	Unknown	NM	Isolated 1985 (1)
		• • • • • • • • • • • • • • • • • • • •			

Unknown

NM

Total West Area inactive facilities 27

Drainage from U-Plant

LEGEND: DB - Diversion Box, TB - Transfer Box

DCRT - Double-Contained Receiver Tank

TK - Tank

SMP - Sump

R - Gausily Seniors replacement

FIC - Surface Level Monitoring Device

MT - Manual Tape

O/B - Cut of Service

SACS - Surrelliance Automated Control System

NM - Not Monitored

ENRAF - Surface Level Monitoring Device

Interim Stabilzed, MT removed 1984 (1)

(1) SOURCE: WASTE STORAGE TANK STATUS & LEAK DETECTION CRITERIA document

361-U-TANK

U Plant

APPENDIX F LEAK VOLUME ESTIMATES

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 1 of 5) April 30, 2001

	Date Declared Confirmed or	Volume	Associated KiloCuries	interim Stabilized	Leak I	Estimate
ank Number	Assumed Leaker (3)	Gallons (2)	137 Cs (9)	Date (11)	Updated	Referen
41-A-103	1987	5500 (8))	06/88	1987	(j)
41-A-104 41-A-105 (1)	1975 1963	500 to 2500 10000 to	0.8 to 1.8 (q		1983	(a)(q)
	1303	277000	85 to 760 (b) 07/79	1991	(b){c}
41-AX-102	1988	3000 (8		09/88	1989	(h)
41-AX-104 41-B-101	1977	(6		08/81	1989	(g)
41-B-103	1974 1978	(8 (8		03/81 02/85	1989 1989	(g)
41-B-105	1978	(6	3)	12/84	1989	(g) (g)
41-B-107 41-B-110	1980 1981	8000 (8		03/85	1986	(d)(f)
41-B-111	1978	10000 (8		03/85 06/85	1986 1989	(d)
11-B-112	1978	2000	•	05/85	1989	(g) (g)
41-B-201	1980	1200 (8		08/81	1984	(e)(f)
41-B-203 41-B-204	1983 1984	300 (8 400 (8		06/84 06/84	1986 1989	(d)
11-BX-101	1972	(6	<u> </u>	09/78	1989	(g)
11-BX-102	1971	70000	50 (1)	11/78	1986	(b)
I1-BX-108 I1-BX-110	1974	2500	0.5 (1)	07/79	1986	(d)
11-BX-111	1976 1984 (13)	(6) (6)		08/85 03/95	1989 1993	(g)
1-BY-103	1973	<5000	<u> </u>	11/97	1983	(g)
1-BY-105	1984	(5		N/A	1989	(a) (g)
1-BY-106	1984	(6		N/A	1989	(g)
11-BY-107 11-BY-108	1984 1972	15100 (8) <5000)	07/79 02/85	1989 1983	(g)
1-C-101	1980)(10)	11/83		(a)
1-C-110	1984	2000 (8)	,,,,,	05/95	1986 1989	(d) (g)
1-C-111	1968	5500 (8))	03/84	1989	(<u>a</u>)
·1-C-201 (4) ·1-C-202 (4)	1988 1988	550 450		03/82	1987	(i)
1-C-203	1984	400 (8))	08/81 03/82	1987 1986	(i) (d)
1-C-204 (4)	1988	350		09/82	1987	(i)
1-S-104	1968	24000 (8))	12/84	1989	(g)
1-SX-104 1-SX-107	1988	6000 (8))	04/00	1988	(k)
1-SX-107	1964 I) 1962	<5000 2400 to	17 to 140	10/79 08/79	1983 1991	(a)
		35000	(m)(q)(t)	00175	1991	(m)(q)(
·1-SX-109 (5)(14 ·1-SX-110	l) 1965 1976	<10000 5500 (8)	<40 (n)		1992	(n)(t)
1-SX-111 (14)	1974	5500 (8) 500 to 2000	0.6 to 2.4 (I)(08/79	1989	(g)
1-SX-112 (14)	1969	30000	0.9 to 2.4 (j)(40 (l)(q)(t) 07/79 t) 07/79	1986 1986	(d)(q)(t) (d)(t)
1-SX-113	1962	15000	8 (1)	11/78	1986	(d)
1-SX-114 1-SX-115	1972 1965	(6) 50000		07/79	1989	(g)
1-T-101	1992	7500 (8)	21 (o)	<u>09/78</u> 04/93	1992 1992	(o)
1-T-103	1974	< 1000 (8)	1	11/83	1989	(p) (g)
1-T-106	1973	115000 (8)		08/81	1986	(d)
1-T-107 1-T-108	1984 1 97 4	(6) (8)		05/96 11/78	1989 1980	(g) (f)
1-T-109	1974	<1000 (8)	(12/84	1989	(r) (g)
1-T-111	1979, 1994 (12)	<1000 (8)	<u> </u>	02/95	1994	(f)(r)
1-TX-105	1977	(6)		04/83	1989	(g)
1-TX-107 (5) 1-TX-110	1984 1977	2500 (6)		10/79 04/83	1986 1989	(d)
1-TX-113	1974	(6)		04/83	1989	(g) (g)
1-TX-114	1974	- (6)		04/83	1989	(g)
1-TX-115 1-TX-116	1977 1977	- (6) (6)		09/83 04/83	1989	(<u>a</u>)
1-TX-117	1977	(6)		03/83	1989 1989	(g) (g)
1-TY-101	1973	<1000 (8)		04/83	1980	(f)
1-TY-103	1973	3000	0.7 (1)	02/83	1986	(d)
1-TY-104 1-TY-105	1981 19 6 0	1400 (8)		11/83	1986	(d)
1-11-105 1-TY-106	1959	35000 20000	4 (I) 2 (I)	02/83 11/78	1986 1986	(d) (d)
1-U-101	1959	30000	20 (I)	09/79	1986	(d)
1-U-104	1961	55000	0.09 (i)	10/78	1986	(d)
1-U-110	1975	5000 to 8100 (8)	0.05 (q)	12/84	1986	(d)(q)
1-U-112	1980	8500 (8)		09/79	1986	(d)

N/A = not applicable (not yet interim stabilized)

TABLE F-1. SINGLE-SHELL LEAK VOLUME ESTIMATES (Sheet 2 of 6)

Footnotes:

- Current estimates [see reference(b)] are that 610 Kgallons of cooling water was added to Tank 241-A-105 from November 1970 to December 1978 to aid in evaporative cooling. In accordance with <u>Dangerous Waste Regulations</u> [Washington Administrative Code 173-303-070 (2)(a)(ii), as amended, Washington State Department of Ecology, 1990, Olympia, Washington], any of this cooling water that has been added and subsequently leaked from the tank must be classified as a waste and should be included in the total leak volume. In August 1991, the leak volume estimate for this tank was updated in accordance with the WAC regulations. Previous estimates excluded the cooling water leaks from the total leak volume estimates because the waste content (concentration) in the cooling water which leaked should be much less than the original liquid waste in the tank (the sludge is relatively insoluble). The total leak volume estimate in this report (10 Kgallons to 277 Kgallons) is based on the following (see References):
 - 1. Reference (b) contains an estimate of 5 Kgallons to 15 Kgallons for the initial leak prior to August 1968.
 - 2. Reference (b) contains an estimate of 5 Kgallons to 30 Kgallons for the leak while the tank was being sluiced from August 1968 to November 1970.
 - 3. Reference (b) contains an estimate of 610 Kgallons of cooling water added to the tank from November 1970 to December 1978 but it was estimated that the leakage was small during this period. This reference contains the statement "Sufficient heat was generated in the tank to evaporate most, and perhaps nearly all, of this water." This results in a low estimate of zero gallons leakage from November 1970 to December 1978.
 - 4. Reference (c) contains an estimate the 378 to 410 Kgallons evaporated out of the tank from November 1970 to December 1978. Subtracting the minimum evaporation estimate from the cooling water added estimate provides a range from 0 to 232 Kgallons of cooling water leakage from November 1970 to December 1978.

	Low Esumate	High Estimat
Prior to August 1968	5,000	15,000
August 1968 to November 1970	5,000	30,000
November 1970 to December 1978	0	232,000
Totals	10,000	277,000

- These leak volume estimates do not include (with some exceptions), such things as: (a) cooling/raw water leaks, (b) intrusions (rain infiltration) and subsequent leaks, (c) leaks inside the tank farm but not through the tank liner (surface leaks, pipeline leaks, leaks at the joint for the overflow or fill lines, etc.), and (d) leaks from catch tanks, diversion boxes, encasements, etc.
- (3) In many cases, a leak was suspected long before it was identified or confirmed. For example, reference (d) shows that Tank 241-U-104 was suspected of leaking in 1956. The leak was "confirmed" in 1961. This report lists the "assumed leaker" date of 1961. Using <u>present</u> standards, Tank 241-U-104 would have been declared an assumed leaker in 1956. In 1984, the criteria designations of "suspected leaker," "questionable integrity," "confirmed leaker," "declared leaker," "borderline" and "dormant," were merged into one category now reported as "assumed leaker." See reference (f) for explanation of when, how long, and how fast some of the tanks leaked. It is highly likely that there have been undetected leaks from single-shell tanks because of the nature of their design and instrumentation.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 3 of 6)

- (4) The leak volume estimate date for these tanks is before the "declared leaker" date because the tank was in a "suspected leaker" or "questionable integrity" status; however, a leak volume had been estimated prior to the tank being reclassified.
- (5) The increasing radiation levels in drywells and laterals associated with these three tanks could be indicating continuing leak or movement of existing radionuclides in the soil. There is no conclusive way to confirm these observations.
- (6) Methods were used to estimate the leak volumes from these 19 tanks based on the <u>assumption</u> that their cumulative leakage is approximately the same as for 18 of the 24 tanks identified in footnote (9). For more details see reference (g). The total leak volume estimate for these tanks is 150 Kgallons (rounded to the nearest Kgallons), for an average of approximately 8 Kgallons for each of 19 tanks.
- (7) The total has been rounded to the nearest 50 Kgallons. Upper bound values were used in many cases in developing these estimates. It is likely that some of these tanks have not actually leaked.
- (8) Leak volume estimate is based solely on observed liquid level decreases in these tanks. This is considered to be the most accurate method for estimating leak volumes.
- (9) The curie content shown is as listed in the reference document and is <u>not</u> decayed to a consistent date: therefore, a cumulative total is inappropriate.
- (10) Tank 241-C-101 experienced a liquid level decrease in the late 1960s and was taken out of service and pumped to a "minimum heel" in December 1969. In 1970, the tank was classified as a "questionable integrity" tank. Liquid level data show decreases in level throughout the 1970s and the tank was saltwell pumped during the 1970s, ending in April 1979. The tank was reclassified as a "confirmed leaker" in January 1980. See references (q) and (r); refer to reference (s) for information on the potential for there to have been leaks from other C-farm tanks (specifically, C-102, C-103, and C-109).
- (11) These dates indicate when the tanks were declared to be interim stabilized. In some cases, the official interim stabilization documents were issued at a later date. Also, in some cases, the field work associated with interim stabilization was completed at an earlier date.
- (12) Tank T-111 was declared an assumed re-leaker on February 28, 1994, due to a decreasing trend in surface level measurement. This tank was pumped, and interim stabilization completed on February 22, 1995.
- (13) Tank BX-111 was declared an assumed re-leaker in April 1993. Preparations for pumping were delayed, following an administrative hold placed on all tank farm operations in August 1993. Pumping resumed and the tank was declared interim stabilized on March 15, 1995.
- (14) The leak volume and curie release estimates on SX-108, SX-109, SX-111, and SX-112 have been reevaluated using a Historical Leak Model [see reference (t)]. In general, the model estimates are much higher
 than the values listed in the table, both for volume and curies released. The values listed in the table do not
 reflect this revised estimate because, "In particular, it is worth emphasizing that this report was never meant to
 be a definitive update for the leak baseline at the Hanford Site. It was rather meant to be an attempt to view the
 issue of leak inventories with a new and different methodology." (This quote is from the first page of the
 referenced report).
- (15) In July 1998, the Washington State Department of Ecology (Ecology) directed the U. S. Department of Energy (DOE) to develop corrective action plans for eight single-shell tank farms (B/BX/BY/S/SX/T/TX/TY) where groundwater contamination likely originated from tank farm operations. A Tri-Party Agreement milestone (M-45 series) was developed that established a formalized approach for evaluating impacts on groundwater quality of losses of tank wastes to the vadose zone underlying these tank farms. Planning documents have been

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 4 of 6)

completed for the S, SX, B, BX, and BY tank farms and will be completed shortly for the T, TX, and TY farms. The phase 1 field investigation is near completion in the S and SX tank farms and has begun in the B, BX, and BY farms. Field work is anticipated in FY-02 for the T, TX, and TY tank farms. The remaining four single-shell tank farms are expected to be included in corrective action plans in the near future.

All of the information included in this appendix is currently under review and significant revisions are anticipated. Recently, major tank farm vadose zone investigation efforts (such as the baseline spectral gammaray logging of all drywells in all single-shell tank farms, as well as drilling and sampling in the SX tank farm) were completed. This appendix will be revised as a better understanding of past tank leak events is developed.

SST Vadose Zone Project drilling and testing activities near tank BX-102 were completed March 2001. A borehole (299-E33-45) was drilled through the postulated uranium plume resulting from the 1951 tank BX-102 overfill event to confirm the presence of uranium, define its present depth, and survey other contaminants of interest such as Tc-99. Thirty-five split-spoon samples were collected for laboratory analyses. This borehole was decommissioned after collection and analysis of groundwater samples.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 5 of 6)

References:

- (a) Murthy, K.S., et al, June 1983, Assessment of Single-Shell Tank Residual Liquid Issues at Hanford Site, Washington, PNL-4688, Pacific Northwest Laboratory, Richland, Washington.
- (b) WHC, 1991a, Tank 241-A-105 Leak Assessment, WHC-MR-0264, Westinghouse Hanford Company, Richland, Washington.
- (c) WHC, 1991b, Tank 241-A-105 Evaporation Estimate 1970 Through 1978, WHC-EP-0410, Westinghouse Hanford Company, Richland, Washington.
- (d) Smith, D. A., January 1986, Single-Shell Tank Isolation Safety Analysis Report, SD-WM-SAR-006, Rev. 1, Westinghouse Hanford Company, Richland, Washington.
- (e) McCann, D. C., and T. S. Vail, September 1984, Waste Status Summary, RHO-RE-SR-14, Rockwell Hanford Operations, Richland, Washington.
- (f) Catlin, R. J., March 1980, Assessment of the Surveillance Program of the High-Level Waste Storage Tanks at Hanford, Hanford Engineering Development Laboratory, Richland, Washington.
- (g) Baumhardt, R. J., May 15, 1989, Letter to R. E. Gerton, U.S. Department of Energy-Richland Operations Office, Single-Shell Tank Leak Volumes, 8901832B R1, Westinghouse Hanford Company, Richland, Washington.
- (h) WHC, 1990a, Occurrence Report, Surface Level Measurement Decrease in Single-Shell Tank 241-AX-102, WHC-UO-89-023-TF-05, Westinghouse Hanford Company, Richland, Washington.
- (i) Groth, D. R., July 1, 1987, Internal Memorandum to R. J. Baumhardt, Liquid Level Losses in Tanks 241-C-201, -202 and -204, 65950-87-517, Westinghouse Hanford Company, Richland, Washington.
- (j) Groth, D. R. and G. C. Owens, May 15, 1987, Internal Memorandum to J. H. Roecker, *Tank 103-A Integrity Evaluation*, Westinghouse Hanford Company, Richland, Washington.
- (k) Dunford, G. L., July 8, 1988, Internal Memorandum to R. K. Welty, Engineering Investigation: Interstitial Liquid Level Decrease in Tank 241-SX-104, 13331-88-416, Westinghouse Hanford Company, Richland, Washington.
- (1) ERDA, 1975, Final Environmental Statement Waste Management Operations, Hanford Reservation, Richland, Washington, ERDA-1538, 2 vols., U.S. Energy Research and Development Administration, Washington, D.C.
- (m) WHC, 1992a, Tank 241-SX-108 Leak Assessment, WHC-MR-0300, Westinghouse Hanford Company, Richland, Washington.
- (n) WHC, 1992b, Tank 241-SX-109 Leak Assessment, WHC-MR-0301, Westinghouse Hanford Company, Richland, Washington.
- (o) WHC, 1992c, Tank 241-SX-115 Leak Assessment, WHC-MR-0302, Westinghouse Hanford Company, Richland, Washington.

TABLE F-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 6 of 6)

- (p) WHC, 1992d, Occurrence Report, Apparent Decrease in Liquid Level in Single Shell Underground Storage Tank 241-T-101, Leak Suspected; Investigation Continuing, RL-WHC-TANKFARM-1992-0073, Westinghouse Hanford Company, Richland, Washington.
- (q) WHC,1990b, A History of the 200 Area Tank Farms, WHC-MR-0132, Westinghouse Hanford Company, Richland, Washington.
- (t) WHC, 1993a, Assessment of Unsaturated Zone Radionuclide Contamination Around Single-Shell Tanks 241-C-105 and 241-C-106, WHC-SD-EN-TI-185, REV OA, Westinghouse Hanford Company, Richland, Washington.
- (s) WHC, 1994, Occurrence Report, Apparent Liquid Level Decrease in Single Shell Underground Storage Tank 241-T-111; Declared an Assumed Re-Leaker, RL-WHC-TANKFARM-1994-0009, Westinghouse Hanford Company, Richland, Washington.
- (t) HNF, 1998, Agnew, S. F. and R. A. Corbin, August 1998, Analysis of SX Farm Leak Histories Historical Leak Model, (HLM), HNF-3233, Rev. 0, Los Alamos National Laboratory, Los Alamos, New Mexico

This page intentionally left blank

APPENDIX G

SINGLE-SHELL TANKS INTERIM STABILIZATION, AND CONTROLLED, CLEAN AND STABLE (CCS) STATUS

TABLE G -1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (Sheet 1 of 3)
April 30, 2001

Tank			Interim				I	Interim	1	***		<u> </u>	Interim	1
	Tank	Tank	Stabil.	Stabil.		Tank	Tank		Stabil.	800	Tank	Tank		Stabil.
101 SOUND NI/A									1			ľ	i	
1-102 SOUND OW99				HASILIEL	- Kara									
1-03 ASMO LCR 0-0/98 AR SC 103 SOUND N/A SC 110 ASMO LCR 0-0/79 AR C 104 SOUND 0-0/98 N/A SC 111 ASMO LCR 0-0/79 AR C 104 SOUND 0-0/98 N/A SC 104 SOUND 0-0/98 N/A SC 100 SOUND 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR C 107 ASMO LCR 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR SC 111 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 AR SC 100 ASMO LCR 0-0/98 ASMO LCR 0-0/9	A-102			SN						2000				
1-104	A-103				- WW				JE!					
1-106	A-104								SN					
1-106	A-105				2,00					-				
X-101 SOUND N/A	A-106				_				 	30000				
X-102 ASMD LKR 09/88 BN 2-C-108 SOUND 03/84 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/81 AR 3-T-204 SOUND 04/83 AR 3-T-204 SOUND 04/85 A	AX-101	SOUND							JET					<u> </u>
X-103 SOUND 09/87 AR \$10-109 SOUND 11/83 AR \$17-20-4 SOUND 09/81 AR \$17-20-4 SOUND 09/81 AR \$1-20-4 SOUND 09/81 AR \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/81 AR \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 AR \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/83 SOUND 09/83 JET \$1-20-4 SOUND 09/83 SOUND 09/83 JET \$1-20-4 SOUND 09/83 SOUND 09/83 SOUND 09/83 JET \$1-20-4 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/83 SOUND 09/85 SN \$1-20-2 ARMO LKR 09/81 AR \$17-104 SOUND 09/83 JET \$1-20-4 SOUND 09/83 JET \$1-20-4 SOUND 09/85 SN \$1-20-2 ARMO LKR 09/82 AR \$17-106 SOUND 09/83 JET \$1-20-4 SOUND 09/85 SN \$1-20-2 SOUND N/A SOUND 09/85 SN \$1-20-2 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND N/A SOUND 09/85 SN \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND 09/85 SN \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1-20-3 SOUND N/A SV \$1	AX-102		-	SN						800			•	
X-104 ASMD KR 0-9/81 AR S-111 ASMD LKR 0-9/85 JET STX-101 SOUND 0-2/84 AR S-101 ASMD KR 0-9/81 SN S-1011 ASMD LKR 0-9/85 SN S-1012 SOUND 0-9/86 AR STX-103 SOUND 0-9/83 JET 103 ASMD KR 0-9/85 SN S-2012 ASMD LKR 0-9/85 AR STX-103 SOUND 0-9/83 JET 103 ASMD KR 0-9/85 SN S-2012 ASMD LKR 0-9/82 AR STX-103 SOUND 0-9/83 JET 104 ASMD KR 0-9/85 SN S-2012 ASMD LKR 0-9/82 AR STX-105 ASMD LKR 0-9/83 JET 106 ASMD KR 12/94 AR C-203 ASMD LKR 0-9/82 AR STX-105 ASMD LKR 0-9/83 JET 107 ASMD LKR 0-9/85 SN S-2014 ASMD LKR 0-9/82 AR STX-105 ASMD LKR 0-9/83 JET 107 ASMD LKR 0-9/85 SN S-102 SOUND N/A STX-106 SOUND 0-9/83 JET 107 ASMD LKR 0-9/85 SN S-102 SOUND N/A STX-106 SOUND 0-9/83 JET 0-9/85 SN S-102 SOUND 0-9/95 JET 0-9/85 SN S-102 SOUND 0-9/95 JET 0-9/85 SN S-102 SOUND 0-9/95 JET 0-9/85 JET 0-9/85 SN S-102 SOUND 0-9/95 JET 0-9/85 SN S-104 SOUND 0-9/96 JET STX-110 ASMD LKR 0-9/85 SN S-106 SOUND 0-9/96 JET STX-112 SOUND 0-9/95 JET 111 ASMD LKR 0-9/85 SN S-106 SOUND 0-9/96 JET STX-112 SOUND 0-9/93 JET 0-9/95 JET	AX-103			AŘ						2000				-
101	AX-104	ASMD LKR	08/81	AR	₩ C	-110	ASMD LKR	05/95						
102	3-101	ASMD IKR	03/81	SN	₩ C	-111	ASMD LKR	03/84	SN					
ASMD KR	3-102	SOUND	08/85	SN	 C-	-112	SOUND	09/90						
105	3-103	ASMD IKR	02/86	SN	 C-	-201	ASMD LKR			88				
106	B-104	SOUND	06/85	SN	∞ C-	-202	ASMD LKR	08/81	AR	80				
100	B-106	ASMD IKR	12/84	AR	∞ C-	-203			-	-				JET
107	3-106	SOUND	03/86	SN	©	-204	ASMD LKR	09/82		-				AR
100	3-107	ASMD LKR	03/85	8N:	₩ 5-	-101	SOUND	N/A		4884				JET
110 ASMO LKR 12/84 AR 8-104 ASMO LKR 12/84 AR 8TX-111 SOUND 04/83 JET 111 ASMO LKR 06/85 SN S-106 SOUND 04/80 JET 8TX-112 SOUND 04/83 JET 1112 ASMO LKR 06/85 SN S-106 SOUND 02/91 JET [10] ST 113 ASMO LKR 04/83 JET 201 ASMO LKR 06/81 AR (3) S-107 SOUND 12/96 JET 17X-112 ASMO LKR 04/83 JET 201 ASMO LKR 06/81 AR (3) S-108 SOUND 12/96 JET 17X-114 ASMO LKR 04/83 JET 202 SOUND 06/86 AR(2) S-108 SOUND 12/96 JET 17X-114 ASMO LKR 04/83 JET 203 ASMO LKR 06/84 AR S-109 SOUND N/A STX-116 ASMO LKR 04/83 JET 204 ASMO LKR 06/84 AR S-109 SOUND N/A JET 17X-117 ASMO LKR 04/83 JET 204 ASMO LKR 06/84 AR S-110 SOUND N/A JET 17X-117 ASMO LKR 04/83 JET 204 ASMO LKR 06/84 AR S-110 SOUND N/A JET 17X-117 ASMO LKR 04/83 JET 204 ASMO LKR 06/84 AR S-111 SOUND N/A JET 17X-117 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-112 SOUND N/A JET 17X-117 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-112 SOUND N/A JET 17X-110 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-112 SOUND N/A JET 17X-110 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-112 SOUND N/A JET 17X-101 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-112 SOUND N/A JET 17X-101 ASMO LKR 04/83 JET 204 ASMO LKR 11/78 AR S-102 SOUND N/A JET 17X-101 ASMO LKR 04/83 JET 204 A	3-108	SOUND	05/86	SN	₩ \$-	-102	SOUND	N/A		-				JET
111	3-109	SOUND	04/85	SN	S-	-103	SOUND	04/00	JET (6)		TX-110	ASMD LKR	04/83	JET
112 ASMD LKR 06/86 SN 5-106 SOUND 02/01 JET 1101 TX-113 ASMD LKR 04/83 JET 201 ASMD LKR 06/81 AR (3) \$5-107 SOUND N/A TX-114 ASMD LKR 04/83 JET 202 SOUND 06/85 AR (2) \$5-108 SOUND 12/89 JET X-116 ASMD LKR 04/83 JET 203 ASMD LKR 06/84 AR 5-109 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 06/84 AR 5-109 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 06/84 AR 5-109 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 09/78 AR 5-111 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 09/78 AR 5-111 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 11/78 AR 5-112 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 11/78 AR 5-112 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 11/78 AR 5-112 SOUND N/A TX-116 SOUND 04/83 JET 204 ASMD LKR 11/83 AR 204 ASMD LKR 11/84 ASMD LKR 04/83 JET 204 ASMD LKR 11/83 AR 204 ASMD LKR 11/84 ASMD LKR 04/83 JET 204 ASMD LKR 11/84 ASMD LKR 04/83 JET 204 ASMD LKR 11/84 ASMD LKR 04/83 JET 204 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/84 ASMD LKR 11/85 AR 24-104 ASMD LKR 04/85 ASMD LKR 11/85 ASMD LKR 11/78 ASMD LKR 04/85 ASMD LKR 11/78 AR 24-104 ASMD LKR 04/85 ASMD LKR 11/78 AR 24-104 ASMD LKR 04/85 ASMD LKR 11/78 AR 24-104 ASMD LKR 04/85 ASMD LKR 11/78 AR 24-104 ASMD LKR 04/85 ASMD LK	-110	ASMD LKR	12/84	AR	∭ S-	-104	ASMD LKR	12/84	AR	333	TX-111	SOUND	04/83	JET
112	-111	ASMD LKR	06/85	SN	S-	-105	SOUND	09/88	JET		TX-112	SOUND	04/83	JET
201	3-112	ASMID LKR	05/85	SN	∭ S-	-106	SOUND	02/01	JET (10)	-				JET
202 SOUND 06/65 AR(2) 8-108 SOUND 12/96 JET TX-115 ASMD LKR 09/83 JET 203 ASMD LKR 06/84 AR 8-109 SOUND N/A TX-116 ASMD LKR 04/83 JET 204 ASMD LKR 06/84 AR 8-110 SOUND N/A TX-116 ASMD LKR 03/83 JET 6-101 ASMD LKR 09/79 AR 8-111 SOUND N/A TX-118 SOUND 04/83 JET 6-102 ASMD LKR 11/78 AR 8-111 SOUND N/A TX-118 SOUND 04/83 JET 6-103 ASMD LKR 11/78 AR 8-112 SOUND N/A TY-101 ASMD LKR 04/83 JET 6-103 SOUND 11/83 AR(2) SX-101 SOUND N/A TY-102 SOUND 06/79 AR 8-103 SOUND N/A TY-102 SOUND 06/79 AR 8-103 SOUND N/A TY-102 SOUND 06/79 AR 8-106 SOUND 07/95 SN SX-103 SOUND N/A TY-103 ASMD LKR 02/83 JET 6-106 SOUND 07/95 SN SX-104 ASMD LKR 04/00 JET 6-106 SOUND 09/90 JET SX-105 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-108 ASMD LKR 07/79 SN SX-109 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-109 SOUND 09/90 JET SX-105 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-109 SOUND 09/90 JET SX-105 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-109 SOUND 09/90 JET SX-105 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-109 SOUND 09/90 JET SX-105 SOUND N/A TY-104 ASMD LKR 02/83 JET 6-109 SOUND 09/90 JET SX-105 ASMD LKR 04/79 AR 0-102 SOUND N/A JET 6-104 ASMD LKR 09/79 AR 0-103 SOUND N/A JET SX-105 ASMD LKR 04/79 AR 0-103 SOUND 09/90 JET SX-105 ASMD LKR 09/79 AR 0-103 SOUND 09/90 JET SX-106 ASMD LKR 09/79 AR 0-103 SOUND 09/90 JET SX-110 ASMD LKR 09/79 AR 0-103 SOUND 09/90 JET SX-110 ASMD LKR 09/79 AR 0-104 ASMD LKR 10/78 AR 0-104 ASMD LKR 10/78 AR 0-104 ASMD LKR 10/78 AR 0-104 ASMD LKR 10/78 AR 0-104 ASMD LKR 10/78 AR 0-105 SOUND N/A 1-104 SOUND 04/85 JET SX-110 ASMD LKR 07/79 AR 0-105 SOUND N/A 1-104 SOUND 04/85 JET SX-111 ASMD LKR 07/79 AR 0-106 SOUND N/A 1-105 SOUND N/A 1-106 SOUND N/A 1-106 SOUND 04/85 JET SX-114 ASMD LKR 07/79 AR 0-106 SOUND N/A 1-106 ASMD LKR 07/79 JET T1-101 ASMD LKR 04/93 SN U-101 ASMD LKR 09/79 AR 0-106 ASMD LKR N/A T1-104 ASMD LKR 09/79 AR 0-106 ASMD LKR 00/79 JET T1-104 ASMD LKR 09/79 AR 0-109 SOUND 04/85 JET SX-114 ASMD LKR 09/79 AR 0-109 SOUND 04/85 JET SX-114 ASMD LKR 09/81 AR 0-109 SOUND 04/85 JET SX-114 ASMD LKR 09/81 AR 0-109 SOUND 06/79 AR 0-1	-201	ASMD LKR	08/81	AR (3)	∭ S-	-107	SOUND	N/A		-				-
203 ASMO LKR 06/84 AR 8-109 SOUND N/A TX-116 ASMO LKR 04/83 JET 204 ASMO LKR 06/84 AR 8-110 SOUND 01/87 JET TX-117 ASMO LKR 03/83 JET 304 ASMO LKR 09/78 AR 8-111 SOUND N/A TX-116 SOUND 04/83 JET 304 ASMO LKR 09/78 AR 8-111 SOUND N/A TX-116 SOUND 04/83 JET 304 ASMO LKR 11/78 AR 8-112 SOUND N/A TY-101 ASMO LKR 04/83 JET 304 ASMO LKR 11/78 AR 8-112 SOUND N/A TY-101 ASMO LKR 04/83 JET 304 ASMO LKR 04/83 ASMO LKR 04/83 SOUND N/A TY-102 SOUND 09/78 AR 304 ASMO LKR 04/83 JET 304 ASMO LKR 04/83 ASMO LKR 04/83 JET 304 ASMO LKR 04/83 ASMO LKR 04/83 JET 304 ASMO LKR 04/83 ASMO LKR 02/83 JET 304 ASMO LKR 04/83 ASMO LKR 02/83 JET 304 ASMO LKR 04/83 ASMO LKR 02/83 JET 304 ASMO LKR 04/83 ASMO LKR 02/83 JET 304 ASMO LKR 04/83 ASMO L	-202	SOUND	05/85	AR(2)			SOUND	12/96	JET			ASMD LKR		
ASMO LKR	-203	ASMD LKR	06/84	AR	⊗ S-	-109	SOUND	N/A						JET
C-101 ASMO LKR 09/78 AR 8-111 SOUND N/A TY-101 ASMO LKR 04/83 JET (-102 ASMO LKR 11/78 AR 5-112 SOUND N/A TY-102 SOUND 04/83 JET (-103 SOUND 11/83 AR(2) SX-101 SOUND N/A TY-102 SOUND 09/79 AR (-104 SOUND 09/89 SN SX-102 SOUND N/A TY-102 SOUND 09/79 AR (-105 SOUND 09/89 SN SX-102 SOUND N/A TY-103 ASMO LKR 02/83 JET (-105 SOUND 09/89 SN SX-102 SOUND N/A TY-103 ASMO LKR 02/83 JET (-106 SOUND 09/89 SN SX-103 SOUND N/A TY-104 ASMO LKR 02/83 JET (-107 SOUND 09/89 SN SX-104 ASMO LKR 04/00 JET (7) TY-106 ASMO LKR 11/83 AR (-108 ASMO LKR 07/79 SN SX-105 SOUND N/A TY-106 ASMO LKR 11/78 AR (-108 ASMO LKR 07/79 SN SX-105 SOUND N/A TY-106 ASMO LKR 09/79 AR (-109 SOUND 09/80 JET SX-107 ASMO LKR 09/79 AR U-101 ASMO LKR 09/79 AR (-101 ASMO LKR 08/85 SN SX-108 ASMO LKR 06/79 AR U-101 ASMO LKR 09/79 AR (-111 ASMO LKR 03/95 JET SX-109 ASMO LKR 06/79 AR U-103 SOUND 09/80 JET SX-106 ASMO LKR 06/79 AR U-104 ASMO LKR 10/78 AR (-112 SOUND 09/80 JET SX-110 ASMO LKR 06/79 AR U-106 SOUND 03/01 JET (110 SOUND 06/84 JET SX-111 ASMO LKR 06/79 AR U-106 SOUND 03/01 JET (110 SOUND 06/84 JET SX-111 ASMO LKR 07/79 AR U-108 SOUND 03/01 JET (110 SOUND 06/84 JET SX-111 ASMO LKR 07/79 AR U-108 SOUND 03/01 JET (110 SOUND 06/84 JET SX-113 ASMO LKR 07/79 AR U-108 SOUND N/A (-104 ASMO LKR 06/79 AR U-108 SOUND N/A (-105 ASMO LKR 06/79 AR U-108 SOUND N/A (-105 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR N/A T-101 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR N/A T-101 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 JET T-103 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 JET T-103 ASMO LKR 06/79 AR U-109 SOUND N/A (-106 ASMO LKR 06/79 JET T-103 ASMO LKR 06/79 AR U-203 SOUND 06/79 AR (-106 ASMO LKR 06/79 JET T-105 SOUND 06/79 AR U-203 SOUND 06/79 AR (-106 ASMO LKR 06/79 JET T-105 SOUND 06/79 AR U-2	-204	ASMD LKR	06/84	AR	8 -	-110	SOUND	01/97	JET		TX-117			_
C-102 ASMD LKR 11/78 AR S-112 SOUND N/A TY-101 ASMD LKR 04/83 JET (-103 SOUND 11/83 ARI2) SX-101 SOUND N/A TY-102 SOUND 09/79 AR (-104 SOUND 09/89 SN SX-102 SOUND N/A TY-103 ASMD LKR 02/83 JET (-106 SOUND 03/81 SN SX-102 SOUND N/A TY-104 ASMD LKR 02/83 JET (-106 SOUND 03/81 SN SX-103 SOUND N/A TY-104 ASMD LKR 02/83 JET (-107 SOUND 09/89 JET SX-104 ASMD LKR 04/00 JET (7) TY-106 ASMD LKR 02/83 JET (-108 ASMD LKR 04/00 JET (8) U-101 ASMD LKR 02/83 JET (-108 ASMD LKR 07/79 SN SX-104 ASMD LKR 04/00 JET (8) U-101 ASMD LKR 02/83 JET (-108 ASMD LKR 07/79 SN SX-106 SOUND 05/00 JET (8) U-101 ASMD LKR 09/79 AR (-109 SOUND 09/80 JET SX-105 SOUND 05/00 JET (8) U-101 ASMD LKR 09/79 AR (-110 ASMD LKR 03/85 JET SX-107 ASMD LKR 08/79 AR U-102 SOUND N/A (-111 ASMD LKR 03/85 JET SX-108 ASMD LKR 06/79 AR U-103 SOUND 09/00 JET (-111 ASMD LKR 03/85 JET SX-106 ASMD LKR 06/79 AR U-103 SOUND 09/00 JET (-111 ASMD LKR 03/85 JET SX-106 ASMD LKR 06/79 AR U-103 SOUND 09/00 JET (-112 SOUND 06/84 JET SX-110 ASMD LKR 06/79 AR U-105 SOUND 03/01 JET (11-101 SOUND 06/84 JET SX-110 ASMD LKR 06/79 AR U-105 SOUND 03/01 JET (11-101 SOUND 06/84 JET SX-111 ASMD LKR 07/79 SN U-106 SOUND 03/01 JET (11-101 SOUND 06/84 JET SX-111 ASMD LKR 07/79 SN U-106 SOUND 03/01 JET (11-101 SOUND 06/84 JET SX-113 ASMD LKR 07/79 AR U-107 SOUND N/A (-104 SOUND 01/85 JET SX-113 ASMD LKR 07/79 AR U-108 SOUND N/A (-104 SOUND 01/85 JET SX-114 ASMD LKR 07/79 AR U-108 SOUND N/A (-106 ASMD LKR 07/79 JET T-101 ASMD LKR 07/79 AR U-109 SOUND N/A (-106 ASMD LKR 07/79 JET T-101 ASMD LKR 07/79 AR U-108 SOUND N/A (-108 ASMD LKR 07/79 JET T-101 ASMD LKR 07/79 AR U-108 SOUND N/A (-108 ASMD LKR 07/79 JET T-101 ASMD LKR 07/79 AR U-108 SOUND N/A (-108 ASMD LKR 07/79 JET T-101 ASMD LKR 07/79 AR U-108 SOUND N/A (-108 ASMD LKR 07/79 JET T-104 SOUND 03/61 AR(2)(3) U-112 ASMD LKR 09/79 AR U-108 SOUND 06/79 AR U-108 ASMD LKR 07/79 JET T-108 ASMD LKR 06/81 AR U-201 SOUND 06/79 AR (-108 ASMD LKR 07/79 JET T-106 ASMD LKR 06/81 AR U-203 SOUND 06/79 AR (-108 ASMD LKR 07/79 JET T-106 ASMD LKR 06/81 AR	3X-101	ASMD LKR	09/78	AR	8 -	·111	SOUND	N/A		-				JET
C-103 SOUND 11/83 AR(2) SX-101 SOUND N/A TY-102 SOUND 09/79 AR C-104 SOUND 09/89 SN SX-102 SOUND N/A TY-103 ASMD LKR 02/83 JET C-106 SOUND 03/81 SN SX-104 ASMD LKR 04/00 JET (7) TY-105 ASMD LKR 11/83 AR C-108 SOUND 07/95 SN SX-104 ASMD LKR 04/00 JET (7) TY-105 ASMD LKR 11/83 AR C-108 SOUND 09/80 JET SX-105 SOUND N/A TY-106 ASMD LKR 11/79 AR C-108 ASMD LKR 07/79 SN SX-105 SOUND N/A TY-106 ASMD LKR 02/83 JET C-108 ASMD LKR 07/79 SN SX-106 SOUND N/A TY-106 ASMD LKR 09/79 AR C-109 SOUND 09/80 JET SX-107 ASMD LKR 10/79 AR U-101 ASMD LKR 09/79 AR C-110 ASMD LKR 08/85 SN SX-108 ASMD LKR 08/79 AR U-103 SOUND 09/00 JET (6) C-111 ASMD LKR 03/85 JET SX-109 ASMD LKR 08/79 AR U-103 SOUND 09/00 JET (6) C-111 ASMD LKR 03/85 JET SX-109 ASMD LKR 06/81 AR U-104 ASMD LKR 10/78 AR C-112 SOUND 09/90 JET SX-110 ASMD LKR 07/79 AR U-105 SOUND 03/01 JET (1) C-103 ASMD LKR 11/87 JET SX-111 ASMD LKR 07/79 AR U-106 SOUND 03/01 JET (1) C-104 SOUND 06/94 JET SX-111 ASMD LKR 07/79 AR U-106 SOUND 03/01 JET (1) C-105 ASMD LKR 11/87 JET SX-113 ASMD LKR 07/79 AR U-107 SOUND N/A C-106 ASMD LKR N/A SX-115 ASMD LKR 07/79 AR U-109 SOUND N/A C-106 ASMD LKR N/A SX-115 ASMD LKR 07/79 AR U-109 SOUND N/A C-106 ASMD LKR N/A SX-115 ASMD LKR 07/79 AR U-109 SOUND N/A C-106 ASMD LKR N/A T-101 ASMD LKR 09/78 AR U-110 ASMD LKR 07/79 AR C-106 ASMD LKR N/A T-101 ASMD LKR 09/78 AR U-109 SOUND N/A C-106 ASMD LKR N/A T-101 ASMD LKR 09/78 AR U-109 SOUND N/A C-106 ASMD LKR N/A T-101 ASMD LKR 09/78 AR U-109 SOUND N/A C-107 ASMD LKR 02/96 JET T-102 SOUND 03/81 AR U-201 SOUND N/A C-108 ASMD LKR 02/96 JET T-108 ASMD LKR 09/81 AR U-202 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-203 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-203 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-204 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-204 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-204 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108 ASMD LKR 09/81 AR U-204 SOUND 08/79 AR C-109 SOUND 01/86 JET T-108	3X-102	ASMO LKR	11/78	AR	∭ S-	-112	SOUND	N/A		_		ASMD LKR		
C-104 SOUND O9/89 SN SX-102 SOUND N/A TY-103 ASMD LKR O2/83 JET C-105 SOUND O3/81 SN SX-103 SOUND N/A SY-104 ASMD LKR O2/83 JET C-107 SOUND O7/85 SN SX-106 SOUND N/A SY-106 ASMD LKR O2/83 JET C-107 SOUND O9/80 JET SX-106 SOUND N/A SY-106 ASMD LKR O2/83 JET C-108 ASMD LKR O7/79 SN SX-106 SOUND O5/00 JET (8) U-101 ASMD LKR O9/79 AR U-102 SOUND O8/80 JET SX-107 ASMD LKR O8/79 AR U-102 SOUND O9/80 JET SX-107 ASMD LKR O8/79 AR U-102 SOUND O9/80 JET SX-108 ASMD LKR O8/79 AR U-104 ASMD LKR O9/78 AR U-104 ASMD LKR O9/78 AR U-104 ASMD LKR O9/78 AR U-104 ASMD LKR O9/78 AR U-105 SOUND O9/80 JET (8) U-101 ASMD LKR O9/78 AR U-106 SOUND O9/80 JET (9) O9/80 JET SX-110 ASMD LKR O5/81 AR U-104 ASMD LKR O9/78 AR U-106 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-106 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-106 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-106 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-107 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-108 SOUND O3/91 JET (117 O9/80 ASMD LKR O9/79 AR U-108 SOUND O9/80 ASMD LKR O9/79 AR U-108 SOUND O9/80 ASMD LKR O9/79 AR U-108 SOUND O9/80 ASMD LKR O9/79 AR U-109 SOUND O9/80 AR U-106 ASMD LKR O9/80 ASMD LKR O9/79 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND O9/80 AR U-109 SOUND	3X-103	SOUND	11/63	AR(2)	S)	X-101	SOUND	N/A			TY-102	SOUND		AR
C-106 SOUND O7/96 SN SX-104 ASMD LKR O4/00 JET (7) TY-106 ASMD LKR O2/83 JET (-107 SOUND O9/90 JET SX-105 SOUND N/A TY-106 ASMD LKR 11/78 AR (-108 ASMD LKR O7/79 SN SX-106 SOUND O5/00 JET (8) U-101 ASMD LKR O9/79 AR (-109 SOUND O9/90 JET SX-107 ASMD LKR O8/79 AR U-102 SOUND O9/90 JET (-110 ASMD LKR O8/79 AR U-103 SOUND O9/90 JET (-111 ASMD LKR O3/96 JET SX-109 ASMD LKR O5/81 AR U-104 ASMD LKR 10/78 AR (-112 SOUND O9/90 JET (-112 SOUND O9/90 JET SX-100 ASMD LKR O5/81 AR U-104 ASMD LKR 10/78 AR (-112 SOUND O5/84 JET SX-111 ASMD LKR O7/79 AR U-106 SOUND O3/01 JET (114 SOUND O5/84 JET SX-112 ASMD LKR O7/79 AR U-107 SOUND O3/01 JET (114 SOUND O1/96 JET SX-112 ASMD LKR O7/79 AR U-107 SOUND N/A O1/96 JET SX-114 ASMD LKR O7/79 AR U-108 SOUND N/A O1/96 JET SX-114 ASMD LKR O7/79 AR U-109 SOUND N/A O1/96 ASMD LKR N/A SX-115 ASMD LKR O7/79 AR U-109 SOUND N/A O1/96 ASMD LKR N/A SX-116 ASMD LKR O9/78 AR U-109 SOUND N/A O1/96 ASMD LKR O7/79 JET T-102 SOUND O3/81 AR(2)(3) U-112 ASMD LKR O9/79 AR U-109 SOUND O8/79 AR O1/96 ASMD LKR O7/79 JET T-103 ASMD LKR O1/96 AR U-201 SOUND O8/79 AR O1/96 ASMD LKR O1/9779 AR U-202 SOUND O8/79 AR O1/979 AR U-203 SOUND O8/79 AR O1/979 AR U-204 SOUND O8/79 AR O1/979 AR U-204 SOUND O8/79 AR O1/979 AR U-204 SOUND O8/79 AR U-107 SOUND O8/79 AR U-108 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR U-109 SOUND O8/79 AR	3X-104	SOUND	09/89	SN	\$	X-102	SOUND	N/A		33X	TY-103	ASMD LKR		JET
C-107 SOUND O9/90 JET SX-105 SOUND N/A TY-106 ASMD LKR 11/78 AR ASMD LKR O7/79 SN SX-109 SOUND O5/00 JET (8) U-101 ASMD LKR O9/79 AR U-102 SOUND O8/90 JET SX-107 ASMD LKR O8/79 AR U-103 SOUND O9/90 JET (110 ASMD LKR O9/79 AR U-103 SOUND O9/90 JET (111 ASMD LKR O9/95 JET SX-109 ASMD LKR O6/81 AR U-104 ASMD LKR O9/78 AR ASMD LKR O9/79 AR U-104 ASMD LKR O9/78 AR U-105 SOUND O9/90 JET (112 SOUND O9/90 JET SX-110 ASMD LKR O6/79 AR U-104 ASMD LKR 10/78 AR ASMD LKR O9/79 AR U-106 SOUND O3/01 JET (117 O3/95 JET SX-111 ASMD LKR O7/79 AR U-106 SOUND O3/01 JET (117 O3/95 JET SX-112 ASMD LKR O7/79 AR U-108 SOUND O3/91 JET (117 O3/95 JET SX-113 ASMD LKR O7/79 AR U-108 SOUND N/A ASMD LKR O9/78 AR U-108 SOUND N/A ASMD LKR O9/78 AR U-109 SOUND N/A ASMD LKR O9/78 AR U-109 SOUND N/A ASMD LKR O9/78 AR U-109 SOUND N/A ASMD LKR O9/78 AR U-109 SOUND N/A ASMD LKR O9/79 AR U-109 SOUND N/A ASMD LKR O9/79 AR U-107 ASMD LKR O9/79 AR U-108 ASMD LKR O9/79 AR U-109 ASMD LKR O9/79 AR U-109 ASMD LKR O9/79 AR U-109 ASMD LKR O9/79 AR U-109 ASMD LKR O9/79 AR U-109 ASMD LKR O9/79 AR U-109 AR U-201 ASMD LKR O9/79 AR U-109 AR U-201 ASMD LKR O9/79 AR U-109 AR U-201 ASMD LKR O9/79 AR U-109 AR U-201 ASMD LKR O9/79 AR U-109 AR U-201 ASMD LKR O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-204 ASOUND O9/79 AR U-109 AR U-109 AR U-109 AR U-109 AR U-109	3X-106	SOUND	03/81	SN	(S)	X-103	SOUND	N/A		***	TY-104	ASMD LKR	11/83	AR
C-108 ASMD LKR O7/79 SN SX-108 SOUND O6/00 JET (8) U-101 ASMD LKR O9/79 AR (-109 SOUND O9/90 JET SX-107 ASMD LKR 10/79 AR U-102 SOUND O9/00 JET (-110 ASMD LKR O3/95 SN SX-108 ASMD LKR O6/79 AR U-103 SOUND O9/00 JET (-111 ASMD LKR O3/95 JET SX-109 ASMD LKR O6/79 AR U-104 ASMD LKR 10/78 AR U-101 ASMD LKR O5/95 AR U-104 ASMD LKR O5/95 AR U-106 SOUND O3/01 JET (112 ASMD LKR O5/95 AR U-106 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-108 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-107 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-107 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-107 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-107 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-108 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-108 SOUND O3/01 JET (112 ASMD LKR O5/79 AR U-109 SOUND O5/04 AR	3X-106	SOUND	07/95	SN	(8	X-104	ASMO LKR	04/00	JET (7)		TY-105	ASMD LKR	02/83	JET
C-109 SOUND 09/90 JET SX-107 ASMD LKR 10/79 AR U-102 SOUND N/A C-110 ASMD LKR 08/85 SN SX-108 ASMD LKR 08/79 AR U-103 SOUND 09/00 JET (C-111 ASMD LKR 03/95 JET SX-109 ASMD LKR 06/81 AR U-104 ASMD LKR 10/78 AR C-112 SOUND 08/90 JET SX-110 ASMD LKR 06/79 AR U-106 SOUND 03/01 JET (17-101 SOUND 06/94 JET SX-111 ASMD LKR 07/79 SN U-108 SOUND 03/01 JET (17-102 SOUND 04/95 JET SX-112 ASMD LKR 07/79 AR U-107 SOUND N/A C-103 ASMD LKR 11/87 JET SX-113 ASMD LKR 07/79 AR U-108 SOUND N/A C-104 SOUND 01/85 JET SX-114 ASMD LKR 11/78 AR U-108 SOUND N/A C-105 ASMD LKR N/A SX-115 ASMD LKR 07/79 AR U-109 SOUND N/A C-106 ASMD LKR N/A SX-116 ASMD LKR 09/78 AR U-109 SOUND N/A C-107 ASMD LKR N/A SX-116 ASMD LKR 09/78 AR U-110 ASMD LKR 12/84 AR C-108 ASMD LKR 07/79 JET T-101 ASMD LKR 04/93 SN U-111 SOUND N/A C-107 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR C-108 ASMD LKR 02/95 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR C-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 AR C-110 SOUND 01/95 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 AR C-111 SOUND 01/95 JET T-106 SOUND 06/97 AR U-203 SOUND 08/79 AR C-111 SOUND 01/95 JET T-106 SOUND 06/97 AR U-203 SOUND 08/79 AR C-111 SOUND 01/95 JET T-106 ASMD LKR 09/81 AR U-204 SOUND 08/79 AR C-112 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-112 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-113 SOUND 01/95 JET T-107 ASMD LKR 06/96 JET C-114 SOUND 01/95 JET T-107 ASMD LKR 06/96 JET C-115 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-116 SOUND 01/95 JET T-107 ASMD LKR 06/96 JET C-117 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-118 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-119 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET C-110 SOUND 06/84 JET T-108 ASMD LKR 06/96 JET C-111 SOUND 06/84 JET T-108 ASMD LKR 06/96 JET C-112 SOUND 06/84 JET T-108 ASMD LKR 06/96 JET C-113 SOUND 06/84 JET T-108 ASMD LKR 06/96 JET C-114 SOUND 06/97 AR 06/96 JET C-115 SOUND 06/97 AR 06/96 JET C-116 SOUND 06/97 AR 06/96 JET C-117 SOUND 06/97 AR 06/96 JET C-118 SOUND 06/97 AR 06/96 JET C-118	3X-107	SOUND	09/90	JET	\$	X-105	SOUND	N/A			TY-106	ASMD LKR	11/78	AR
C-110 ASMD LKR 08/85 SN SX-108 ASMD LKR 08/79 AR U-103 SOUND 09/00 JET (C-111 ASMD LKR 03/96 JET SX-109 ASMD LKR 06/81 AR U-104 ASMD LKR 10/78 AR (C-112 SOUND 09/90 JET SX-110 ASMD LKR 06/81 AR U-106 SOUND 03/01 JET (17/101 SOUND 06/84 JET SX-111 ASMD LKR 07/79 AR U-106 SOUND 03/01 JET (17/102 SOUND 06/84 JET SX-111 ASMD LKR 07/79 AR U-107 SOUND N/A (C-102 SOUND 04/96 JET SX-112 ASMD LKR 07/79 AR U-107 SOUND N/A (C-103 ASMD LKR 11/87 JET SX-113 ASMD LKR 07/79 AR U-107 SOUND N/A (C-104 SOUND 01/85 JET SX-114 ASMD LKR 07/79 AR U-109 SOUND N/A (C-106 ASMD LKR N/A SX-115 ASMD LKR 09/78 AR U-109 SOUND N/A (C-106 ASMD LKR N/A SX-115 ASMD LKR 09/78 AR U-100 SOUND N/A (C-107 ASMD LKR N/A T-101 ASMD LKR 04/93 SN U-111 SOUND N/A (C-108 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR (C-109 SOUND 07/97 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR (C-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 AR (C-109 SOUND 01/86 JET T-103 ASMD LKR 08/81 AR U-201 SOUND 08/79 AR (C-109 SOUND 01/86 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 AR (C-109 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 08/79 AR (C-109 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 08/79 SN (C-112 SOUND 06/84 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN (C-112 SOUND 06/84 JET T-107 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN (C-112 SOUND 06/84 JET T-107 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN (C-112 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET (C-108 ASM	3X-108	ASMD LKR	07/79	SN SN	\$	X-106	SOUND	06/00	JET (8)	*	U-101	ASMD LKR	09/79	AR
C-111	3X-109	SOUND	09/90	JET	(3	X-107	ASMD LKR	10/79	AR		U-102	SOUND	N/A	
SOUND O9/90 JET SX-110 ASMD LKR O9/79 AR U-105 SOUND O3/01 JET (17/101 SOUND O6/84 JET SX-111 ASMD LKR O7/79 SN U-108 SOUND O3/01 JET (17/102 SOUND O4/95 JET SX-112 ASMD LKR O7/79 AR U-107 SOUND N/A	3X-110	ASMD LKR	08/85	SN	∭ S>	X-108	ASMD LKR	08/79	AR	**	U-103	SOUND	09/00	JET (9
7-101 SOUND 05/84 JET SX-111 ASMD LKR 07/79 SN U-108 SOUND 03/01 JET (1: 7-102 SOUND 04/96 JET SX-112 ASMD LKR 07/79 AR U-107 SOUND N/A 7-103 ASMD LKR 11/97 JET SX-113 ASMD LKR 11/78 AR U-108 SOUND N/A 7-104 SOUND 01/86 JET SX-114 ASMD LKR 07/79 AR U-109 SOUND N/A 7-105 ASMD LKR N/A SX-115 ASMD LKR 09/78 AR U-109 SOUND N/A 7-106 ASMD LKR N/A T-101 ASMD LKR 04/93 SN U-111 SOUND N/A 7-107 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR 7-108 ASMD LKR 02/86 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 AR 7-110 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/86 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-106 ASMD LKR 06/96 JET 7-112 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-107 ASMD LKR 09/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-106 ASMD LKR 06/96 JET 7-108 ASMD LKR 09/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-108 ASMD LKR 05/96 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/84 JET T-107 ASMD LKR 06/96 JET 7-109 SOUND 06/97 AR T-10	3X-111	ASMD LKR	03/95	JET	₩ S>	X-109	ASMD LKR	05/81	AR	300 (U-104	ASMD LKR	10/78	AŘ
Not yet interim stabilized Not yet interi	X-112	SOUND	09/90	JET	≅ S≻	X-110	ASMD LKR	08/79	AR	***	U-105	SOUND	03/01	JET (11)
ASMD LKR	Y-101	SOUND	05/84	JET	(2	X-111	ASMD LKR	07/78	SN	900	U-106	SOUND	03/01	JET (12)
7-104 SOUND 01/85 JET SX-114 ASMD LKR 07/79 AR U-109 SOUND N/A 7-106 ASMD LKR N/A SX-115 ASMD LKR 09/78 AR U-110 ASMD LKR 12/84 AR 7-106 ASMD LKR N/A T-101 ASMD LKR 04/93 SN U-111 SOUND N/A 7-107 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR 7-108 ASMD LKR 02/85 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 SN 7-110 SOUND 01/85 JET T-105 SOUND 08/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/85 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-107 ASMD LKR 05/96 JET T-108 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-108 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 06/99 SN T-109 SOUND 06/99	Y-102	SOUND	04/95	JET	8 8 X	X-112	ASMD LKR	07/79	AR		U-107	SOUND	N/A	
Not yet interim stabilized Not yet interi	Y-103	ASMD LKR	11/97	JET	S)	X-113	ASMD LKR	11/78	AR		U-108	SOUND	N/A	
7-105 ASMO LKR N/A SX-115 ASMO LKR 09/78 AR U-110 ASMO LKR 12/84 AR 7-106 ASMO LKR N/A T-101 ASMO LKR 04/93 SN U-111 SOUND N/A 7-107 ASMO LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMO LKR 09/79 AR 7-108 ASMO LKR 02/85 JET T-103 ASMO LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 SN 7-110 SOUND 01/85 JET T-105 SOUND 06/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/85 JET T-106 ASMO LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMO LKR 06/96 JET T-107 ASMO LKR 06/96 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-107 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/84 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/98 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/98 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/98 JET T-108 ASMO LKR 06/96 JET T-109 SOUND 06/99 SN T-108 ASMO LKR 06/96 JET T-109 SOUND 06/99 SN T-108 ASMO LKR 06/96 JET T-109 SOUND 06/99 SN T-108 ASMO LKR 06/96 JET JET JET JET JET JET JET JET JET JET	Y-104	SOUND	01/85	JET	∰ S>	X-114	ASMD LKR	07/79	AR		U-109	SOUND		
7-106 ASMD LKR N/A T-101 ASMD LKR 04/93 SN U-111 SOUND N/A 7-107 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR 7-108 ASMD LKR 02/86 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 06/79 SN 7-110 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 06/79 AR 7-111 SOUND 01/86 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 06/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET GEND: AR = Administratively interim stabilized JET = Seltwell jet pumped to remove drainable interstitial liquid SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	Y-105	ASMO LKR	N/A				ASMD LKR	09/78						AR
7-107 ASMD LKR 07/79 JET T-102 SOUND 03/81 AR(2)(3) U-112 ASMD LKR 09/79 AR 7-108 ASMD LKR 02/86 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 SN 7-110 SOUND 01/86 JET T-106 SOUND 08/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/86 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET T-107 ASMD LKR 05/96 JET T-108 ASMD LKR 05/96 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-107 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-108 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-107 ASMD LKR 05/96 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 05/96 JET T-109 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/84 JET T-108 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN T-112 SOUND 08/79 AR T-112 SOUND 08/79 AR T-112 SOUND 08/79 AR T-113 SOUND 08/79 AR T-114 SOUND 08/79 AR T-115 SOUND 08/79 AR T-116 SOUND 08/79 AR T-117 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/79 AR T-118 SOUND 08/81 AR T-118 SOUND 08/79 AR T-118 SOUND 08/81 AR T-118 SOU	Y-106	ASMD LKR	N/A		∰ T-1	101	ASMD LKR		SN					
7-108 ASMD LKR 02/86 JET T-103 ASMD LKR 11/83 AR U-201 SOUND 08/79 AR 7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 06/79 SN 7-110 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/86 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET SOUND 06/84 JET T-107 ASMD LKR 05/96 JET SET T-107 ASMD LKR 05/96 JET SET T-107 ASMD LKR 05/96 JET SET T-107 ASMD LKR 05/96 JET T	Y-107	ASMD LKR		JET										AR
7-109 SOUND 07/97 JET T-104 SOUND 11/99 (4) JET U-202 SOUND 08/79 SN 7-110 SOUND 01/86 JET T-106 SOUND 06/87 AR U-203 SOUND 08/79 AR 7-111 SOUND 01/86 JET T-106 ASMD LKR 08/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET GEND: AR = Administratively interim stabilized AR = Administratively interim stabilized SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	Y-108	ASMD LKR												
7-110 BOUND 01/86 JET T-106 BOUND 06/87 AR U-203 BOUND 08/79 AR 7-111 BOUND 01/85 JET T-106 ASMD LKR 08/81 AR U-204 BOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET GEND: AR = Administratively interim stabilized AR = Administratively interim stabilized JET = Seltwell jet pumped to remove drainable interstitial liquid SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	Y-109	SOUND	07/97	JET	T-1	104								
7-111 SOUND 01/85 JET T-106 ASMD LKR 06/81 AR U-204 SOUND 08/79 SN 7-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET GEND: AR = Administratively interim stabilized Interim Stabilized Interim Stabilized Tanks 12 JET = Seltwell jet pumped to remove drainable interstitial liquid Not Yet Interim Stabilized 2 SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Tanks 14	Y-110	BOUND	01/86	JET	T-1	105	SOUND	06/87		_				AR
-112 SOUND 06/84 JET T-107 ASMD LKR 05/96 JET GEND: AR = Administratively interim stabilized Interim Stabilized Interim Stabilized Tanks 12 JET = Seltwell jet pumped to remove drainable interstitial liquid Not Yet Interim Stabilized 2 SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	Y-111	SOUND	01/85	JET	T-1	106	ASMD LKR	08/81		-				
GEND: AR = Administratively interim stabilized Interim Stabilized Tanks 12 JET = Seltwell jet pumped to remove drainable interstitial liquid Not Yet Interim Stabilized 2 SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	Y-112	SOUND	06/84	JET	∭ T-1	107								
AR = Administratively interim stabilized Interim Stabilized Interim Stabilized Tanks 12 JET = Saltwell jet pumped to remove drainable interstitial liquid Not Yet Interim Stabilized 2 SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks 14	EGEND:			E						-	·			
JET = Saltwell jet pumped to remove drainable interstitial liquid SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks		dministratively	interim et:	bilized						1	Interim St	ebilized Tenk		126
SN = Supernate pumped (Non-Jet pumped) N/A = Not yet interim stabilized Total Single-Shell Tanks			•		abla	interetis	ial liquid							21
N/A = Not yet interim stabilized Total Single-Shell Tanks 14			•			······································	inquit				1011	ann otavili	LUU	2.
·		•		r hamban	,						Total 9	Single-Shell T	Cenke .	140
VOILIR FI/1: - VESTING FAGVAI		•									10181	andio-autil	#1 IR.5	142
· I	ASIAID F	PIGIT - MOSGIII	EVERSI					•						

TABLE G-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (sheet 2 of 3)

Footnotes:

- (1) These dates indicate when the tanks were actually interim stabilized. In some cases, the official interim stabilization documents were issued at a later date.
- (2) Although tanks, BX-103, T-102 and T-112 met the interim stabilization administrative procedure at the time they were stabilized, they no longer meet the recently updated administrative procedure. The tanks were reevaluated in 1996 and memo 9654456, J. H. Wicks to Dr. J. K. McClusky, DOE-RL, dated September 1996, was issued which recommended that no further pumping be performed on these tanks, based on an economic evaluation.

Document RPP-5556, Rev. 0, "Updated Drainable Interstitial Liquid Volume Estimates for 119 Single-Shell Tanks Declared Stabilized," J. G. Field, February 7, 2000, states that five tanks no longer meet the stabilization criteria (BX-103, T-102, and T-112 exceed the supernate criteria, and BY-103 and C-102 exceed the DIL criteria).

An intrusion investigation was completed on tank B-202 in 1996 because of a detected increase in surface level. As a result of this investigation, it was determined that this tank no longer meets the recently updated administrative procedure for 200 series tanks.

- Original Interim Stabilization data are missing on four tanks: B-201, T-102, T-112, and T-201. Document HNF-SD-RE-TI-178, Rev. 7, dated February 9, 2001, added three additional tanks to those missing stabilization data: A-104, BX-101, and SX-115.
- (4) Tank 241-T-104 was Interim Stabilized on November 19, 1999. In-tank video taken October 7, 1999, shows the surface is clearly sludge-type waste with no saltcake present. No visible water on surface. Waste surface appears level across tank with numerous cracks. There is a minimal collapsed area around the saltwell screen, with no visible bottom.
- (5) Tank 241-T-110 was Interim Stabilized on January 5, 2000, due to major equipment failure. An in-tank video taken October 7, 1999 (pumping was discontinued on August 12, 1999), showed the surface of this tank as smooth, brown-tinted sludge with visible cracks.
- (6) Tank 241-S-103 was declared Interim Stabilized April 18, 2000. The surface is a rough, black and brown-colored waste with yellow patches of saltcake visible throughout. The surface appears to be damp but not saturated, and shows irregular cracking typically seen with surfaces beginning to dry out. A pool of supernatant liquid (10 feet in diameter, 5 feet deep, 1.0 Kgallons) is visible from video observations.
- (7) Tank 241-SX-104 was declared Interim Stabilized April 26, 2000, due to major equipment failure. The surface is a rough, yellowish gray saltcake waste with an irregular surface of visible cracks and shelves that were created as the surface dried out. The waste surface appears to be dry and shows no standing water within the tank.
- (8) Tank 241-SX-106 was declared Interim Stabilized May 5, 2000. The surface is a smooth, white-colored saltcake waste. The surface level slopes slightly from the tank sidewall down to a large depression in the center of the tank. A second depression surrounds both saltwell screens and an abandoned LOW. The waste surfaces appear dry and show no standing water within the tank.

TABLE G-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (sheet 3 of 3)

- (9) Tank 241-U-103 was declared Interim Stabilized September 11, 2000. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 30% of the waste surface is covered by the salt formations. The surface level slopes slightly from the tank sidewall down to the first of two depressions in the center of the tank. The waste surface appears dry and shows signs of drying and cracking due to saltwell pumping. LOW readings indicate an average adjusted ILL of 60.2 inches. There is a small pool of supernatant liquid estimated to be 500 gallons.
- (10) Tank 241-S-106 was declared Interim Stabilized on February 1, 2001. The surface is a rough, brown and yellow-colored saltcake waste with an irregular surface of mounds and saltcake crystals that were created as the surface was dried out. The waste surface appears to be dry and shows no standing water within the tank. There is no evidence of supernatant liquid from video observations. The waste surface slopes gradually from the tank sidewall to the depression in the center of the tank. The depression surrounds both of the saltwell screens, but does not extend around the temperature probe and ENRAF devices.
- (11) Tank 241-U-105 was declared Interim Stabilized on March 29, 2001, due to major equipment failure. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 15% of the surface is covered by the salt formations. The surface level slopes to the first of two depressions in the center of the tank; the first depression is cone shaped and estimated to be 22 feet in diameter. The second depression, inside the first, is cylindrically shaped and has a diameter of approximately 10 feet. Both depressions are centered on the saltwell screen. The waste surface appears dry and shows signs of cracking due to saltwell pumping. There is no visible liquid in the tank.
- (12) Tank 241-U-106 was declared Interim Stabilized on March 9, 2001. The surface is a dark brown/yellow colored waste that is covered with many stalagmite-type crystals growing on the surface. The crystals cover approximately 75% of the waste surface. The waste surface is irregular, appears dry, and shows only minimal signs of cracking due to saltwell pumping. The supernatant pool is estimated to be 13.3 feet in diameter based on the visible portion of the saltwell screen. The pool is centered on the saltwell screen.

TABLE G-2. SINGLE-SHELL TANK INTERIM STABILIZATION MILESTONES April 30, 2001 (sheet 1 of 2)

New single-shell tank interim stabilization milestones were negotiated in 1999 and are identified in the "Consent Decree." The Consent Decree was approved on August 16, 1999.

CONSENT DECREE Attachments A-1 and A-2

Following is the schedule for pumping liquid waste from the remaining twenty-nine (29) single-shell tanks. This schedule is enforceable pursuant to the terms of the Decree except for the "Project Pumping Completion Dates," which are estimates only and not enforceable. (Note: Schedule does not include C-106)

Tank		Projected Pumping	Actual Pumping	Projected Pumping	Interim Stabilization
Designation		Start Date	Start Date	Completion Date	Date
1.	T-104	Already initiated	March 24, 1996	May 30, 1999	November 19, 1999
2.	T-110	Already initiated	May 12, 1997	May 30, 1999	January 5, 2000
3.	SX-104	Already initiated	September 26, 1997	December 30, 2000	April 26, 2000
4.	SX-106	Already initiated	October 6, 1998	December 30, 2000	May 5, 2000
5.	S-102	July 31, 1999	March 18, 1999	March 30, 2001	
6.	S-106	July 31, 1999	April 16, 1999	March 30, 2001	February 1, 2001
7.	S-103	July 31, 1999	June 4, 1999	March 30, 2001	April 18, 2000
8.	U-103*	June 15, 2000	September 26, 1999	April 15, 2002	September 11, 2000
9.	U-105*	June 15, 2000	December 10, 1999	April 15, 2002	March 29, 2001
10.	U-102*	June 15, 2000	January 20, 2000	April 15, 2002	
11.	U-109*	June 15, 2000	March 11, 2000	April 15, 2002	
12.	A-101	October 30, 2000	May 6, 2000	September 30, 2003	
13.	AX-101	October 30, 2000	July 29, 2000	September 30, 2003	
14.	SX-105	March 15, 2001	August 8, 2000	February 28, 2003	
15.	SX-103	March 15, 2001	October 26, 2000	February 28, 2003	
16.	SX-101	March 15, 2001	November 22, 2000	February 28, 2003	
17.	U-106*	March 15, 2001	August 24, 2000	February 28, 2003	March 9, 2001
18.	BY-106	July 15, 2001		June 30, 2003	
19.	BY-105	July 15, 2001		June 30, 2003	
20.	U-108	December 30, 2001		August 30, 2003	
21.	U-107	December 30, 2001		August 30, 2003	
22.	S-111	December 30, 2001		August 30, 2003	
23.	SX-102	December 30, 2001		August 30, 2003	
24.	U-111	November 30, 2002		September 30, 2003	
25.	S-109	November 30, 2002	September 23, 2000	September 30, 2003	
26.	S-112	November 30, 2002		September 30, 2003	
27.	S-101	November 30, 2002		September 30, 2003	
28.	S-107	November 30, 2002		September 30, 2003	

^{29.} C-103

No later than December 30, 2000, DOE will determine whether the organic layer and pumpable liquids will be pumped from this tank together or separately, and will establish a deadline for initiating pumping of this tank. The parties will incorporate the initiation deadline into this schedule as provided in Section VI of the Decree.

ORP issued a letter to WDOE on December 22, 2000, meeting the requirements of this milestone.

^{*} Tanks containing organic complexants.

TABLE G-2. SINGLE-SHELL TANK INTERIM STABILIZATION MILESTONES (sheet 2 of 2)

<u>Completion of Interim Stabilization</u>. DOE will complete interim stabilization of all 29 single-shell tanks listed above by September 30, 2004.

Percentage of Pumpable Liquid Remaining to be Removed:

93% of Total Liquid	9/30/1999 (1)
38% of Organic Complexed Pumpable Liquids	9/30/2000 (2)
5% of Organic Complexed Pumpable Liquids	9/30/2001
18% of Total Liquid	9/30/2002
2% of Total Liquid	9/30/2003

The "percentage of pumpable liquid remaining to be removed" is calculated by dividing the volume of pumpable liquid remaining to be removed from tanks not yet interim stabilized by the sum of the total amount of liquid that has been pumped and the pumpable liquid that remains to be pumped from all tanks.

- (1) The Pumpable Liquid Remaining was reduced to 88%, by 9/30/99, exceeding this milestone. Reference LMHC-9957926 R1, D. I. Allen, LHMC RPP to D. C. Bryson, DOE-OPP, dated October 26, 1999
- (2) The Complexed Pumpable Liquid Remaining was reduced to 38%, by 9/15/00. Reference CHG-0004752, R. F. Wood, CHG, to J. J. Short, DOE-RPP, dated September 13, 2000.

TABLE G-3. SINGLE-SHELL TANKS STABILIZATION STATUS SUMMARY April 30, 2001

Partial Interim Isolated (PI)	intrusion Preve	ntion Completed (IP)	Interim Stab	IIIZEQ (13)
EAST AREA	EAST AREA	WEST AREA	EAST AREA	WEST AREA
A-101	A-103	S-104	A-102	S-103
A-102	§A-104	S-105	ẫA-103	S-104
	§A-105		A-104	S-105
AX-101	§A-106	SX-107	A-105	S-106
		SX-108	A-106	S-108
BY-102	AX-102	8X-109		S-110
BY-103	AX-103	SX-110	AX-102	
BY-105	AX-104	SX-111	AX-103	SX-104
BY-106		SX-112	AX-104	SX-108
BY-109	B-FARM - 16 tanks	SX-113		SX-107
	BX-FARM - 12 tanks	SX-114	B-FARM - 16 tanks	SX-108
C-103		SX-115	BX-FARM - 12 tanks	SX-109
C-105	BY-101			SX-110
C-106	BY-104	T-102	BY-101	SX-111
East Area 11	BY-107	T-103	BY-102	SX-112
	BY-108	T-105	BY-103	SX-113
WEST AREA	BY-110	T-106	BY-104	SX-114
S-101	BY-111	T-108	BY-107	
	& = · · · · ·		38	SX-115
S-102	BY-112	T-109	BY-108	4041
S-103		T-112	BY-109	T-Farm - 16 tanks
S-106	C-101	T-201	BY-110	TX-FARM - 18 tanks
S-107	C-102	T-202	BY-111	TY-FARM - 6 tanks
S-108	C-104	T-203	BY-112	
S-109	ਊ C-107	T-204		U-101
S-110	C-108		C-101	U-103
S-111	C-109	TX-FARM - 18 tanks	§C-102	U-104
S-112	C-110	TY-FARM - 6 tanks	§C-104	U-105
	C-111		© C-105	U-106
SX-101	C-112	U-101	§C-107	U-110
SX-102	C-201	U-104	€C-108	U-112
SX-103	€ C-202	U-112	§C-109	U-201
SX-104	C-203	U-102	§C-110	U-202
SX-105	C-204	U-202	§ C-111	U-203
SX-106	ELEKTO SI	U-203	®C-112	U-204
		Ü-204	©-201	West Area (
T-101		West Area 53		7511
T-104		1600 (G)	C-203	
T-107			C-204	
T-110			East Area 60	
T-111				***
1-111				
11.400	Controlled, Clean, a	and Stable (CCS)		
U-102	S CONTROLLED, CICAN, 8	IN STRING (COS)		
U-103	S FACT ABEA	WEST ADE		
U-105	EAST AREA	WEST AREA		
U-106	BX-FARM - 12 Tanks	TX-FARM - 18 tanks		
U-107	3	TY FARM - 6 tanks		
U-108	EACH, 100 12	Welkin 2		
U-109				
U-110				
U-111	Note: CCS activities			
West Area 29	until funding is availa	ıble.		
Total 40	_			

This page intentionally left blank.

APPENDIX H

TANKS AND EQUIPMENT CODE AND STATUS DEFINITIONS

TABLE H - 1. TANK AND EQUIPMENT CODE/STATUS DEFINITIONS April 30, 2001

1. TANK STATUS CODES

WASTE TYPE (also see definitions, section 2 below)

AW	Aging Waste (Neutralized Current Acid Waste [NCAW])
CC	Complexant Concentrate Waste
CP	Concentrated Phosphate Waste
DC	Dilute Complexed Waste
DN	Dilute Non-Complexed Waste
DSS	Double-Shell Slurry
DSSF	Double-Shell Slurry Feed
NCPLX	Non-Complexed Waste
PD	Plutonium-Uranium Extraction (PUREX) Neutralized Cladding
	Removal Waste (NCRW), transuranic waste (TRU)

TANK USE (DOUBLE-SHELL TANKS ONLY)

CWHT	Concentrated Waste Holding Tank
DRCVR	Dilute Receiver Tank
EVFD	Evaporate Feed Tank
SRCVR	Slurry Receiver Tank

2. **DEFINITIONS**

WASTE TANKS - GENERAL

Waste Tank Safety Issue

A potentially unsafe condition in the handling of waste material in underground storage tanks that requires corrective action to reduce or eliminate the unsafe condition.

Watch List Tank

An underground storage tank containing waste that requires special safety precautions because it may have a serious potential for release of high level radioactive waste because of uncontrolled increases in temperature or pressure. Special restrictions have been placed on these tanks by "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the *National Defense Authorization Act for Fiscal Year 1991*, November 5, 1990, Public Law 101-510, (also known as the Wyden Amendment).

Characterization

Characterization is understanding the Hanford tank waste chemical, physical, and radiological properties to the extent necessary to insure safe storage and interim operation, and ultimate disposition of the waste.

WASTE TYPES

Aging Waste (AW)

High level, first cycle solvent extraction waste from the PUREX plant (NCAW)

Concentrated Complexant (CC)

Concentrated product from the evaporation of dilute complexed waste.

Concentrated Phosphate Waste (CP)

Waste originating from the decontamination of the N Reactor in the 100 N Area. Concentration of this waste produces concentrated phosphate waste.

Dilute Complexed Waste (DC)

Characterized by a high content of organic carbon including organic complexants: ethylenediamineterraacetic acid (EDTA), citric acid, and hydroxyethyl-ethylenediaminetriacetic acid (HEDTA), being the major complexants used. Main sources of DC waste in the DST system are saltwell liquid inventory (from SSTs).

Dilute Non-Complexed Waste (DN)

Low activity liquid waste originating from T and S Plants, the 300 and 400 Areas, PUREX facility (decladding supernatant and miscellaneous wastes), 100 N Area (sulfate waste), B Plant, saltwells, and PFP (supernate).

Double-Shell Slurry (DSS)

Waste that exceeds the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. For reporting purposes, DSS is considered a solid.

Double-Shell Slurry Feed (DSSF)

Waste concentrated just before reaching the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. This form is not as concentrated as DSS.

Non-complexed (NCPLX)

General waste term applied to all Hanford Site (NCPLX) liquors not identified as complexed.

PUREX Decladding (PD)

PUREX Neutralized Cladding Removal Waste (NCRW) is the solids portion of the PUREX plant neutralized cladding removal waste stream; received in Tank Farms as a slurry. NCRW solids are classified as transuranic (TRU) waste.

Drainable Interstitial Liquid (DIL)

Interstitial liquid that is not held in place by capillary forces, and will therefore migrate or move by gravity. (See also Section 4 below)

Supernate

The liquid above the solids or in large liquid pools covered by floating solids in waste storage tanks. (See also Section 4 below)

Ferrocvanide

A compound of iron and cyanide commonly expressed as FeCN. The actual formula for the ferrocyanide anion is $[Fe(CN)_6]^4$.

INTERIM STABILIZATION (Single-Shell Tanks only)

Interim Stabilized (IS)

A tank which contains less than 50 Kgallons of drainable interstitial liquid and less than 5 Kgallons of supernatant liquid. If the tank was jet pumped to achieve interim stabilization, then the jet pump flow or saltwell screen inflow must also have been at or below 0.05 gpm before interim stabilization criteria is met

Jet Pump

The jet pump system includes 1) a jet assembly with foot valve mounted to the base of two pipes that extend from the top of the well to near the bottom of the well casing inside the saltwell screen, 2) a centrifugal pump to supply power fluid to the down-hole jet assembly, 3) flexible or rigid transfer jumpers, 4) a flush line, and 5) a flowmeter. The jumpers contain piping, valves, and pressure and limit switches.

The centrifugal pump and jet assembly are needed to pump the interstitial liquid from the saltwell screen into the pump pit, nominally a 40-foot elevation rise. The power fluid passes through a nozzle in the jet assembly and acts to convert fluid pressure head to velocity head, thereby reducing the pressure in the jet assembly chamber. The reduction in pressure allows the interstitial liquid to enter the jet assembly chamber and mix with the power fluid. Velocity head is converted to pressure head above the nozzle, lifting power fluid, and interstitial liquid to the pump pit. Pumping rates vary from 0.05 gallons to about 4 gpm.

Saltwell Screen

The saltwell system is a 10-inch diameter saltwell casing consisting of a stainless steel saltwell screen welded to a Schedule 40 carbon steel pipe. The casing and screen are to be inserted into the 12-inch tank riser located in the pump pit. The stainless steel screen portion of the system will extend through the tank waste to near the bottom of the tank. The saltwell screen portion of the casing is an approximately 10-foot length of 300 Series, 10-inch diameter, stainless steel pipe with screen openings (slots) of 0.05 inches.

Emergency Pumping Trailer

A 45-foot tractor-type trailer is equipped to provide storage space and service facilities for emergency pumping equipment: this consists of two dedicated jet pump jumpers and two jet pumps, piping and dip tubes for each, two submersible pumps and attached piping, and a skid-mounted Weight Factor Instrument Enclosure (WFIE) with an air compressor and electronic recording instruments. The skid also contains a power control station for the pumps, pump pit leak detection, and instrumentation. A rack for over 100 feet of overground double-contained piping is also in the trailer.

INTRUSION PREVENTION (ISOLATION) Single-Shell Tanks only

Partially Interim Isolated (PI)

The administrative designation reflecting the completion of the physical effort required for Interim Isolation except for isolation of risers and piping that is required for jet pumping or for other methods of stabilization.

Interim Isolated (II)

The administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. In June 1993, Interim Isolation was replaced by Intrusion Prevention.

Intrusion Prevention (IP)

Intrusion Prevention is the administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. Under no circumstances are electrical or instrumentation devices disconnected or disabled during the intrusion prevention process (with the exception of the electrical pump).

Controlled, Clean, and Stable (CCS)

Controlled, Clean, and Stable reflects the completion of several objectives: "Controlled" - provide remote monitoring for required instrumentation and implement controls required in the TWRS Authorization Basis; "Clean" - remove surface soil contamination and downpost the Tank Farms to RBA/URMA/RA radiological control status, remove abandoned equipment, and place reusuable equipment in compliant storage; and "Stable" - remove pumpable liquids from the SSTs and IMUSTs and isolate the tanks.

TANK INTEGRITY

Sound

The integrity classification of a waste storage tank for which surveillance data indicate no loss of liquid attributed to a breach of integrity.

Assumed Leaker

The integrity classification of a waste storage tank for which surveillance data indicate a loss of liquid attributed to a breach of integrity.

Assumed Re-Leaker

A condition that exists after a tank has been declared as an "assumed leaker" and then the surveillance data indicates a new loss of liquid attributed to a breach of integrity.

TANK INVESTIGATION

Intrusion

A term used to describe the infiltration of liquid into a waste tank.

SURVEILLANCE INSTRUMENTATION

Drywells

Historically, the drywells were monitored with gross logging tools as part of a secondary leak monitoring system. In some cases, neutron-moisture sensors were used to monitor moisture in the soil as a function of well depth, which could be indicative of tank leakage. The routine gross gamma logging data were stored electronically from 1974 through 1994. The routine gross gamma logging program ended in 1994. A program was initiated in 1995 to log each of the available drywells in each tank farm with a spectral gamma logging system. The spectral gamma logging system provides quantitative values for gamma-emitting radionuclides. The baseline spectral gamma logging database is available electronically.

Repeat spectral drywell scans are not part of the established Tank Farm leak detection program, but can be run on request if special needs arise. A select subset of drywells is routinely monitored by the Vadose Zone Characterization Project to assess movement of gamma-emitting radionuclides in the subsurface.

Laterals

Laterals are horizontal drywells positioned under single-shell waste storage tanks to detect radionuclides in the soil which could be indicative of tank leakage. These drywells can be monitored by radiation detection probes. Laterals are 4-inch inside diameter steel pipes located 8 to 10 feet below the tank's concrete base. There are three laterals per tank. Laterals are located only in A and SX farms. There are currently no functioning laterals and no plan to prepare them for use.

Surface Levels

The surface level measurements in all waste storage tanks are monitored by manual or automatic conductivity probes, and recorded and transmitted or entered into the Surveillance Analysis Computer System (SACS).

Automatic FIC

An automatic waste surface level measurement device is manufactured by the Food Instrument Company (FIC). The instrument consists of a conductivity electrode (plummet) connected to a calibrated steel tape, a steel tape reel housing and a controller that automatically raises and lowers the plummet to obtain a waste surface level reading. The controller can provide a digital display of the data and until February 1999, the majority of the FICs transmitted readings to the CASS. Since CASS retirement, all FIC gauges are read manually. FICs are being replaced by ENRAF detectors (see below).

ENRAF 854 ATG Level Detector

FICs and some manual tapes are in the process of being replaced by the ENRAF ATG 854 level detector. The ENRAF gauge, fabricated by ENRAF Incorporated, determines waste level by detecting variations in the weight of a displacer suspended in the tank waste. The displacer is connected to a wire wound onto a precision measuring drum. A level causes a change in the weight of the displacer which will be detected by the force transducer. Electronics within the gauge causes the servo motor to adjust the position of the displacer and compute the tank level based on the new position of the displacer drum. The gauge displays the level in decimal inches. The first few ENRAFs that received remote reading capability transmit liquid level data via analog output to the Tank Monitor and Control System (TMACS). The remaining ENRAFs and future installations will transmit digital level data to TMACS via an ENRAF Computer Interface Unit (CIU). The CIU allows fully remote communication with the gauge, minimizing tank farm entry.

Annulus

The annulus is the space between the inner and outer shells on DSTs only. Drain channels in the insulating and/or supporting concrete carry any leakage to the annulus space where conductivity probes are installed. The annulus conductivity probes and radiation detectors are the primary means of leak detection for all DSTs.

Liquid Observation Well (LOW)

In-tank liquid observation wells are used for monitoring the interstitial liquid level (ILL) in single-shell waste storage tanks. The wells are usually constructed of fiberglass or TEFZEL-reinforced epoxy-polyester resin (TEFZEL, a trademark of E. I. du Pont de Nemours & Company). There are a few LOWs constructed of steel. LOWs are sized to extend to within 1 inch of the bottom of the waste tank, are sealed at their bottom ends and have a nominal outside diameter of 3.5 inches. Two probes are used to monitor changes in the ILL; gamma and neutron, which can indicate intrusions or leakage by increases or decreases in the ILL. There are 65 LOWs (64 are in operation) installed in SSTs that contain or are capable of containing greater than 50 Kgallons of drainable interstitial liquid, and in two DSTs only. The LOWs installed in two DSTs, (SY-102 and AW-103 tanks), are used for special, rather than routine, surveillance purposes only.

Thermocouple (TC)

A thermocouple is a thermocouple device used to measure temperature. More than one thermocouple on a device (probe) is called a thermocouple tree. In DSTs there may be one or more thermocouple trees in risers in the primary tank. In addition, in DSTs only, there are thermocouple elements installed in the insulating concrete, the lower primary tank knuckle, the secondary tank concrete foundation, and in the outer structural concrete.

These monitor temperature gradients within the concrete walls, bottom of the tank, and the domes. In SSTs, one or more thermocouples may be installed directly in a tank, although some SSTs do not have any trees installed. A single thermocouple (probe) may be installed in a riser, or lowered down an existing riser or LOW. There are also four thermocouple laterals beneath Tank 105-A in which temperature readings are taken in 34 thermocouples.

In-tank Photographs and Videos

In-tank photographs and videos may be taken to aid in resolving in-tank measurement anomalies and determine tank integrity. Photographs and videos help determine sludge and liquid levels by visual examination.

TERMS/ACRONYMS

<u>CCS</u> Controlled, Clean and Stable (tank farms)

FSAR Final Safety Analysis Report (replaces BIOS, effective October 18, 1999)

II Interim Isolated

IP Intrusion Prevention Completed

IS Interim Stabilized

MT/FIC/ENRAF Manual Tape, Food Instrument Corporation, ENRAF Corporation (surface level measurement devices)

OSD Operating Specifications Document

PI Partial Interim Isolated

SAR Safety Analysis Reports

SHMS Standard Hydrogen Monitoring System

TMACS Tank Monitor and Control System

<u>TPA</u> Hanford Federal Facility Consent and Compliance Order, "Washington State Department of

Ecology, U. S. Environmental Protection Agency, and U. S. Department of Energy," Fourth

Amendment, 1994 (Tri-Party Agreement)

TSR Technical Safety Requirements

USO Unreviewed Safety Question

Wyden Amendment "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the National Defense Authorization Act for Fiscal Year 1991, November 5, 1990, Public Law 101-510.

3. <u>INVENTORY AND STATUS BY TANK - COLUMN VOLUME CALCULATIONS AND DEFINITIONS FOR TABLE A-6 (SINGLE-SHELL TANKS)</u>


COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS		
Total Waste	Solids volume plus Supernatant liquid. Solids include sludge and saltcake (see definitions below).		
Supernate (1)	May be either measured or estimated. Supernate is either the estimated or measured liquid floating on the surface of the waste or under a floating solids crust. In-tank photographs or videos are useful in estimating the liquid volumes; liquid floating on solids and core sample data are useful in estimating large liquid pools under a floating crust.		
Drainable Interstitial Liquid (DIL) (1)	This is initially calculated. Drainable interstitial liquid is calculated based on the saltcake and sludge volumes, using calculated porosity values from past pumping or actual data for each tank. Interstitial liquid is liquid that fills the interstitial spaces of the solids waste. The sum of the interstitial liquid contained in saltcake and sludge minus an adjustment for capillary height is the initial volume of drainable interstitial liquid.		


COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS
Pumped This Month	Net total gallons of liquid pumped from the tank during the month. If supernate is present, pump production is first subtracted from the supernatant volume. The remainder is then subtracted from the drainable interstitial liquid volume.
Total Pumped (1)	Cumulative net total gallons of liquid pumped from 1979 to date.
Drainable Liquid Remaining (DLR) (1)	Supernate plus Drainable Interstitial Liquid. The total Drainable Liquid Remaining is the sum of drainable interstitial liquid and supernate.
Pumpable Liquid Remaining (PLR) (1)	<u>Drainable Liquid Remaining minus unpumpable volume</u> . Not all drainable interstitial liquid is pumpable.
Sludge	Solids formed during sodium hydroxide additions to waste. Sludge usually was in the form of suspended solids when the waste was originally received in the tank from the waste generator. In-tank photographs or videos may be used to estimate the volume.
Saltcake	Results from crystallization and precipitation after concentration of liquid waste, usually in an evaporator. If saltcake is layered over sludge, it is only possible to measure total solids volume. In-tank photographs or videos may be used to estimate the saltcake volume.
Solids Volume Update	Indicates the latest update of any change in the solids volume.
Solids Update Source - See Footnote	Indicates the source or basis of the latest solids volume update.
Last In-tank Photo	Date of last in-tank photographs taken.
Last In-tank Video	Date of last in-tank video taken.
See Footnotes for These Changes	Indicates any change made the previous month. A footnote explanation for the change follows the Inventory and Status by Tank Appendix (Table E-6).

⁽¹⁾ As pumping continues, supernate, DIL, DLR, PLR, and total gallons pumped are adjusted accordingly based on actual pump volumes.

APPENDIX I

TANK FARM CONFIGURATION, STATUS AND FACILITIES CHARTS



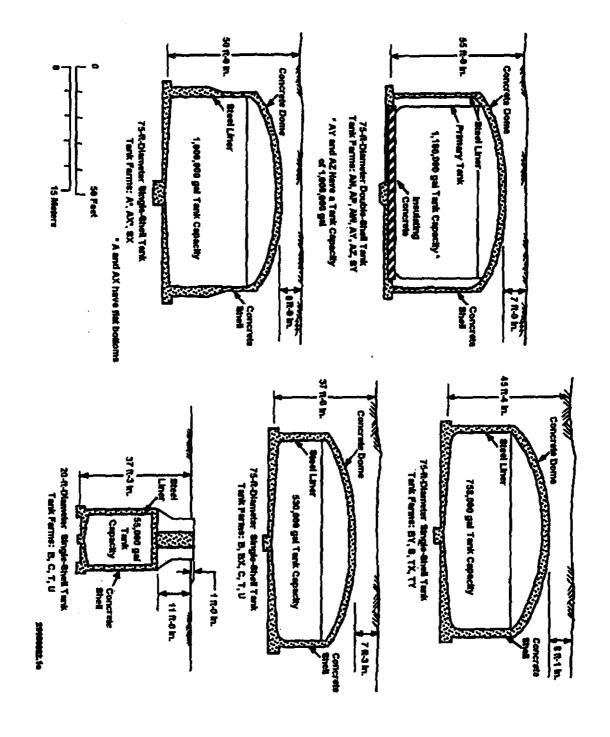

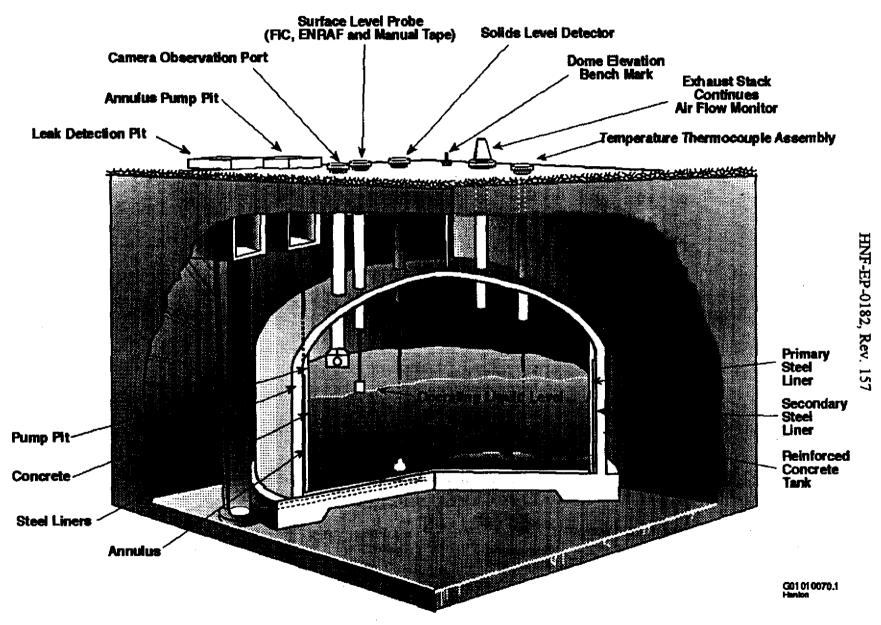


Figure I-2. Double-Shell Tank Instrumentation Configuration

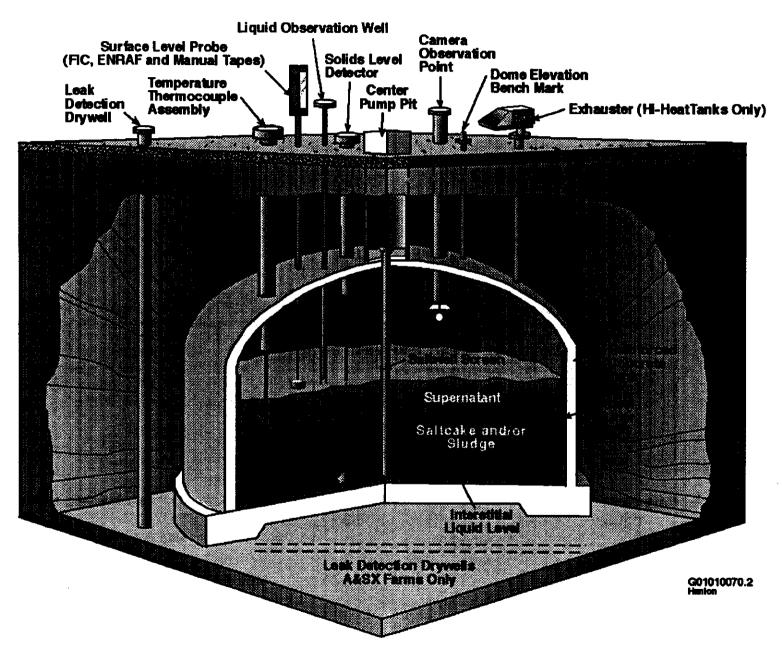


Figure I-3. Single-Shell Tank Instrumentation Configuration

THE TANK FARM FACILITIES CHARTS (colored foldouts)

ARE ONLY BEING INCLUDED IN THIS REPORT ON A QUARTERLY BASIS

(i.e., months ending March 31, June 30, September 30, and December 31)

NOTE: COPIES OF THE FACILITES CHARTS CAN BE OBTAINED FROM DENNIS BRUNSON, LMSI MULTI-MEDIA SERVICES 376-2345, G3-51

ALMOST ANY SIZE IS AVAILABLE, WHICH CAN BE LAMINATED

P-CARD IS REQUIRED

This page intentionally left blank

DISTRIBUTION

Number of copies

OFFSITE - USA

2 Congress of the United States

U. S. Senate

717 Hart Senate Building Washington D.C. 20510

Senator Ron Wyden

U. S. House of Representatives 1323 Longworth House Office Building Washington D. C. 20515

Congressman Richard "Doc" Hastings, 4th District Atten: Jeff Markey

4 <u>U. S. Department of Energy-Headquarters</u>

1000 Independence Avenue, SW Washington, D. C. 20585

H. Calley

EM-38 Cloverleaf Bldg.

Willam M. Levitan

EM-1 FORS/5A-014

U. S. Department of Energy-Headquarters

19901 Germantown Rd Germantown, MD 20874

Kurt Juroff

EM-44

Ralph Lightener

EM-44

1 <u>U. S. Nuclear Regulatory Commission</u>

Division of Fuel Cycle, Safeguards & Security Mail Stop T8-A33

Mail Stop T8-A33 Washington, DC 20555

Robert Pierson, Chief FSPB/FCSS (ADDRESSEE ONLY)

1 Washington State Department of Ecology

Nuclear Waste Program 300 Desmond Drive Lacey, WA 98504

Roger Stanley

1 Washington State Department of Health

Radiation Protection 7171 Cleanwater Lane P. O. Box 47827 Olympia, WA 98504-7827

Allen W. Conklin

1 Oregon State Department of Energy 625 Marion St. NE, Suite 1 Salem, OR 97301 Dirk Dunning Do not remove from distribution without permission from ODOE 1 Oak Ridge National Laboratory P. O. Box 2008 Oak Ridge, TN 37831-6180 C. Forsberg MS-6180 1 Donald T. Oakley 9612 Hall Road Potomac, MD 20854 1 Foster-Miller, Inc. Power Systems Technology Group 350 Second Avenue Waltham, MA 02451-1196 Maureen Williams 1 **MACTEC** 8310 Centerbrook Place Alexandra, VA 22308 Stanley Blacker, Vice President 1 Framatome Advanced Nuclear Power 3315 Old Forrest Rd Lynchburg, VA 24506 Brian Butler TRI-CITIES: **ARES Corporation** 1 636 Jadwin Ave., Suite B Richland, WA 99352 1 **Babad Technical Services** 2540 Cordoba Court Richland, WA 99352 Wastren Inc. l 1050 Gilmore Ave, Suite C Richland, WA 99352 Gary Dunford **ONSITE BAT** R. T. Winward

Ġ

1

H6-60

1	MACTEC - ERS J. F. Bertsch	B1-42	
1 .	General Accounting Office C. R. Abraham	A1-80	
1	Washington State Department of Library	Ecology B5-18	
1	U. S. Environmental Protection A. D. R. Sherwood	Agency B5-01	
7	U.S. Department of Energy		
	D. C. Bryson Wen-Shou Liou J. Polehn M. J. Royack A. B. Sidpara D. J. Williams Reading Room	H6-60 H6-60 H6-60 H6-60 H6-60 H2-53	
2	Pacific National Northwest Labo	ratories	
	J. L. Huckaby B. E. Opitz	K7-15 K6-75	
86	CH2M Hill (CHG), and Affiliated Companies		
	D. I. Allen J. C. Ailen-Floyd K. M. Bowen V. C. Boyles D. L. Carlile R. J. Cash C. Defigh-Price M. P. Delozier M. L. Dexter (12) R. A. Dodd A. F. Erhart S. D. Estey J. G. Field L. A. Fort K. D. Fowler G. T. Frater J. R. Freeman-Pollard J. S. Garfield B. C. Gooding B. M. Hanlon (8) D.C. Hedengren C. C. Hendersen B. A. Higley S. W. Hildreth K. M. Hodgson T. M. Hohl B. A. Johnson G. D. Johnson G. D. Johnson T. E. Jones	S5-07 H6-06 R2-12 R2-11 T4-07 R1-44 T4-08 H6-08 R1-51 S5-07 R3-73 R2-11 R2-12 R2-12 R2-12 R2-11 T4-08 R1-57 L4-07 T4-07 T4-07 R3-73 B2-05 R3-73 B2-05 R3-73 T4-07 R2-14 R3-73 S7-02 R1-44 HO-22	

J. Kalia	R1-43
M. R. Kembel	S7-03
R. A. Kirkbride	R3-73
P. F. Kison	T4-07
N. W. Kirch	R2-11
J. S. Konyu	S7-64
G. M. Koreski	R2-11
J. G. Kristofzski	R2-50
J. A. Lechelt	R2-11
P. Ohl	H4-01
T. May	R2-11
M. A. Payne	H6-63
R. E. Pohto	R2-84
R. E. Raymond (2)	T4-08
W. E. Ross	S7-83
N. J. Scott-Proctor	S5-00
P. P. Sederburg	R2-50
J. N. Strode	R3-73
D. D. Taylor	H6-64
R. R. Thompson	T4-08
D. T. Vladimiroff	S7-20
L. R. Webb (10)	R1-10
Central Files	B1-07
200 West Shift Office	T4-00
200 East Shift Office	S5-04
Environmental	
Data Mgmt Center (2)	H6-08
Unified Dose Assessment	
Center (UDAC)	A0-20
Document Processing Center	A3-94
• • • • • • • • • • • • • • • • • • • •	
