


ENGINEERING CHANGE NOTICE

Page 1 of 21. ECN **671068**Proj.
ECN

2. ECN Category (mark one) Supplemental <input type="checkbox"/> Direct Revision <input checked="" type="checkbox"/> Change ECN <input type="checkbox"/> Temporary <input type="checkbox"/> Standby <input type="checkbox"/> Supersedeure <input type="checkbox"/> Cancel/Void <input type="checkbox"/>		3. Originator's Name, Organization, MSIN, and Telephone No. B. M. Hanlon, Inventory & Flowsheet Eng. R3-72, 373-2053		4. USQ Required? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No		5. Date 01/07/02	
		6. Project Title/No./Work Order No. Waste Tank Summary Report for Month Ending November 30, 2001		7. Bldg./Sys./Fac. No. N/A		8. Approval Designator N/A	
		9. Document Numbers Changed by this ECN (includes sheet no. and rev.) HNF-EP-0182, Rev. 163		10. Related ECN No(s). N/A		11. Related PO No. N/A	
12a. Modification Work <input type="checkbox"/> Yes (fill out Bk. 12b) <input checked="" type="checkbox"/> No (NA Bk. 12b, 12c, 12d)		12b. Work Package No. N/A		12c. Modification Work Completed N/A Design Authority/Cog. Engineer Signature & Date		12d. Restored to Original Condition (Temp. or Standby ECNs only) N/A Design Authority/Cog. Engineer Signature & Date	
13a. Description of Change Complete revision				13b. Design Baseline Document? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No			
<div style="text-align: right;">  RECEIVED MAR 25 2002 EDMC </div> <p>Computer generated:</p> <p>File: \\AP001\CHG-DOC-TRANSFER-TEMP-HNF-EP-0182-1590 KB 1,593 KB 1,587 KB</p> <p>Size: 1.55 MB (1,628,160) bytes 1,630,720 bytes 1,624,576 bytes</p> <p>Modified: Wednesday, JANUARY 16, 2002 3:51:30 PM</p> <p>Thursday, Jan 17, 2002 12:35:06 PM</p> <p>Monday, Feb 4, 2002 10:23:05 AM</p>							
14a. Justification (mark one) Criteria Change <input type="checkbox"/> Design Improvement <input type="checkbox"/> Environmental <input type="checkbox"/> Facility Deactivation <input type="checkbox"/> As-Found <input type="checkbox"/> Facilitate Const. <input type="checkbox"/> Const. Error/Omission <input type="checkbox"/> Design Error/Omission <input type="checkbox"/>		14b. Justification Details This ECN is being generated to update waste tank farm summary information.					
15. Distribution (include name, MSIN, and no. of copies) Distribution list attached following document Also: Electronic copy to John Vann only							

RELEASE STAMP

FEB 04 2002

DATE:

STA: 4

HANFORD
RELEASE

ENGINEERING CHANGE NOTICE

Page 2 of 2

1. ECN (use no. from pg. 1)

671068

16. Design Verification Required

☐ Yes

☒ No

17. Cost Impact

ENGINEERING

Additional ☐ \$ _____

Savings ☐ \$ _____

CONSTRUCTION

Additional ☐ \$ _____

Savings ☐ \$ _____

18. Schedule Impact (days)

Improvement ☐ _____

Delay ☐ _____

19. Change Impact Review: Indicate the related documents (other than the engineering documents identified on Side 1) that will be affected by the change described in Block 13. Enter the affected document number in Block 20.

SDD/DD	<input type="checkbox"/>	Seismic/Stress Analysis	<input type="checkbox"/>	Tank Calibration Manual	<input type="checkbox"/>
Functional Design Criteria	<input type="checkbox"/>	Stress/Design Report	<input type="checkbox"/>	Health Physics Procedure	<input type="checkbox"/>
Operating Specification	<input type="checkbox"/>	Interface Control Drawing	<input type="checkbox"/>	Spares Multiple Unit Listing	<input type="checkbox"/>
Criticality Specification	<input type="checkbox"/>	Calibration Procedure	<input type="checkbox"/>	Test Procedures/Specification	<input type="checkbox"/>
Conceptual Design Report	<input type="checkbox"/>	Installation Procedure	<input type="checkbox"/>	Component Index	<input type="checkbox"/>
Equipment Spec.	<input type="checkbox"/>	Maintenance Procedure	<input type="checkbox"/>	ASME Coded Item	<input type="checkbox"/>
Const. Spec.	<input type="checkbox"/>	Engineering Procedure	<input type="checkbox"/>	Human Factor Consideration	<input type="checkbox"/>
Procurement Spec.	<input type="checkbox"/>	Operating Instruction	<input type="checkbox"/>	Computer Software	<input type="checkbox"/>
Vendor Information	<input type="checkbox"/>	Operating Procedure	<input type="checkbox"/>	Electric Circuit Schedule	<input type="checkbox"/>
OM Manual	<input type="checkbox"/>	Operational Safety Requirement	<input type="checkbox"/>	ICRS Procedure	<input type="checkbox"/>
FSAR/SAR	<input type="checkbox"/>	IEFD Drawing	<input type="checkbox"/>	Process Control Manual/Plan	<input type="checkbox"/>
Safety Equipment List	<input type="checkbox"/>	Cell Arrangement Drawing	<input type="checkbox"/>	Process Flow Chart	<input type="checkbox"/>
Radiation Work Permit	<input type="checkbox"/>	Essential Material Specification	<input type="checkbox"/>	Purchase Requisition	<input type="checkbox"/>
Environmental Impact Statement	<input type="checkbox"/>	Fac. Proc. Samp. Schedule	<input type="checkbox"/>	Tickler File	<input type="checkbox"/>
Environmental Report	<input type="checkbox"/>	Inspection Plan	<input type="checkbox"/>		<input type="checkbox"/>
Environmental Permit	<input type="checkbox"/>	Inventory Adjustment Request	<input type="checkbox"/>		<input type="checkbox"/>

20. Other Affected Documents: (NOTE: Documents listed below will not be revised by this ECN.) Signatures below indicate that the signing organization has been notified of other affected documents listed below.

Document Number/Revision

Document Number/Revision

Document Number/Revision

N/A

21. Approvals

Signature

Date

Signature

Date

Design Authority _____

Design Agent _____

Cog. Eng. B.M. Hanlon *B.M. Hanlon* 1/7/02

PE _____

Cog. Mgr. N.W. Kirch *N.W. Kirch* 1/17/02

QA _____

QA _____

Safety _____

Safety _____

Design _____

Environ. _____

Environ. _____

Other _____

Other _____

DEPARTMENT OF ENERGY

Signature or a Control Number that tracks the Approval Signature

ADDITIONAL

WASTE TANK SUMMARY REPORT FOR MONTH ENDING NOVEMBER 30, 2001

BM HANLON

CH2M HILL Hanford Group, Inc.

Richland, WA 99352

U.S. Department of Energy Contract DE-AC27-99RL14047

EDT/ECN: ECN-671068

UC:

Cost Center:

Charge Code:

B&R Code:


Total Pages: 5 24/02

Key Words: REPORT, WASTE TANK SUMMARY


Abstract: See page iii of document

TRADEMARK DISCLAIMER. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

Printed in the United States of America. To obtain copies of this document, contact: Document Control Services, P.O. Box 950, Mailstop H6-06, Richland WA 99352, Phone (509) 372-2420; Fax (509) 376-4989.


Release Approval

11/17/02
Date



Release Stamp

Approved For Public Release

Waste Tank Summary Report for Month Ending November 30, 2001

B. M. Hanlon
CH2M HILL Hanford Group, Inc.

Date Published
January 2001

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

CH2MHILL
Hanford Group, Inc.

P. O. Box 1500
Richland, Washington

Contractor for the U.S. Department of Energy
Office of River Protection under Contract DE-AC27-99RL14047

Approved for Public Release; Further Dissemination Unlimited

WASTE TANK SUMMARY REPORT

B. M. Hanlon

ABSTRACT

This report is the official inventory for radioactive waste stored in underground tanks in the 200 Areas at the Hanford Site. Data that depict the status of stored radioactive waste and tank vessel integrity are contained within the report. This report provides data on each of the existing 177 large underground waste storage tanks and 60 smaller miscellaneous underground storage tanks and special surveillance facilities, and supplemental information regarding tank surveillance anomalies and ongoing investigations. This report is intended to meet the requirement of U. S. Department of Energy Order 435.1 (DOE-HQ, August 28, 2001, Radioactive Waste Management, U. S. Department of Energy-Washington D.C.) requiring the reporting of waste inventories and space utilization for Hanford Tank Farm tanks.

This page intentionally left blank.

TABLE OF CONTENTS

SUMMARY	1
I. WASTE TANK STATUS	1
II. WASTE TANK INVESTIGATIONS	1
III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS	2

Appendixes:

A. DOUBLE-SHELL TANKS – MONTHLY SUMMARY TABLES	A-1
<u>Tables:</u>	
1 Inventory and Status by Tank - Double-Shell Tanks	A-2
2 Summary of Waste Transactions in the Double-Shell Tank System	A-4
3 Double-Shell Tank Space Usage and Inventory by Waste Type	A-5
4 Double-Shell Tank Monitoring Compliance Status	A-6
B. SINGLE-SHELL TANKS – MONTHLY SUMMARY TABLES	B-1
<u>Tables:</u>	
1 Inventory and Status by Tank - Single-Shell Tanks	B-2
2 Single-Shell Tanks Stabilization Status Summary	B-13
3 Single-Shell Tanks Interim Stabilization Status	B-14
4 Single-Shell Tanks Interim Stabilization Milestones (Consent Decree)	B-17
5 Single-Shell Tanks Leak Volume Estimates	B-19
6 Single-Shell Tanks Monitoring Compliance Status	B-25
C. MISCELLANEOUS UNDERGROUND STORAGE TANKS AND SPECIAL SURVEILLANCE FACILITIES	C-1
<u>Tables:</u>	
1 Miscellaneous Underground Storage Tanks and Special Surveillance Facilities (Active)	C-2
2 East Area Underground Storage Tanks and Special Surveillance Facilities (Inactive)	C-3
3 West Area Underground Storage Tanks and Special Surveillance Facilities (Inactive)	C-4
D. GLOSSARY OF TERMS	D-1
<u>Tables:</u>	
1 Glossary of Terms	D-2
E. TANK CONFIGURATION AND FACILITIES CHARTS	E-1
<u>Figures:</u>	
1 High Level Waste Tank Configuration	E-2
2 Double-Shell Tank Instrumentation Configuration	E-3
3 Single-Shell Tank Instrumentation Configuration	E-4

METRIC CONVERSION CHART		
1 inch	=	2.54 centimeters
1 foot	=	30.48 centimeters
1 gallon	=	3.79 liters
1 ton	=	0.91 metric tons
$^{\circ}\text{F} = \left(\frac{9}{5} ^{\circ}\text{C} \right) + 32$		
1 Btu/h = 0.2931 watts (International Table)		

WASTE TANK SUMMARY REPORT

For Month Ending November 30, 2001

Note: Changes from the previous month are in bold print.

I. WASTE TANK STATUS

Double-Shell Tanks (DST)	28 double-shell	10/86
Single-Shell Tanks (SST)	149 single-shell	1966
Assumed Leaker Tanks	67 single-shell	07/93
Sound Tanks	28 double-shell 82 single-shell	1986 07/93
Interim Stabilized Tanks ^a (IS)	129 single-shell	06/01
Not Interim Stabilized ^b	20 single-shell	06/01
Isolated -Intrusion Prevention Completed (IP)	108 single-shell	09/96
Controlled, Clean, and Stable ^c (CCS)	36 single-shell	09/96
Misc. Underground Storage Tanks and Special Surveillance Facilities (Active)	10 Tanks East Area 7 Tanks West Area	03/01
Misc. Underground Storage Tanks and Special Surveillance Facilities (Inactive) ^d	18 Tanks East Area 25 Tanks West Area	11/01

^a Of the 129 tanks classified as Interim Stabilized, 65 are listed as Assumed Leakers. (See Table B-5)

^b Two of these tanks are Assumed Leakers (BY-105 and BY-106). (See Table B-5)

^c The TY tank farm was officially declared Controlled, Clean, and Stable (CCS) in March 1996. The TX tank farm and BX tank farms were declared CCS in September 1996.

^d Tables C-2 and C-3, the Inactive Underground Storage Tanks (IMUST) now reflect only those tanks managed by CHG.

II. WASTE TANK INVESTIGATIONS

This section includes all single- or double-shell tanks or catch tanks which are showing surface level or interstitial liquid level (ILL) decreases, or drywell radiation level increases in excess of established criteria.

A. Assumed Leakers or Assumed Re-leakers: (See Appendix D for definition of "Re-leaker")

This section includes all single- or double-shell tanks or catch tanks for which an off-normal or unusual occurrence report has been issued, or for which a waste tank investigation is in progress, for assumed leaks or re-leaks. Tanks/catch tanks will remain on this list until either

a) completion of Interim Stabilization, b) the updated occurrence report indicates that the tank/catch tank is not an assumed leaker, or c) the investigation is completed.

B. Tanks with increases indicating possible intrusion:

This section includes all single-shell tanks and related receiver tanks for which the surveillance data show that the surface level or ILL has met or exceeded the increase criteria, or are still being investigated.

Candidate Intrusion List: As a result of a detailed review of the surface level behavior and physical phenomenon, the four tanks listed below are removed from the Candidate Intrusion List. (Reference D.T. Heimberger to K. M. Hodgson, November 28, 2001, Memo 7G300-01-KMH-001, "Tank Intrusion Evaluation.")

Tank 241-B-202
Tank 241-BX-101
Tank 241-BX-103
Tank 241-BY-103

III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS

A. Single-Shell Tanks Saltwell Jet Pumping (See Table B-1 footnotes for further information)

Tank 241-A-101 - Pumping began May 6, 2000. No pumping has occurred since August 2000; a total of 14.1 Kgallons has been pumped from this tank since the start of pumping in May 2000.

Tank 241-AX-101 - Pumping began July 29, 2000. No pumping occurred between August 2000 and March 2001; pumping began again on March 22, 2001. Pumping was shut down on April 3, 2001, due to a transfer line failure. A total of 21.7 Kgallons has been pumped since the start of pumping in July 2000.

Tank 241-BY-105 - Pumping began July 11, 2001. During July, a total of 8.8 Kgallons was pumped from this tank. Pumping was halted in August 2001 due to transfer line leak detectors not meeting all operability requirements of the Technical Safety Requirements. Compensatory actions have been established to allow resumption of pumping. During November 2001 a total of 3.4 Kgallons was pumped from this tank; a total of 12.2 Kgallons has been pumped since the start of pumping in July 2001.

Tank 241-BY-106 - Pumping originally started in August 1995 and was halted in October 1995 due to an Unreviewed Safety Question (USQ) evaluation for flammable gas concerns. Pumping was restarted July 11, 2001. Pumping was halted in August 2001 due to transfer line leak detectors not meeting all operability requirements of the Technical Safety Requirements (TSR). Compensatory actions have been established to allow resumption of pumping. Pumping resumed in November 2001. During November 2001 a total of 12.1 Kgallons were pumped

from this tank; a total of 82.1 Kgallons has been pumped since the start of pumping in July 2001.

Tank 241-S-102 - Pumping problems forced many shutdowns. The pump was replaced and pumping resumed on February 19, 2000. Problems with the new pump forced a shutdown on March 23, 2000. Pumping was interrupted in early June 2000. Pumping was shut down due to equipment failure; the lower piping needs to be replaced. No pumping has occurred since June 2000; a total of 56.8 Kgallons has been pumped from this tank since the start of pumping in March 1999.

Tank 241-SX-101 - Pumping began November 22, 2000. The pump failed on December 9, 2000, and pumping was shut down. Pumping resumed in September 2001 following replacement of the saltwell pump and lower piping. Pumping was shut down in November 2001 due to high motor bearing temperature and low pump pressures. A total of 31.8 Kgallons has been pumped from this tank since the start of pumping in November 2000.

Tank 241-SX-103 - Pumping began October 26, 2000. Pumping was shut down on April 22, 2001 due to leak detector and subsequent shielding problems in the pump pit. Pumping resumed on September 14, 2001. During November 2001, a total of 1.2 Kgallons was pumped; a total of 127.0 Kgallons has been pumped from this tank since the start of pumping in October 2000.

Tank 241-SX-105 - Pumping began August 8, 2000. Pumping was shut down in late April 2001 when the saltwell screen in-flow rate was measured at approximately 0.02 GPM. This tank is being evaluated to determine if it can be declared interim stabilized. A total of 152.6 Kgallons has been pumped since the start of pumping in August 2000.

Tank 241-U-102 - Pumping began January 20, 2000. During September 2001 a total of 200 gallons was pumped; a total of 86.5 Kgallons has been pumped from this tank since the start of pumping in January 2000. This tank was placed in observation mode in September 2001 to evaluate whether interim stabilization has been completed.

Tank 241-U-107 - Pumping began September 29, 2001. Pumping was shut down during November 2001 and will remain down until the annual leak test is completed satisfactorily on two transfer lines. No pumping in November 2001. A total of 11.7 Kgallons has been pumped from this tank since the start of pumping in September 2001 (net decrease of zero gallons in September due to equipment/priming flushes).

Tank 241-U-109 - Pumping began March 11, 2000. The saltwell pump was replaced following its failure in December 2000, and pumping was restarted March 30, 2001. The tank was last pumped in September 2001 when 100 gallons were transferred; a total of 78.4 Kgallons has been pumped from this tank since the start of pumping in March 2000. This tank was placed in observation mode in September 2001 to evaluate whether interim stabilization has been completed.

C. Changes to this Report:

Tables C-2 and C-3, Inactive Miscellaneous Underground Storage Tanks (IMUST) and Special Surveillance Facilities, only reflect those facilities managed by CH2MHILL Hanford Group.

Table A-1, Inventory and Status by Tank – Double-Shell Tanks, now reflects the maximum volume limits per HNF-SD-WM-SP-012, "Tank Farm Contractor and Utilization Plan," Rev. 3, dated September 27, 2001. See Table A-1 for further details.

APPENDIX A
DOUBLE-SHELL TANKS
MONTHLY SUMMARY TABLES

TABLE A-1. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

November 30, 2001

						WASTE VOLUMES				PHOTOS/VIDEOS		SEE FOOTNOTES FOR THESE CHANGES
			EQUIVA- LENT	TOTAL	AVAIL. SPACE	SUPER- NATANT			SOLIDS	LAST	LAST	
TANK	TANK INTEGRITY	TANK STATUS	WASTE INCHES	WASTE (Kgal)	(1) (Kgal)	LIQUID (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	VOLUME UPDATE	IN-TANK PHOTO	IN-TANK VIDEO	
AN TANK FARM STATUS												
AN-101	SOUND	DRCVR	91.6	252	892	252	0	0	06/30/99			
AN-102	SOUND	CWHT	392.7	1080	64	991	0	89	06/30/99			
AN-103	SOUND	CWHT	349.1	960	184	501	0	458	06/30/99	10/29/87		
AN-104	SOUND	CWHT	383.3	1054	90	808	0	445	06/30/99	06/19/88		
AN-105	SOUND	CWHT	409.8	1127	17	635	0	492	06/30/99	01/26/88		
AN-106	SOUND	CWHT	13.8	38	1106	21	0	17	06/30/99			
AN-107	SOUND	CWHT	378.5	1041	103	794	0	247	06/30/99	09/01/88		
7 DOUBLE-SHELL TANKS TOTALS:				5552	2456	3803	0	1749				
AP TANK FARM STATUS												
AP-101	SOUND	DRCVR	405.1	1114	30	1114	0	0	05/01/89			
AP-102	SOUND	DRCVR	33.1	91	1053	91	0	0	07/11/89			
AP-103	SOUND	DRCVR	102.2	281	863	281	0	0	05/31/88			
AP-104	SOUND	DRCVR	402.9	1108	36	1108	0	0	10/13/88			
AP-105	SOUND	CWHT	412.0	1133	11	1044	0	89	06/30/99		09/27/95	
AP-106	SOUND	DRCVR	415.3	1142	2	1142	0	0	10/13/88			
AP-107	SOUND	DRCVR	354.9	976	168	976	0	0	10/13/88			
AP-108	SOUND	DRCVR	285.5	785	359	785	0	0	10/13/88			
8 DOUBLE-SHELL TANKS TOTALS:				6630	2522	6541	0	89				
AW TANK FARM STATUS												
AW-101	SOUND	CWHT	410.2	1128	16	740	0	388	10/31/00	03/17/88		
AW-102	SOUND	EVFD	34.2	94	1034	64	30	0	01/31/01	02/02/83		
AW-103	SOUND	DRCVR	400.7	1102	42	789	273	40	06/30/99			
AW-104	SOUND	DRCVR	114.5	315	829	92	66	157	06/30/99	02/02/83		
AW-105	SOUND	DRCVR	154.9	426	718	171	255	0	06/30/99			
AW-106	SOUND	SRCVR	107.6	296	848	57	0	239	06/30/99	02/02/83		
6 DOUBLE-SHELL TANKS TOTALS:				3361	3487	1913	624	824				

A-2

HNF-EP-0182, Rev. 164

TABLE A-1. INVENTORY AND STATUS BY TANK - DOUBLE-SHELL TANKS

November 30, 2001

						WASTE VOLUMES			PHOTOS/VIDEOS			SEE FOOTNOTES FOR THESE CHANGES	
TANK	TANK INTEGRITY	TANK STATUS	EQUIVA- LENT	TOTAL	AVAIL.	SUPER- NATANT LIQUID (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO		
			WASTE INCHES	WASTE (Kgal)	SPACE (1) (Kgal)								
<u>AY TANK FARM STATUS</u>													
AY-101	SOUND	DRCVR	65.5	180	621	84	96	0	06/30/99	12/28/82			
AY-102	SOUND	DRCVR	225.8	621	380	437	184	0	10/31/00	04/28/81			
2 DOUBLE-SHELL TANKS			TOTALS:	801	1201	521	280	0					
<u>AZ TANK FARM STATUS</u>													
AZ-101	SOUND	CWHT	350.2	963	38	911	52	0	06/30/98	08/18/83			
AZ-102	SOUND	DRCVR	382.5	997	4	892	106	0	06/30/99	10/24/84			
2 DOUBLE-SHELL TANKS			TOTALS:	1960	42	1803	157	0					
<u>SY TANK FARM STATUS</u>													
SY-101	SOUND	CWHT	352.4	969	175	694	0	275	06/30/99	04/12/89			
SY-102	SOUND	DRCVR	370.9	1020	108	949	71	0	06/30/99	04/29/81			
SY-103	SOUND	CWHT	268.7	738	405	397	0	342	06/30/99	10/01/85			
3 DOUBLE-SHELL TANKS			TOTALS:	2728	688	2040	71	617					
GRAND TOTAL				21108	10274	16697	1132	3279					

Note: +/- 1 Kgal differences are the result of computer rounding

Maximum volume limits per HNF-SD-WM-SP-012, "Tank Farm Contractor and Utilization Plan," Rev. 3, dated September 27, 2001

Tank Farms		Exceptions:	
AN, AP, AW	1144 Kgal	AW-102	1128 Kgal
AY, AZ	1001 Kgal		
SY	1144 Kgal	SY-102	1062 Kgal

NOTE: Supernatant + Sludge (includes liquid) + Saltcake (includes liquid) = Total Wastes

(1) Available Space volumes include restricted space

HNF-EP-0182, Rev. 164

TABLE A-2. SUMMARY OF WASTE TRANSACTIONS IN THE DOUBLE-SHELL TANK (DST) SYSTEM

November 30, 2001

All volumes in Kilo-Gallons (Kgal)

- The DST system received waste additions from SST pumping, AZ-151, A-350, nitrite, BX-244 (DCRT), & raw water in November.
- There was a net change of +115,000 gallons in the DST system for November.
- The total DST inventory as of November 30, 2001, was 21.108 million gallons.
- There were ~41 Kgal of Saltwell Liquid (SWL) pumped to the East Area DSTs (AP-102) in November, which reflect two transfers of BX-244 (DCRT) to AP-102; not the volume pumped from SSTs BY-105 and BY-106 in November. BX-244 is used for interim storage of BY farm stabilization waste. The first BX-244 to AP-102 transfer contained waste from the BY farm that was pumped in July 2001.
- There were ~6 Kgal of SWL (1 Kgal SWL + 5 Kgal water) pumped to the West Area DSTs (SY-102) in November.
- The SWL numbers are preliminary and are subject to change once the system engineers do a validation; the volumes reported contain the actual waste volume plus any water added for dilution and transfer line flushes.
- A transfer of ~2,833 gallons of waste was sent from tank AP-108 to tank AP-106 (for transfer pump priming) prior to a transfer of ~520,273 gallons from tank AP-106 to tank AP-108. After the AP-106 to AP-108 transfer, tank AP-106 received ~1,038,950 gallons from Tank AP-102. These transfers free up storage space in AP-102 to now receive and store cross-site transfer and newly generated waste receipts.
- The PFP facility sent ~4,000 gallons of waste to DCRT TX-244 for interim storage in November. This waste will be accounted for when TX-244 is transferred to the DST system. TX-244 presently contains ~13,211 gallons of PFP waste and water, plus ~6,000 gallons of waste & water from SWL pumping of tanks T-104 and T-110.
- The maximum volume limits for each of the DST's were adjusted in November. These new volume limits are provided by HNF-SD-WM-SP-012, "Tank Farm Contractor and Utilization Plan," Rev. 3, dated September 27, 2001.

NOVEMBER 2001 DST WASTE RECEIPTS					
FACILITY GENERATIONS		OTHER GAINS ASSOCIATED WITH		OTHER LOSSES ASSOCIATED WITH	
SWL (West)	+6 Kgal (SY-102)	SLURRY	+3 Kgal	SLURRY	-4 Kgal
SWL (East)	+41 Kgal (AP-102)	CONDENSATE	+13 Kgal	CONDENSATE	-5 Kgal
Nitrite (NaNO)	+63 Kgal (AY-102)	INSTRUMENTATION	+0 Kgal	INSTRUMENTATION	-0 Kgal
Tank Farms	+3 Kgal (AP-102, AW-102)	UNKNOWN	+1 Kgal	UNKNOWN	-6 Kgal
TOTAL = +113 Kgal		TOTAL = +17 Kgal		TOTAL = -15 Kgal	

PROJECTED VERSUS ACTUAL WASTE VOLUMES						
	ACTUAL DST WASTE RECEIPTS	PROJECTED DST WASTE RECEIPTS (1)	MISC. DST CHANGES (+/-)	PROJECTED WVR (1)	NET DST CHANGE	TOTAL DST VOLUME
OCT 01	74	114	-5	0	69	20993
NOV 01	113	388	2	0	115	21108
DEC 01	0	647	0	0	0	0
JAN 02	0	544	0	0	0	0
FEB 02	0	528	0	0	0	0
MAR 02	0	-151	0	0	0	0
APR 02	0	316	0	0	0	0
MAY 02	0	185	0	0	0	0
JUN 02	0	180	0	0	0	0
JUL 02	0	-678	0	0	0	0
AUG 02	0	168	0	0	0	0
SEP 02	0	109	0	0	0	0

(1): The "PROJECTED DST WASTE RECEIPTS" and "WVR" numbers were updated in November 2001, the projected volumes will be updated as new and/or more accurate information is obtained. The projected volumes are the most current available, as supplied by cognizant system engineers.

242-A Evaporator Waste Volume Reduction:	
Campaign 94-1 (04/15/94 - 06/13/94)	-2417
Campaign 94-2 (08/22/94 - 11/18/94)	-2787
Campaign 95-1 (08/09/95 - 07/28/95)	-2161
Campaign 96-1 (05/07/96 - 05/25/96)	-1117
Campaign 97-1 (03/24/97 - 04/02/97)	-351
Campaign 97-2 (09/16/97 - 09/30/97)	-653
Campaign 99-1 (07/24/99 - 08/15/99)	-818
Campaign 00-1 (04/20/00 - 05/05/00)	-682
Campaign 01-1 (03/13/01 - 03/27/01)	-682
Total waste reduction (WVR) since restart on 4/15/94	-11668

Table A-3. Double-Shell Tank Space Usage and Inventory by Waste Type

November 30, 2001

TOTAL AVAILABLE DST SPACE	
NON-AGING =	27378
AGING =	4004
TOTAL =	31382

MONTHLY INVENTORY CHANGE	
INVENTORY ON 10/31/01	20993
INVENTORY ON 11/30/01	21108
CHANGE =	115

Tank Space Usage

UNUSED TANK SPACE CHANGE	
10/31/01 TANK SPACE	10304
11/30/01 TANK SPACE	10274
CHANGE =	-30

OPERATIONAL SPACE	
AN-101 =	892
AP-108 =	359
AW-102 =	1034
AW-105 =	718
AW-108 =	848
SY-102 =	57
TOTAL =	3908

RESTRICTED SPACE	
AN-102 =	64
AN-103 =	184
AN-104 =	90
AN-105 =	17
AN-107 =	103
AP-102 =	1053
AP-106 =	2
AW-101 =	16
AZ-101 =	25
AZ-102 =	5
SY-103 =	405
TOTAL =	1964

NON-ALLOCATED SPACE	
AN-106 =	1106
AP-101 =	30
AP-103 =	863
AP-104 =	39
AP-105 =	11
AP-107 =	168
AW-103 =	42
AW-104 =	829
AY-101 =	822
AY-102 =	320
SY-101 =	175
TOTAL =	4402
EMERGENCY SPACE	-1144
LAW or HLW RETURN	-1144
REMAINING SPACE	1947

Inventory Calculation by Waste Type:

DILUTE SUPERNATANT (DN/DC)	
AN-101 =	252
AP-107 = (DC)	976
AP-108 =	785
AW-102 =	64
AW-104 =	92
AW-105 =	171
AY-101 = (DC)	83
AY-102 =	497
SY-102 = (DC)	954
TOTAL DN/DC =	3874
TOTAL SOLIDS =	859

SLURRY SUPERNATANT (DSS/DSSF)	
AN-103 =	501
AN-104 =	609
AN-105 =	635
AP-101 =	1114
AP-105 =	1044
AW-101 =	740
AW-103 =	789
AW-106 =	57
TOTAL DSS/DSSF =	5489
TOTAL SOLIDS =	2425

COMPLEXED SUPERNATANT (CC)	
AN-102 =	991
AN-106 =	21
AN-107 =	794
AP-103 =	281
AP-104 =	1108
SY-101 =	694
SY-103 =	397
TOTAL DC/CC =	4286
TOTAL SOLIDS	970

AGING SUPERNATANT (AW)	
AZ-101 =	924
AZ-102 =	891
TOTAL AW =	1815
TOTAL SOLIDS	157

PHOSPHATE SUPERNATANT (CP)	
AP-102 =	91
AP-106 =	1142
TOTAL CP =	1233
TOTAL SOLIDS	0

Note: Unused Tank Space Change does not equal Monthly Inventory Change because the maximum volume limits for the tanks were changed this month (see Table A-1)

GRAND TOTALS	
DILUTE SUPERNATANT (DN/DC) =	3874
SLURRY (DSS/DSSF) =	5489
CONCENTRATED COMPLEXED (CC) =	4286
CONCENTRATED PHOSPHATE (CP) =	1233
AGING SUPERNATANT (AW) =	1815
DST SOLIDS (SL/SC) =	4411
TOTAL =	21108

TABLE A-4. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS
November 30, 2001

All Double-Shell Tanks were in compliance this month.

Legend:	
O/C	Noncompliance with applicable documentation
FIC/ENRAF/MT (a)	Surface level measurement devices
OSD	OSD-T-151-0007, OSD-T-151-00031
FSAR/TSR	Final Safety Analysis Report/Technical Safety Requirements
None	Applicable equipment not installed
N/A	Not Applicable (not monitored or no monitoring scheduled)

(a) ENRAF is a trademark of the ENRAF Corporation, Houston, Texas.

Notes:

Psychrometrics monitoring is on an as needed basis.

In-tank photos/videos are taken on an as needed basis.

Drywell monitoring is no longer required.

APPENDIX B
SINGLE-SHELL TANKS
MONTHLY SUMMARY TABLES

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements.

See footnotes for information on tanks in process of Interim Stabilization

				WASTE VOLUMES										PHOTOS/VIDEOS		SEE FOOTNOTES FOR THESE CHANGES
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER- NATANT LIQUID (Kgal)	DRAINABLE INTERSTITIAL LIQUID (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAINABLE LIQUID REMAINING (Kgal)	PUMPABLE LIQUID REMAINING (Kgal)	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO		
A TANK FARM STATUS																
A-101	SOUND	/PI	877	(a)	(a)	0.0	14.1	(a)	(a)	3	380	08/30/99	08/21/85	(a)		
A-102	SOUND	IS/PI	41	4	8	0.0	39.5	12	4	15	22	07/27/89	07/20/89			
A-103	ASMD LKR	IS/IP	371	5	45	0.0	111.0	50	43	366	0	08/03/88	12/28/88			
A-104	ASMD LKR	IS/IP	28	0	4	0.0	0.0	4	0	28	0	01/27/78	08/25/86			
A-105	ASMD LKR	IS/IP	37	0	0	0.0	0.0	0	0	37	0	10/31/00	08/20/86			
A-106	SOUND	IS/IP	125	0	9	0.0	0.0	9	1	125	0	08/07/82	08/19/86			
6 TANKS - TOTALS			1479							574	402					
AX TANK FARM STATUS																
AX-101	SOUND	/PI	662	(b)	(b)	0.0	21.7	(b)	(b)	3	295	08/30/99	08/18/87	(b)		
AX-102	ASMD LKR	IS/IP	30	0	7	0.0	13.0	7	0	7	23	08/30/99	08/05/88			
AX-103	SOUND	IS/IP	112	0	23	0.0	0.0	23	11	8	104	08/30/99	08/13/87			
AX-104	ASMD LKR	IS/IP	8	0	1	0.0	0.0	1	0	8	0	08/30/99	08/18/87			
4 TANKS - TOTALS			812							26	422					
B TANK FARM STATUS																
B-101	ASMD LKR	IS/IP	113	0	24	0.0	0.0	24	17	0	113	08/30/99	05/19/83			
B-102	SOUND	IS/IP	32	4	7	0.0	0.0	11	4	0	28	08/30/99	08/22/86			
B-103	ASMD LKR	IS/IP	59	0	11	0.0	0.0	11	3	0	58	08/30/99	10/13/88			
B-104	SOUND	IS/IP	371	1	45	0.0	0.0	46	42	309	61	08/30/99	10/13/88			
B-105	ASMD LKR	IS/IP	158	0	20	0.0	0.0	20	16	28	130	08/30/99	05/19/88			
B-106	SOUND	IS/IP	117	1	25	0.0	0.0	26	19	0	116	02/29/00	02/28/86			
B-107	ASMD LKR	IS/IP	185	1	22	0.0	0.0	23	19	93	71	08/30/99	02/28/86			
B-108	SOUND	IS/IP	94	0	15	0.0	0.0	15	11	53	41	08/30/99	05/10/86			
B-109	SOUND	IS/IP	127	0	21	0.0	0.0	21	17	63	64	08/30/99	04/02/86			
B-110	ASMD LKR	IS/IP	246	1	27	0.0	0.0	28	20	245	0	02/28/85	03/17/88			
B-111	ASMD LKR	IS/IP	237	1	23	0.0	0.0	24	29	236	0	08/28/86	08/28/86			
B-112	ASMD LKR	IS/IP	33	3	4	0.0	0.0	7	3	30	0	05/31/86	05/29/86			
B-201	ASMD LKR	IS/IP	29	1	4	0.0	0.0	5	1	28	0	04/28/82	11/12/86	08/23/95		
B-202	SOUND	IS/IP	27	0	4	0.0	0.0	4	0	27	0	05/31/85	05/29/85	08/15/85		
B-203	ASMD LKR	IS/IP	51	1	5	0.0	0.0	6	1	50	0	05/31/84	11/13/86			
B-204	ASMD LKR	IS/IP	50	1	5	0.0	0.0	6	1	49	0	05/31/84	10/22/87			
16 TANKS - TOTALS			1909							1211	683					

B-2

HNF-EP-0182, Rev. 164

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements.

See footnotes for information on tanks in process of Interim Stabilization.

				WASTE VOLUMES								PHOTOS/VIDEOS			SEE FOOTNOTES FOR THESE CHANGES
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER- NATANT	DRAINABLE INTERSTITIAL	PUMPED THIS MONTH	TOTAL PUMPED	DRAINABLE LIQUID REMAINING	PUMPABLE LIQUID REMAINING	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO	
				LIQUID (Kgal)	LIQUID (Kgal)	(Kgal)	(Kgal)	(Kgal)	(Kgal)						
BX TANK FARM STATUS															
BX-101	ASMD LKR	IS/IP/CCS	43	1	4	0.0	0.0	5	1	42	0	04/28/82	11/24/88	11/10/94	
BX-102	ASMD LKR	IS/IP/CCS	96	0	0	0.0	0.0	0	0	96	0	04/28/82	08/18/86		
BX-103	SOUND	IS/IP/CCS	71	9	4	0.0	0.0	13	9	62	0	11/28/83	10/31/88	10/27/94	
BX-104	SOUND	IS/IP/CCS	93	3	4	0.0	17.4	7	3	90	0	02/28/00	08/21/89		
BX-105	SOUND	IS/IP/CCS	51	5	4	0.0	15.0	9	5	46	0	06/30/99	10/23/86		
BX-106	SOUND	IS/IP/CCS	38	0	4	0.0	14.0	4	0	38	0	08/01/95	06/18/88	07/17/95	
BX-107	SOUND	IS/IP/CCS	345	1	36	0.0	23.1	37	33	344	0	08/18/90	08/11/90		
BX-108	ASMD LKR	IS/IP/CCS	26	0	4	0.0	0.0	4	0	26	0	07/31/79	05/05/84		
BX-109	SOUND	IS/IP/CCS	193	0	25	0.0	8.2	25	20	193	0	08/17/90	09/11/90		
BX-110	ASMD LKR	IS/IP/CCS	207	3	28	0.0	1.5	31	26	133	71	06/30/99	07/15/94	10/13/94	
BX-111	ASMD LKR	IS/IP/CCS	162	1	5	0.0	116.9	6	2	25	136	06/30/99	05/19/94	02/28/95	
BX-112	SOUND	IS/IP/CCS	165	1	9	0.0	4.1	10	7	164	0	08/17/90	08/11/90		
12 TANKS - TOTALS			1490							1259	207				
BY TANK FARM STATUS															
BY-101	SOUND	IS/IP	387	0	28	0.0	35.8	28	24	109	278	05/30/84	09/19/89		
BY-102	SOUND	IS/PI	277	0	40	0.0	159.0	40	33	0	277	05/01/95	09/11/87	04/11/95	
BY-103	ASMD LKR	IS/PI	400	0	58	0.0	95.9	58	53	9	391	06/30/99	09/07/88	02/24/97	
BY-104	SOUND	IS/IP	326	0	40	0.0	329.5	40	36	150	176	06/30/99	04/27/83		
BY-105	ASMD LKR	/PI	491	(c)	(c)	3.4	12.2	(c)	(c)	48	443	11/30/01	07/01/86	(c)	
BY-106	ASMD LKR	/PI	544	(d)	(d)	12.1	82.1	(d)	(d)	84	460	11/30/01	11/04/82	(d)	
BY-107	ASMD LKR	IS/IP	266	0	39	0.0	56.4	39	35	40	226	06/30/99	10/15/86		
BY-108	ASMD LKR	IS/IP	228	0	33	0.0	27.5	33	26	154	74	04/28/82	10/15/86		
BY-109	SOUND	IS/PI	290	0	31	0.0	167.1	31	26	57	233	07/06/87	06/18/97		
BY-110	SOUND	IS/IP	398	0	21	0.0	213.3	21	17	103	295	09/10/79	07/26/84		
BY-111	SOUND	IS/IP	459	0	14	0.0	313.2	14	6	0	459	06/30/99	10/31/86		
BY-112	SOUND	IS/IP	291	0	24	0.0	116.4	24	12	0	291	06/30/99	04/14/88		
12 TANKS - TOTALS			4357							754	3603				

B-3

HNF-EP-0182, Rev. 164

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements

See footnotes for information on tanks in process of Interim Stabilization

				WASTE VOLUMES								PHOTOS/VIDEOS				SEE FOOTNOTES FOR THESE CHANGES		
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER- NATANT LIQUID (Kgal)	DRAINABLE INTERSTITIAL LIQUID (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAINABLE LIQUID REMAINING (Kgal)	PUMPABLE LIQUID REMAINING (Kgal)	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO				
C TANK FARM STATUS																		
C-101	ASMD LKR	IS/IP	88	0	4	0.0	0.0	4	0	88	0	11/28/83	11/17/87					
C-102	SOUND	IS/IP	316	0	62	0.0	46.7	62	55	316	0	08/30/95	06/18/78	08/24/95				
C-103	SOUND	/PI	198	79	18	0.0	0.0	97	83	119	0	12/31/98	07/28/87					
C-104	SOUND	IS/IP	263	0	0	0.0	0.0	0	0	263	0	02/01/00	07/25/90					
C-105	SOUND	IS/PI	132	0	20	0.0	0.0	20	0	132	0	02/29/00	06/05/94	08/30/95				
C-106	SOUND	/PI	48	42	0	0.0	0.0	42	8	6	0	10/31/99	08/05/94	08/08/94				
C-107	SOUND	IS/IP	257	0	30	0.0	40.8	30	25	257	0	06/30/99	00/00/00					
C-108	SOUND	IS/IP	66	0	4	0.0	0.0	4	0	66	0	02/24/84	12/05/74	11/17/94				
C-109	SOUND	IS/IP	66	4	4	0.0	0.0	8	4	62	0	11/28/83	01/30/76					
C-110	ASMD LKR	IS/IP	178	1	37	0.0	15.5	38	30	177	0	06/14/95	06/12/86	05/23/95				
C-111	ASMD LKR	IS/IP	57	0	4	0.0	0.0	4	0	57	0	04/28/82	02/25/70	02/02/95				
C-112	SOUND	IS/IP	104	0	6	0.0	0.0	6	1	104	0	09/18/90	09/18/90					
C-201	ASMD LKR	IS/IP	2	0	0	0.0	0.0	0	0	2	0	03/31/82	12/02/86					
C-202	ASMD LKR	IS/IP	1	0	0	0.0	0.0	0	0	1	0	01/19/79	12/08/86					
C-203	ASMD LKR	IS/IP	5	0	0	0.0	0.0	0	0	5	0	04/28/82	12/09/86					
C-204	ASMD LKR	IS/IP	3	0	0	0.0	0.0	0	0	3	0	04/28/82	12/08/86					
16 TANKS - TOTALS			1784									1658	0					
S TANK FARM STATUS																		
S-101	SOUND	/PI	427	12	63	0.0	0.0	95	80	211	204	12/31/98	03/18/86					
S-102	SOUND	/PI	492	(a)	(a)	0.0	56.8	(a)	(a)	105	387	05/31/00	03/18/86			(a)		
S-103	SOUND	IS/PI	237	1	45	0.0	23.9	46	39	9	227	04/30/00	06/01/88	01/28/00				
S-104	ASMD LKR	IS/IP	294	1	34	0.0	0.0	35	31	293	0	12/20/84	12/12/84					
S-105	SOUND	IS/IP	456	0	42	0.0	114.3	42	33	2	454	08/26/88	04/12/88					
S-106	SOUND	IS/PI	455	0	26	0.0	203.6	26	2	0	455	02/28/01	03/17/88	01/28/00				
S-107	SOUND	/PI	376	14	61	0.0	0.0	75	61	293	69	06/30/99	03/12/87					
S-108	SOUND	IS/PI	432	0	0	0.0	199.8	0	0	5	427	10/01/99	03/12/87	12/03/96				
S-109	SOUND	IS/PI	533	0	16	0.0	34.0	16	12	13	520	06/30/01	12/31/96					
S-110	SOUND	IS/PI	390	0	30	0.0	203.1	30	27	131	259	05/14/92	03/12/87	12/11/96				
S-111	SOUND	/PI	501	48	62	0.0	3.3	130	97	116	337	08/30/99	08/10/88					
S-112	SOUND	/PI	523	0	81	0.0	125.1	81	70	6	517	12/31/98	03/24/87					
12 TANKS - TOTALS			5116									1184	3866					

B-1

HNF-EP-0182, Rev. 164

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements

See footnotes for information on tanks in process of Interim Stabilization

				WASTE VOLUMES										PHOTOS/VIDEOS		SEE
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAINABLE INTERSTITIAL LIQUID (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAINABLE LIQUID REMAINING (Kgal)	PUMPABLE LIQUID REMAINING (Kgal)	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO	FOOTNOTES FOR THESE CHANGES	
SX TANK FARM STATUS																
SX-101	SOUND	/PI	426	(f)	(f)	0.0	22.5	(f)	(f)	0	426	09/30/01	03/10/89		(f)	
SX-102	SOUND	/PI	514	134	95	0.0	0.0	229	216	0	380	04/30/00	01/07/88			
SX-103	SOUND	/PI	507	(g)	(g)	1.2	127.0	(g)	(g)	109	398	11/30/01	12/17/87		(g)	
SX-104	ASMD LKR	IS/PI	448	0	48	0.0	231.3	48	44	136	310	04/30/00	09/08/88	02/04/88		
SX-105	SOUND	/PI	484	(h)	(h)	0.0	152.6	(h)	(h)	65	419	04/30/01	06/15/88		(h)	
SX-106	SOUND	IS/PI	397	0	37	0.0	147.5	37	31	0	397	05/31/99	06/01/89			
SX-107	ASMD LKR	IS/IP	102	0	0	0.0	0.0	0	0	85	17	10/31/00	03/06/87			
SX-108	ASMD LKR	IS/IP	87	0	0	0.0	0.0	0	0	87	0	12/31/93	03/06/87			
SX-109	ASMD LKR	IS/IP	249	0	0	0.0	0.0	0	0	80	189	10/31/00	05/21/86			
SX-110	ASMD LKR	IS/IP	62	0	0	0.0	0.0	0	0	62	0	10/06/76	02/20/87			
SX-111	ASMD LKR	IS/IP	122	0	8	0.0	0.0	8	3	122	0	06/30/99	06/09/94			
SX-112	ASMD LKR	IS/IP	108	0	6	0.0	0.0	6	1	108	0	06/30/99	03/10/87			
SX-113	ASMD LKR	IS/IP	31	0	0	0.0	0.0	0	0	31	0	06/30/99	03/18/88			
SX-114	ASMD LKR	IS/IP	165	0	0	0.0	0.0	0	0	44	121	10/31/00	02/26/87			
SX-115	ASMD LKR	IS/IP	12	0	0	0.0	0.0	0	0	12	0	04/28/82	03/31/88			
15 TANKS - TOTALS:			3712							921	2657					

T TANK FARM STATUS

T-101	ASMD LKR	IS/PI	102	1	20	0.0	25.3	21	16	37	64	06/30/99	04/07/83		
T-102	SOUND	IS/IP	32	13	3	0.0	0.0	16	11	19	0	06/31/84	08/28/88		
T-103	ASMD LKR	IS/IP	27	4	3	0.0	0.0	7	3	23	0	11/29/83	07/03/84		
T-104	SOUND	IS/PI	317	0	31	0.0	149.5	31	27	317	0	12/31/99	06/29/89	10/07/99	
T-105	SOUND	IS/IP	98	0	5	0.0	0.0	5	0	98	0	05/29/87	05/14/87		
T-106	ASMD LKR	IS/IP	21	2	0	0.0	0.0	2	2	19	0	04/28/82	06/29/89		
T-107	ASMD LKR	IS/PI	173	0	34	0.0	11.0	34	20	173	0	05/31/98	07/12/84	05/09/98	
T-108	ASMD LKR	IS/IP	44	0	5	0.0	0.0	5	0	21	23	06/30/99	07/17/84		

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements.

See footnotes for information on tanks in process of Interim Stabilization.

				WASTE VOLUMES										PHOTOS/VIDES		SEE FOOTNOTES FOR THESE CHANGES
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER- NATANT LIQUID (Kgal)	DRAINABLE INTERSTITIA LIQUID (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAINABLE LIQUID REMAINING (Kgal)	PUMPABLE LIQUID REMAINING (Kgal)	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO		
T-109	ASMD LKR	IS/IP	58	0	10	0.0	0.0	10	3	0	58	06/30/99	02/25/83			
T-110	SOUND	IS/PI	369	1	48	0.0	50.3	48	43	368	0	01/31/00	07/12/84	10/07/99		
T-111	ASMD LKR	IS/PI	446	0	38	0.0	9.6	38	35	446	0	04/18/94	04/13/84	02/13/95		
T-112	SOUND	IS/IP	67	7	4	0.0	0.0	11	7	60	0	04/28/82	08/01/84			
T-201	SOUND	IS/IP	28	1	4	0.0	0.0	5	1	28	0	05/31/78	04/15/86			
T-202	SOUND	IS/IP	21	0	3	0.0	0.0	3	0	21	0	07/12/81	07/06/89			
T-203	SOUND	IS/IP	35	0	5	0.0	0.0	5	0	35	0	01/31/78	08/03/89			
T-204	SOUND	IS/IP	38	0	5	0.0	0.0	5	0	38	0	07/22/81	08/03/89			
16 TANKS - TOTALS			1877							1703	145					
TX TANK FARM STATUS																
TX-101	SOUND	IS/IP/CCS	87	3	8	0.0	0.0	11	7	74	10	06/30/99	10/24/85			
TX-102	SOUND	IS/IP/CCS	217	0	27	0.0	94.4	27	16	0	217	08/31/84	10/31/85			
TX-103	SOUND	IS/IP/CCS	157	0	18	0.0	68.3	18	11	0	157	06/30/99	10/31/85			
TX-104	SOUND	IS/IP/CCS	65	5	9	0.0	3.6	14	9	23	37	06/30/99	10/16/84			
TX-105	ASMD LKR	IS/IP/CCS	609	0	25	0.0	121.5	25	14	0	609	08/22/77	10/24/89			
TX-106	SOUND	IS/IP/CCS	341	0	37	0.0	134.6	37	30	0	341	06/30/99	10/31/85			
TX-107	ASMD LKR	IS/IP/CCS	36	1	6	0.0	0.0	7	1	8	27	06/30/99	10/31/85			
TX-108	SOUND	IS/IP/CCS	134	0	8	0.0	13.7	8	1	6	128	06/30/99	08/12/89			
TX-109	SOUND	IS/IP/CCS	384	0	6	0.0	72.3	6	2	384	0	06/30/99	10/24/89			
TX-110	ASMD LKR	IS/IP/CCS	462	0	14	0.0	115.1	14	10	37	425	06/30/99	10/24/89			
TX-111	SOUND	IS/IP/CCS	370	0	10	0.0	98.4	10	6	43	327	06/30/99	08/12/89			
TX-112	SOUND	IS/IP/CCS	649	0	26	0.0	94.0	26	21	0	649	05/30/83	11/19/87			
TX-113	ASMD LKR	IS/IP/CCS	653	0	30	0.0	19.2	30	0	0	653	10/31/00	04/11/83	09/23/94		
TX-114	ASMD LKR	IS/IP/CCS	535	0	17	0.0	104.3	17	11	4	531	06/30/99	04/11/83	02/17/95		
TX-115	ASMD LKR	IS/IP/CCS	568	0	25	0.0	99.1	25	15	0	568	06/30/99	08/15/86			
TX-116	ASMD LKR	IS/IP/CCS	631	0	21	0.0	23.8	21	17	68	563	06/30/99	10/17/89			
TX-117	ASMD LKR	IS/IP/CCS	628	0	10	0.0	54.3	10	5	29	597	06/30/99	04/11/83			
TX-118	SOUND	IS/IP/CCS	286	0	0	0.0	89.1	0	0	21	265	02/01/00	12/19/79			
18 TANKS - TOTALS			6810							697	6104					

B-6

HNF-EP-0182, Rev. 164

TABLE B-1. INVENTORY AND STATUS BY TANK - SINGLE-SHELL TANKS

November 30, 2001

These volumes are the result of engineering calculations and may not agree with surface level measurements.
See footnotes for information on tanks in process of Inertial Stabilization.

				WASTE VOLUMES										PHOTOS/VIDEOS		SEE FOOTNOTES FOR THESE CHANGES
TANK NO.	TANK INTEGRITY	TANK STATUS	TOTAL WASTE (Kgal)	SUPER- NATANT LIQUID (Kgal)	DRAINABLE INTERSTITIAL LIQUID (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAINABLE LIQUID REMAINING (Kgal)	PUMPABLE LIQUID REMAINING (Kgal)	SLUDGE (Kgal)	SALT CAKE (Kgal)	SOLIDS VOLUME UPDATE	LAST IN-TANK PHOTO	LAST IN-TANK VIDEO		
TY TANK FARM STATUS																
TY-101	ASMD LKR	IS/IP/CCS	118	0	2	0.0	8.2	2	0	72	46	06/30/99	06/22/99			
TY-102	SOUND	IS/IP/CCS	64	0	12	0.0	6.6	12	5	0	64	06/28/82	07/07/87			
TY-103	ASMD LKR	IS/IP/CCS	162	0	20	0.0	11.5	20	16	162	0	07/09/82	06/22/98			
TY-104	ASMD LKR	IS/IP/CCS	43	0	4	0.0	0.0	4	0	43	0	06/27/90	11/03/97			
TY-105	ASMD LKR	IS/IP/CCS	231	0	12	0.0	3.6	12	10	231	0	04/28/82	09/07/99			
TY-106	ASMD LKR	IS/IP/CCS	21	0	3	0.0	0.0	3	0	21	0	06/30/99	06/22/99			
6 TANKS - TOTALS			639							529	110					
U TANK FARM STATUS																
U-101	ASMD LKR	IS/IP	25	3	3	0.0	0.0	8	2	22	0	04/28/82	06/19/79			
U-102	SOUND	/PI	289	(f)	(f)	0.0	86.3	(f)	(f)	43	246	08/31/01	06/08/99	(f)		
U-103	SOUND	IS/PI	418	1	33	0.0	98.9	34	26	13	404	06/31/00	06/13/98			
U-104	ASMD LKR	IS/IP	122	0	0	0.0	0.0	0	0	79	43	06/30/99	06/10/99			
U-105	SOUND	IS/PI	353	0	44	0.0	87.5	44	32	32	321	03/31/01	07/07/98			
U-106	SOUND	IS/PI	172	2	36	0.0	39.1	38	30	0	170	03/31/01	07/07/98			
U-107	SOUND	/PI	397	(j)	(j)	0.0	11.7	(j)	(j)	15	349	10/31/01	10/27/98	(j)		
U-108	SOUND	/PI	468	24	108	0.0	0.0	132	124	29	415	12/31/98	09/12/84			
U-109	SOUND	/PI	387	(k)	(k)	0.0	78.4	(k)	(k)	35	352	08/31/01	07/07/98	(k)		
U-110	ASMD LKR	IS/PI	186	0	18	0.0	0.0	18	14	186	0	12/30/84	12/11/84			
U-111	SOUND	/PI	329	0	80	0.0	0.0	80	71	26	303	12/31/98	06/23/98			
U-112	ASMD LKR	IS/IP	49	4	4	0.0	0.0	8	4	45	0	02/10/84	06/03/99			
U-201	SOUND	IS/IP	5	1	1	0.0	0.0	2	1	4	0	06/15/79	06/06/99			
U-202	SOUND	IS/IP	5	1	1	0.0	0.0	2	1	4	0	06/15/79	06/06/99			
U-203	SOUND	IS/IP	3	1	0	0.0	0.0	1	1	2	0	06/15/79	06/13/99			
U-204	SOUND	IS/IP	3	1	0	0.0	0.0	1	1	2	0	06/15/79	06/13/99			
16 TANKS - TOTALS			3211							537	2603					
GRAND TOTAL			33196							11053	20792					

B-7

HNF-EP-0182, Rev. 164

TABLE B-1. INVENTORY AND STATUS BY TANK – SINGLE-SHELL TANKS

November 30, 2001

Footnotes:

Total waste is calculated as the sum of Sludge and Saltcake plus Supernatant. The category "Interim Isolated (II)" was changed to "Intrusion Prevention (IP)" in June 1993.

Stabilization information is from WHC-SD-RE-TI-178, "SST Stabilization Record," latest revision, or from the SST Stabilization Project or the System Engineer.

All estimated initial volumes are per HNF-2978, Rev. 2, "Updated Pumpable Liquid Volume Estimates and Jet Pump Operations for Interim Stabilization of Remaining Single-Shell Tanks," August 2000.

(a) A-101 Initial estimated Pumpable Liquid volume: 588.5 Kgal

Pumping began on May 6, 2000. No pumping since August 2000. It is expected pumping will resume in December 2001.

Final volumes will be determined at completion of Interim Stabilization.

(b) AX-101 Initial estimated Pumpable Liquid volume: 444.0 Kgal

Pumping began July 29, 2000, shut down in August 2000, and resumed March 22, 2001. Pumping shut down April 3, 2001, due to failure of the transfer line. No pumping since April 2001. It is expected pumping will resume in December 2001.

Final volumes will be determined at completion of Interim Stabilization.

(c) BY-105 Initial estimated Pumpable Liquid volume: 109.9 Kgal

Pumping began July 11, 2001. Remaining volumes are based on HNF-2978, Rev. 2. Saltcake volume adjusted to correspond to current waste removal.

Pumping was shut down in August 2001 due to transfer line leak detectors not meeting all operability requirements of the TSR. Compensatory actions were established to allow resumption of pumping. Additionally, field work for Project W-314, "Tank Farm Upgrades," took the primary transfer route out of service. No pumping from August to November 2001 when pumping resumed.

Final volumes will be determined at completion of Interim Stabilization

(d) BY-106 Initial estimated Pumpable Liquid volume: 182.7 Kgal

Pumping was originally started August 10, 1995, and shut down October 17, 1995, due to an Unreviewed Safety Question (USQ) for flammable gas concerns. Total pumped by October 1995 was 63.7 Kgal.

Pumping was restarted July 11, 2001. Pumping was shut down in August 2001 due to transfer line leak detectors not meeting all operability requirements of the TSR. Compensatory actions were established to allow resumption of pumping. Additionally, field work for Project W-314, "Tank Farm Upgrades," has taken the primary transfer route out of service. No pumping from July to November 2001 when pumping resumed.

Final volumes will be determined at completion of Interim Stabilization

(e) S-102 Initial estimated Pumpable Liquid volume: 145.8 Kgal

Pumping commenced March 18, 1999. Many pumping problems occurred over the following months, and the pump was replaced several times. Pumping was interrupted again in June 2000. No pumping since June 2000.

Final volumes will be determined at completion of Interim Stabilization

- (f) SX-101 Initial estimated Pumpable Liquid volume: 99.0 Kgal

Pumping began November 22, 2000. No pumping since December 2000 due to pump failure. Pumping resumed in September 2001, following replacement of the saltwell pump and lower piping. No pumping in October or November 2001.

Final volumes will be determined at completion of Interim Stabilization

- (g) SX-103 Initial estimated Pumpable Liquid volume: 132.0 Kgal

Pumping began October 26, 2000. Pumping was shut down April 22, 2001 due to leak detector and subsequent shielding problems in the pump pit. Pumping resumed September 14, 2001.

Final volumes will be determined at completion of Interim Stabilization

- (h) SX-105 Initial estimated Pumpable Liquid volume: 141.0 Kgal

Saltwell pumping began August 8, 2000. Pumping was shut down in late April 2001 when the saltwell screen in-flow rate was measured at about 0.02 gpm. Interstitial fluid level is now being allowed to stabilize to determine if the tank can be declared interim stabilized. An in-tank video will be taken.

Final volumes will be determined at completion of Interim Stabilization

- (i) U-102 Initial estimated Pumpable Liquid volume: 93.0 Kgal

Pumping began in this tank on January 20, 2000.

This tank was placed in observation mode in September 2001 for evaluation to determine if it meets the interim stabilization criteria.

Final volumes will be determined at completion of Interim Stabilization

- (j) U-107 Initial estimated Pumpable Liquid volume: 115.0 Kgal

Pumping began September 29, 2001.

Final volumes will be determined at completion of Interim Stabilization

- (k) U-109 Initial estimated Pumpable Liquid volume: 119.4 Kgal

Pumping began March 11, 2000. Pumping was shut down on December 3, 2000, due to jet pump failure. Attempts to restart the pump were unsuccessful; the pump was replaced and restarted March 30, 2001.

This tank has been placed in observation mode for evaluation to determine if it meets the interim stabilization criteria.

Final volumes will be determined at completion of Interim Stabilization

TABLE B-2. SINGLE-SHELL TANKS STABILIZATION STATUS SUMMARY

November 30, 2001

Partial Interim Isolated (PI)	Intrusion Prevention Completed (IP)		Interim Stabilized (IS)	
<u>EAST AREA</u>	<u>EAST AREA</u>	<u>WEST AREA</u>	<u>EAST AREA</u>	<u>WEST AREA</u>
A-101	A-103	S-104	A-102	S-103
A-102	A-104	S-105	A-103	S-104
	A-105		A-104	S-105
AX-101	A-106	SX-107	A-105	S-106
		SX-108	A-106	S-108
BY-102	AX-102	SX-109		S-109
BY-103	AX-103	SX-110	AX-102	S-110
BY-105	AX-104	SX-111	AX-103	
BY-106		SX-112	AX-104	SX-104
BY-109	B-FARM - 16 tanks	SX-113		SX-106
	BX-FARM - 12 tanks	SX-114	B-FARM - 16 tanks	SX-107
		SX-115	BX-FARM - 12 tanks	SX-108
C-103	BY-101			SX-109
C-105	BY-104	T-102	BY-101	SX-110
C-106	BY-107	T-103	BY-102	SX-111
East Area 11	BY-108	T-105	BY-103	SX-112
<u>WEST AREA</u>	BY-110	T-106	BY-104	SX-113
S-101	BY-111	T-108	BY-107	SX-114
S-102	BY-112	T-109	BY-108	SX-115
S-103		T-112	BY-109	
S-106	C-101	T-201	BY-110	T-Farm - 16 tanks
S-107	C-102	T-202	BY-111	TX-Farm - 18 tanks
S-108	C-104	T-203	BY-112	TY-Farm - 6 tanks
S-109	C-107	T-204		
S-110	C-108		C-101	U-101
S-111	C-109	TX-FARM - 18 tanks	C-102	U-103
S-112	C-110	TY-FARM - 6 tanks	C-104	U-104
	C-111		C-105	U-105
SX-101	C-112	U-101	C-107	U-106
SX-102	C-201	U-104	C-108	U-110
SX-103	C-202	U-112	C-109	U-112
SX-104	C-203	U-201	C-110	U-201
SX-105	C-204	U-202	C-111	U-202
SX-106	East Area 55	U-203	C-112	U-203
		U-204	C-201	U-204
T-101		West Area 53	C-202	West Area 69
T-104		Total 108	C-203	Total 128
T-107			C-204	
T-110			East Area 60	
T-111				
U-102	Controlled, Clean, and Stable (CCS)			
U-103				
U-105	<u>EAST AREA</u>	<u>WEST AREA</u>		
U-106	BX-FARM - 12 Tanks	TX-FARM - 18 tanks		
U-107		TY FARM - 6 tanks		
U-108	East Area 12	West Area 24		
U-109		Total 36		
U-110				
U-111				
West Area 29				
Total 40				

Note: CCS activities have been deferred until funding is available for this work.

TABLE B-3. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS

November 30, 2001

Tank Number	Tank Integrity	Interim Stabil. Date (1)	Stabil. Method	Tank Number	Tank Integrity	Interim Stabil. Date (1)	Stabil. Method	Tank Number	Tank Integrity	Interim Stabil. Date (1)	Stabil. Method
A-101	SOUND	N/A		C-101	ASMD LKR	11/83	AR	T-108	ASMD LKR	11/78	AR
A-102	SOUND	06/86	SN	C-102	SOUND	09/86	JET(2)	T-109	ASMD LKR	12/84	AR
A-103	ASMD LKR	06/88	AR	C-103	SOUND	N/A		T-110	SOUND	01/00 (5)	JET
A-104	ASMD LKR	06/78	AR(2)	C-104	SOUND	09/88	SN	T-111	ASMD LKR	02/86	JET
A-105	ASMD LKR	07/79	AR	C-105	SOUND	10/86	AR	T-112	SOUND	03/81	AR(2)(3)
A-106	SOUND	06/82	AR	C-106	SOUND	N/A		T-201	SOUND	04/81	AR (3)
AX-101	SOUND	N/A		C-107	SOUND	09/86	JET	T-202	SOUND	06/81	AR
AX-102	ASMD LKR	09/88	SN	C-108	SOUND	03/84	AR	T-203	SOUND	04/81	AR
AX-103	SOUND	08/87	AR	C-109	SOUND	11/83	AR	T-204	SOUND	06/81	AR
AX-104	ASMD LKR	06/81	AR	C-110	ASMD LKR	06/86	JET	TX-101	SOUND	02/84	AR
B-101	ASMD LKR	03/81	SN	C-111	ASMD LKR	03/84	SN	TX-102	SOUND	04/83	JET
B-102	SOUND	08/86	SN	C-112	SOUND	09/90	AR	TX-103	SOUND	06/83	JET
B-103	ASMD LKR	02/86	SN	C-201	ASMD LKR	03/82	AR	TX-104	SOUND	06/79	SN
B-104	SOUND	06/86	SN	C-202	ASMD LKR	06/81	AR	TX-105	ASMD LKR	04/83	JET
B-105	ASMD LKR	12/84	AR	C-203	ASMD LKR	03/82	AR	TX-106	SOUND	06/83	JET
B-106	SOUND	03/86	SN	C-204	ASMD LKR	09/82	AR	TX-107	ASMD LKR	10/79	AR
B-107	ASMD LKR	03/86	SN	S-101	SOUND	N/A		TX-108	SOUND	03/83	JET
B-108	SOUND	05/86	SN	S-102	SOUND	N/A		TX-109	SOUND	04/83	JET
B-109	SOUND	04/86	SN	S-103	SOUND	04/00	JET (6)	TX-110	ASMD LKR	04/83	JET
B-110	ASMD LKR	12/84	AR	S-104	ASMD LKR	12/84	AR	TX-111	SOUND	04/83	JET
B-111	ASMD LKR	06/86	SN	S-105	SOUND	08/88	JET	TX-112	SOUND	04/83	JET
B-112	ASMD LKR	06/86	SN	S-106	SOUND	02/01	JET (10)	TX-113	ASMD LKR	04/83	JET
B-201	ASMD LKR	06/81	AR (3)	S-107	SOUND	N/A		TX-114	ASMD LKR	04/83	JET
B-202	SOUND	05/86	AR(2)	S-108	SOUND	12/86	JET	TX-115	ASMD LKR	09/83	JET
B-203	ASMD LKR	06/84	AR	S-109	SOUND	06/01	JET (13)	TX-116	ASMD LKR	04/83	JET
B-204	ASMD LKR	06/84	AR	S-110	SOUND	01/87	JET	TX-117	ASMD LKR	03/83	JET
BX-101	ASMD LKR	06/78	AR	S-111	SOUND	N/A		TX-118	SOUND	04/83	JET
BX-102	ASMD LKR	11/78	AR	S-112	SOUND	N/A		TY-101	ASMD LKR	04/83	JET
BX-103	SOUND	11/83	AR(2)(3)	SX-101	SOUND	N/A		TY-102	SOUND	06/79	AR
BX-104	SOUND	09/88	SN	SX-102	SOUND	N/A		TY-103	ASMD LKR	02/83	JET
BX-105	SOUND	03/81	SN	SX-103	SOUND	N/A		TY-104	ASMD LKR	11/83	AR
BX-106	SOUND	07/86	SN	SX-104	ASMD LKR	04/00	JET (7)	TY-105	ASMD LKR	02/83	JET
BX-107	SOUND	09/80	JET	SX-105	SOUND	N/A		TY-106	ASMD LKR	11/78	AR
BX-108	ASMD LKR	07/79	SN	SX-106	SOUND	05/00	JET (8)	U-101	ASMD LKR	06/79	AR
BX-109	SOUND	33117	JET	SX-107	ASMD LKR	10/79	AR	U-102	SOUND	N/A	
BX-110	ASMD LKR	08/86	SN	SX-108	ASMD LKR	06/79	AR	U-103	SOUND	09/00	JET (9)
BX-111	ASMD LKR	03/86	JET	SX-109	ASMD LKR	05/81	AR	U-104	ASMD LKR	10/78	AR
BX-112	SOUND	06/80	JET	SX-110	ASMD LKR	06/79	AR	U-105	SOUND	03/01	JET (11)
BY-101	SOUND	05/84	JET	SX-111	ASMD LKR	07/79	SN	U-106	SOUND	03/01	JET (12)
BY-102	SOUND	04/86	JET	SX-112	ASMD LKR	07/79	AR	U-107	SOUND	N/A	
BY-103	ASMD LKR	11/87	JET	SX-113	ASMD LKR	11/78	AR	U-108	SOUND	N/A	
BY-104	SOUND	01/86	JET	SX-114	ASMD LKR	07/79	AR	U-109	SOUND	N/A	
BY-105	ASMD LKR	N/A		SX-115	ASMD LKR	09/78	AR(3)	U-110	ASMD LKR	12/84	AR
BY-106	ASMD LKR	N/A		T-101	ASMD LKR	04/83	SN	U-111	SOUND	N/A	
BY-107	ASMD LKR	07/79	JET	T-102	SOUND	03/81	AR(2)(3)	U-112	ASMD LKR	09/79	AR
BY-108	ASMD LKR	02/86	JET	T-103	ASMD LKR	11/83	AR	U-201	SOUND	06/79	AR
BY-109	SOUND	07/87	JET	T-104	SOUND	11/89 (4)	JET	U-202	SOUND	06/79	SN
BY-110	SOUND	01/86	JET	T-105	SOUND	06/87	AR	U-203	SOUND	06/79	AR
BY-111	SOUND	01/86	JET	T-106	ASMD LKR	06/81	AR	U-204	SOUND	06/79	SN
BY-112	SOUND	06/84	JET	T-107	ASMD LKR	05/86	JET				

LEGEND:

AR = Administratively interim stabilized

JET = Saltwell jet pumped to remove drainable interstitial liquid

SN = Supernatant pumped (Non-Jet pumped)

N/A = Not yet interim stabilized

ASMD

LKR = Assumed Leaker

Interim Stabilized Tanks 129

Not Yet Interim Stabilized 20

Total Single-Shell Tanks 149

TABLE B-3. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS

Footnotes: (in chronological order)

- (1) These dates indicate when the tanks were actually interim stabilized. In some cases, the official interim stabilization documents were issued at a later date.
- (2) Although tanks 241-BX-103, T-102, and T-112 met the interim stabilization administrative procedure at the time they were stabilized, they no longer meet the recently updated administrative procedure. The tanks were re-evaluated in 1996 and letter 9654456, J. H. Wicks to J. K. McClusky, DOE-RL, dated September 1996, was issued which recommended that no further pumping be performed on these tanks, based on an economic evaluation.

Document RPP-5556, Rev. 0, "Updated Drainable Interstitial Liquid Volume Estimates for 119 Single-Shell Tanks Declared Stabilized," J. G. Field, February 7, 2000, states that five tanks no longer meet the stabilization criteria (241-BX-103, T-102, and T-112 exceed the supernatant criteria, and BY-103 and C-102 exceed the Drainable Interstitial Liquid [DIL] criteria).

An intrusion investigation was completed on tank 241-B-202 in 1996 because of a detected increase in surface level. As a result of this investigation, it was determined that this tank no longer meets the recently updated administrative procedure for 200 series tanks.

- (3) Earlier versions of HNF-SD-RE-TI-178, "SST Stabilization Record," indicated that original Interim Stabilization data are missing on four tanks: 241-B-201, T-102, T-112, and T-201. HNF-SD-RE-TI-178, Rev. 7, dated February 9, 2001, added three additional tanks to those missing stabilization data: 241-A-104, BX-101, and SX-115.
- (4) Tank 241-T-104 was Interim Stabilized on November 19, 1999. In-tank video taken October 7, 1999, shows the surface is clearly sludge-type waste with no saltcake present. No visible supernatant on the surface. Waste surface appears level across tank with numerous cracks. There is a minimal collapsed area around the saltwell screen, with no visible bottom.
- (5) Tank 241-T-110 was Interim Stabilized on January 5, 2000, after a major equipment failure. An in-tank video taken October 7, 1999 (pumping was discontinued on August 12, 1999), showed the surface of this tank as smooth, brown-tinted sludge with visible cracks.
- (6) Tank 241-S-103 was declared Interim Stabilized April 18, 2000. The surface is a rough, black and brown-colored waste with yellow patches of saltcake visible throughout. The surface appears to be damp, but not saturated, and shows irregular cracking typically seen with surfaces beginning to dry out. A pool of supernatant liquid (10 feet in diameter, 5 feet deep, 1.0 Kgallons) is visible from video observations.
- (7) Tank 241-SX-104 was declared Interim Stabilized April 26, 2000, after a major equipment failure. The surface is a rough, yellowish gray saltcake waste with an irregular surface of visible cracks and shelves that were created as the surface dried out. The waste surface appears to be dry and shows no standing liquid within the tank.
- (8) Tank 241-SX-106 was declared Interim Stabilized May 5, 2000. The surface is a smooth, white-colored saltcake waste. The surface level slopes slightly from the tank sidewall down to a large depression in the center of the tank. A second depression surrounds both saltwell screens and an abandoned Liquid Observation Well (LOW). The waste surfaces appear dry and show no standing liquid within the tank.

- (9) Tank 241-U-103 was declared Interim Stabilized September 11, 2000. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 30% of the waste surface is covered by the salt formations. The surface level slopes slightly from the tank sidewall down to the first of two depressions in the center of the tank. The waste surface appears dry and shows signs of drying and cracking due to saltwell pumping. LOW readings indicate an average adjusted ILL of 60.2 inches. There is a small pool of supernatant estimated to be 500 gallons.
- (10) Tank 241-S-106 was declared Interim Stabilized on February 1, 2001. The surface is a rough, brown and yellow-colored saltcake waste with an irregular surface of mounds and saltcake crystals that were created as the surface was dried out. The waste surface appears to be dry and shows no standing liquid within the tank. There is no evidence of supernatant from video observations. The waste surface slopes gradually from the tank sidewall to the depression in the center of the tank. The depression surrounds both of the saltwell screens, but does not extend around the temperature probe and ENRAF devices.
- (11) Tank 241-U-105 was declared Interim Stabilized on March 29, 2001, after a major equipment failure. The surface is a brown colored waste with irregular patches of white salt crystal. Approximately 15% of the surface is covered by the salt formations. The surface level slopes to the first of two depressions in the center of the tank; the first depression is cone shaped and estimated to be 22 feet in diameter. The second depression, inside the first, is cylindrically shaped and has a diameter of approximately 10 feet. Both depressions are centered on the saltwell screen. The waste surface appears dry and shows signs of cracking due to saltwell pumping. There is no visible liquid in the tank.
- (12) Tank 241-U-106 was declared Interim Stabilized on March 9, 2001. The surface is a dark brown/yellow colored waste that is covered with many stalagmite-type crystals growing on the surface. The crystals cover approximately 75% of the waste surface. The waste surface is irregular, appears dry, and shows only minimal signs of cracking due to saltwell pumping. The supernatant pool is estimated to be 13.3 feet in diameter based on the visible portion of the saltwell screen. The pool is centered on the saltwell screen.
- (13) Tank 241-S-109 was declared Interim Stabilized on June 11, 2001. The surface is primarily a white colored salt crystal with small patches of dark salt visible due to saltwell/sampling activities. Approximately 95% of the waste surface is covered by the salt formations. The surface level slopes slightly from the tank sidewall down to a depression in the center of the tank. The waste surface appears rough and dry and shows signs of cracking and slumping due to saltwell pumping.

TABLE B-4. SINGLE-SHELL TANK INTERIM STABILIZATION MILESTONES
November 30, 2001

New single-shell tank interim stabilization milestones were negotiated in 1999 and are identified in the "Consent Decree." The Consent Decree was approved on August 16, 1999.

CONSENT DECREE
Attachments A-1 and A-2

The following table is the schedule for pumping liquid waste from the remaining twenty-nine (29) single-shell tanks. This schedule is enforceable pursuant to the terms of the Decree except for the "Projected Pumping Completion Dates," which are estimates only and not enforceable. Also, this schedule does not include tank C-106.

Tank Designation	Project Pumping Start Date	Actual Pumping Start Date	Projected Pumping Completion Date	Interim Stabilization Date
1. T-104	Already initiated	March 24, 1996	May 30, 1999	November 19, 1999
2. T-110	Already initiated	May 12, 1997	May 30, 1999	January 5, 2000
3. SX-104	Already initiated	September 26, 1997	December 30, 2000	April 26, 2000
4. SX-106	Already initiated	October 6, 1998	December 30, 2000	May 5, 2000
5. S-102	Already initiated	March 18, 1999	March 30, 2001	
6. S-106	Already initiated	April 16, 1999	March 30, 2001	February 1, 2001
7. S-103	Already initiated	June 4, 1999	March 30, 2001	April 18, 2000
8. U-103 *	June 15, 2000	September 26, 1999	April 15, 2002	September 11, 2000
9. U-105 *	June 15, 2000	December 10, 1999	April 15, 2002	March 29, 2001
10. U-102 *	June 15, 2000	January 20, 2000	April 15, 2002	
11. U-109 *	June 15, 2000	March 11, 1000	April 15, 2002	
12. A-101	October 30, 2000	May 6, 2000	September 30, 2003	
13. AX-101	October 30, 2000	July 29, 2000	September 30, 2003	
14. SX-105	March 15, 2001	August 8, 2000	February 28, 2003	
15. SX-103	March 15, 2001	October 26, 2000	February 28, 2003	
16. SX-101	March 15, 2001	November 22, 2000	February 28, 2003	
17. U-106 *	March 15, 2001	August 24, 2000	February 28, 2003	March 9, 2001
18. BY-106	July 15, 2001	July 11, 2001	June 30, 2003	
19. BY-105	July 15, 2001	July 11, 2001	June 30, 2003	
20. U-108	December 30, 2001		August 30, 2003	
21. U-107	December 30, 2001	September 29, 2001	August 30, 2003	
22. S-111	December 30, 2001		August 30, 2003	
23. SX-102	December 30, 2001		August 30, 2003	
24. U-111	November 30, 2001		September 30, 2003	
25. S-109	November 30, 2002	September 23, 2000	September 30, 2003	June 11, 2001
26. S-112	November 30, 2002		September 30, 2003	
27. S-101	November 30, 2002		September 30, 2003	
28. S-107	November 30, 2002		September 30, 2003	
29. C-103	The Decree states that no later than December 30, 2000, DOE will determine whether the organic layer and pumpable liquids will be pumped from this tank together or separately, and will establish a deadline for initiating pumping of this tank; the parties will incorporate the initiation deadline into this schedule as provided in Section VI of the Decree. This action is complete: ORP issued a letter to WDOE on December 22, 2000, meeting the requirements of this milestone.			

* Tanks containing organic complexants.

Completion of Interim Stabilization. DOE will complete interim stabilization of all 29 single-shell tanks listed above by September 30, 2004.

Percentage of Pumpable Liquid Remaining to be Removed:

93% of Total Liquid	9/30/1999 (1)
38% of Organic Complexed Pumpable Liquids	9/30/2000 (2)
5% of Organic Complexed Pumpable Liquids	9/30/2001 (3)
18% of Total Liquid	9/30/2002
2% of Total Liquid	9/30/2003

The "percentage of pumpable liquid remaining to be removed" is calculated by dividing the volume of pumpable liquid remaining to be removed from tanks not yet interim stabilized by the sum of the total amount of liquid that has been pumped and the pumpable liquid that remains to be pumped from all tanks.

- (1) The Pumpable Liquid Remaining was reduced to 88% by September 30, 1999. Reference LMHC- 9957926 R1, D. I. Allen, LHMC, to D. C. Bryson, DOE-ORP, dated October 26, 1999.
- (2) The Complexed Pumpable Liquid Remaining was reduced to 38% by September 15, 2000. Reference CHG-0004752, R. F. Wood, CHG, to J. J. Short, DOE-ORP, dated September 13, 2000.
- (3) Reference CHG-0104859, R. F. Wood, CHG, to J. S. O'Connor, DOE-ORP, dated September 20, 2001: this reference states that tanks U-102 and U-109 appear to have met the interim stabilization criteria, thereby reducing the Complexed Pumpable Liquid Remaining to zero; however, it may take three or more months before the settling waste levels approach equilibrium so that the final liquid levels and volumes can be calculated.

TABLE B-5. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 1 of 6)

November 30, 2001

Tank Number	Date Declared Confirmed or Assumed Leaker (3)	Volume Gallons (2)	Associated KiloCuries 137 Cs (9)	Interim Stabilized Date (11)	Leak Estimate	
					Updated	Reference
241-A-103	1987	5500 (8)		06/88	1987	(j)
241-A-104	1975	500 to 2500	0.8 to 1.8 (q)	09/78	1983	(a)(q)
241-A-105 (1)	1983	10000 to 277000	85 to 760 (b)	07/79	1991	(b)(c)
241-AX-102	1988	3000 (8)		09/88	1989	(h)
241-AX-104	1977	-- (8)		08/81	1989	(g)
241-B-101	1974	-- (8)		03/81	1989	(g)
241-B-103	1978	-- (8)		02/85	1989	(g)
241-B-105	1978	-- (8)		12/84	1989	(g)
241-B-107	1980	8000 (8)		03/85	1986	(d)(f)
241-B-110	1981	10000 (8)		03/85	1986	(d)
241-B-111	1978	-- (8)		06/85	1989	(g)
241-B-112	1978	2000		05/85	1989	(g)
241-B-201	1980	1200 (8)		08/81	1984	(e)(f)
241-B-203	1983	300 (8)		06/84	1986	(d)
241-B-204	1984	400 (8)		06/84	1989	(g)
241-BX-101	1972	-- (8)		09/78	1989	(g)
241-BX-102	1971	70000	50 (l)	11/78	1986	(d)
241-BX-108	1974	2500	0.5 (l)	07/79	1986	(d)
241-BX-110	1976	-- (8)		08/85	1989	(g)
241-BX-111	1984 (13)	-- (8)		03/95	1993	(g)
241-BY-103	1973	<5000		11/97	1983	(a)
241-BY-105	1984	-- (8)		N/A	1989	(g)
241-BY-106	1984	-- (8)		N/A	1989	(g)
241-BY-107	1984	15100 (8)		07/79	1989	(g)
241-BY-108	1972	<5000		02/85	1983	(a)
241-C-101	1980	20000 (8)(10)		11/83	1986	(d)
241-C-110	1984	2000		05/95	1989	(g)
241-C-111	1968	5500 (8)		03/84	1989	(g)
241-C-201 (4)	1988	550		03/82	1987	(i)
241-C-202 (4)	1988	450		08/81	1987	(i)
241-C-203	1984	400 (8)		03/82	1986	(d)
241-C-204 (4)	1988	350		09/82	1987	(i)
241-S-104	1968	24000 (8)		12/84	1989	(g)
241-SX-104	1988	6000 (8)		04/00	1988	(k)
241-SX-107	1964	<5000		10/79	1983	(a)
241-SX-108 (5)(14)	1962	2400 to 35000	17 to 140 (m)(q)(t)	08/79	1991	(m)(q)(t)
241-SX-109 (5)(14)	1965	<10000	<40 (n)(t)	05/81	1992	(n)(t)
241-SX-110	1976	5500 (8)		08/79	1989	(g)
241-SX-111 (14)	1974	500 to 2000	0.6 to 2.4 (l)(q)(t)	07/79	1986	(d)(q)(t)
241-SX-112 (14)	1969	30000	40 (l)(t)	07/79	1986	(d)(t)
241-SX-113	1962	15000	8 (l)	11/78	1986	(d)
241-SX-114	1972	-- (8)		07/79	1989	(g)
241-SX-115	1965	50000	21 (o)	09/78	1992	(o)
241-T-101	1992	7500 (8)		04/93	1992	(p)
241-T-103	1974	<1000 (8)		11/83	1989	(g)
241-T-106	1973	115000 (8)	40 (l)	08/81	1986	(d)
241-T-107	1984	-- (8)		05/96	1989	(g)
241-T-108	1974	<1000 (8)		11/78	1980	(f)
241-T-109	1974	<1000 (8)		12/84	1989	(g)
241-T-111	1979, 1984 (12)	<1000 (8)		02/95	1994	(f)(r)
241-TX-105	1977	-- (8)		04/83	1989	(g)
241-TX-107 (5)	1984	2500		10/79	1986	(d)
241-TX-110	1977	-- (8)		04/83	1989	(g)
241-TX-113	1974	-- (8)		04/83	1989	(g)
241-TX-114	1974	-- (8)		04/83	1989	(g)
241-TX-115	1977	-- (8)		09/83	1989	(g)
241-TX-116	1977	-- (8)		04/83	1989	(g)
241-TX-117	1977	-- (8)		03/83	1989	(g)
241-TY-101	1973	<1000 (8)		04/83	1980	(f)
241-TY-103	1973	3000	0.7 (l)	02/83	1986	(d)
241-TY-104	1981	1400 (8)		11/83	1986	(d)
241-TY-105	1960	35000	4 (l)	02/83	1986	(d)
241-TY-106	1959	20000	2 (l)	11/78	1986	(d)
241-U-101	1959	30000	20 (l)	09/79	1986	(d)
241-U-104	1961	55000	0.08 (l)	10/78	1986	(d)
241-U-110	1975	5000 to 8100 (8)	0.05 (q)	12/84	1986	(d)(q)
241-U-112	1980	8500 (8)		09/79	1986	(d)

87 Tanks <750,000 - 1,050,000 (7)

N/A = not applicable (not yet interim stabilized)

TABLE B-5. SINGLE-SHELL TANKS LEAK VOLUME ESTIMATES

Footnotes:

- (1) Current estimates [see Reference (b)] are that 610 Kgallons of cooling water was added to tank 241-A-105 from November 1970 to December 1978 to aid in evaporative cooling. In accordance with Dangerous Waste Regulations [Washington Administrative Code 173-303-070 (2)(a)(ii), as amended, Washington State Department of Ecology, 1990, Olympia, Washington], any of this cooling water that has been added and subsequently leaked from the tank must be classified as a waste and should be included in the total leak volume. In August 1991, the leak volume estimate for this tank was updated in accordance with the WAC regulations. Previous estimates excluded the cooling water leaks from the total leak volume estimates because the waste content (concentration) in the cooling water which leaked should be much less than the original liquid waste in the tank (the sludge is relatively insoluble). The total leak volume estimate in this report (10 to 277 Kgallons) is based on the following (see References):

1. Reference (b) contains an estimate of 5 to 15 Kgallons for the initial leak prior to August 1968.
2. Reference (b) contains an estimate of 5 to 30 Kgallons for the leak while the tank was being sluiced from August 1968 to November 1970.
3. Reference (b) contains an estimate of 610 Kgallons of cooling water added to the tank from November 1970 to December 1978, but it was estimated that the leakage was small during this period. This reference contains the statement "Sufficient heat was generated in the tank to evaporate most, and perhaps nearly all, of this water." This results in a low estimate of zero gallons leakage from November 1970 to December 1978.
4. Reference (c) contains an estimate the 378 to 410 Kgallons evaporated out of the tank from November 1970 to December 1978. Subtracting the minimum evaporation estimate from the cooling water added estimate provides a range from 0 to 232 Kgallons of cooling water leakage from November 1970 to December 1978.

	<u>Low Estimate</u>	<u>High Estimate</u>
Prior to August 1968	5,000	15,000
August 1968 to November 1970	5,000	30,000
November 1970 to December 1978	0	232,000
Totals	10,000	277,000

- (2) These leak volume estimates do not include (with some exceptions), such things as: (a) cooling/raw water leaks, (b) intrusions (rain infiltration) and subsequent leaks, (c) leaks inside the tank farm but not through the tank liner (surface leaks, pipeline leaks, leaks at the joint for the overflow or fill lines, etc.), and (d) leaks from catch tanks, diversion boxes, encasements, etc.
- (3) In many cases, a leak was suspected long before it was identified or confirmed. For example, Reference (d) shows that tank 241-U-104 was suspected of leaking in 1956. The leak was confirmed in 1961. This report lists the "assumed leaker" date of 1961. Using present standards, tank 241-U-104 would have been declared an assumed leaker in 1956. In 1984, the criteria designations of "suspected leaker," "questionable integrity," "confirmed leaker," "declared leaker," "borderline and dormant," were merged into one category now reported as "assumed leaker." See Reference (f) for explanation of when, how long, and how fast some of the tanks leaked. It is highly likely that there have been undetected leaks from single-shell tanks because of the nature of their design and instrumentation.
- (4) The leak volume estimate date for these tanks is before the declared leaker date because the tank was in a suspected leaker or questionable integrity status; however, a leak volume had been estimated prior to the tank being reclassified.

- (5) The increasing radiation levels in drywells and laterals associated with these three tanks could be indicating continuing leak or movement of existing radionuclides in the soil. There is no conclusive way to confirm these observations. (Repeat spectral drywell scans are not part of the current Tank Farm leak detection program but can be run on request a special needs arise. A select subset of drywells is routinely monitored by the Vadose Zone Characterization Project to assess movement of gamma-emitting radionuclides in the subsurface. There are currently no functioning laterals and no plan to prepare them for use).
- (6) Methods were used to estimate the leak volumes from these 19 tanks based on the assumption that their cumulative leakage is approximately the same as for 18 of the 24 tanks identified in footnote (9). For more details see Reference (g). The total leak volume estimate for these tanks is 150 Kgallons (rounded to the nearest Kgallon), for an average of approximately 8 Kgallons for each of 19 tanks.
- (7) The total has been rounded to the nearest 50 Kgallons. Upper bound values were used in many cases in developing these estimates. It is likely that some of these tanks have not actually leaked.
- (8) Leak volume estimate is based solely on observed liquid level decreases in these tanks. This is considered to be the most accurate method for estimating leak volumes.
- (9) The curie content shown is as listed in the reference document and is not decayed to a consistent date: therefore, a cumulative total is inappropriate.
- (10) Tank 241-C-101 experienced a liquid level decrease in the late 1960s and was taken out of service and pumped to a minimum heel in December 1969. In 1970, the tank was classified as a "questionable integrity" tank. Liquid level data show decreases in level throughout the 1970s and the tank was saltwell pumped during the 1970s, ending in April 1979. The tank was reclassified as a "confirmed leaker" in January 1980. See References (q) and (r); refer to Reference (s) for information on the potential for there to have been leaks from other C-farm tanks (specifically, C-102, C-103, and C-109).
- (11) These dates indicate when the tanks were declared to be interim stabilized. In some cases, the official interim stabilization documents were issued at a later date. Also, in some cases, the field work associated with interim stabilization was completed at an earlier date.
- (12) Tank 241-T-111 was declared an "assumed re-leaker" on February 28, 1994, due to a decreasing trend in surface level measurement. This tank was pumped, and interim stabilization completed on February 22, 1995.
- (13) Tank 241-BX-111 was declared an "assumed re-leaker" in April 1993. Preparations for pumping were delayed, following an administrative hold placed on all tank farm operations in August 1993. Pumping resumed and the tank was declared interim stabilized on March 15, 1995.
- (14) The leak volume and curie release estimates on tanks 241- SX-108, SX-109, SX-111, and SX-112 have been re-evaluated using a Historical Leak Model [see Reference (t)]. In general, the model estimates are much higher than the values listed in the table, both for volume and curies released. The values listed in the table do not reflect this revised estimate because, "In particular, it is worth emphasizing that this report was never meant to be a definitive update for the leak baseline at the Hanford Site. It was rather meant to be an attempt to view the issue of leak inventories with a new and different methodology." (This quote is from the first page of the referenced report).
- (15) In July 1998, the Washington State Department of Ecology (Ecology) directed the U. S. Department of Energy (DOE) to develop corrective action plans for eight single-shell tank farms (B/BX/BY/S/SX/T/TX/TY) where groundwater contamination likely originated from tank farm operations. A Tri-Party Agreement milestone (M-45 series) was developed that established a formalized approach for evaluating impacts on groundwater quality of loss of tank wastes to the vadose zone underlying these tank farms. Planning documents have been completed for the S, SX, B, BX, and BY tank farms and will be completed shortly for the T, TX, and TY farms. The phase 1 field investigation is near completion in the

S and SX tank farms and has begun in the B, BX, and BY farms. Field work is anticipated in FY-02 for the T, TX, and TY tank farms. The remaining four single-shell tank farms are expected to be included in corrective action plans in the near future.

All of the information included in this appendix is currently under review and significant revisions are anticipated. Recently, major tank farm vadose zone investigative efforts (such as the baseline spectral gamma-ray logging of all drywells in all single-shell tank farms, as well as drilling and sampling in the SX tank farm) were completed. This appendix will be revised as a better understanding of past tank leak events is developed.

SST Vadose Zone Project drilling and testing activities near tank 241-BX-102 were completed in March 2001. A borehole (299-E33-45) was drilled through the postulated uranium plume resulting from the 1951 tank 241-BX-102 overflow event to confirm the presence of uranium, define its present depth, and survey other contaminants of interest such as Tc-99. Thirty-five split-spoon samples were collected for laboratory analyses. This borehole was decommissioned after collection and analysis of groundwater samples.

Borehole W33-46, adjacent to tank 241-B-110, was drilled to a depth of approximately 190 feet in July 2001. Soil samples were collected for analysis as part of the tank farm vadose zone characterization activities. During decommissioning, this borehole was completed as a vadose zone monitoring structure. Work was accomplished in cooperation with scientists from Idaho National Engineering and Environmental Laboratory and Pacific Northwest National Laboratory. This borehole is now the first fully instrumented vadose zone hydrographic monitoring structure to be completed in a Hanford site tank farm.

References:

- (a) Murthy, K. S., et al., June 1983, *Assessment of Single-Shell Tank Residual Liquid Issues at Hanford Site*, Washington, PNL-4688, Pacific Northwest Laboratory, Richland, Washington.
- (b) WHC, 1991a, *Tank 241-A-105 Leak Assessment*, WHC-MR-0264, Westinghouse Hanford Company, Richland, Washington.
- (c) WHC, 1991b, *Tank 241-A-105 Evaporation Estimate 1970 Through 1978*, WHC-EP-0410, Westinghouse Hanford Company, Richland, Washington.
- (d) Smith, D. A., January 1986, *Single-Shell Tank Isolation Safety Analysis Report*, SD-WM-SAR-006, Rev. 1, Westinghouse Hanford Company, Richland, Washington.
- (e) McCann, D. C., and T. S. Vail, September 1984, *Waste Status Summary*, RHO-RE-SR-14, Rockwell Hanford Operations, Richland, Washington.
- (f) Catlin, R. J., March 1980, *Assessment of the Surveillance Program of the High-Level Waste Storage Tanks at Hanford*, Hanford Engineering Development Laboratory, Richland, Washington.
- (g) Baumhardt, R. J., May 15, 1989, Letter to R. E. Gerton, U.S. Department of Energy-Richland Operations Office, *Single-Shell Tank Leak Volumes*, 8901832B R1, Westinghouse Hanford Company, Richland, Washington.
- (h) WHC, 1990a, Occurrence Report, *Surface Level Measurement Decrease in Single-Shell Tank 241-AX-102*, WHC-UO-89-023-TF-05, Westinghouse Hanford Company, Richland, Washington.
- (i) Groth, D. R., July 1, 1987, Internal Memorandum to R. J. Baumhardt, *Liquid Level Losses in Tanks 241-C-201, -202 and -204*, 65950-87-517, Westinghouse Hanford Company, Richland, Washington.
- (j) Groth, D. R., and G. C. Owens, May 15, 1987, Internal Memorandum to J. H. Roecker, *Tank 103-A Integrity Evaluation*, Westinghouse Hanford Company, Richland, Washington.
- (k) Dunford, G. L., July 8, 1988, Internal Memorandum to R. K. Welty, *Engineering Investigation: Interstitial Liquid Level Decrease in Tank 241-SX-104*, 13331-88-416, Westinghouse Hanford Company, Richland, Washington.
- (l) ERDA, 1975, *Final Environmental Statement Waste Management Operations, Hanford Reservation*, Richland, Washington, ERDA-1538, 2 vols., U.S. Energy Research and Development Administration, Washington, D.C.
- (m) WHC, 1992a, *Tank 241-SX-108 Leak Assessment*, WHC-MR-0300, Westinghouse Hanford Company, Richland, Washington.
- (n) WHC, 1992b, *Tank 241-SX-109 Leak Assessment*, WHC-MR-0301, Westinghouse Hanford Company, Richland, Washington.
- (o) WHC, 1992c, *Tank 241-SX-115 Leak Assessment*, WHC-MR-0302, Westinghouse Hanford Company, Richland, Washington.
- (p) WHC, 1992d, Occurrence Report, *Apparent Decrease in Liquid Level in Single Shell Underground Storage Tank 241-T-101, Leak Suspected; Investigation Continuing*, RL-WHC-TANKFARM-1992-0073, Westinghouse Hanford Company, Richland, Washington.
- (q) WHC, 1990b, *A History of the 200 Area Tank Farms*, WHC-MR-0132, Westinghouse Hanford Company, Richland, Washington.

- (r) WHC, 1993a, *Assessment of Unsaturated Zone Radionuclide Contamination Around Single-Shell Tanks 241-C-105 and 241-C-106*, WHC-SD-EN-TI-185, REV OA, Westinghouse Hanford Company, Richland, Washington.
- (s) WHC, 1994, Occurrence Report, *Apparent Liquid Level Decrease in Single Shell Underground Storage Tank 241-T-111; Declared an Assumed Re-Leaker*, RL-WHC-TANKFARM-1994-0009, Westinghouse Hanford Company, Richland, Washington.
- (t) HNF, 1998, Agnew, S. F., and R. A. Corbin, August 1998, *Analysis of SX Farm Leak Histories - Historical Leak Model (HLM)*, HNF-3233, Rev. 0, Los Alamos National Laboratory, Los Alamos, New Mexico

TABLE B-6. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS
149 Tanks
November 30, 2001

All Single-Shell Tanks were in compliance for this month.

Legend:	
O/C	Noncompliance with applicable documentation
N/A	Not Applicable (not monitored, or no monitoring schedule)
None	Applicable equipment not installed
LOW	LOW reading taken by Neutron Probe (Exception: Tank AX-101 taken by gamma sensors)
POP	Plant Operating Procedure, TO-040-650
MT/FIC/ENRAF	Surface level measurement devices
OSD	Operating Specification Document OSD-T-151-00013, -00030, and -00031
FSAR/TSR	Final Safety Analysis Report/Technical Safety Requirements

Notes:

All Dome Elevation Survey monitoring is in compliance.
 Drywell monitoring is no longer required.
 Psychrometrics monitoring is on an as needed basis.
 In-tank photos/videos are taken on an as needed basis.

TABLE B-7. TEMPERATURE MONITORING
November 30, 2001

SINGLE-SHELL TANKS WITH HIGH HEAT LOADS (>26,000 Btu/hr)

Twelve single-shell tanks have been identified as having high heat loads, of which nine tanks have other characteristics that require temperature surveillance (HNF-SD-WM-TSR-006, *Tank Farm Technical Safety Requirements*). In an analysis, WHC-SD-WM-SARR-010, Rev. 1, *Heat Removal Characteristics of Waste Storage Tanks*, Kummerer, 1995, it was estimated that these nine tanks have heat sources >26,000 Btu/hr, which is the criterion for determining high heat load tanks.

Temperatures in these tanks did not exceed the Technical Safety Requirements (TSR) for this month. The tanks are monitored by TMACS.

	<u>Tank No.</u>	
C-106 (1)	SX-108	SX-111
SX-103	SX-109	SX-112
SX-107	SX-110	SX-114

- (1) The final thermal analysis report for tank C-106 was issued August 9, 2000 (RPP-6463, Rev. 0) and concluded that the best estimate for C-106 was between 7,000 and 11,000 Btu/hr, therefore, this tank no longer meets the criterion for a high heat load tank. An AB Amendment is required to revise the temperature control limits and monitoring frequency for C-106. It is expected this AB Amendment will be approved by ORP in December 2001.

Active ventilation:

There are 13 SX tanks on active ventilation (SX-101 through SX-114, with the exception of SX-113). Eight of these SX tanks are on the high heat load tank list – see above.

SINGLE-SHELL TANKS WITH LOW HEAT LOADS (<26,000Btu/hr)

There are 137 low heat load tanks. Temperatures in tanks connected to TMACS are monitored by TMACS; temperatures in those tanks not yet connected to TMACS are manually taken semiannually in January and July. These temperatures have been within historical ranges for the applicable tank.

No temperatures have been obtained for several years in the 14 tanks listed below. Most of these tanks have no thermocouple trees.

	<u>Tank No.</u>			
BX-104	C-104	T-102	TX-110	TX-117
BY-102	C-204	T-105	TX-114	U-104
BY-109	SX-115	TX-101	TX-116	

This page intentionally left blank

APPENDIX C
MISCELLANEOUS UNDERGROUND STORAGE TANKS
AND SPECIAL SURVEILLANCE FACILITIES

**TABLE C-1. EAST AND WEST AREA MISCELLANEOUS UNDERGROUND STORAGE TANKS
AND SPECIAL SURVEILLANCE FACILITIES**

ACTIVE - still running transfers through the associated diversion boxes or pipeline encasements

November 30, 2001

<u>FACILITY</u>	<u>LOCATION</u>	<u>PURPOSE (receives waste from:)</u>	<u>WASTE (Gallons)</u>	<u>MONITORED BY</u>	<u>REMARKS</u>
EAST AREA					
241-A-302-A	A Farm	A-151 DB	888	SACS/ENRAF/Manually	Pumped to AW-105 7/00
241-ER-311	B Plant	ER-151, ER-152 DB	2152	SACS/ENRAF/Manually	
241-AZ-151	AZ Farm	AZ-702 condensate	2340	SACS/ENRAF/TMACS	Volume changes daily - pumped to AZ-101 or AZ-102 as needed.
241-AZ-154	AZ Farm		25	SACS/MT	
244-BX-TK/SMP	BX Complex	DCRT - Receives from several farms	24086	SACS/MT	Using Manual Tape for tank/sump. Pumped several times 7/01 to 11/01. Sump O/S 2/5/01.
244-A-TK/SMP	A Complex	DCRT - Receives from several farms	7569	MCS/SACS/WTF	WTF - pumped 3/99 to AP-108
A-350	A Farm	Collects drainage	257	MCS/SACS/WTF	WTF (uncorrected) pumped as needed
AR-204	AY Farm	Tanker trucks from various facilities	360	DIP TUBE	Alarms on SACS-pumped to AP-108, 7/00
A-417	A Farm		13814	SACS/WTF	Pumped 4/98; WTF O/S 6/01; readings taken with zip cord
CR-003-TK/SUMP	C Farm	DCRT	2984	MT/ZIP CORD	Zip cord in sump O/S, 3/96; water intrusion, 1/98
WEST AREA					
241-TX-302-C	TX Farm	TX-154 DB	165	SACS/ENRAF/Manually	
241-U-301-B	U Farm	U-151, U-152, U-153, U-252 DB	8024	SACS/ENRAF/Manually	Returned to service 12/30/93
241-UX-302-A	U Plant	UX-154 DB	3488	SACS/ENRAF/Manually	
241-S-304	S Farm	S-151 DB	130	SACS/ENRAF/Manually	Replaced S-302-A, 10/91; ENRAF installed 7/98. Sump not alarming.
244-S-TK/SMP	S Farm	From original tanks to SY-102	27340	SACS/Manually	WTF (uncorrected); transferred from S-219, 6/01
244-TX-TK/SMP	TX Farm	From original tanks to SY-102	17017	SACS/Manually	MT - pumped PFP 241-Z tank D-5 to 244-TX DCRT 12/1/01, level now 93.75 in.
Vent Station Catch Tank		Cross Country Transfer Line	376	SACS/Manually	MT

Total Active Facilities 17

LEGEND:	DB -	Diversion Box
	DCRT -	Double-Contained Receiver Tank
	TK, SMP -	Tank, Sump
	FIC, ENRAF -	Surface Level Measurement Devices
	MT -	Manual Tape - Surface Level Measurement Device
	Zip Cord -	Surface Level Measurement Device
	WTF -	Weight Time Factor - can be recorded as WTF, CWF (corrected), and Uncorrected WTF
	SACS -	Surveillance Automated Control System
	MCS -	Monitor and Control System
	Manually -	Not connected to any automated system
	O/S -	Out of Service

HNF-EP-0182, Rev 164

TABLE C-2. EAST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES
(CURRENTLY MANAGED BY CHG)
INACTIVE - no longer receiving waste transfers
November 30, 2001

<u>FACILITY</u>	<u>LOCATION</u>	<u>RECEIVED WASTE FROM: (or descrip.)</u>	<u>WASTE (Gallons)</u>	<u>MONITORED BY</u>	<u>REMARKS</u>
209-E-TK-111	209 E Bldg	Decon Catch Tank	Empty	NM	Removed from service 1988
216-BY-201	BY Farm	TBP Waste Line	Unknown	NM	
241-A-302-B	A Farm	A-152 DB	5798	SACS/MT	Isolated 1985, Project B-138 Interim Stabilized 1990, Rain intrusion
241-AX-151	N of PUREX	PUREX	Unknown	NM	Isolated 1985
241-AX-152	AX Farm	AX-152 DB	0	SACS/MT	Declared Assumed Leaker; pumped to AY-102 3/1/01, no longer being used
241-B-301-B	B Farm	B-151, B-152, B-153, B-252 DB	22250	NM	Isolated 1985 (1)
241-B-302-B	B Farm	B-154 DB	4930	NM	Isolated 1985 (1)
241-BX-302-A	BX Farm	BR-152, BX-153, BXR-152, BYR-152 DB	840	NM	Isolated 1985 (1)
241-BX-302-B	BX Farm	BX-154 DB	1040	NM	Isolated 1985 (1)
241-BX-302-C	BX Farm	BX-155 DB	870	NM	Isolated 1985 (1)
241-BY-ITS2-Tk 2	BY Farm	Heater Flush Tank	Unknown	NM	Stabilized 1977
241-C-301-C	C Farm	C-151, C-152, C-153, C-252 DB	10470	NM	Isolated 1985 (1)
241-ER-311A	SW B Plant	ER-151 DB	Empty	NM	Abandoned in place 1954
244-AR Vault	A Complex	Between farms & B-Plant	Unknown	NM	Not actively being used, systems activated for final clean out.
244-BXR-TK/SMP-001	BX Farm	Transfer lines	7200	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-002	BX Farm	Transfer lines	2180	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-003	BX Farm	Transfer lines	1810	NM	Interim Stabilization 1985 (1)
244-BXR-TK/SMP-011	BX Farm	Transfer lines	7100	NM	Interim Stabilization 1985 (1)

Total East Area Inactive Facilities 18

LEGEND:	DB -	Diversion Box
	DCRT -	Double-Contained Receiver Tank
	MT -	Manual Tape
	SACS -	Surveillance Automated Control System
	TK, SMP -	Tank, Sump
	R -	Replacement
	NM -	Not Monitored

(1) SOURCE: WHC-SD-WM-TI-356, "Waste Storage Tank Status & Leak Detection Criteria," Rev. 0, September 30, 1988

HNF-EP-0182, Rev. 164

TABLE C-3. WEST AREA INACTIVE MISC. UNDERGROUND STORAGE TANKS AND SPECIAL SURV. FACILITIES
(CURRENTLY MANAGED BY CHG)
INACTIVE - no longer receiving waste transfers
November 30, 2001

<u>FACILITY</u>	<u>LOCATION</u>	<u>RECEIVED WASTE FROM: (or descr (Gallons))</u>	<u>WASTE MONITORED</u>	<u>BY</u>	<u>REMARKS</u>
213-W-TK-1	E of 213-W Compressor Facility	Water Retention Tank	Unknown	NM	Contains only water
231-W-151-001	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
231-W-151-002	N. of Z Plant	231-Z Floor drains	Unknown	NM	Inactive, last data 1974
241-S-302	S Farm	240-S-151 DB	8340	SACS/ENRAF	Assumed Leaker EPDA 85-04
241-S-302-A	S Farm	241-S-151 DB	0		Assumed Leaker TF-EFS-90-042
Partially filled with grout 2/91, determined still to be an assumed leaker after leak test. Manual FIC readings are unobtainable due to dry grouted surface. CASS monitoring system retired 2/23/99; intrusion readings discontinued. S-304 replaced S-302-A					
241-S-302-B	S Farm	S Encasements	Empty	NM	Isolated 1985 (1)
241-SX-302 (SX-304)	SX Farm	SX-151 DB, 151 TB	Unknown	NM	Isolated 1987
241-T-301	T Farm	DB T-151, -151, -153, -252	Unknown	NM	Isolated 1985 (241-T-301B)
241-TX-302	TX Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TX-302-X-B	TX Farm	TX Encasements	Unknown	NM	Isolated 1985 (1)
241-TX-302-B	TX Farm	TX-155 DB	1600	SACS/MT	New MT installed 7/16/93
241-TX-302-B(R)	E. of TX Farm	TX-155 DB	Unknown	NM	Isolated
241-TY-302-A	TY Farm	TX-153 DB	Unknown	NM	Isolated 1985 (1)
241-TY-302-B	TY Farm	TY Encasements	Empty	NM	Isolated 1985 (1)
241-Z-8	E. of Z Plant	Recuplex waste	Unknown	NM	Isolated, 1974, 1975
242-T-135	T Evaporator	T Evaporator	Unknown	NM	Isolated
242-TA-R1	T Evaporator	Z Plant waste	Unknown	NM	Isolated
243-S-TK-1	N. of S Farm	Personnel Decon. Facility	Empty	NM	Isolated
244-TXR-TK/SMP-001	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-002	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-TXR-TK/SMP-003	TX Farm	Transfer lines	Unknown	NM	Interim Stabilized, MT removed 1984 (1)
244-UR-001 Vault TK	U-Farm	Tank, Sump and Cell	4220	NM	Stabilized 1985
244-UR-002 Vault TK	U-Farm	Tank, Sump and Cell	1400	NM	Stabilized 1985
244-UR-003 Vault Tk	U-Farm	Tank, Sump and Cell	5996	NM	Stabilized 1985
244-UR-004 Vault Tk	U-Farm	Tank, Sump and Cell	Empty	NM	Stabilized 1985

Total West Area Inactive Facilities 25

LEGEND:	DB, TB -	Diversion Box, Transfer Box
	DCRT -	Double-Contained Receiver Tank
	FIC, ENRAF -	Surface Level Measurement Devices
	MT -	Manual Tape - Surface Level Measurement Device
	TK, SMP -	Tank, Sump
	SACS -	Surveillance Automated Control System
	R -	Replacement
	NM -	Not Monitored

(1) SOURCE: WHC-SD-WM-TI-356, "Waste Storage Tank Status & Leak Detection Criteria," Rev. 0, September 30, 1988

HNF-EP-0182, Rev. 164

APPENDIX D
GLOSSARY OF TERMS

TABLE D-1. GLOSSARY OF TERMS

1. TANK STATUS CODES

TANK USE (Double-Shell Tanks Only)

CWHT	Concentrated Waste Holding Tank
DRCVR	Dilute Receiver Tank
EVFD	Evaporate Feed Tank
SRCVR	Slurry Receiver Tank

2. DEFINITIONS

WASTE TANKS - General

Waste Tank Safety Issue

A potentially unsafe condition in the handling of waste material in underground storage tanks that requires corrective action to reduce or eliminate the unsafe condition. There are currently no waste tank safety issues.

Characterization

Characterization is understanding the Hanford tank waste chemical, physical, and radiological properties to the extent necessary to ensure safe storage and interim operation, and ultimate disposition of the waste.

WASTE TYPES

Aging Waste (AW)

High level, first cycle solvent extraction waste from the PUREX plant (NCAW).

Concentrated Complexant (CC)

Concentrated product from the evaporation of dilute complexed waste.

Concentrated Phosphate Waste (CP)

Waste originating from the decontamination of the N Reactor in the 100 N Area. Concentration of this waste produces concentrated phosphate waste.

Dilute Complexed Waste (DC)

Characterized by a high content of organic carbon including organic complexants: ethylenediaminetetraacetic acid (EDTA), citric acid, and hydroxyethyl-ethylenediaminetriacetic acid (HEDTA), were the major complexants used. Main sources of DC waste in the DST system are saltwell liquid inventory (from SSTs).

Dilute Non-Complexed Waste (DN)

Low activity liquid waste originating from S and T Plants, the 300 and 400 Areas, PUREX facility (decladding supernatant and miscellaneous wastes), 100 N Area (sulfate waste), B Plant, saltwells, and PFP (supernatant).

Drainable Interstitial Liquid (DIL)

Interstitial liquid that is not held in place by capillary forces and will, therefore, migrate or move by gravity. (See also Section 3 below)

Double-Shell Slurry (DSS)

Waste that exceeds the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. For reporting purposes, DSS is considered a solid.

Double-Shell Slurry Feed (DSSF)

Waste concentrated just before reaching the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. This form is not as concentrated as DSS.

Supernatant Liquid

The liquid above the solids or in large liquid pools covered by floating solids in waste storage tanks. (See also Section 3 below)

INTERIM STABILIZATION (Single-Shell Tanks only)

Interim Stabilized (IS)

A tank which contains less than 50 Kgallons of drainable interstitial liquid and less than 5 Kgallons of supernatant. If the tank was jet pumped to achieve interim stabilization, then the jet pump flow or saltwell screen inflow must also have been at or below 0.05 gpm before interim stabilization criteria are met.

Jet Pump

The jet pump system includes 1) a jet assembly with foot valve mounted to the base of two pipes that extend from the top of the well casing to near the bottom of the well casing inside the saltwell screen, 2) a centrifugal pump to supply power fluid to the down-hole jet assembly, 3) flexible or rigid transfer jumpers, 4) a flush line, and 5) a flowmeter. The jumpers contain piping, valves, and pressure and limit switches.

The centrifugal pump and jet assembly are needed to pump the interstitial liquid from the saltwell screen into the pump pit, nominally a 40-foot elevation rise. The power fluid passes through a nozzle in the jet assembly and acts to convert fluid pressure head to velocity head, thereby reducing the pressure in the jet assembly chamber. The reduction in pressure allows the interstitial liquid to enter the jet assembly chamber and mix with the power fluid. Velocity head is converted to pressure head above the nozzle, lifting power fluid, and interstitial liquid to the pump pit. Pumping rates vary from 0.05 to about 4 gpm.

Saltwell Screen

The saltwell system is a 10-inch diameter saltwell casing consisting of a stainless steel saltwell screen welded to a Schedule 40 carbon steel pipe. The casing and screen are to be inserted into the 12-inch tank riser located in the pump pit. The stainless steel screen portion of the system will extend through the tank waste to near the bottom of the tank. The saltwell screen portion of the casing is an approximately 10-foot length of 300 Series, 10-inch diameter, stainless steel pipe with screen openings (slots) of 0.05 inches.

Emergency Pumping Trailer

A 45-foot tractor-type trailer is equipped to provide storage space and service facilities for emergency pumping equipment: this consists of two dedicated jet pump jumpers and two jet pumps, piping and dip tubes for each, two submersible pumps and attached piping, and a skid-mounted Weight Factor Instrument Enclosure with an air compressor and electronic recording instruments. The skid also contains a power control station for the pumps, pump pit leak detection, and instrumentation. A rack for over 100 feet of overground double-contained piping is also in the trailer.

INTRUSION PREVENTION (ISOLATION) (Single-Shell Tanks only)

Partially Interim Isolated (PI)

The administrative designation reflecting the completion of the physical effort required for Interim Isolation except for isolation of risers and piping that is required for jet pumping or for other methods of stabilization.

Interim Isolated (II)

The administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. In June 1993 the term "Interim Isolation" was replaced by "Intrusion Prevention."

Intrusion Prevention (IP)

Intrusion Prevention is the administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. Under no circumstances are electrical or instrumentation devices disconnected or disabled during the intrusion prevention process (with the exception of the electrical pump).

Controlled, Clean, and Stable (CCS)

Controlled, Clean, and Stable reflects the completion of several objectives: "Controlled" - provide remote monitoring for required instrumentation and implement controls required in the TWRS Authorization Basis; "Clean" - remove surface soil contamination and downpost the Tank Farms to RBA/URMA/RA radiological control status, remove abandoned equipment, and place reusable equipment in compliant storage; and "Stable" - remove pumpable liquids from the SSTs and IMUSTs and isolate the tanks.

TANK INTEGRITY

Sound

The integrity classification of a waste storage tank for which surveillance data indicate no loss of liquid attributed to a breach of integrity.

Assumed Leaker

The integrity classification of a waste storage tank for which surveillance data indicate a loss of liquid attributed to a breach of integrity.

Assumed Re-Leaker

A condition that exists after a tank has been declared as an "assumed leaker" and then the surveillance data indicate a new loss of liquid attributed to a breach of integrity.

TANK INVESTIGATION

Intrusion

A term used to describe the infiltration of liquid into a waste tank.

SURVEILLANCE INSTRUMENTATION

Drywells

Historically, the drywells were monitored with gross logging tools as part of a secondary leak monitoring system. In some cases, neutron-moisture sensors were used to monitor moisture in the soil as a function of well depth, which could be indicative of tank leakage. The routine gross gamma logging data were stored electronically from 1974 through 1994. The routine gross gamma logging program ended in 1994. A program was initiated in 1995 to log each of the available drywells in each tank farm with a spectral gamma logging system. The spectral gamma logging system provides quantitative values for gamma-emitting radionuclides. The baseline spectral gamma logging database is available electronically.

Repeat spectral drywell scans are not part of the established Tank Farm leak detection program, but they can be run on request if special needs arise. A select subset of drywells is routinely monitored by the Vadose Zone Characterization Project to assess movement of gamma-emitting radionuclides in the subsurface.

Laterals

Laterals are horizontal drywells positioned under single-shell waste storage tanks to detect radionuclides in the soil which could be indicative of tank leakage. These drywells can be monitored by radiation detection probes. Laterals are 4-inch inside diameter steel pipes located 8 to 10 feet below the tank's concrete base. There are three laterals per tank. Laterals are located only in A and SX farms. There are currently no functioning laterals and no plan to prepare them for use.

Surface Levels

The surface level measurements in all waste storage tanks are monitored by manual or automatic conductivity probes, and recorded and transmitted or entered into the Surveillance Analysis Computer System (SACS).

Automatic FIC

An automatic waste surface level measurement device is manufactured by the Food Instrument Company (FIC). The instrument consists of a conductivity electrode (plummet) connected to a calibrated steel tape, a steel tape reel housing and a controller that automatically raises and lowers the plummet to obtain a waste surface level reading. The controller can provide a digital display of the data and until February 1999, the majority of the FICs transmitted readings to the CASS. Since CASS retirement, all FIC gauges are read manually. FICs are being replaced by ENRAF detectors (see below).

ENRAF 854 ATG Level Detector

FICs and some manual tapes are in the process of being replaced by the ENRAF ATG 854 level detector. The ENRAF gauge, fabricated by ENRAF Incorporated, determines waste level by detecting variations in the weight of a displacer suspended in the tank waste. The displacer is connected to a wire wound onto a precision measuring drum. A change in the waste level causes a change in the weight of the displacer which will be detected by the force transducer. Electronics within the gauge causes the servo motor to adjust the position of the displacer and compute the tank level based on the new position of the displacer drum. The gauge displays the level in decimal inches. The first few ENRAFs that received remote reading capability transmit liquid level data via analog output to the TMACS. The remaining ENRAFs and future installations will transmit digital level data to TMACS via an ENRAF Computer Interface Unit (CIU). The CIU allows fully remote communication with the gauge, minimizing tank farm entry.

Annulus

The annulus is the space between the inner and outer shells on DSTs only. Drain channels in the insulating and/or supporting concrete carry any leakage to the annulus space where conductivity probes are installed. The annulus conductivity probes and radiation detectors are the primary means of leak detection for all DSTs.

Liquid Observation Well (LOW)

In-tank liquid observation wells are used for monitoring the interstitial liquid level (ILL) in single-shell tanks. The wells are usually constructed of fiberglass or TEFZEL-reinforced epoxy-polyester resin (TEFZEL is a trademark of E. I. du Pont de Nemours & Company). There are a few LOWs constructed of steel. LOWs are sized to extend to within 1 inch of the bottom of the waste tank, are sealed at their bottom ends, and have a nominal outside diameter of 3.5 inches. Gamma and neutron probes are used to monitor changes in the ILL, and can indicate intrusions or leakage by increases or decreases in the ILL. There are 65 LOWs (64 are in operation) installed in SSTs that contain or are capable of containing greater than 50 Kgallons of drainable interstitial liquid. Two LOWs installed in DSTs SY-102 and AW-103 are used for special, rather than routine, surveillance purposes only.

Thermocouple (TC)

A thermocouple is a thermoelectric device used to measure temperature. More than one thermocouple element on a device (probe) is called a thermocouple tree. In DSTs there may be one or more thermocouple trees in risers in the primary tank. In addition, in DSTs only, there are TC elements installed in the insulating concrete, the lower primary tank knuckle, the secondary tank concrete foundation, and in the outer structural concrete.

These monitor temperature gradients within the concrete walls, bottom of the tank, and the domes. In SSTs, one or more thermocouples may be installed directly in a tank, although some SSTs do not have any trees installed. A single TC element may be installed in a riser or lowered down an existing riser or LOW. There are also four thermocouple laterals beneath tank 105-A in which temperature readings are taken in 34 TC elements.

In-tank Photographs and Videos

In-tank photographs and videos may be taken to aid in resolving in-tank measurement anomalies and determine tank integrity. Photographs and videos help determine sludge and liquid levels by visual examination.

ACRONYMS

<u>CCS</u>	Controlled, Clean, and Stable (tank farms)
<u>FSAR</u>	Final Safety Analysis Report effective October 18, 1999
<u>II</u>	Interim Isolated
<u>IP</u>	Intrusion Prevention Completed
<u>IS</u>	Interim Stabilized
<u>MT/FIC/ENRAF</u>	Manual Tape, Food Instrument Corporation, ENRAF Corporation (surface level measurement devices)
<u>OSD</u>	Operating Specifications Document
<u>PI</u>	Partial Interim Isolated
<u>SAR</u>	Safety Analysis Report
<u>SHMS</u>	Standard Hydrogen Monitoring System
<u>TMACS</u>	Tank Monitor and Control System
<u>TPA</u>	Hanford Federal Facility Consent and Compliance Order, "Washington State Department of Ecology, U. S. Environmental Protection Agency, and U. S. Department of Energy," as amended (Tri-Party Agreement)
<u>TSR</u>	Technical Safety Requirement
<u>USQ</u>	Unreviewed Safety Question

3. INVENTORY AND STATUS BY TANK – COLUMN VOLUME CALCULATIONS AND DEFINITIONS
FOR TABLE B-1 (Single-Shell Tanks only)

COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS
Total Waste	<u>Solids volume plus Supernatant Liquid.</u> Solids include sludge and saltcake (see definitions below).
Supernatant Liquid (1)	<u>May be either measured or estimated.</u> Supernatant is either the estimated or measured liquid floating on the surface of the waste or under a floating solids crust. In-tank photographs or videos are useful in estimating the liquid volumes; liquid floating on solids and core sample data are useful in estimating large liquid pools under a floating crust.

COLUMN HEADING	COLUMN VOLUME CALCULATIONS (Underlined)/DEFINITIONS
Drainable Interstitial Liquid (DIL) (1)	<u>This is initially calculated.</u> Drainable interstitial liquid is calculated based on the saltcake and sludge volumes, using calculated porosity values from past pumping or actual data for each tank. Interstitial liquid is liquid that fills the interstitial spaces of the solids waste. The sum of the interstitial liquid contained in saltcake and sludge minus an adjustment for capillary height is the initial volume of drainable interstitial liquid.
Pumped This Month	<u>Net total gallons of liquid pumped from the tank during the month.</u> If supernatant is present, pump production is first subtracted from the supernatant volume. The remainder is then subtracted from the drainable interstitial liquid volume.
Total Pumped (1)	<u>Cumulative net total gallons of liquid pumped from 1979 to date.</u>
Drainable Liquid Remaining (DLR) (1)	<u>Supernatant plus Drainable Interstitial Liquid.</u> The total Drainable Liquid Remaining is the sum of drainable interstitial liquid and supernatant.
Pumpable Liquid Remaining (PLR) (1)	<u>Drainable Liquid Remaining minus unpumpable volume.</u> Not all drainable interstitial liquid is pumpable.
Sludge	<u>Solids formed during sodium hydroxide additions to waste.</u> Sludge was usually in the form of suspended solids when the waste was originally received in the tank from the waste generator. In-tank photographs or videos may be used to estimate the volume.
Saltcake	<u>Results from crystallization and precipitation after concentration of liquid waste, usually in an evaporator.</u> If saltcake is layered over sludge, it is only possible to measure total solids volume. In-tank photographs or videos may be used to estimate the saltcake volume.
Solids Volume Update	<u>Indicates the latest update of any change in the solids volume.</u>
Solids Update Source - See Footnote	<u>Indicates the source or basis of the latest solids volume update.</u>
Last In-Tank Photo	<u>Date of last in-tank photographs taken.</u>
Last In-Tank Video	<u>Date of last in-tank video taken.</u>
See Footnotes for These Changes	<u>Indicates any change made the previous month.</u> A footnote explanation for the change follows the Inventory and Status by Tank Appendix (Table B-1).

(1) Volumes for supernatant, DIL, DLR, and PLR are not shown in these columns until interim stabilization is completed. Total gallons pumped, total waste, sludge, and saltcake volumes are shown and adjusted based on actual pumping volumes.

This page intentionally left blank.

APPENDIX E

TANK CONFIGURATION AND FACILITIES CHARTS

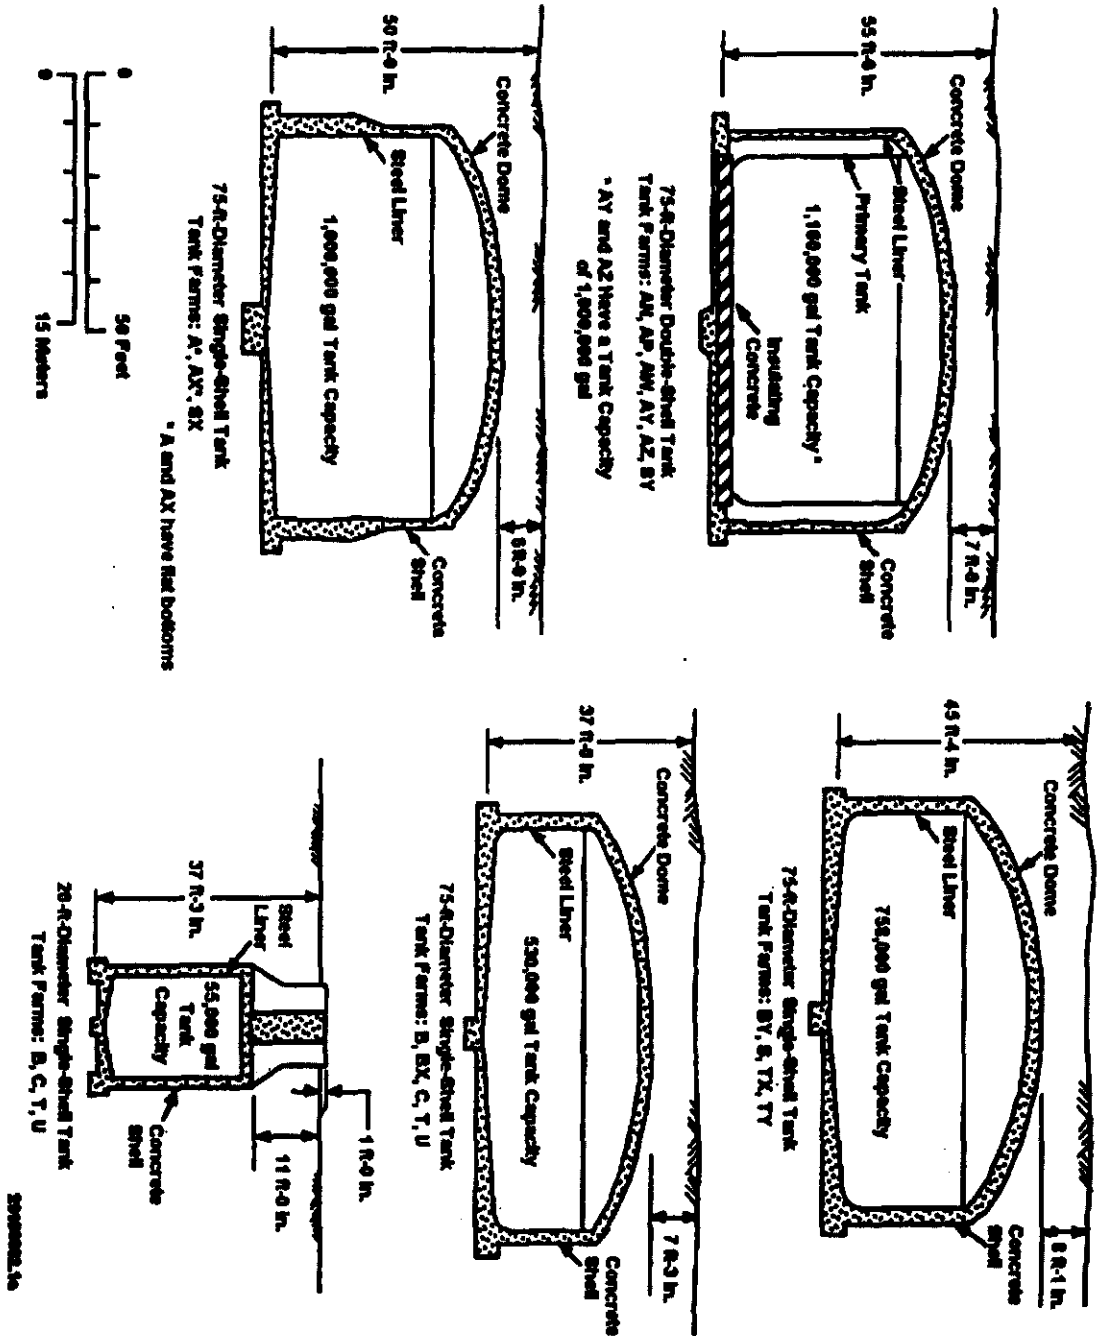


Figure E-1. High-Level Waste Tank Configuration

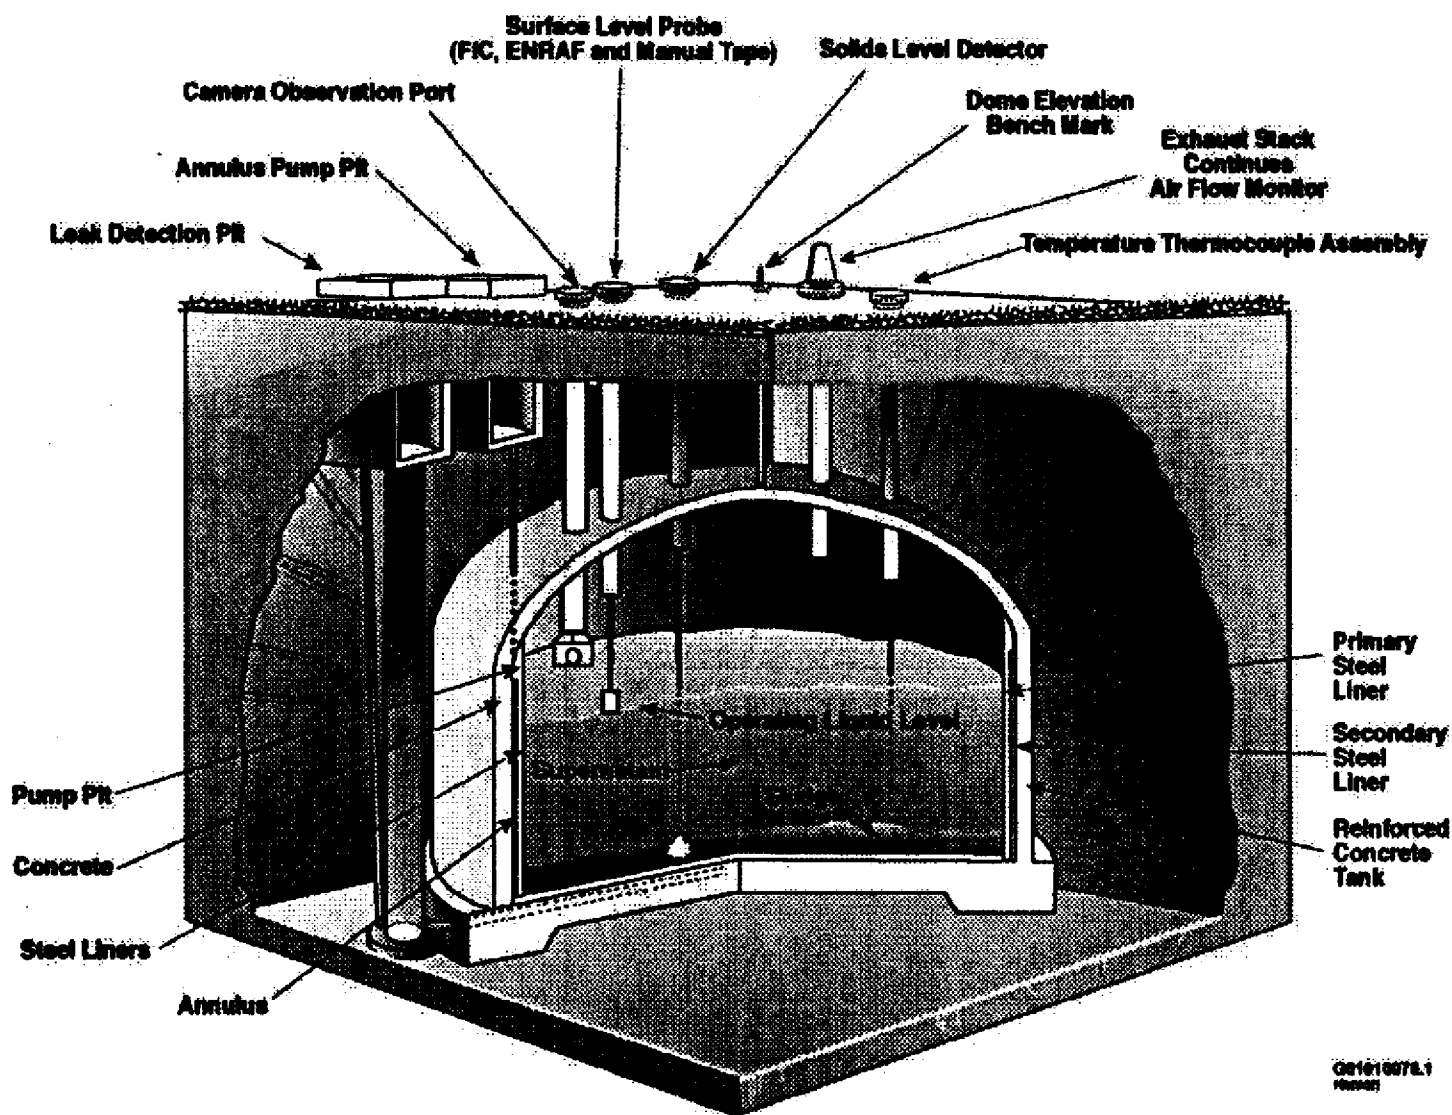


Figure E-2. Double-Shell Tank Instrumentation Configuration

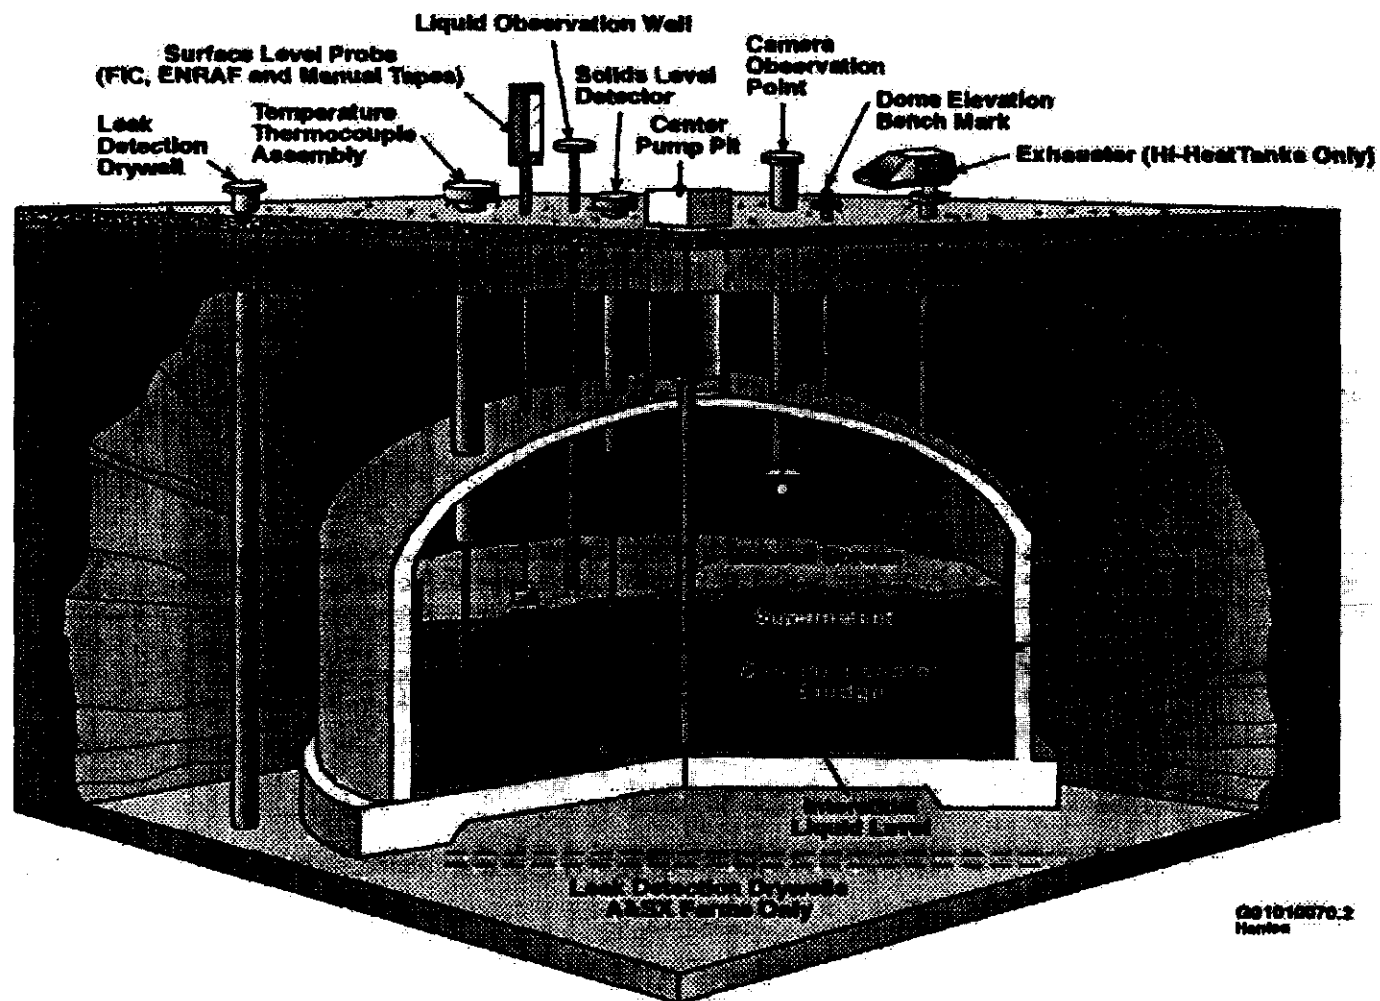


Figure E-3. Single-Shell Tank Instrumentation Configuration

THE TANK FARM FACILITIES CHARTS (colored foldouts)
ARE ONLY BEING INCLUDED IN THIS REPORT ON A QUARTERLY BASIS
(i.e., months ending March 31, June 30, September 30, and December 31)

NOTE: COPIES OF THE FACILITIES CHARTS CAN BE OBTAINED
FROM DENNIS BRUNSON, LMSI MULTI-MEDIA SERVICES

376-2345, G3-51

ALMOST ANY SIZE IS AVAILABLE, WHICH CAN BE LAMINATED
A PURCHASING CARD (P-Card) IS REQUIRED

This page intentionally left blank

DISTRIBUTION

October 31, 2001

Number of copies

OFFSITE - USA

2

Congress of the United States

U. S. Senate
717 Hart Senate Building
Washington D.C. 20510

Senator Ron Wyden

U. S. House of Representatives
1323 Longworth House Office Building
Washington D. C. 20515

Congressman Richard "Doc" Hastings, 4th District
Atten: Jeff Markey

4

U. S. Department of Energy-Headquarters

1000 Independence Avenue, SW
Washington, D. C. 20585

Harry Calley	EM-38 Cloverleaf Bldg.
William M. Levitan	EM-1 FORS/5A-014

U. S. Department of Energy-Headquarters

19901 Germantown Rd
Germantown, MD 20874

Kurt Juroff	EM-44
Ralph Lightener	EM-44

1

Washington State Department of Ecology

Nuclear Waste Program
P. O. Box 47600
Olympia, WA 98504-7600

Roger Stanley

1

Washington State Department of Health

Radiation Protection
7171 Cleanwater Lane
P. O. Box 47827
Olympia, WA 98504-7827

Allen W. Conklin

1

Oregon State Office of Energy

625 Marion St. NE, Suite 1
Salem, OR 97301

Dirk Dunning

Do not remove from distribution without permission from ODOE

1 Donald T. Oakley
4750 41st St., NW, #1
Washington, DC 20016

1 **MACTEC**
8310 Centerbrook Place
Alexandra, VA 22308

Stanley Blacker, Vice President
Do not remove from distribution without permission from addressee

1 **CH2M HILL**
6060 S. Willow Drive
Greenwood Village, CO 80111-5142

Dr. Bob Iotti, President and General Manager

TRI-CITIES:

1 **ARES Corporation**
636 Jadwin Ave., Suite B
Richland, WA 99352

1 **Winward Environmental**
3110 W. Metaline
Kennewick, WA 99336

R. T. Winward

1 Richard Welty
409 S. 41st Ave
W. Richland, WA 99353

ONSITE

1 **MACTEC - ERS**
J. F. Bertsch B2-62

1 **General Accounting Office**
C. R. Abraham A1-80

1 **Washington State Department of Ecology**
Library B5-18

1 **U. S. Environmental Protection Agency**
D. R. Sherwood B5-01

9 **U. S. Department of Energy**

D. C. Bryson H6-60
V. L. Callahan H6-60
E. J. Cruz H6-60
D. H. Irby H6-60
Wen-Shou Liou H6-60
J. L. Polehn H6-60
M. J. Royack H6-60

D. J. Williams	H6-60
Reading Room	H2-53

2 **Pacific National Northwest Laboratories**

J. L. Huckaby	K7-15
B. E. Opitz	K6-75

94 **CH2M Hill (CHG), and Affiliated Companies**

D. I. Allen	R2-50
J. C. Allen-Floyd	H6-06
E. S. Aromi	H6-63
K. M. Bowen	R2-12
V. C. Boyles	R2-11
R. J. Cash	R1-04
J. L. Cowin	T4-08
W. L. Cowley	R1-44
C. DeFigh-Price	R2-58
J. N. Doeler	T7-04
R. A. Dodd	H6-22
A. F. Erhart	R3-73
S. D. Estey	R2-11
A. C. Etheridge	H6-04
J. G. Field	R2-12
L. A. Fort	R2-11
K. D. Fowler	R2-11
G. T. Frater	S5-05
R. L. Frink	T4-08
J. C. Fulton	R2-50
J. R. Freeman-Pollard	R2-50
J. S. Garfield	L4-07
K. A. Gasper	L4-07
B. C. Gooding	T4-07
B. M. Hanlon (6)	R3-72
D.C. Hedengren	R3-73
C. C. Hendersen	B2-05
B. A. Higley	R3-73
S. W. Hildreth	T4-07
K. M. Hodgson	R1-14
T. M. Hohl	R3-73
B. A. Johnson	S7-02
T. E. Jones	H0-22
J. Kalia	R1-43
M. R. Kembel	S5-07
R. A. Kirkbride	R3-73
P. F. Kison	T4-07
N. W. Kirch	R3-73
J. S. Konyu	S7-64
G. M. Koreski	R2-11
J. G. Kristofzski	R2-39
J. A. Lechelt	R2-11
T. H. May	R2-11
J.A. McDonald Jr.	R2-50
D. L. Parker	R1-04

M. A. Payne	H6-63
R. E. Pohio	S7-95
R. S. Popielarczyk	S5-07
R. E. Raymond (2)	R2-50
B. J. Rabe	S7-03
W. E. Ross	S7-83
N. J. Scott-Proctor	S5-00
J. P. Sederburg	R1-04
J. N. Strobe	R3-73
T. D. Taylor	H6-64
R. R. Thompson	H6-22
D. T. Vladimiroff	S7-20
J. A. Voogd	R2-50
L. R. Webb (10)	R1-10
L. D. Wiberg (12)	R1-51
Central Files	B1-07
200 West Shift Office	T4-00
200 East Shift Office	S7-02
Environmental	
Data Mgmt Center (2)	H6-08
Unified Dose Assessment Center (UDAC)	A0-20

M. A. Payne	H6-63
R. E. Pohio	S7-95
R. S. Popielarczyk	S5-07
R. E. Raymond (2)	R2-50
B. J. Rabe	S7-03
W. E. Ross	S7-83
N. J. Scott-Proctor	S5-00
J. P. Sederburg	R1-04
J. N. Strobe	R3-73
T. D. Taylor	H6-64
R. R. Thompson	H6-22
D. T. Vladimiroff	S7-20
J. A. Voogd	R2-50
L. R. Webb (10)	R1-10
L. D. Wiberg (12)	R1-51
Central Files	B1-07
200 West Shift Office	T4-00
200 East Shift Office	S7-02
Environmental	
Data Mgmt Center (2)	H6-08
Unified Dose Assessment Center (UDAC)	A0-20
