1219482
[0089648]

SGW-34277
Revision 1

Waste Control Plan for the BC Cribs and Trenches Area in the 200-BC-1 OU

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Project Hanford Management Contractor for the
U.S. Department of Energy under Contract DE-AC06-96RL13200

FLUOR.

P.O. Box 1000
Richland, Washington

ref TPA-CA-278
0081244

RECEIVED
FEB 27 2013
EDMC

Approved for Public Release;
Further Dissemination Unlimited

30 pgs

SGW-34277
Revision 1

Waste Control Plan for the BC Cribs and Trenches Area in the 200-BC-1 OU

Program/Project: S&GWR

D. Todak
Fluor Hanford, Inc.

Date Published
June 2008

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Project Hanford Management Contractor for the
U.S. Department of Energy under Contract DE-AC06-96RL13200

FLUOR®
P.O. Box 1000
Richland, Washington

GE Bratton 6/28/2008
Release Approval Date

Approved for Public Release;
Further Dissemination Unlimited

TRADEMARK DISCLAIMER

Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

This report has been reproduced from the best available copy.

Printed in the United States of America

WASTE CONTROL PLAN

Work Scope Description:
200-BC-1 Operable Unit (OU) characterization in the BC Cribs and Trenches Area. The scope of work includes installing wells, direct push technology boreholes, test pit excavations, and collecting soil and groundwater samples that will be analyzed for radiological and non-radiological contaminants of concern. Geophysical logging will also be conducted in the BC Cribs and Trenches Area. The 216-B-26 Trench, 216-B-14 Crib, and 216-B-53A Trench will be evaluated using up to approximately 155 direct push boreholes. Also, up to five boreholes are to be drilled to evaluate potential correlation of electrical resistivity characterization data with soil contaminant concentrations. Additionally, decommissioning of the direct push boreholes and some existing wells will be performed upon completion or as deemed necessary in future years. Finally, the treatability test includes the planned excavation of near-surface contamination at three specific waste sites- the 216-B-26 Trench, the 216-B-53A Trench, and the 216-B-14 Crib.

List Contaminants of Concern:
Contaminants of concern at the 200-BC-1 OU include radionuclides, metals, anions, and volatile and semi-volatile organic compounds. See SGW-34278, *Data Quality Objective Summary Report for the Designation of Investigation-Derived Wastes in the 200-BC-1 Operable Unit.*

Site Description:
Waste sites in the 200-BC-1 OU include the BC Cribs and Trenches south of the 200 East Area of the Hanford Site in southeastern Washington State. The OU includes 24 waste sites that were formerly in the 200-TW-1 OU and 4 that were in the 200-LW-1 OU. The OU includes 6 cribs, 20 trenches, a siphon tank, and a pipeline. Figure 1 shows the location of these waste sites as well as the locations of the planned boreholes. Additional information on these sites is presented in DOE/RL-2000-38, DOE/RL-2003-44, and DOE/RL-2006-66.

References:
DOE/RL-2000-38, *200-TW-1 Scavenged Waste Group Operable Unit and 200-TW-2 Tank Waste Group Operable Unit RI/FS Work Plan, Rev. 0 Addendum Draft A*
DOE/RL-2003-44, *BC Cribs and Trenches 200-TW-1 Operable Unit Borehole Sampling and Analysis Plan*, Rev. 0
DOE/RL-2006-66, *Focused Feasibility Study for the BC Cribs and Trenches Area Waste Sites*, Draft A
DOE/RL-2007-13,, *Sampling and Analysis Plan for Electrical Resistivity Correlation for the BC Cribs and Trenches Area Waste Site*, Rev. 0
DOE/RL-2007-14,, *Sampling and Analysis Plan for Phase 1 of the BC Cribs and Trenches Area Waste Sites Excavation-Based Treatability Test*, Rev. 0
DOE/RL-2007-15, *Excavation-Based Treatability Test for the BC Cribs and Trenches Area Waste Sites*, Rev. 0
D&D-31659, *Geophysical Investigations by High Resolution Resistivity for the BC Cribs and Trenches Area, 2004-2006* , Rev. 0

Date Approved July 2007

Preparer: David Todak **Date** 6-26-08
Print/Sign Name

Impact Level N/A

Project Task Lead: G. D. Roosendaal **IDW Coordinator:** M.W. Vermillion

Planned Drilling Start and Finish Dates: From: September 2007 **To:** September 2009

Waste Storage Facility ID Number(s) N/A

WASTE CONTROL PLAN

Field Screening Methods

Method	Frequency	Reference	Detection Limit or Range	Analyst
Alpha/beta-gamma detector	Continuous	DOE/RL-2007-13, Rev. 0 DOE/RL-2007-14, Rev. 0 DOE/RL-2007-15, Rev. 0	100 d/min alpha 1921 d/min gamma-beta	RCT
Dose rate, gamma	Continuous	DOE/RL-2007-13, Rev. 0 DOE/RL-2007-14, Rev. 0 DOE/RL-2007-15, Rev. 0	0.5 mR/h	RCT
Photo ionization detector, 11.7, and 11.8 eV lamp for organics	As required in the Health and Safety Plan	DOE/RL-2007-13, Rev. 0 DOE/RL-2007-14, Rev. 0	0 to 1,000 ppmv	SSO
Spectral gamma logging	Section 1.4.3 Sections B3.4 & B3.5	DOE/RL-2007-14, Rev. 0 DOE/RL-2007-15, Rev. 0	Table 2-1 Table A-13	Contracted borehole logger

Laboratory Methods (Contaminants of concern)

Method	Frequency	Reference	Detection Range	Analyst
Tables 1-5 and 3-8	Section 3.2	DOE/RL-2007-13, Rev. 0	Table 1-5	On or off site Laboratory
Table 2-2	Section 1.4.3	DOE/RL-2007-14, Rev. 0	Table 2-2	On or off site Laboratory
Table A-13	Section B3.4 Section B3.5	DOE/RL-2007-15, Rev. 0	Table A-13	On or off site Laboratory

200-BC-1 OU Drill Site Location: Multiple locations have been identified for installation of boreholes through direct push and drilling methods as shown in Figure 1.

Decommissioning: The only wells currently identified for decommissioning in this OU are the direct push boreholes to be installed as described above and shown in Figure 1. As additional wells are identified for decommissioning, approval will be sought and granted through discussion at the Unit Manager's Meeting (UMM) and recorded in the UMM minutes.

Waste Container Storage Area(s) Coordinate Location(s): Three waste container storage areas, including the queue for ERDF cans, will be established in the BC Cribs and Trenches Area to manage the investigation-derived wastes generated by the proposed drilling, excavating, sampling and decommissioning activities. If these locations need to be moved to accommodate future work, such changes will be approved in Unit Manager's Meetings.

Requirements for Spoils Pile Sampling (if any): Not applicable –All drill cuttings/spoils will be containerized.

Non-regulated Material Disposal Location(s): An off-site Subtitle "D" landfill can be used for disposal of non-regulated miscellaneous solid waste that has been surveyed for radiological release in accordance with *PHMC Radiological Control Procedures* (HNF-13536), Section 4.1.1, "Standard Radiological Release Survey for Material and Equipment." Non-regulated soil waste may be returned to the ground at or near the point of excavation in accordance with GRP-EE-02-14.5: *Returning Vadose Zone Drill Cuttings/Soils to the Environment*, the location of which will be documented in the field logbook. Liquid wastes (e.g. purgewater, decontamination fluids) will be collected and taken to the Purgewater Storage and Treatment Facility (PSTF) or the Effluent Treatment Facility (ETF).

200-BC-1 OU Sketch of Work Site: Figure 1 identifies the borehole locations and waste container storage areas at the BC Cribs and Trenches Area.

APPROVALS (Print/Sign Name and Date)	
Lead Regulatory Agency Representative Brian L. Charboneau DOE-RL	Michael Vermillion IDW Coordinator Project Task Lead

ATTACHMENT

DESCRIPTION OF WORK

CONTENTS

1.0 DESCRIPTION OF WORK 1
1.1 WASTE STREAMS 2
1.2 WASTE GENERATION AND MANAGEMENT 2
1.2.1 Miscellaneous Solid Waste 3
1.2.2 Vadose Zone Drill Cuttings 3
1.2.3 Excavation Waste 3
1.2.4 Decontamination Fluids 4
1.2.5 Equipment and Construction Materials 4
1.2.6 Non-dangerous/No-Radiation-Added Solid Waste 5
1.2.7 Unplanned Release 5
1.3 MANAGEMENT OF WASTE CONTAINERS 5
1.4 STORAGE AND FINAL DISPOSAL 6
1.4.1 Material Handling and Transportation 7
1.5 RECORDS 7
1.6 ESTIMATE OF INVESTIGATION-DERIVED WASTE QUANTITIES 7
1.7 IDENTIFICATION OF WELLS AND DIRECT PUSHES 7

2.0 REFERENCES 15

FIGURES

Figure 1. 200-BC-1 Location Map and Waste Container Storage Areas 8

TABLES

Table 1. Estimate of Investigation-Derived Waste Quantities 8

Table 2. 200-BC-1 Borehole Well List 9

Table 3. 200-BC-1 Direct Push List 10

TERMS

CERCLA	*Comprehensive Environmental Response, Compensation and Liability Act of 1980*
ERDF	Environmental Restoration Disposal Facility
ID	identification
IDW	investigation-derived waste
MSW	miscellaneous solid waste
OU	operable unit
PPE	personal protective equipment
PUREX	Plutonium-Uranium Extraction (Plant)
RCRA	*Resource Conservation and Recovery Act of 1976*
RCT	radiological control technician
REDOX	Reduction-Oxidation (Plant)
TRU	transuranic (waste materials contaminated with 100 nCi/g of transuranic materials having half-lives longer than 20 years)
TSD	treatment, storage, and disposal
WAC	*Washington Administrative Code*
WESF	Waste Encapsulation and Storage Facility

This page intentionally left blank

1.0 DESCRIPTION OF WORK

This waste control plan (WCP) governs the management of investigation-derived waste (IDW) generated at the BC Cribs and Trenches (Figure 1) under the Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA). The planned work scope includes activities detailed in the *Sampling and Analysis Plan for Electrical Resistivity Correlation for the BC Cribs and Trenches Area* (DOE/RL-2007-13, Draft A) and the *Sampling and Analysis Plan for Phase 1 of the BC Cribs and Trenches Area Waste Sites Excavation-Based Treatability Test* (DOE/RL-2007-14, Draft A), and *Excavation-Based Treatability Test Plan for the BC Cribs and Trenches Area Waste Sites* (DOE/RL-2007-15). The electrical resistivity characterization geophysical method is being applied at the BC Cribs and Trenches Area in an attempt to identify the lateral and/or vertical distribution of targeted contaminants of potential concern in the vadose zone. The treatability test will assess the field conditions related to removal, treatment, and disposal of near-surface contamination present in representative wastes sites.

The work activities currently planned include the drilling of up to five boreholes, the installation of numerous DPT boreholes, and excavation of near-surface contamination from selected waste sites. The up-to five electrical resistivity characterization boreholes are a part of the ongoing analytical data correlation activities and will be located outside of individual waste site boundaries. The DPT boreholes and excavations are part of the excavation-based treatability test plan work scope and will be located in the 216-B-14 Crib, 216-B-26 Trench, and 216-B-53A Trench. The DPT holes in the 216-B-14 Crib, 216-B-26 Trench, and 216-B-53A Trench will be used to characterize those waste sites via geophysical logging and sediment sampling prior to excavation. Some of the holes will be located in the footprints of the waste sites, some will be located on the edges of the waste to ascertain the extent of lateral contamination spread, and others will be dedicated to sampling.

The DPT boreholes will not be constructed to meet current standards for construction and maintenance of wells, and will be decommissioned. Although these are the only boreholes currently slated for decommissioning, there may be other wells in the 200-BC-1 OU that do not meet modern construction criteria and which will be similarly decommissioned. Waste generated from decommissioning activities is IDW and will be designated based on sample data and/or surrounding waste site characterization data.

Near-surface contamination will be removed from the 216-B-26 Trench, the 216-B-14 Crib, and the 216-B-53A Trench in accordance with DOE/RL-2007-15, *Excavation-Based Treatability Test for the BC Cribs and Trenches Area Waste Sites*. Focus is on collecting information to refine cost and worker dose estimates for excavation of highly-contaminated near-surface soil, and assessing subsidence potential of remnant crib structures. Not all material removed will be disposed of as waste; the top few feet will be reserved for later return to the excavation, unless it is required to treat (down blend) the highly contaminated soil to meet ERDF acceptance or transportation requirements.

Any wastes generated during this project will be managed in accordance with this waste control plan and state and Federal regulations. An overview of the waste management strategy for the 200 Areas waste sites is presented in Appendix E of DOE/RL-98-28, *200 Areas Remedial Investigation/Feasibility Study Implementation Plan – Environmental Restoration Program*. Every effort will be used to minimize waste generated during this project.

1.1 WASTE STREAMS

One or all of the below waste streams are anticipated and may fall into any combination of the following categories: transuranic (TRU), radioactive, mixed, hazardous, dangerous, suspect radioactive, suspect dangerous, suspect mixed, and nonregulated:

- Miscellaneous solid waste (e.g., rubber, glass, paper, personal protective equipment, cloth, plastic, metal)
- Drill cuttings, soils, and slurries
- Decontamination fluids
- Equipment and construction materials (e.g., well casing, drill string, drive barrel, construction equipment and materials, sampling equipment, decommissioning materials, wooden pallets)
- Nondangerous/no-radiation-added (nonradioactive) solid waste (e.g., paper, wood, construction debris, metal, plastic, glass)
- Unplanned release and associated cleanup material
- Well decommissioning waste (e.g. miscellaneous solid waste (MSW), drill cuttings, soils & slurry, decontamination fluids and purgewater, equipment and construction debris).

1.2 WASTE GENERATION AND MANAGEMENT

All waste generated will be recorded in the geologist and/or buyer technical representative logbook, with such details as the location and type of waste, depth of sample, date of initial placement into container, date the container was sealed, and Package Identification Number. Marking, labeling, segregation, and staging of waste containers will be performed in accordance with a waste packaging and labeling instruction or as directed by the waste transportation specialist.

Waste will be stored at the site-specific waste container storage areas as shown in Figures 1 and 2. Future well decommissioning activities may require additional site-specific waste container storage areas, which will be approved in the Unit Manager's Meeting (UMM) and recorded in the UMM minutes. The IDW will be stored at these areas until analytical data are evaluated for proper waste designation and will be disposed of at the Environmental Restoration Disposal Facility (ERDF) if it meets the waste acceptance criteria specified in BHI-00139, *Environmental Restoration Disposal Facility Waste Acceptance Criteria*. If TRU waste is encountered, it will be sent to the Hanford Site Central Waste Complex for storage. In addition, if any waste needs to be transported to the Central Waste Complex, the EPA will be contacted to make an offsite determination before the waste is shipped. Any waste transported to the Central Waste Complex for storage must be dispositioned in accordance with the work plan required by TPA Milestone M-016-93 for TRU waste generated by CERCLA cleanup actions of the Hanford Site, and the final MO-016 Cleanup Schedule.

If, after characterization and designation of the waste is completed, the waste must be stored for longer than six months at the Waste Container Storage Area, the U.S. Department of Energy,

Richland Operations Office (RL) will obtain concurrence from the lead regulatory agency on the current storage, treatment, and disposal options and schedule for disposition of the waste.

Details on the types and management of expected wastes are provided in the following subsections.

1.2.1 Miscellaneous Solid Waste

Well decommissioning wastes are to be treated as suspect dangerous or suspect mixed waste based on process knowledge and representative waste site characterization sample results. Refer to the specific data quality objective for process knowledge and representative analytical data. Some waste associated with decommissioning may be considered environmentally controlled material or nondangerous/no-radiation-added solid waste based on process knowledge and representative analytical data. Decommissioning waste shall be containerized, marked, segregated, staged and dispositioned as stated below.

Miscellaneous solid waste (MSW) that has contacted suspect dangerous or suspect mixed waste will be treated as such. Field screening will be used to segregate radioactive IDW from no-radiation-added (non-radioactive) IDW. The MSW will be placed in a plastic bag, taped closed, marked to indicate the associated borehole footage interval, and placed in container(s) specific to each area of potential contamination. Container(s) will be properly marked and labeled. The containers will be segregated from other materials, based on field screening results and location, and then staged at the designated site-specific waste container storage area. The containers of MSW will be dispositioned using analytical results obtained from the soil contacted.

1.2.2 Vadose Zone Drill Cuttings

Vadose zone drill cuttings are to be treated as suspect radioactive, dangerous, or mixed waste, based on process knowledge and field screening results. Drill cuttings shall be containerized in properly labeled mid-performance coated drums with 10-mil reinforced plastic liners to mitigate the spread of contaminants to the environment. Containers will be properly marked and labeled. Mark the container lid with the date, well name, start and close date, start depth and ending depth, gross weight, and sampling date. If screening levels indicate that the cuttings may be characterized as TRU waste, the cuttings containers also will have vented lids. The containers will be segregated from other materials, based on field screening results and location, and then staged at the designated site-specific waste container storage area. The containers of drill cuttings will be dispositioned using analytical results associated with the contaminated media contacted.

1.2.3 Excavation Waste

Material removed during excavation of near-surface contaminated soil is to be treated as suspect radioactive, dangerous, or mixed waste, based on process knowledge and field screening results. In addition to contaminated soil, remnant steel casing (2.5-in. diameter) from previous direct push technology hole (DPT) installation will be removed. The ERDF waste acceptance criteria BHI-00139, *Environmental Restoration Disposal Facility Waste Acceptance Criteria*) size reduction requirements will be used. Soil and debris will be containerized on site (e.g., containers, bulk shipment) and transported to the ERDF, located near the 200 West Area. Low-

level radioactive waste and/or hazardous waste are acceptable for disposal at the ERDF in accordance with the waste acceptance criteria (BHI-00139, *Environmental Restoration Disposal Facility Waste Acceptance Criteria*).

Miscellaneous solid waste (MSW) that has contacted suspect dangerous or suspect mixed waste will be treated and marked as such. Field screening will be used to segregate radioactive from no-radiation-added (non-radioactive) waste. Containers will be properly marked and labeled. The containers will be segregated from other materials, based on field screening results and location, and then staged at the designated site-specific waste container storage area. The containers of MSW will be dispositioned using analytical results obtained from the soil contacted.

Visible dust emissions from active excavations are not permitted and will result in work suspension. Active excavations shall use water or other methods for dust control, in accordance with agreements between the U.S. Department of Energy, Richland Operations Office (DOE-RL), EPA and the Washington State Department of Health. Water usage for dust control shall be minimized to protect against contamination migration. Crusting agents or fixatives shall be applied to any disturbed portion of the contamination area that will be inactive for more than 24 hours. Material to be disposed at ERDF shall also comply with the moisture content and other applicable requirements of BHI-00139, *Environmental Restoration Disposal Facility Waste Acceptance Criteria*.

1.2.4 Decontamination Fluids

Decontamination fluids (water and/or non-dangerous cleaning solutions) generated from cleaning equipment and tools in the OU will be contained, transported, and discharged at the 200 Area Effluent Treatment Facility, or at the Hanford Site 600 Area Purgewater Storage and Treatment Facility (ModuTanks)[1] in accordance with Appendix F of the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989). If necessary, decontamination fluids can be containerized and stored at the designated site-specific waste container storage area.

Additional chemical decontamination of sample equipment may be conducted at the Waste Sampling and Characterization Facility, because decontamination and containment systems already are established at this location. The waste generated at the Waste Sampling and Characterization Facility is not considered IDW and will be managed in accordance with applicable regulations and requirements.

1.2.5 Equipment and Construction Materials

Equipment and construction materials in contact with suspect dangerous and suspect mixed waste will be decontaminated with a three-bucket wash or a high-temperature and high-pressure wash (180 °F and >1000 lbf/in^2) within a wash basin capable of retaining rinsate, or it will be treated as MSW. Steam cleaning may be used if other methods are ineffective. All water used for decontamination activities shall be potable (i.e., Hanford Site potable water or City of Richland water). Rinsate shall be managed as described in Section 1.2.3. All sampling equipment shall be cleaned and decontaminated for chemical contamination after radiological

[1] ModuTank is a trademark of ModuTank Inc., Long Island City, New York.

release by a radiological control technician (RCT). If contamination is determined to be fixed for any equipment or materials, the radiological control technician and task manager will make the decision to remove the contamination using more aggressive methods or to dispose of the equipment. If necessary, equipment and construction materials can be containerized and stored at the designated site-specific waste container storage area.

1.2.6 Non-dangerous/No-Radiation-Added Solid Waste

All non-dangerous/no-radiation-added (non-radioactive) solid waste that is radiologically released will be disposed to an offsite solid-waste landfill. This waste will not have contacted any suspect dangerous or mixed waste and will be free of any liquids. Items in this category include paper, wood, construction debris, metals, plastic, food waste, glass, etc. A radiological release certification form and/or the well identification number and date of generation should be attached and visible from outside the trash bag. If necessary, non-dangerous/no-radiation-added solid waste can be containerized, segregated, and stored at the designated site-specific waste container storage area.

1.2.7 Unplanned Release

The initial response to emergency and non-emergency events and conditions shall follow the direction provided in the individual work location Health and Safety Plan (HASP). Once the initial assessment is completed and appropriate measures have been taken to curtail and contain the spill or release, the waste specialist will ensure that compatible waste container(s) are properly marked, labeled, and segregated from other materials based on process knowledge, field screening results, and location and then will be staged at a designated site-specific waste container storage area. The containers will be dispositioned using analytical results or process knowledge. These actions will be conducted in accordance with the requirements of WAC 173-303-145, "Dangerous Waste Regulations," and 40 *Code of Federal Regulations* (CFR) 302, "Designation, Reportable Quantities, and Notification."

1.3 MANAGEMENT OF WASTE CONTAINERS

All containers of IDW will be managed in accordance with the applicable substantive federal and/or state requirements including labels which define the known major risks, dangerous waste codes, and if awaiting analysis, wording which states "waste pending analysis" with the date of initial sampling. The containers will be stored inside the applicable site-specific waste container storage area. The waste container storage areas shown in Figure 1 may be relocated within or adjacent to the identified waste sites to accommodate changes in the field operations. If a waste container storage area is relocated, the lead regulatory agency will be notified before the change and relocation of the waste container storage area. Containers awaiting analytical results will be marked and labeled "Waste Pending Analysis," as prescribed in the preceding sections. If dangerous waste is present at the storage areas, weekly inspections will be performed to document the integrity of containers/packages; proper marking or labeling; physical container and package placement; storage area boundaries, identification, warning signs; and spill control. Containers and packages showing signs of deterioration will be identified on the container inspection form and immediately over packed or repackaged.

Spills or releases will be reported as stated above. In the event of a spill or release, appropriate immediate action will be taken to protect human health and the environment.

1.4 STORAGE AND FINAL DISPOSAL

It is anticipated that all IDW will be stored at the site-specific waste container storage area until the waste samples are returned and the proper waste shipping papers are completed. In the event that samples returns are delayed, the majority of waste containers may be shipped for disposal, provided that sufficient, appropriate containers remain in the WCSA for packaging of samples upon their return. The process to develop proper waste shipping papers includes the following: receipt of analytical results, designation, profiling, and proper disposition of paperwork. The designation process ensures that the waste will be profiled for the proper disposal facility. Waste profiling provides information concerning each waste stream. The designation and profiling are conducted in accordance with dangerous waste regulation requirements (WAC 173-303-070, "Designation of Dangerous Waste" through 173-303-100). Dangerous waste will be evaluated for applicable land disposal restrictions in accordance with WAC 173-303-140, "Land Disposal Restrictions." The presence of polychlorinated biphenyls will be evaluated in accordance with the *Toxic Substances Control Act of 1976* and WAC 173-303-9904, "Dangerous Sources List." Radiological wastes will be determined to be acceptable for near surface (onsite) disposal if the concentrations of radionuclides are below those in BHI-00139.

The IDW that does not meet the ERDF waste acceptance criteria will remain at the designated site-specific waste container storage area pending disposal at an appropriate location.
A case-by-case disposal determination will be made in instances where IDW exceeds the ERDF waste acceptance criteria. Any IDW requiring treatment before disposal, and/or disposal at an off site facility, requires approval by the lead regulatory agency.

Wastes that cannot be radiologically released that do meet the ERDF waste acceptance criteria will be transported to the ERDF for disposal (ERDF is an "onsite" approved waste disposal facility). Non-radiologically contaminated dangerous waste may be shipped onsite to ERDF or to an offsite facility, contingent upon the waste meeting the offsite RCRA disposal facility's waste acceptance criteria and offsite determination of acceptability by the U.S. Environmental Protection Agency.

If TRU levels of contamination are encountered, the suspect waste will be placed within engineered segregated boundaries of the designated storage area and posted according to radiological posting requirements. After representative samples are analyzed and the material is designated/characterized, the proper disposal facility will be selected. If the Central Waste Complex (CWC) is selected for long-term storage, soil sample(s) designated as TRU waste will be returned and placed back into the stored waste drum associated with the interval from which the sample was taken before it is shipped. Offsite determination of acceptability for waste selected for long-term storage at CWC will be obtained from the U.S. Environmental Protection Agency. In addition, if any waste needs to be transported to the Central Waste Complex, the EPA will be contacted to make any offsite determination before the waste is shipped. Any waste transported to the Central Waste Complex must be dispositioned in accordance with the work plan required by TPA milestone M-016-93 for TRU waste generated by CERCLA cleanup actions at the Hanford Site and in accordance with the final M-016 cleanup schedule.

Miscellaneous solid waste identified as non-dangerous/no-radiation-added solid waste that does not require disposal at ERDF and meets the Hanford Site free-release criteria may be disposed of in an appropriate solid waste disposal facility (Subtitle "D" landfill).

1.4.1 Material Handling and Transportation

All contaminated materials, including excavated soils, debris, disposable protective clothing, and trash, will be properly packaged, handled, and transported in accordance with this Waste Control Plan. Contaminated bulk materials will be hauled in the standard ERDF open-top, hinged-gate roll-off boxes that are designed for a maximum payload of approximately 18.1 metric tones (20 tons) or an approved alternative. The bulk containers will be transported on roll-on/roll-off trailers with hydraulic dumping capabilities that are towed by conventional tractor units. Containers will be transported from the BC Cribs and Trenches Area to the ERDF over existing Hanford Site roadways. Each shipment transported to ERDF will be referenced to a waste profile that is intended to bound the levels of hazardous constituents in the material found at the waste site. The waste profile is in effect unless and until the characteristics of the excavation site change significantly. Empty containers returning from the ERDF will be removed from the ERDF tractor trailers in the CERCLA Waste Management Area and rolled on to project haul trucks for refilling.

Containers and ERDF haul trucks being released from radiologically-controlled areas will meet exterior contamination limits for staging and transport.

1.5 RECORDS

Original copies of all sampling records, waste inventory documentation, and waste container certification forms will be forwarded to the assigned waste management specialist to be included in the waste file and to initiate waste tracking in the *Solid Waste Information Tracking System*. The completed waste files will be included in the project file following final waste disposition in accordance with applicable records management processes.

1.6 ESTIMATE OF INVESTIGATION-DERIVED WASTE QUANTITIES

Estimates of the amount of waste that will be generated during this field investigation are given in Table 1. These quantities are based on IDW generated during previous 200 Areas drilling and excavation activities.

1.7 IDENTIFICATION OF WELLS AND DIRECT PUSHES

Tables 2 and 3 identify the wells and direct pushes planned, respectively.

Figure 1. 200-BC-1 Location Map and Waste Container Storage Areas

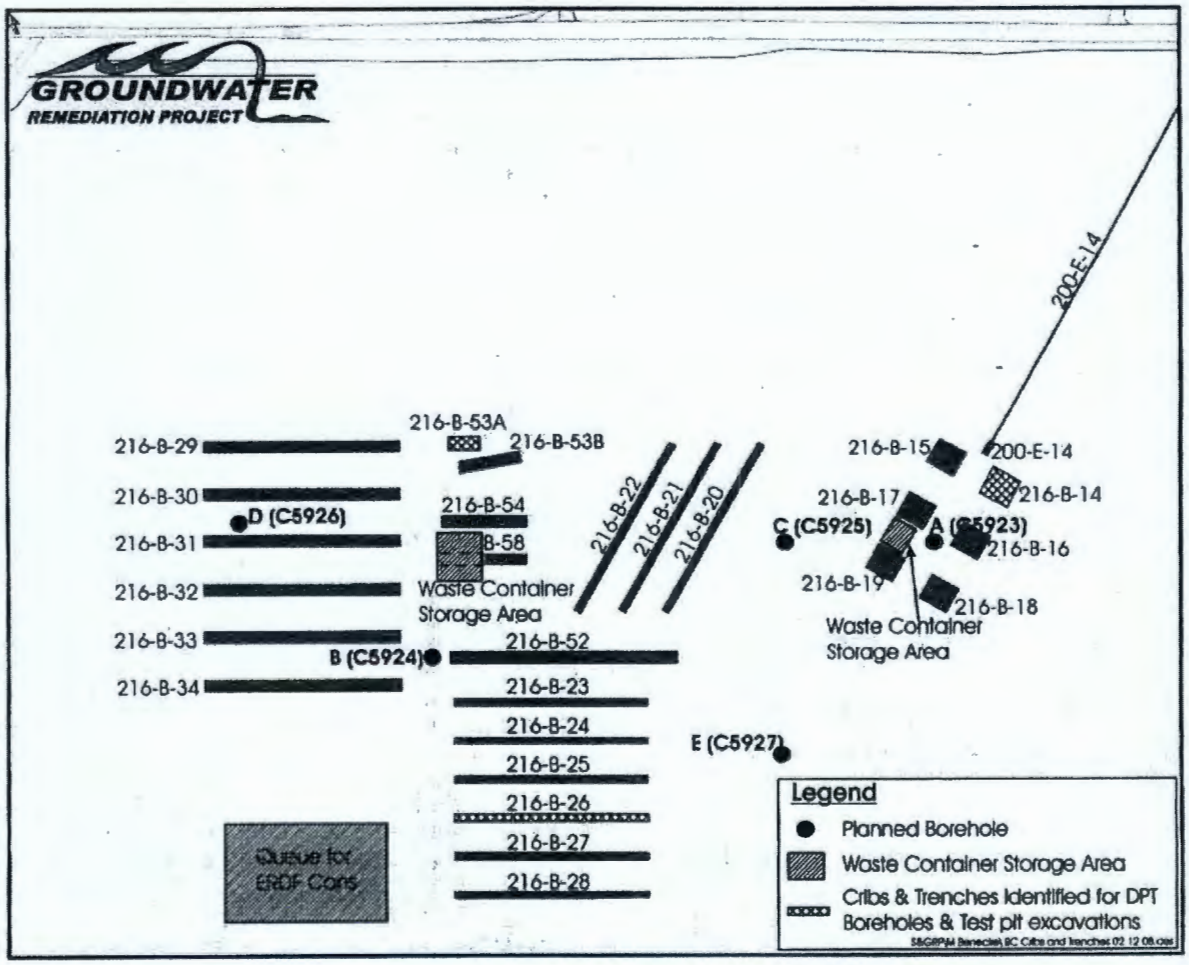

Table 1. Estimate of Investigation-Derived Waste Quantities.

Operable Unit	Method	Liquid Wastes	Soil Wastes	Miscellaneous Solid Waste	
		Purgewater and decon fluids (drums[a])	Containers	PPE/Trash	Disposable Equipment
200-BC-1	Drilling	10	50 drums[a]	15 drums[a]	1000 linear feet drill casing 1000 linear feet 2.5" push rod
200-BC-1	Decommisioning	N/A	N/A	TBD	TBD
200-BC-1	Excavation	N/A	300 ERDF roll-off boxes[b]	50 drums[a]	TBD

[a]208-L (55-gal) drums.
ERDF roll-off box max payload: 18.1 MT (20 tons).
PPE = personal protective equipment.

Table 2. 200-BC-1 Borehole Well List.

Area	Operable Unit	Waste Site Code	Site Type	Hanford Well ID
200 East	200-BC-1	216-B-16/17	Crib	C5923
200 East	200-BC-1	216-B-23	Trench	C5924
200 East	200-BC-1	NA	N/A	C5925
200 East	200-BC-1	216-B-30/31	Trench	C5926
200 East	200-BC-1	N/A	N/A	C5927

Table 3. 200-BC-1 Direct Push List				
Area	Operable Unit	Waste Site Code	Site Type	Hanford Well ID
200-East	200-BC-1	216-B-26	Trench	C5863 [3]
200-East	200-BC-1	216-B-26	Trench	C5864 [3]
200-East	200-BC-1	216-B-26	Trench	C5865 [3]
200-East	200-BC-1	216-B-26	Trench	C5866 [3]
200-East	200-BC-1	216-B-26	Trench	C5867 [3]
200-East	200-BC-1	216-B-26	Trench	C5868 [3]
200-East	200-BC-1	216-B-26	Trench	C5869 [3]
200-East	200-BC-1	216-B-26	Trench	C5870 [3]
200-East	200-BC-1	216-B-26	Trench	C5871 [3]
200-East	200-BC-1	216-B-26	Trench	C5872 [3]
200-East	200-BC-1	216-B-26	Trench	C5873 [3]
200-East	200-BC-1	216-B-26	Trench	C5874 [3]
200-East	200-BC-1	216-B-26	Trench	C5875 [1]
200-East	200-BC-1	216-B-26	Trench	C5876 [1]
200-East	200-BC-1	216-B-26	Trench	C5877 [1]
200-East	200-BC-1	216-B-26	Trench	C5878 [1]
200-East	200-BC-1	216-B-26	Trench	C5879 [1]
200-East	200-BC-1	216-B-26	Trench	C5880 [1]
200-East	200-BC-1	216-B-26	Trench	C5881 [1]
200-East	200-BC-1	216-B-26	Trench	C5882 [1]
200-East	200-BC-1	216-B-26	Trench	C5883 [1]
200-East	200-BC-1	216-B-26	Trench	C5884 [1]
200-East	200-BC-1	216-B-26	Trench	C5885 [1]
200-East	200-BC-1	216-B-26	Trench	C5886 [1]
200-East	200-BC-1	216-B-26	Trench	C5887 [4]
200-East	200-BC-1	216-B-26	Trench	C5888 [1]
200-East	200-BC-1	216-B-26	Trench	C5889 [1]
200-East	200-BC-1	216-B-26	Trench	C5890 [1]
200-East	200-BC-1	216-B-26	Trench	C5891 [1]
200-East	200-BC-1	216-B-26	Trench	C5892 [1]
200-East	200-BC-1	216-B-26	Trench	C5893 [1]
200-East	200-BC-1	216-B-26	Trench	C5894 [1]
200-East	200-BC-1	216-B-26	Trench	C5895 [1]
200-East	200-BC-1	216-B-26	Trench	C5896 [1]

200-East	200-BC-1	216-B-26	Trench	C5897 [1]
200-East	200-BC-1	216-B-26	Trench	C5998 [1]
200-East	200-BC-1	216-B-26	Trench	C5899 [1]
200-East	200-BC-1	216-B-26	Trench	C5900 [3]
200-East	200-BC-1	216-B-26	Trench	C5901 [3]
200-East	200-BC-1	216-B-26	Trench	C5902 [3]
200-East	200-BC-1	216-B-26	Trench	C5903 [3]
200-East	200-BC-1	216-B-26	Trench	C5904 [3]
200-East	200-BC-1	216-B-26	Trench	C5905 [3]
200-East	200-BC-1	216-B-26	Trench	C5906 [3]
200-East	200-BC-1	216-B-26	Trench	C5907 [3]
200-East	200-BC-1	216-B-26	Trench	C5908 [3]
200-East	200-BC-1	216-B-26	Trench	C5909 [3]
200-East	200-BC-1	216-B-26	Trench	C5910 [3]
200-East	200-BC-1	216-B-26	Trench	C5911 [3]
200-East	200-BC-1	216-B-26	Trench	C5912 [3]
200-East	200-BC-1	216-B-26	Trench	C5913 [3]
200-East	200-BC-1	216-B-26	Trench	C5914 [3]
200-East	200-BC-1	216-B-26	Trench	C5915 [2]
200-East	200-BC-1	216-B-26	Trench	C5916 [2]
200-East	200-BC-1	216-B-26	Trench	C5917 [2]
200-East	200-BC-1	216-B-26	Trench	C5918 [2]
200-East	200-BC-1	216-B-26	Trench	C5919 [2]
200-East	200-BC-1	216-B-26	Trench	C5920 [2]
200-East	200-BC-1	216-B-26	Trench	C5921 [2]
200-East	200-BC-1	216-B-26	Trench	C5922 [2]
200-East	200-BC-1	216-B-26	Trench	C6106 [3]
200-East	200-BC-1	216-B-26	Trench	C6107 [3]
200-East	200-BC-1	216-B-26	Trench	C6108 [3]
200-East	200-BC-1	216-B-26	Trench	C6109 [5]
200-East	200-BC-1	216-B-26	Trench	C6110 [5]
200-East	200-BC-1	216-B-26	Trench	C6111 [5]
200-East	200-BC-1	216-B-26	Trench	C6112 [5]
200-East	200-BC-1	216-B-26	Trench	C6113 [5]
200-East	200-BC-1	216-B-26	Trench	C6114 [5]
200-East	200-BC-1	216-B-26	Trench	C6115 [5]
200-East	200-BC-1	216-B-26	Trench	C6116 [5]
200-East	200-BC-1	216-B-26	Trench	C6117 [5]

200-East	200-BC-1	216-B-26	Trench	C6118 [5]
200-East	200-BC-1	216-B-26	Trench	C6119 [5]
200-East	200-BC-1	216-B-26	Trench	C6120 [5]
200-East	200-BC-1	216-B-26	Trench	C6121 [5]
200-East	200-BC-1	216-B-26	Trench	C6122 [5]
200-East	200-BC-1	216-B-26	Trench	C6123 [5]
200-East	200-BC-1	216-B-26	Trench	C6124 [5]
200-East	200-BC-1	216-B-26	Trench	C6125 [5]
200-East	200-BC-1	216-B-26	Trench	C6126 [5]
200-East	200-BC-1	216-B-26	Trench	C6127 [5]
200-East	200-BC-1	216-B-26	Trench	C6128 [5]
200-East	200-BC-1	216-B-26	Trench	C6129 [5]
200-East	200-BC-1	216-B-26	Trench	C6130 [5]
200-East	200-BC-1	216-B-14	Crib	C6796 [1]
200-East	200-BC-1	216-B-14	Crib	C6797 [1]
200-East	200-BC-1	216-B-14	Crib	C6798 [1]
200-East	200-BC-1	216-B-14	Crib	C6799 [1]
200-East	200-BC-1	216-B-14	Crib	C6800 [1]
200-East	200-BC-1	216-B-14	Crib	C6801 [1]
200-East	200-BC-1	216-B-14	Crib	C6802 [1]
200-East	200-BC-1	216-B-14	Crib	C6803 [1]
200-East	200-BC-1	216-B-14	Crib	C6804 [2]
200-East	200-BC-1	216-B-14	Crib	C6805 [2]
200-East	200-BC-1	216-B-14	Crib	C6806 [2]
200-East	200-BC-1	216-B-14	Crib	C6807 [2]
200-East	200-BC-1	216-B-14	Crib	C6808 [2]
200-East	200-BC-1	216-B-14	Crib	C6809 [2]
200-East	200-BC-1	216-B-14	Crib	C6810 [2]
200-East	200-BC-1	216-B-14	Crib	C6811 [2]
200-East	200-BC-1	216-B-14	Crib	C6812 [3]
200-East	200-BC-1	216-B-14	Crib	C6813 [3]
200-East	200-BC-1	216-B-14	Crib	C6814 [3]
200-East	200-BC-1	216-B-14	Crib	C6815 [3]
200-East	200-BC-1	216-B-14	Crib	C6816 [3]
200-East	200-BC-1	216-B-14	Crib	C6817 [3]
200-East	200-BC-1	216-B-14	Crib	C6818 [3]
200-East	200-BC-1	216-B-14	Crib	C6819 [3]
200-East	200-BC-1	216-B-14	Crib	C6820 [3]

200-East	200-BC-1	216-B-14	Crib	C6821 [3]
200-East	200-BC-1	216-B-14	Crib	C6822 [3]
200-East	200-BC-1	216-B-14	Crib	C6823 [3]
200-East	200-BC-1	216-B-14	Crib	C6824 [3]
200-East	200-BC-1	216-B-14	Crib	C6825 [3]
200-East	200-BC-1	216-B-53A	Trench	C6754 [1]
200-East	200-BC-1	216-B-53A	Trench	C6755 [1]
200-East	200-BC-1	216-B-53A	Trench	C6756 [1]
200-East	200-BC-1	216-B-53A	Trench	C6757 [1]
200-East	200-BC-1	216-B-53A	Trench	C6758 [1]
200-East	200-BC-1	216-B-53A	Trench	C6759 [1]
200-East	200-BC-1	216-B-53A	Trench	C6760 [1]
200-East	200-BC-1	216-B-53A	Trench	C6761 [1]
200-East	200-BC-1	216-B-53A	Trench	C6762 [1]
200-East	200-BC-1	216-B-53A	Trench	C6763 [1]
200-East	200-BC-1	216-B-53A	Trench	C6764 [1]
200-East	200-BC-1	216-B-53A	Trench	C6765 [1]
200-East	200-BC-1	216-B-53A	Trench	C6766 [1]
200-East	200-BC-1	216-B-53A	Trench	C6767 [1]
200-East	200-BC-1	216-B-53A	Trench	C6768 [1]
200-East	200-BC-1	216-B-53A	Trench	C6769 [1]
200-East	200-BC-1	216-B-53A	Trench	C6770 [2]
200-East	200-BC-1	216-B-53A	Trench	C6771 [2]
200-East	200-BC-1	216-B-53A	Trench	C6772 [2]
200-East	200-BC-1	216-B-53A	Trench	C6773 [2]
200-East	200-BC-1	216-B-53A	Trench	C6774 [2]
200-East	200-BC-1	216-B-53A	Trench	C6775 [2]
200-East	200-BC-1	216-B-53A	Trench	C6776 [2]
200-East	200-BC-1	216-B-53A	Trench	C6777 [2]
200-East	200-BC-1	216-B-53A	Trench	C6778 [3]
200-East	200-BC-1	216-B-53A	Trench	C6779 [3]
200-East	200-BC-1	216-B-53A	Trench	C6780 [3]
200-East	200-BC-1	216-B-53A	Trench	C6781 [3]
200-East	200-BC-1	216-B-53A	Trench	C6782 [3]
200-East	200-BC-1	216-B-53A	Trench	C6783 [3]
200-East	200-BC-1	216-B-53A	Trench	C6784 [3]
200-East	200-BC-1	216-B-53A	Trench	C6785 [3]
200-East	200-BC-1	216-B-53A	Trench	C6786 [3]

200-East	200-BC-1	216-B-53A	Trench	C6787 [3]
200-East	200-BC-1	216-B-53A	Trench	C6788 [3]
200-East	200-BC-1	216-B-53A	Trench	C6789 [3]
200-East	200-BC-1	216-B-53A	Trench	C6790 [3]
200-East	200-BC-1	216-B-53A	Trench	C6791 [3]
200-East	200-BC-1	216-B-53A	Trench	C6792 [3]
200-East	200-BC-1	216-B-53A	Trench	C6793 [3]
200-East	200-BC-1	216-B-53A	Trench	C6794 [3]
200-East	200-BC-1	216-B-53A	Trench	C6795 [3]

[1] Logging hole in waste site footprint.
[2] Sampling hole in waste site footprint.
[3] Logging hole placed to ascertain extent of contamination spread.
[4] Demonstration hole.
[5] Well number reserved for future use.

2.0 REFERENCES

40 CFR 302, "Designation, Reportable Quantities, and Notification," Title 40, *Code of Federal Regulations*, Part 302, as amended.

90-ERB-040, 1990, *Strategy for Handling and Disposing of Purgewater at the Hanford Site, Washington* (letter to P.T. Day, U.S. Environmental Protection Agency, and T.L. Nord, Washington State Department of Ecology, from R.D. Izatt), U.S. Department of Energy, Richland Operations Office, Richland, Washington, July 19, 1990.

DOE/RL-98-28, 1999, *200 Areas Remedial Investigation/Feasibility Study Implementation Plan – Environmental Restoration Program*, Rev. 0, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2000-38, 2006, *200-TW-1 Scavenged Waste Group Operable Unit and 200-TW-2 Tank Waste Group Operable Unit RI/FS Work Plan*, Rev. 0 Addendum Draft A, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2003-44, 2003, *BC Cribs and Trenches 200-TW-1 Operable Unit Borehole Sampling and Analysis Plan*, Rev. 0, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2003-66, 2003, *Focused Feasibiltiy Study for the BC Cribs and Trenches Area Waste Sites*, Draft A, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2007-13, 2007, *Sampling and Analysis Plan for High-Resolution Resistivity Correlation for the BC Cribs and Trenches Area*, Rev. 0, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2007-14, 2007, *Sampling and Analysis Plan for Phase 1 of the BC Cribs and Trenches Area Waste Sites Excavation-Based Treatability Test*, Rev. 0, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

DOE/RL-2007-15, 2007, *Excavation-Based Treatability Test Plan for the BC Cribs and Trenches Area Waste Sites*, Rev. 0, U.S. Department of Energy, Richland Operations Office, Richland, Washington.

Ecology, EPA, and DOE, 1989, *Hanford Federal Facility Agreement and Consent Order*, 2 vols., Washington State Department of Ecology, U.S. Environmental Protection Agency, and U.S. Department of Energy, Olympia, Washington, as amended.

Resource Conservation and Recovery Act of 1976, 42 USC 6901, et seq.

WAC 173-303, "Dangerous Waste Regulations," *Washington Administrative Code*, as amended, Washington State Department of Ecology, Olympia, Washington.

WAC 173-303-070 through 173-303-100, "Designation of Dangerous Waste," *Washington Administrative Code*, as amended, Washington State Department of Ecology, Olympia, Washington.

WAC 173-303-140, "Land Disposal Restrictions," *Washington Administrative Code*, as amended, Washington State Department of Ecology, Olympia, Washington.

WAC 173-303-145, "Spills and Discharges to the Environment," *Washington Administrative Code*, as amended, Washington State Department of Ecology, Olympia, Washington.

WAC 173-340-747, "Deriving Soil Concentrations for Ground Water Protection," *Washington Administrative Code*, as amended, Washington State Department of Ecology, Olympia, Washington.

WCH-191, 2008, *Environmental Restoration Disposal Facility Waste Acceptance Criteria*, Rev. 0, Washington Closure Hanford, Richland, Washington.

DISTRIBUTION

Onsite

2	U.S. Department of Energy Richland Operations Office	
	B.L. Foley	A6-38
	DOE Public Reading Room	H2-53
1	U.S. Environmental Protection Agency	
	R.A. Lobos	B1-46
18	Fluor Hanford, Inc.	
	M.W. Benecke	E6-44
	K. D. Christensen	S0-01
	D. L. Dewey(3)	E6-35
	L.R. Fitch	E6-44
	S.E. Imhoff	S0-12
	D.L. Klages	H8-12
	R.W. Oldham	E6-35
	D.E. Richards	R3-50
	G.D. Roosendaal	E6-35
	L.C. Swanson	E6-35
	W.R. Thackaberry	E6-35
	D. Todak(3)	E6-35
	M.W. Vermillion	R3-50
	J.A. Winterhalder	E6-35
2	Lockheed Martin Information Technology	
	Document Processing Center	H6-08
1	WCH, Inc (OHC Support)	
	B.A. Nielsen	N3-20

This page intentionally left blank.
