162

START

0037334

WHC-EP-0182-72

Tank Farm Surveillance and Waste Status Summary Report for March 1994

JUN 1994
RECEIVED
EPIC

Prepared for the U.S. Department of Energy
Office of Environmental Restoration and
Waste Management

Westinghouse
Hanford Company Richland, Washington

Hanford Operations and Engineering Contractor for the
U.S. Department of Energy under Contract DE-AC06-87RL10930

Approved for Public Release

START

DOE/MA/3279.0003

LEGAL DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

This report has been reproduced from the best available copy.

Printed in the United States of America

DISCLM-2.CHP (1-91)

WHC-EP-0182-72

UC-721

Tank Farm Surveillance and Waste Status Summary Report for March 1994

B. M. Hanlon

Date Published
June 1994

9413279.0004

Prepared for the U.S. Department of Energy
Office of Environmental Restoration and
Waste Management

Westinghouse Hanford Company
P.O. Box 1970
Richland, Washington 99352

Hanford Operations and Engineering Contractor for the
U.S. Department of Energy under Contract DE-AC06-87RL10930

Approved for Public Release

THIS PAGE INTENTIONALLY
LEFT BLANK

APPROVAL

Prepared by: B. M. Hanlon — 4/28/94
B. M. Hanlon — Date

Approved by: R E Raymond — 5/10/94
R. E. Raymond — Date
Manager, Waste Tank
Plant Engineering

9413279.0005

Date Received: 5/12/94 YMB	INFORMATION RELEASE REQUEST	Reference: WHC-CM-3-4

Complete for all Types of Release

Purpose

[] Speech or Presentation
- [] Full Paper
- [] Summary
- [] Abstract
- [] Visual Aid

(Check only one suffix)

[] Speakers Bureau
[] Poster Session
[] Videotape

[] Reference
[X] Technical Report
[] Thesis or Dissertation
[] Manual
[] Brochure/Flier
[] Software/Database
[] Controlled Document
[] Other

ID Number (include revision, volume, etc.): WHC-EP-0182-72

List attachments.

Date Release Required

Title	Unclassified Category	Impact Level
TANK FARMS SURVEILLANCE AND WASTE STATUS SUMMARY REPORT FOR FEBRUARY 1994	UC-721	2

New or novel (patentable) subject matter? [X] No [] Yes
If "Yes", has disclosure been submitted by WHC or other company?
[] No [] Yes Disclosure No(s).

Information received from others in confidence, such as proprietary data, trade secrets, and/or inventions?
[X] No [] Yes (Identify)

Copyrights? [X] No [] Yes
If "Yes", has written permission been granted?
[] No [] Yes (Attach Permission)

Trademarks?
[] No [X] Yes (Identify) TEFZEL, trademark of E. I. du Pont de Nemours & Company

Complete for Speech or Presentation

Title of Conference or Meeting

Group or Society Sponsoring

Date(s) of Conference or Meeting

City/State

Will proceedings be published? [] Yes [] No
Will material be handed out? [] Yes [] No

Title of Journal

CHECKLIST FOR SIGNATORIES

Review Required per WHC-CM-3-4	Yes	No	Reviewer - Signature Indicates Approval: Name (printed)	Signature	Date
Classification/Unclassified Controlled Nuclear Information	[]	[X]			
Patent - General Counsel	[X]	[]	OGC Memo 2/4/93		
Legal - General Counsel	[X]	[]	OGC Memo 2/4/93		
Applied Technology/Export Controlled Information or International Program	[]	[X]			
WHC Program/Project	[]	[X]			
Communications	[]	[X]			
RL Program/Project	[X]	[]	G. E. Bishop	[signature]	5/20/94
Publication Services	[X]	[]	M. Turner	[signature]	6/9/94
Other Program/Project	[]	[X]			

Information conforms to all applicable requirements. The above information is certified to be correct.

	Yes	No
References Available to Intended Audience	[X]	[]
Transmit to DOE-HQ/Office of Scientific and Technical Information	[X]	[X] CW

Author/Requestor (Printed/Signature) Date
B. M. Hanlon [signature] 4/28/94

Intended Audience
[] Internal [] Sponsor [X] External

Responsible Manager (Printed/Signature) Date
R. E. Raymond [signature] 5/10/94

INFORMATION RELEASE ADMINISTRATION APPROVAL STAMP

Stamp is required before release. Release is contingent upon resolution of mandatory comments.

APPROVED FOR RELEASE
OFFICIAL DOCUMENT
CW
Date 6/9/94

Date Cancelled

Date Disapproved

TANK FARM SURVEILLANCE AND WASTE STATUS SUMMARY REPORT FOR MARCH 1994

B. M. Hanlon

9413279.0007

ABSTRACT

This report is the official inventory for radioactive waste stored in underground tanks in the 200 Areas at the Hanford Site. Data that depict the status of stored radioactive waste and tank vessel integrity are contained within the report. This report provides data on each of the existing 177 large underground waste storage tanks and 49 smaller catch tanks and special surveillance facilities, and supplemental information regarding tank surveillance anomalies and ongoing investigations. This report is intended to meet the requirement of U. S. Department of Energy-Richland Operations Office Order 5820.2A, Chapter I, Section 3.e. (3) (DOE-RL, 1990, Radioactive Waste Management, U. S. Department of Energy-Richland Operation Office, Richland, Washington) requiring the reporting of waste inventories and space utilization for Hanford Tank Farm Tanks.

This page intentionally left blank.

9413279.0008

CONTENTS

SUMMARY 1
I. WASTE TANK STATUS 1
II. WASTE TANK INVESTIGATIONS 2
III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS 7

Appendixes:

A. WASTE TANK SURVEILLANCE MONITORING TABLES A-1
Tables:
1 Watch List Tanks A-3
2 Tanks Containing >1000 Gram Mole of Ferrocyanide A-5
3 Tanks With Potential for Hydrogen or Flammable Gas Accumulation above the Flammability Limit A-7
4 Single-Shell Tanks Containing Concentrations of Organic Salts . A-8
5 Single-Shell Tanks With High Heat Loads (>40,000 Btu/h) A-10
6 Non-Watch List Low Heat Load Tanks (<40,000 Btu/h) A-12
7 Single-Shell Tanks Monitoring Compliance Status A-15
8 Double-Shell Tanks Monitoring Compliance Status A-20
9 Automatic Food Instrument Corporation (FIC) Gauges Out of Service A-22
Figures:
1 Discrepancy Report Status A-23
2 Discrepancy Report Cumulative Total A-24
3 Discrepancy Report Status by Age A-25

B. DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION B-1
Tables:
1 Double-Shell Tank Waste Type and Space Allocation B-3
2 Double-Shell Tank Waste Inventory B-14
Figures:
1 Current Status and Contingency Space for the 242-A Evaporator Restart B-4
2 Total Available Usable Tank Space B-5
3 Priority Space Availablity and Usage B-6
4 Comparison of Monthly Average Waste Generation to Management Limit by Facility B-7
5 PUREX Monthly Waste Generations B-8
6 Tank Farm Monthly Waste Generations B-9
7 B Plant Monthly Waste Generations B-10
8 T Plant Monthly Waste Generations B-11
9 S Plant Monthly Waste Generations B-12
10 300 Area Monthly Waste Generations B-13

C. TANK AND EQUIPMENT CODE AND STATUS DEFINITIONS C-1
1 Tank and Equipment Code/Status Definitions C-3

9413279.0009

This page intentionally left blank

9413279.0010

D. TANK FARM CONFIGURATION, STATUS AND FACILITY CHARTS D-1
Figures:
1 High-Level Waste Tank Configuration D-3
2 Double-Shell Tank Instrumentation Configuration D-4
3 Single-Shell Tank Instrumentation Configuration D-5
4 Double-Shell Tank Status D-7/8
5 200 E Single-Shell Tank Status D-9/10
6 200 W Single-Shell Tank Status D-11/12
7 Hanford Tank Farms Facilities Chart: 200-East Area D-13/14
8 Hanford Tank Farms Facilities Chart: 200-West Area D-15/16

E. MONTHLY SUMMARY E-1
Tables:
1 Monthly Summary E-3
2 Tank Use Summary E-4
3 Inventory Summary by Tank Farm E-5
4 Inventory and Status by Tank - Double-Shell Tanks E-6
5 Inventory and Status by Tank - Single-Shell Tanks E-9

F. PERFORMANCE SUMMARY F-1
Table:
1 Performance Summary F-3

G. PUMPING RECORD/LIQUID STATUS AND PUMPABLE LIQUID REMAINING IN TANKS . . G-1
Tables:
1 Pumping Record G-3
2 Liquid Status and Pumpable Liquid Remaining in Tanks G-4

H. CATCH TANKS AND SPECIAL SURVEILLANCE FACILITIES H-1
Tables:
1 East and West Area Catch Tanks and Special Surveillance Facilities (Active) H-3
2 East Area Catch Tanks and Special Surveillance Facilities (Inactive) H-4
3 West Area Catch Tanks and Special Surveillance Facilities (Inactive) H-5

I. LEAK VOLUME ESTIMATES I-1
Table:
1 Single-Shell Tank Leak Volume Estimates I-3

J. INTERIM STABILIZATION STATUS J-1
Table:
1 Single-Shell Tanks Interim Stabilization Status J-3

K. TANK FARM OPERATIONS SAMPLING SCHEDULE STATUS K-1
Table:
1 Tank Farm Operations Sampling Schedule Status K-3

METRIC CONVERSION CHART		
1 inch	=	2.54 centimeters
1 foot	=	30.48 centimeters
1 gallon	=	3.80 liters
1 ton	=	0.90 metric tons

$$°F = \left(\frac{9}{5}\ °C\right) + 32$$

1 Btu/h = 2.930711 E-01 watts
(International Table)

9413279.0012

TANK FARM SURVEILLANCE AND WASTE STATUS SUMMARY REPORT FOR MARCH 1994 SUMMARY

Note: Changes from the previous month are in bold print.

I. WASTE TANK STATUS

Category	Quantity	Date of Last Change
In-Service Tanks[c]	28 double-shell	10/86
Out-of-Service Tanks[a]	149 single-shell	07/88
Assumed Leaker Tanks[f]	67 single-shell	7/93
Sound Tanks	28 double-shell 82 single-shell	1986 7/93
Interim Stabilized Tanks[b,d]	106 single-shell	04/93
Not Interim Stabilized [f]	43 single-shell	04/93
Intrusion Prevention Completed[e]	98 single-shell	09/91
Watch List Tanks [g] Total	46 single-shell 6 double-shell 52 tanks	2/94[h] 6/93

[a] Although all 149 single-shell tanks were removed from service (i.e., no longer authorized to receive waste) as of November 21, 1980, the category of "Out-of-Service" was not established until July 1988.

[b] Of the 106 tanks classified as interim stabilized, 59 are listed as assumed leakers. The total of 106 interim stabilized tanks includes six tanks that do not meet current established supernatant and interstitial liquid stabilization criteria: B-104, B-110, B-111, T-102, T-112, and U-110. (These six tanks did meet the criteria in existence when they were declared interim stabilized). B-110, B-111, and U-110 are assumed leakers but surveillance data do not show an indication of a continuing leak.

[c] Six double-shell tanks listed as "in service" are currently included on the Hydrogen Watch List and are thus prohibited from receiving waste in accordance with "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the National Defense Authorization Act for Fiscal Year 1991, November 5, 1990, Public Law 101-510.

[d] Of the 46 single-shell tanks on Watch Lists, 19 have been Interim Stabilized.

[e] Of the 46 single-shell tanks on Watch Lists, 28 have completed Intrusion Prevention (this category replaced Interim Isolation). See Appendix C, Tank and Equipment Codes and Status Definitions, for "Intrusion Prevention" definition.

[f] Eight of the tanks are both assumed leakers and not Interim Stabilized. See Appendix I, Leak Volume Estimates, for more details. Tank SX-102 was declared an assumed leaker in May, and reclassified as Sound in July, 1993. See "Waste Tank Investigations" section of the July 1993 report for more details.

[g] See Tables A-1 through A-5 for more information on Watch List Tanks. Four tanks (S-102, SX-106, TX-118, U-107) are currently on more than one Watch List.

[h] Dates for the Watch List tanks are "officially added to the Watch List" dates. See Table A-1, Watch List Tanks, for further information.

9413279.0013

II. WASTE TANK INVESTIGATIONS

This section includes all single-shell tanks or catch tanks which are showing surface level or interstitial liquid level (ILL) decreases, or drywell/ lateral radiation level increases in excess of established criteria.

There were no tanks under investigation for ILL decreases or drywell/lateral radiation level increases which exceeded the criteria in March 1994.

A. Assumed Leakers or Assumed Re-leakers: (See Appendix C for definition of "Re-leaker")

This section includes all single- or double-shell tanks or catch tanks for which an off-normal or unusual occurrence report has been issued for assumed leaks or re-leaks. Tanks/catch tanks will remain on this list until either a) completion of Interim Stabilization, or b) the updated occurrence report indicates that the tank/catch tank is not an assumed leaker.

Tank 241-BX-111. This tank was declared an assumed re-leaker on April 30, 1993. Pumping of the tank commenced on October 22, 1993. Although it was previously reported that no pumping was done in February, further reviews show that 1.5 Kgal was pumped. (See Table E-5 footnotes for further information). Saltwell jet pumping was halted in BX-110 and BX-111 pending the results of an Operational Safety Requirement/Operations Specifications Document compliance assessment. This assessment has been completed and changes made to assure compliance for this waste transfer. Pumping resumed on March 25; 7.2 Kgal was pumped in March, making a total of 79.3 Kgals pumped as of March 30, 1994. Resolution status: Upon completion of pumping, the surface level baseline for the tank will be adjusted.

Tank 241-T-111. The surface level has shown a steady decrease since the automatic FIC was repaired in August 1993. The surface level measurement after the FIC repair was 161.70 inches and continued to decrease to 161.10 inches by January 31, 1994. This is a 1.00-in decrease from the reference baseline of 162.10 inches. Off-Normal Occurrence Report RL-WHC-TANKFARM-1994-0009 was issued on February 24, 1994. This tank was declared an assumed re-leaker on February 25, 1994. The surface level has remained stable at 161.10 inches through March 1994.

Evaluation of the surface level data indicates the level began decreasing in January 1993. Efforts to begin emergency pumping of the tank have begun. Upon completion of pumping, the tank will be re-baselined. This tank had been previously partial interim stabilized.

Tank T-111 was also added to the Organics Watch List on February 28, 1994.

Preparations for emergency pumping were initiated in March as follows:

Organized an Emergency Pumping Team consisting of more than 50 direct and indirect team members.

Prepared an emergency pumping work plan and schedule that accomplishes start of pumping by May 30, 1994.

9413279.0014

Obtained liquid samples from T-111 and liquid and sludge samples from SY-102. Lab tests are underway to determine compatibility.

Successfully pressure tested transfer lines from T-111 to DCRT 244-TX.

Jet pump being prepared and calibrated. Pump equipment controls and instrumentation successfully completed OTP tests and run-in.

Training and recertification for saltwell pumping underway.

DOE-RL has proposed that the start of pumping of this tank become an interim Tri-Party Agreement milestone.

B. Tanks with increases indicating possible intrusions:

This section includes all single-shell tanks for which the surveillance data show that the surface level or ILL has met or exceeded the increase criteria, or are still being investigated.

Tank 241-B-202. A steady increase in the surface level measurement has been observed since December 1984. The manual tape pencil plummet is contacting liquid. When the quarterly reading was obtained on October 6, 1992, the level was recorded as 144.75 inches, thus exceeding the 2.00-inch increase criteria from the established baseline of 142.50 inches. The surface level measurement was rechecked on October 9, 1992, (145.50 inches), verifying the increase and that the criteria had been exceeded. Occurrence Report RL-WHC-TANKFARM-1993-0024 was issued February 13, 1993. **The surface level remained stable at 145.50 inches during March.** The monitoring frequency has been increased from quarterly to daily. This tank is Sound, Interim Stabilized, and Intrusion Prevention completed.

Resolution status: A photo package was initiated on May 11, 1993, to investigate the possibility of an intrusion. Review of previous photos was inconclusive. New photos are required to determine the actual supernatant increase, if any. A temporary baseline was established at 145.25 inches, until the new photos are available.

Tank 241-BX-101. On September 2, 1993, the surface level increased from 10.00 to 12.00 inches. **The surface level was 11.75 inches on March 31, 1994.** In-tank photographs show the manual tape donut plummet contacting liquid in a shallow pool. This tank is an Assumed Leaker, Interim Stabilized, and Intrusion Prevention completed.

Resolution Status: Comparison of October 1986 photos with November 1988 photos shows evidence of an ongoing intrusion. A work package was initiated October 14, 1993, to obtain in-tank photographs which will be used to inspect the area under the plummet and investigate the possible intrusion. A site-wide in-tank photography program is being formed and photo schedules will be produced upon finalization. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

Tank 241-BX-103. This tank has shown an erratic increase in surface level measurements since January 6, 1986. On January 18, 1993, the surface level measurement in 103-BX exceeded the 0.50-inch increase criteria from the reference baseline of 19.50 inches, and was verified on January 20, 1993.

9413279.0015

Discrepancy Report S&DA 93-522 was issued January 21, 1993. Occurrence Report RL-WHC-TANKFARM-1993-0036 was issued March 25, 1993. **The surface level measurement is currently 20.50 inches.** The FIC plummet is contacting liquid as indicated by in-tank photographs taken October 31, 1986. This tank is Sound, Interim Stabilized, and Intrusion Prevention completed.

Resolution status: The current level is greater than that prior to stabilization in November 1983. The tank was previously determined to have experienced an intrusion from 1977 to March 1983 (prior to stabilization). Subsequent isolation was expected to halt the intrusion, however, the intrusion is apparently ongoing. A work package was initiated on May 11, 1993, to re-seal pits and risers and to obtain in-tank photos. The photos will be used to assess the current stabilization status of the tank. A visual survey of the area was performed to determine possible paths for precipitation to enter the tank. The weather covering on the pits and risers was found in place and undamaged. The existing grade is level and revealed no obvious draining problems. Ongoing design/isolation drawing review revealed that nozzles, floor drains and some transfer lines entering the heel pit have been left open. Photo verification of the intrusion will determine the need to provide additional isolation measures. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

9413279.0016

Tank 241-BY-105. **The ILL is currently at 13.76 feet. The baseline is 13.812 feet.** Although the surface level and ILL are within the criteria limits, the data indicates unusual behavior trends that merit continued observation. The monitoring frequency has been increased from quarterly to weekly. This tank is on the ferrocyanide Watch List, an Assumed Leaker, and not yet Interim Stabilized.

Resolution Status: The surface level and ILL are displaying behavior similar to TX-113 and TX-115. The ILL is showing an increase, while the surface level measurement is showing a decrease. This phenomena could be due to either solids dissolution or formation of a depression in the solids beneath the plummet in conjunction with an intrusion. Review of previous photos indicates the liquid volume is increasing, although it cannot be verified that the solids level is decreasing. A photo package was initiated to investigate the possibility of intrusion, or solids dissolution. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

Tank 241-S-102. The FIC was out of service from November 16, 1993, to January 14, 1994. The surface level reading after the FIC was repaired on January 14 was 207.00 inches. This level exceeded the 3.00-inch increase criteria from the reference baseline of 202.30 inches. Reference Discrepancy Report S&DA-904-672. This tank has a history of erratic increases/decreases. In-tank photographs taken March 18, 1988, show the FIC plummet contacting an uneven, dry surface. A verification of the reference elevation was completed February 27, 1994. The FIC counter was found to be out of calibration by +2.60 inches. **The FIC surface level reading on March 31 was 205.50 inches. The LOW ILL was within the 0.10-foot tolerance when last scanned on March 28, 1994.**

Resolution status: Photos taken in March 1988, show the surface consists of very uneven solids with scattered liquid pools. Photos taken in 1983 compared with the 1988 photos indicate the waste is shifting, possibly causing a change

in surface level under the plummet. Reevaluation of the ILL using the "new method" shows an increasing trend of about 0.4 inches per year. Occurrence Report 77-191 attributed previous intrusions into the tank to drainage from the SA and SB valve pits. Because neither the tank nor the pits are interim isolated, the intrusion is likely ongoing. A photo package was initiated on May 17, 1993, to confirm the ongoing intrusion. This tank is on the hydrogen and organic salts Watch List. A safety evaluation has been issued establishing required controls in order to perform photo missions on hydrogen Watch List tanks. Either intrinsically safe camera equipment must be used, or a continuous flammable gas monitoring system must be installed. An engineering service request (ESR) was submitted on January 6 to perform a vendor search for an acceptable camera design. A monitoring system is not expected to be in place before mid-1994.

9413279.0017

Tank 241-S-103. The FIC was out of service from March 8 to May 14, 1993. The surface level increased from 104.15 inches on March 8 to 104.80 inches after FIC repair on May 14, 1993. On August 20, 1993, a temporary baseline of 104.80 inches was established, with a criteria of +2.00 inches. This tank has previously been on report for an increase but showed an erratic decreasing trend the latter part of November 1993. The readings ranged from 104.80 to 103.80 inches. **Readings continue to fluctuate between 104.10 and 104.70 inches. The surface level on March 31, 1994, was 104.40 inches. The LOW, last scanned March 28, 1994, did not exceed the .08-foot tolerance.** This tank is Sound, and not yet Interim Stabilized.

Resolution status: After recalibration of the FIC on June 7, 1993, the surface level (SL) remained stable at approximately 104.65 inches. Historical SL shows a general increase since 1981. The SL has continued to increase since the recent jump following FIC calibration. Normally, recalibration returns the SL to previous levels. Reevaluation of surface level data indicates a steady decrease from 104.90 on November 18, to 104.40 inches on December 31, 1993. **FIC calibration performed on March 7, 1994, verified the surface level readings and supports the observed decrease. The ILL baseline using the count rate method is set at .35 inches/year increase which is substantiated by a previous intrusion investigation performed in 1984. The majority of the most recent ILL readings are below baseline. No action criteria have been exceeded. The surface level behavior in this tank will be re-evaluated by May 16, 1994.**

Tank 241-TX-111. Although the surface level and ILL measurements do not exceed the criteria, the data indicates unusual behavior trends that merit continued observation. This tank is Sound, Interim Stabilized, and Intrusion Prevention completed.

Resolution Status: The ILL trend was re-analyzed for this tank using the new "count rate" method. A steady, significant increase of 1.32 inch/year is evident. Surface level data is showing a decrease. Photos show a dry surface. The surface level decrease is expected to be caused by crumbling of the waste beneath the plummet. Overall, the waste level behavior of the tank is similar to that of TX-113 and 115. A photo package was initiated on October 13, 1993, to investigate the possibility of an intrusion. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

Tank 241-TX-113. Although the surface level and ILL measurements do not exceed the criteria, the data indicates unusual behavior trends that merit continued observation. This tank is an Assumed Leaker, Interim Stabilized, and Intrusion Prevention completed.

Resolution status: The technical evaluation of the alert condition in this tank was completed April 14, 1993. The results were inconclusive, with recommendation to accelerate the October 1997 waste characterization of the tank. This characterization is expected to confirm that solids are dissolving, causing an increase in ILL. Acceleration of waste characterization is not possible. Watch List tanks have first priority for core sampling. A photo package has been written. LOW scans and SL readings have been increased from a quarterly to a monthly frequency. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

9413279.0018

Tank 241-TX-115. Although the surface level and ILL measurements do not exceed the criteria, the data indicates unusual behavior trends that merit continued observation. This tank is an Assumed Leaker, Interim Stabilized, and Intrusion Prevention completed.

Resolution status: The technical evaluation of the alert condition in this tank was completed April 14, 1993. The results were inconclusive, with recommendation to accelerate the October 1997 waste characterization. Waste characterization is expected to confirm that solids are dissolving, causing an increase in ILL. Acceleration of waste characterization is not possible for non-Watch List tanks. The 1981 photos show evidence of rain intrusion through a central pump pit riser. However, it cannot be concluded from the 1988 photos that the intrusion is ongoing. This tank will be included in the waste characterization with TX-113. LOW scans are taken weekly, and surface level readings have been increased from a quarterly to a monthly frequency. A finalized photo schedule is not complete, however, in-tank photos for this tank are may be available by late 1995.

Tank 241-TY-102. Discrepancy Report S&DA-92-489 was issued November 9, 1992, when the surface level measurement exceeded the 0.50-inch increase criteria from the established baseline of 31.40 inches. The increase criteria of 0.50 inch, considered to be an extremely tight tolerance for this tank, was revised to 1.00 inch, which is more in line with other tanks that exhibit similar erratic surface level behavior. The tank has a history of intrusions and icicle-shaped mineral buildup on the FIC plummet. The FIC plummet is contacting a shallow pool of liquid. The surface level measurement remained stable during March 1994. This tank is Sound, Interim Stabilized, and Intrusion Prevention completed.

Resolution status: This tank is experiencing an ongoing intrusion as is evident by comparison of November 1984 photos with July 1987 photos and an increasing trend in surface level data. A visual survey was conducted to determine possible paths for precipitation to enter the tank. The grade around the tank is level and weather covering is on the pits and intact. The photo package, initiated May 17, 1993, will be required to assess the current stabilization status of the tank, and to assist in determining the possible paths of intrusion. Ongoing design/isolation drawing review revealed that nozzles, floor drains and some transfer lines entering the pump pit have been left open. Photo verification of the intrusion will determine the need to

provide additional isolation measures. A finalized photo schedule is not complete, however, in-tank photos for this tank may be available by late 1995.

AX-152 Diverter Station. The surface level measurement exceeds the 30.00-in action limit and the 48.00-inch maximum operating limit, but does not exceed the Operating Specifications Document (OSD) limit of 77.00 inches.

Resolution status: Alternative methods to supply water for transfer are underway due to a water line leak in the A-Farm complex. Pumping should begin approximately mid-April.

241-E/W-151 Vent Station Catch Tank. The zip cord surface level reading exceeds the maximum operating limit of 36.00 inches. The manual tape was out of service from July 7, 1992, to December 16, 1992, when a temporary zip cord was installed. A surface level reading of 45.50 inches was obtained, exceeding the active tank limit of 50% volume of 40 inches (400 gallons). Discrepancy Report S&DA-92-511 was issued December 24, 1992. Transfers are not permitted until the tank is pumped and the level is within limits. A new calibrated zip cord was installed December 16, 1993, and the surface level reading went from 71.00 to 59.00 inches. Discrepancy Report 93-655 was issued December 17, 1993. The zip cord was replaced with a new manual tape on December 23, 1993. The level reading was 60.50 inches. The surface level reading on March 31, 1994, was 62.50 inches.

Resolution status: The catch tank was sampled on December 23, 1993. The waste is to be transferred using existing cross-site lines. The required procedure is in approval stages; other documentation has been completed. Transferring with this method could be ready by late April.

UX-302-A Catch Tank. The surface level measurement exceeds the maximum operating limit of 50.00 inches. Discrepancy report S&DA-92-465 was issued May 12, 1992. The current surface level reading is 66.90 inches, which exceeds the 50% volume of 54 inches (8840 gallons). The FIC plummet is contacting liquid.

Resolution status: Work packages for the transfer of waste from UX-302-A and the repair of necessary instrumentation are being prepared, and the transfer of waste is being scheduled as a prestart item for the cross-site transfer. A work package has been prepared to sample/pump this catch tank. Transfer will begin after completing Vent Station transfer. Procedures are being prepared.

III. SURVEILLANCE AND WASTE TANK STATUS HIGHLIGHTS

1. BX Tanks Saltwell Jet Pumping

Tank 241-BX-110 - Saltwell jet pumping began December 4, 1993, to pump contents of this tank into 244-BX Double Container Receiver Tank (DCRT). Saltwell pumping was shut down on December 9, 1993, for repair of system air leaks. After repair of the leaks, it was determined other problems existed, resulting in a work order to modify the system to run the pump manually. It is uncertain whether any further waste can actually be pumped. A total of 4.0 Kgal has been pumped from BX-110.

Tank 241-BX-111 - Saltwell jet pumping began on October 22, 1993, to pump tank BX-111 into 244-BX Double Container Receiver Tank. 7.2 Kgal was pumped in March. A total of 79.3 Kgal has been pumped. (See Table E-5 for further information on recalculations made due to errors found in pumping volumes).

2. Tank Waste Remediation System Safety Initiatives

The U. S. Secretary of Energy has directed that six safety initiatives be implemented in the Tank Waste Remediation System Program to accelerate the mitigation/resolution of the higher priority waste tank safety issues at the Hanford Site. Forty-two milestones were established for accomplishing the initiatives. Two Safety Initiatives were completed during March:

(a) "Issue approved criticality safety analysis, and if needed, a control plan, and close the Unreviewed Safety Question by March 1994." The USQ was closed March 17, 1994. (See Item #5 below)

(b) "Complete sampling and safety evaluation of liquid organic Tank C-103 by March 1994."

Also, "Close Ferrocyanide Unreviewed Safety Question," which was completed February 28, was approved by DOE on March 1, 1994. The ferrocyanide Unreviewed Safety Question was closed based on the necessary technical justification and an ample margin of safety delineated in the support documentation. The closure of the USQ does not resolve the ferrocyanide safety issues. Resolution will require characterization of the ferrocyanide tank waste to confirm that the criteria are met. Also, the necessary monitoring, controls, and procedures must be in place to ensure that operations are conducted within the criteria prior to resolution of the ferrocyanide safety issue.

3. Tank Farms Stand Down (Administrative Hold)

On August 12, 1993, non-essential work activities in the tank farms were put on administrative hold by WHC senior management until operators, supervisors and managers are retrained to perform their duties in a safe and accountable manner. Minimal essential activities required for safety, monitoring and compliance, including the daily "pump-bumping" of the SY-101 mixer pump, will continue. The administrative hold has impacted several programmatic goals for Tank Waste Remediation System (TWRS). A letter from WHC senior management has been submitted to DOE-RL addressing these programmatic delays. Further corrective actions were addressed in a Tank Waste Remediation System Tank Farm Resumption of Work Plan, dated September 13, 1993. Contained within the Work Plan is the Integrated Schedule for reinitiating individual work activities on an ongoing basis.

Testing of the SY-101 mixer pump continues to be successfully accomplished. Many other tank farm work activities have now been fully resumed. In addition, reorganization is taking place to reduce management layers, and the Integrated Upgrade Plan of Action was issued January 31, 1994.

9413279.0020

4. Tank 241-SY-101 Mixer Pump

Full Scale Test #23 was started on March 30. The pump was run at 750 RPM (at 35, 65, 95, 125, 155, and 185 degree orientation), for 30 minutes each. Hydrogen peaked at 530.0 ppm. Nitrous Oxide and Ammonia peaked at 617.0 ppm and 117.0 ppm, respectively.

5. Criticality Safety Issues

On April 30, 1992, an Unreviewed Safety Question (USQ) concerning criticality safety issues in the Tank Farms was declared to be a reportable event. Unusual Occurrence report RL-WHC-TANKFARM-1992-0037 was issued. A prohibition was placed on all waste transfers into and between the tank farm facilities which is negatively affecting various Hanford programs. On September 1, 1992, the approved Justification For Continued Operations (JCO) was received. This establishes the limitations for all tanks receiving transfers and also excludes any interim stabilization of single-shell tanks until further evaluations are completed and approved by DOE-HQ. On December 15, 1992, the approved JCO was issued as WHC-SD-WM-JCO-001, "Justification for Continued Operations of Hanford High Level Waste Tanks Resulting From the Criticality USQ, 492-CRITSAS."

9413279.0021

On March 31, 1994, DOE approved the WHC request to close the criticality USQ (see item #2 above). This approval does not resolve the outstanding criticality safety issues pending in the tank farms. Resolution of these issues will require WHC to complete actions described in "Upgrade Activities for the Criticality Safety Program of Hanford High-Level Radioactive Waste Tank Farm," dated September 1992.

Also, the existing JCO will remain in effect until WHC completes the following: 1) Criticality Safety Evaluation Reports for single-shell and double-shell tanks; 2) Criticality Prevention Specifications; 3) Criticality operating procedures; and 4) Operator training for the revised operating procedures.

6. Tank 241-C-102 Treated as an Organic Watch List Tank

Tank C-102 continues to be treated as an Organic Watch List tank, relative to tank intrusive activities. See WHC-EP-0182-71 (February) for further information.

7. Additional Thermocouple Tree Connections to Tank Monitor & Control System (TMACS)

Thermocouple trees in C-Farm have now all been connected to TMACS, (a continuous computer monitoring system), with the exception of C-204 which does not have a thermocouple tree, and the new tree installed in C-108. TMACS will begin reading the new sensors on April 4, 1994.

Construction is underway to connect BX-Farm thermocouple trees to TMACS. If the schedule holds, BX-Farm could be operational on TMACS by April 30, 1994.

Construction to connect T-Farm and AN-Farm thermocouple trees to TMACS is scheduled to restart in April 1994. No estimated completion dates are yet available for these farms.

8. Occurrence Reports

RL-WHC-TANKFARM-1994-0009 (UNUSUAL OCCURRENCE) - APPARENT DECREASE IN LIQUID LEVEL IN SINGLE-SHELL UNDERGROUND STORAGE TANK 241-T-111 (10-Day Report 2/28/94)

The liquid level in Tank 241-T-111, as measured by an automatic surface level indicating device, has decreased 1.6 inches during the past year.

Tank 241-T-111 was previously declared an assumed leaker in 1984 with an assumed leak volume of <1000 gallons. From 1984 to January 1993, the level has shown a steadily increasing trend (liquid level increased approximately 0.6 inches above the baseline). Since January 1993, the level has decreased to 1.0 inches below the liquid level baseline. The leak detection decrease criteria for this tank is 2 inches. This criteria has not been exceeded. This tank was pumped in 1978. Approximately 87,000 gallons were transferred out.

In addition to the automatic liquid level surface measurements taken on this tank, periodic Liquid Observation Well (LOW) readings are taken. This method uses a neutron source inserted into a drywell installed in the tank and measures liquid level by the reflection of radiation from the liquid surface interface. These readings also appear to show a decrease in liquid level during this time period although it is difficult to quantify the exact amount.

A review of drywell data which measures underground gamma radiation levels outside of the tank does not indicate any leakage to the soil surrounding the tank.

The last in-tank photographs were taken in 1984.

Tank 241-T-111 contains 458,000 gallons of waste material (predominantly sludge); 51,000 gallons of liquid of which 45,000 is assumed pumpable.

This tank is currently being treated as a Watch List tank (Organics).

On February 25, the occurrence was upgraded from Off-Normal to Unusual Occurrence.

RL-WHC-TANKFARM-1994-005 (OFF-NORMAL) - ALARMS FOR DOUBLE-CONTAINED RECEIVER TANKS DISCOVERED NOT INSTALLED RESULTS IN OSD NON-CONFORMANCE: OSD LIMITS FOR LEVEL/PRESSURE NOT EXCEEDED (10-Day Report [latest], 3/11/94)

On January 27, 1994, during a review of operating procedures, it was discovered that requirements of OSD-T-151-00011, "Operating Specifications for Saltwell Receiver Vessels," section 11.2.B, "Liquid Level," and section 11.2.E, "Primary Tank Pressure," had not been met.

9413279.0022

Section 11.2.B requires a high liquid level alarm be connected to the liquid level conductivity probe. This alarm has not been installed in the Double-Contained Receiver Tanks (DCRT).

Section 11.2.E requires a high pressure alarm for the primary tank pressure. This alarm has not been installed in the DCRTs.

It has been determined that 244-TX and 244-BX are in non-conformance to the OSD, and it is assumed that the remaining DCRTs are also deficient. Tanks 244-TX, 244-S, 244-U and 244-CR are in a static condition, either receiving or transferring waste. Tank 244-BX is being used to receive saltwell liquid. On January 28, the transfer of waste from 241-BX-111 to 244-BX DCRT was secured following verification of the non-conformance. At that time, tank pressure and liquid levels were within OSD limits.

9413279.0023

All OSDs are being reviewed by Tank Waste Operations to ensure that adequate implementation can be demonstrated.

The root cause is inadequate administrative control. The OSD for Saltwell Receiver Vessel DCRTs was developed, issued and implemented for use by operations without an adequate field verification process. This allowed for sections of the OSD to be implemented without the necessary equipment in place for compliance.

To allow for East and West Tank Farms to complete their review of all OSDs and to ensure that adequate implementation can be demonstrated, the final report due March 11, 1994, will be postponed until June 30.

RL-WHC-TANKFARM-1993-0105 (UNUSUAL) - DISCOVERY OF NEW GAS (METHANE GAS) IN WASTE TANK 241-SY-101 DISCOVERED TO ADD 10% ENERGY TO THE BURN ANALYSIS RESULTS IS BEING INCLUDED IN THE CURRENT SAFETY ASSESSMENT (Final Report, 3/31/94)

On December 2, 1993, WHC Operations was notified by Los Alamos National Laboratories (LANL) that upon further review of the data from Tank SY-101 window "I" which occurred on June 26, 1993, methane gas (CH_4) was found in the amount of 1000 parts per million (ppm) in the tank vapor space. LANL also advice WHC operations that methane has 3.2 times the heating value of hydrogen (H_2). This in turn adds fuel to the burn analysis in the current safety assessment.

All mixer pump activities were halted, with the exception of the pump bump operations, until further resolution was obtained. The Technical Review Group met with LANL and concurred with the presentation from LANL to continue with mixer pump testing. DOE-RL concurred with WHC to lower the maximum level to 406 inches and continue with pump testing. The control to lower the maximum level to 406 inches was implement on December 2, 1993. The current level of the tank is 400 inches and an auto shut-off is installed that would immediately shut off the pump if the tank level rises two inches during pump bump operations.

The lowering of the maximum level allowable for mixer pump operations from 408 to 406 inches will provide an adequate safety margin bounded within the current safety assessment. The impact of the occurrence on

the environment, safety and health of workers and the public, is negligible.

LANL prepared a document to outline the controls needed to allow continued mixer pump operations and testing. The basis for the LANL report was that methane adds approximately 10% fuel to the burn analysis. With this additional fuel LANL's recommendation was to lower the maximum level for mixer pump operations to 406 inches from 408 inches. The current level of the tank is 400 inches and an automatic shut-off is installed that would immediately shut off the pump if the tank level rises two inches during pump bump operations.

On February 10, 1994, the Plant Review Committee declared the event an Unreviewed Safety Question. It was also concluded that the safest configuration for the tank was to continue pump operation and maintain waste levels below 406 inches with a preferred level of 402 inches. A Justification for Continued Operation (JCO) is not required since operation in the safest configuration is within the limits of the authorization basis.

On February 11, 1994, the occurrence was upgraded to an Unusual Occurrence.

Final evaluation - The root cause was determined to be administrative controls less than adequate, based on the lack of a formal reporting method, coupled with the lack of review of the presentation information and lack of attention to the significance of the data presented.

Immediate and appropriate action was taken by LANL in an effort to prevent future occurrences of this type. Monthly status/update meetings are now scheduled between the gas analysis and the safety assessment groups plus both groups have recognized the need to communicate more often should the situation dictate.

9. Changes to the Report

(a) An updated Watch List Tanks pocket list is included with this report (see next page).

(b) Appendix C. Tank and Equipment Code/Status Definitions

Definitions for three new terms have been added to this section; Jet Pump, Saltwell Screen, and Emergency Pumping Trailer (See page C-5).

Two new acronyms have been added to this section: TMACS and CASS (see page C-9)

9413279.0024

If you have a need for the following Watch List Tanks pocket list, please tear this page out and cut out the list and fold it. Tape it closed if you wish.

You are encouraged to urge your fellow employees to replace their obsolete pocket card with the list below. You may duplicate this list or cc:mail the author for additional copies.

The list will be updated and included in this report as changes occur.

3/31/94

Watch List Tanks

		SST	
A-101	H	SX-109	H
AX-101	H	T-107	F
AX-103	H	T-110	H
B-103	O	T-111	O
BX-102	F	TX-105	O
BX-106	F	TX-118	F,O
BY-103	F	TY-101	F
BY-104	F	TY-103	F
BY-105	F	TY-104	F
BY-106	F	U-103	H
BY-107	F	U-105	H
BY-108	F	U-106	O
BY-110	F	U-107	O,H
BY-111	F	U-108	H
BY-112	F	U-109	H
C-103	O	U-111	O
C-106	HH		
C-108	F	**DST**	
C-109	F	AN-103	H
C-111	F	AN-104	H
C-112	F	AN-105	H
S-102	H,O	AW-101	H
S-111	H	SY-101	H
S-112	H	SY-103	H
SX-101	H		
SX-102	H	**Legend**	
SX-103	H	H - Hydrogen	
SX-104	H	F - Ferrocyanide	
SX-105	H	O - Organics	
SX-106	H,O	HH - High Heat	

Ferrocyanide

BX-102 BY-112
BX-106 C-108
BY-103 C-109
BY-104 C-111
BY-105 C-112
BY-106 T-107
BY-107 TX-118
BY-108 TY-101
BY-110 TY-103
BY-111 TY-104
20 Tanks

Hydrogen

SST
A-101 T-110
AX-101 U-103
AX-103 U-105
S-102 U-107
S-111 U-108
S-112 U-109
SX-101 19 tanks
SX-102
SX-103 DST
SX-104 AN-103
SX-105 AN-104
SX-106 AN-105
SX-109 AW-101
SY-101
SY-103
6 tanks
25 tanks

Organics

B-103 TX-105
C-103 TX-118
S-102 U-106
SX-106 U-107
T-111 U-111
10 Tanks

High Heat

C-106

Total of 52 tanks on Watch Lists (S-102, SX-106, TX-118, U-107 are on more than one list)

9413279.0025

This page intentionally left blank.

9413279.0026

APPENDIX A

WASTE TANK SURVEILLANCE MONITORING TABLES

This page intentionally left blank

9413279.0028

TABLE A-1. WATCH LIST TANKS (Sheet 1 of 2)

These tanks have been identified as Watch List Tanks in accordance with Public Law 101-510, Section 3137, " Safety Measures for Waste Tanks at Hanford Nuclear Reservation," (1990). These tanks have been identified as the Priority 1 Hanford Site Tank Farm Safety Issues: "Issues/situations that contain most necessary conditions that could lead to worker (onsite) or offsite radiation exposure through an uncontrolled release of fission products, e.g., Tank SY-101."

March 31, 1994

Single-Shell Tanks Tank No.		Category	Officially Added to Watch List
A-101	(2)	Hydrogen	1/91
AX-101	(2)	Hydrogen	1/91
AX-103	(2)	Hydrogen	1/91
B-103	(2)	Organic Salts	1/91
BX-102	(2)	Ferrocyanide	1/91
BX-106	(2)	Ferrocyanide	1/91
BY-103	(2)	Ferrocyanide	1/91
BY-104	(2)	Ferrocyanide	1/91
BY-105	(2)	Ferrocyanide	1/91
BY-106	(2)	Ferrocyanide	1/91
BY-107	(2)	Ferrocyanide	1/91
BY-108	(2)	Ferrocyanide	1/91
BY-110	(2)	Ferrocyanide	1/91
BY-111	(2)	Ferrocyanide	1/91
BY-112	(2)	Ferrocyanide	1/91
C-103	(2)(4)	Organic Salts	1/91
C-106	(2)	High Heat Load	1/91
C-108	(2)	Ferrocyanide	1/91
C-109	(2)	Ferrocyanide	1/91
C-111	(2)	Ferrocyanide	1/91
C-112	(2)	Ferrocyanide	1/91

Single-Shell Tanks Tank No.		Category	Officially Added to Watch List
S-102	(2)	Hydrogen,	1/91
	(2)	Organic Salts	1/91
S-111	(2)	Hydrogen	1/91
S-112	(2)	Hydrogen	1/91
SX-101	(1)(2)	Hydrogen	1/91
SX-102	(1)(2)	Hydrogen	1/91
SX-103	(1)(2)	Hydrogen	1/91
SX-104	(1)(2)	Hydrogen	1/91
SX-105	(1)(2)	Hydrogen	1/91
SX-106	(1)(2)	Hydrogen,	1/91
	(1)(2)	Organic Salts	1/91
SX-109	(1)(2)	Hydrogen because other tanks vent thru it	1/91
T-107	(3)	Ferrocyanide	2/91
T-110	(2)	Hydrogen	1/91
T-111	(8)	Organic Salts	2/94
TX-105	(2)	Organic Salts	1/91
TX-118	(2)	Ferrocyanide,	1/91
	(2)	Organic Salts	1/91

Single-Shell Tanks Tank No.		Category	Officially Added to Watch List
TY-101	(2)	Ferrocyanide	1/91
TY-103	(2)	Ferrocyanide	1/91
TY-104	(2)	Ferrocyanide	1/91
U-103	(2)	Hydrogen	1/91
U-105	(2)	Hydrogen	1/91
U-106	(2)	Organic Salts	1/91
U-107	(2)	Organic Salts	1/91
	(6)	Hydrogen	12/93
U-108	(2)	Hydrogen	1/91
U-109	(2)	Hydrogen	1/91
U-111	(7)	Organic Salts	8/93
46 Tanks			

Double-Shell Tanks Tank No.		Category	
AN-103	(1)(2)	Hydrogen	1/91
AN-104	(1)(2)	Hydrogen	1/91
AN-105	(1)(2)	Hydrogen	1/91
AW-101	(1)(5)	Hydrogen	6/93
SY-101	(1)(2)	Hydrogen	1/91
SY-103	(1)(2)	Hydrogen	1/91
6 Tanks			

Four tanks (S-102, SX-106, TX-118, U-107) are on more than one Watch List

See footnotes next page

TABLE A-1 WATCH LIST TANKS (Sheet 2 of 2)

Footnotes:

(1) These eight single-shell tanks and the six double-shell tanks on the Watch List are actively ventilated.

Although on various dates beginning in March 1990, WHC identified tanks containing ferrocyanide, organic salts, etc., which were then added to this report as Watch List tanks, the following official notifications were made to DOE-RL:

(2) Letter 9059124, H. D. Harmon, WHC, to R. E. Gerton, DOE-RL, "Safety Measures for Waste Tanks at Hanford Site, Richland, Washington," dated January 8, 1991, identified 23 ferrocyanide tanks, 23 tanks with potential for accumulation of flammable gas, eight organic tanks, and one high heat load tank, as being Watch List tanks. (52 tanks)

The ferrocyanide and hydrogen tanks were declared Unresolved Safety Questions (USQ); the organic tanks and the high heat load tank were within the safety envelope as defined by the safety analysis reports and were not designated as USQs. On March 1, 1994, the ferrocyanide USQ was closed. See Table A-2 footnote (1) for further information.

(3) Letter 9059124.1 (revision to 9059124 above), dated February 8, 1991, added T-107 to the Ferrocyanide Watch List. (53 tanks)

(4) Tank C-103 was declared a USQ per Unusual Occurrence Report RL-WHC-TANKFARM-1992-0069, issued September 1992, because of an organic layer covering the surface. This tank was previously identified as a Watch List tank in footnote (2) above.

(5) Letter 9354700, J. C. Fulton, WHC, to R. E. Gerton, DOE-RL, "Addition of Tank 241-AW-101 to Flammable Gas Watch List," dated June 3, 1993, added this double-shell tank to the Watch List. (54 tanks)

(6) Letter 9353957, J. C. Fulton, WHC, to R. E. Gerton, DOE-RL, "Single-Shell Waste Tank 241-U-111," dated May 24, 1993, recommended this tank be included on the Organic Tanks Watch List. This tank was added to the Watch List on August 31, 1993.

(7) Tank U-107 was declared a USQ per Occurrence Report RL-WHC-TANKFARM-1993-0115, issued December 1993, because of an increase in slurry growth. This tank is also on the Organics Watch List.

(8) Tank T-111 was added to the Organic Salts Watch List on February 28, 1994, upon recommendation by WHC Waste Tank Safety Program.

Note: BX-110, BX-111, BY-101 and T-101 were removed from the Ferrocyanide Watch List in July 1993, per letter 93-CAB-223, John H. Anttonen, DOE-RL, to T. M. Anderson, WHC, "Resolution of Unreviewed Safety Question for Four Ferrocyanide Tanks," dated July 9, 1993.

TABLE A-2. TANKS CONTAINING >1000 GRAM MOLE OF FERROCYANIDE (Watch List Tanks)(Sheet 1 of 2)

The Unreviewed Safety Question (USQ) associated with these tanks was closed March 1, 1994. (1)

Temperatures in these tanks did not exceed the maximum temperature criteria for March 1994.
All Watch List tanks are reviewed for increasing temperature trends. Tanks connected to TMACS are required to be monitored continuously; those not connected are required to be monitored weekly. Temperatures are taken in the waste unless indicated otherwise.

Tank No.	Riser No.	Highest Temperature Reading in Waste (F.)	Date of Reading	Readings Taken by TMACS (5)	Total Waste (inches) (6)	FeCN (2) (x1000 g mol)	Estimated Heat Load (3) (Btu/h)	Estimated Heat Load (3) (kW)	Date Declared Assumed Leaker	Interim Stabilized Date
BX-102	8	64	03/16/94	No	42	<1	2800	<2.93	1971	11/78
BX-106	1	64	03/16/94	No	24	<1	2500	<2.93	Sound	N/A
BX-106	7	62	03/14/94	No	24	<1	2500	<2.93	Sound	N/A
BY-103	1	81	03/27/94	Yes	153	66	5500	2.52	1973	N/A
BY-104	1	126	03/25/94	Yes	155	83	8700	1.61	Sound	1/85
BY-104	10B	114	03/25/94	Yes	155	83	8700	1.61	Sound	1/85
BY-105	10C	113	03/30/94	Yes	190	36	8700	0.97	1984	N/A
BY-105	1	120	03/30/94	Yes	190	36	8700	0.97	1984	N/A
BY-106	1	128	03/31/94	Yes	241	70	10100	0.97	1984	N/A
BY-107	1	94	03/30/94	Yes	104	42	8900	4.25	1984	7/79
BY-108	8	109	03/31/94	Yes	90	58	9200	6.74	1972	2/85
BY-110	1	117	03/28/94	Yes	152	71	6900	7.39	Sound	1/85
BY-110	10A	108	03/13/94	Yes	152	71	6900	7.39	Sound	1/85
BY-111	LOW-1	87	03/30/94	Yes	174	6	5500	10.02	Sound	1/85
BY-111	14	84	03/24/94	Yes	174	6	5500	10.02	Sound	1/85
BY-112	LOW-15	82	03/31/94	Yes	113	2	6100	<2.93	Sound	5/85
BY-112	2	88	03/30/94	Yes	113	2	6100	<2.93	Sound	5/85
C-108	5	69	03/30/94	No	31	25	6000	<2.93	Sound	3/84
C-108	1	77	03/07/94	No	31	25	6000	<2.93	Sound	3/84
C-109	8	76	03/08/94	No	31	30	7000	1.11	Sound	11/83
C-109	3	76	03/07/94	No	31	30	7000	1.11	Sound	11/83
C-111	5	72	03/30/94	No	28	33	6400	<2.93	1968	3/84
C-112	1	79	03/08/94	No	45	31	7500	<2.93	Sound	9/90
C-112	8	77	03/08/94	No	45	31	7500	<2.93	Sound	9/90
T-107	4	67	03/07/94	No	73	5	3000	<2.93	1984	N/A
TX-118 (4)	4	76	03/31/94	No	134	<1	4600	1.44	Sound	4/83
TY-101	4	64	03/30/94	No	50	23	3100	<2.93	1973	8/83
TY-103	4	67	03/31/94	No	66	28	4000	<2.93	1973	2/83
TY-104	4	64	03/31/94	No	24	12	3000	<2.93	1981	1/83
20 Tanks			Legend: TMACS = Tank Monitor & Control System							

Note: Tanks BX-110, BX-111, BY-101 and T-101 were removed from this Watch List in July 1993, per letter 93-CAB-223, John H. Anttonen, DOE-RL, to T. M. Anderson, WHC, "Resolution of Unreviewed Safety Question for Four Ferrocyanide Tanks," dated July 9, 1993.

FOOTNOTES: See next page

TABLE A-2. TANKS CONTAINING >1000 GRAM MOLE OF FERROCYANIDE (Watch List Tanks) (Sheet 2 of 2)

FOOTNOTES:

(1) Closure of the Ferrocyanide Unreviewed Safety Question (USQ) was approved in U.S. DOE Memorandum EM-36, Thomas P. Grumbly, to Manager, DOE Richland Operations Office, "Approval of the Request to Close the Ferrocyanide Unreviewed Safety Question at the Hanford High-Level Waste Tank Farms," dated March 1, 1994; and DOE-RL letter 94-SST-052, T. R. Sheridan, to President, WHC, "Closure of the Ferrocyanide Unreviewed Safety Question," dated March 4, 1994.

(2) The amount of FeCN reported in the tanks is based on WHC-SD-WM-ER-133-REV 0, "An Assessment of the Inventories of the FeCN Watch List Tanks," (Table 3-7), October 1991.

(3) The estimated heat generation rates are from WHC-EP-0709, "Estimatation of Heat Load in Waste Tanks Using Average Vapor Space Temperatures," December 1993. This document analyzed all ferrocyanide tanks.

(4) This tank also contains a high concentration (>3% wt TOC) of organic salts.

(5) This column indicates which tanks are being monitored by the Tank Monitor & Control System (TMACS); automatic temperature readings are taken continuously. Temperatures in tanks connected to TMACS but temporarily not being monitored by TMACS are taken manually. Thermocouple trees in all C-Farm tanks have been connected to TMACS as of March 31, 1994, (with the exception of C-201 which has no thermocouple tree, and the new tree in C-108). Readings will begin April 4, 1994.

(6) Total waste in Kgal taken from Table E-5, Inventory and Status by Tanks for SSTs. Kgal/inches calculations for the temperature tables are as follows: (waste in inches is an approximation only for these temperature tables)

$$\frac{\text{Kgal waste} - 12.5\ \text{Kgal waste}^*}{2.75\ \text{Kgal/inch}} + 12\ \text{inches}^*$$

* The bottom 12 inches in dish bottom tanks contain 12.5 Kgal. All tanks are calculated as dish bottom tanks for the temperature tables, although A and AX farms have flat bottoms. Inches are from centerline tank bottom.

TABLE A-3. TANKS WITH POTENTIAL FOR HYDROGEN OR FLAMMABLE GAS ACCUMULATION ABOVE THE FLAMMABILITY LIMIT (Watch List Tanks)

These tanks have an Unreviewed Safety Question (USQ) because of the potential consequences of a radiological release resulting from a flammable gas burn, an event not analyzed in the SST Safety Analysis Report.

Temperatures in these tanks did not exceed the applicable maximum temperature criteria for the month of March 1994.
All Watch List tanks are reviewed for increasing temperature trends. Temperatures are taken in the waste unless indicated otherwise.

Tank No.	Riser No.		Highest Temperature Reading (F.) in Waste	Date of Reading	Total Waste (3) (inches)	Monitoring Frequency	Assumed Leaked Date	Interim Stabilized Date
A-101	R-12		156	03/23/94	354	Weekly	SOUND	N/A
AX-101	R-9b		139	03/23/94	279	Weekly	SOUND	N/A
AX-103	R-13c		113	03/23/94	48	Weekly	SOUND	8/87
S-102 (2)	R-3		107	03/14/94	207	Weekly	SOUND	N/A
S-111	R-4		92	03/14/94	224	Weekly	SOUND	N/A
S-112	R-4		85	03/07/94	239	Weekly	SOUND	N/A
SX-101 (5)	R-15		138	03/09/94	173	Weekly	SOUND	N/A
SX-102	R-16		152	03/09/94	205	Weekly	1993	N/A
SX-103	R-2		175	03/14/94	245	Weekly	SOUND	N/A
SX-104	R-2		168	03/09/94	231	Weekly	1988	N/A
SX-105	R-2		180	03/09/94	256	Weekly	SOUND	N/A
SX-106 (2)	R-16		110	03/09/94	203	Weekly	SOUND	N/A
SX-109 (1)	R-10		147	03/14/94	98	Weekly	1965	5/81
SX-109 (1)	R-19		151	03/07/94	98	Weekly	1965	5/81
T-110	R-8		61	03/28/94	145	Weekly	SOUND	N/A
U-103	R-1		86	03/21/94	178	Weekly	SOUND	N/A
U-105	R-1		88	03/21/94	159	Weekly	SOUND	N/A
U-107 (2)(5)	R-1		77	03/21/94	155	Weekly	SOUND	N/A
U-108	R-1		90	03/21/94	178	Weekly	SOUND	N/A
U-109	R-1		92	03/08/94	176	Weekly	SOUND	N/A
AN-103		Double-shell tank	118	03/30/94		Weekly	SOUND	N/A
AN-104		Double-shell tank	120	03/23/94		Weekly	SOUND	N/A
AN-105		Double-shell tank	116	03/07/94		Weekly	SOUND	N/A
AW-101 (4)		Double-shell tank	104	03/07/94		Weekly	SOUND	N/A
SY-101	Riser 17b	Double-shell tank	118	03/27/94		Daily	SOUND	N/A
SY-101	Riser 17c	Double-shell tank	118	03/21/94		Daily	SOUND	N/A
SY-103		Double-shell tank	96	03/14/94		Weekly	SOUND	N/A
25 Tanks							Legend: N/A = Not Applicable	

(1) Tank SX-109 has the potential for flammable gas accumulation only because other SX tanks vent through it.
(2) Tanks S-102, SX-106, and U-107 are also on the Organics Watch List.
(3) See footnote (6) in Table A-2 (Ferrocyanide Tanks) for Total Waste/Inches calculations. Waste in inches is an approximation for temperature tables only.
(4) Tank AW-101 was added to this list per letter 9354700, J. C. Fulton, WHC, To R. E. Gerton, DOE-RL, "Addition of Tank 241-AW-101 to Flammable Gas Watch List," dated June 3, 1993.
(5) Tank U-107 was added to this list per Unusual Occurrence Report RL-WHC-TANKFARM-0115, issued December 1993, because of an increase in slurry growth.

TABLE A-4. SINGLE-SHELL TANKS CONTAINING CONCENTRATIONS OF ORGANIC SALTS >3 WEIGHT % TOTAL ORGANIC CARBON (TOC) (Watch List Tanks) (Sheet 1 of 2)

These tanks have organic chemicals which are potentially flammable and mixtures of organic materials mixed with nitrate and nitrate salts can deflagrate. They are listed here because of their "potential for release of high level waste because of uncontrolled increases in the temperature or pressure." Double-Shell tanks have >3 Weight % TOC and are not on the Watch List because they contain mostly liquid and there is no credible organic safety concern for tanks which contain mostly liquid. The safety concern is with tanks that primarily contain solids because they could dry out and heat up, and "high organic concentrations in the tanks could support an exothermic reaction at elevated temperatures (350 degrees F/180 degrees C)." These tanks (with the exception of C-103), do not have an associated USQ because the presence of organic material was reviewed in the SST Safety Analysis Report.

Temperatures in these tanks did not exceed the applicable maximum temperature criteria for the month of March 1994. These tanks are monitored weekly. All Watch List tanks are reviewed for increasing temperature trends.

Temperatures are taken in the waste unless indicated otherwise.

Tank No.	Temperature Reading (F.) in waste	Date of Reading	Total Waste Inches (4)	Assumed Leaked Date	Interim Stabilized Date	Source of Waste	Organic Content (wt.%) (6)	NaNO 3 and NaNO 2 (wt.%)(6)	TOC (WT.%) (7)	Waste Surface Potentially Dry (8)	Last Date Sampled
B-103	61	03/07/94	29	1978	2/85	First and second cycle waste from B Plant and in-tank solidification (ITS-1 & ITS-2) evaporator bottoms (11)	11.4 (9)	60.5 (9)	3.3	x	9/75
C-103 (3)	117	03/08/94	78	SOUND	N/A	PUREX and insoluble strontium-rich sluicing solids from the operation of 244-CR Vault (11)	-	-	-		9/90
S-102 (1)	107	03/14/94	207	SOUND	N/A	REDOX (11)	21.0 (10)	41.0 (10)	6.1	x	2/80
SX-106 (1)	110	03/09/94	203	SOUND	N/A	Salt waste and first cycle condensate from REDOX, and 242-S Evaporator bottoms (11)	14.6 (9)	80.9 (9)	4.3		8/79
T-111 (12)	61	03/07/94	232	1984 Assumed Re-leaker 1994	N/A	Second cycle waste, 224 waste, Decontamination & Decommissioning operatings at T-Plant (13)	14.0 (14)	NO 3, 4.1 wet, NO 2, 0.08 (15)	4.1	x	3/94 (16)
TX-105	97	03/07/94	228	1977	9/83	) Tributyl phosphate (TBP)	12.8 (9)	52.7 (9)	3.7	x	1/81
TX-118 (2)	76	03/31/94	134	SOUND	4/83	) process waste and 242-T	20.2 (10)	50.4 (10)	5.9	x	9/81
U-106	79	03/21/94	90	SOUND	N/A	) Evaporator bottoms (11)	46.6 (10)	52.4 (10)	13.6		6/77
U-107 (1)	77	03/21/94	155	SOUND	N/A	)	14.7 (9)	75.4 (9)	4.3		12/74
U-111 (5)	78	03/21/94	127	SOUND	N/A	Concentrated B Plant Waste (11)	48.2 (10)	—(10)	14.1	x	7/93
10 Tanks											

See Footnotes next page

TABLE A-4. SINGLE-SHELL TANKS CONTAINING CONCENTRATIONS OF ORGANIC SALTS >3 WEIGHT % TOTAL ORGANIC CARBON (TOC) (Sheet 2 of 2)

Footnotes:

(1) These tanks also have the potential for hydrogen or flammable gas accumulation.

(2) Tank TX-118 also contains ferrocyanide.

(3) Tank C-103 was declared a USQ because of an organic layer covering the surface, reference Unusual Occurrence Report RL-WHC-TANKFARM-1992-0069, issued September 1992.

(4) See footnote (6) in Table A-2 (Ferrocyanide Temperature Table) for Total Waste/Inches calculations. Waste inches calculations are approximations only for temperature tables.

(5) Tank U-111 was added August 31, 1993. See August 1993 Summary Highlights for information and Table A-1. "Watch List Tanks" for applicable reference.

(6) WHC, 1990, "The Kyshtym Explosion and Explosion Hazards with Nitrate-Nitrite Bearing Wastes with Acetates and Other Organic Salts," WHC-SD-LB-033, Westinghouse Hanford Company, Richland, Washington

(7) Dry wt.% basis. Calculated as wt.% sodium acetate equivalent X.2928.

(8) Due to absence of supernatant liquid.

(9) Calculated from data developed by Track Radioactive Components (TRAC) computer code, 1984.

(10) "Removal of Radionuclides from Hanford Defense Waste Solutions," RHO-SA-51, 1980, Rockwell Hanford Operations, Richland, Washington. All or part of liquid from which composition data were derived may have been transferred to double-shell tanks.

(11) WHC, 1993, "Action Plan for Responses to Abnormal Conditions in Hanford Site Radioactive Waste Tanks with High Organic Content," WHC-EP-0461, Rev. 1, Westinghouse Hanford, Richland, Washington.

(12) Tank 241-T-111 was added to the Organic Salts Watch List on February 28, 1994, upon recommendation by WHC Waste Tank Safety Program.

(13) WHC, 1990, "A History of the 200 Area Tank Farms," WHC-MR-0132, Westinghouse Hanford, Richland, Washington.

(14) Pacific Northwest Laboratories analysis on Core 33, Segment 2, dated January 14, 1994.

(15) WHC, 1993, "Single-Shell Tank Characterization, Tank T-111, Cores 31 and 33," WHC-SM-PD-024, Rev 0A, Westinghouse Hanford, Richland, Washington.

(16) Data not yet available.

TABLE A-5. SINGLE-SHELL TANKS WITH HIGH HEAT LOADS (>40,000 Btu/h)(Sheet 1 of 2)

High heat load tanks have temperature surveillance requirements established by SD-WM-SAR-006 REV 1, "SST Isolation Safety Analysis Report," dated January 1986, and OSD-T-151-00013 REV D-O, "Operating Specifications for Single-Shell Waste Storage Tanks," dated August 1990. While all of these tanks are considered high heat load tanks per SAR definition, only one (241-C-106) is on the High Heat Watch List.

Temperatures in these tanks did not exceed SAR or OSD requirement limits for the month of March 1994. All high heat load tanks are on active ventilation unless indicated otherwise in the footnotes. These high heat tanks are reviewed for increasing temperature trends.

Temperatures are taken in the waste unless indicated otherwise.

Tank No.	Riser No. (6)	Temperature Reading (F.) in Waste	Date of Reading	Total Waste Inches (7)	Monitoring Frequency	Estimated Heat Load (1) (Btu/h)	Estimated Heat Load (1) (kW)	Date Declared Assumed Leaker	Interim Stabilized Date
A-104 (4)	R-18	192	03/23/94	18	Weekly	50000	15	1975	9/78
A-105 (4)	R-16	151	03/28/94	14	Weekly	50000	15	1963	7/79
C-106 (2)(3)	R-8	149	03/14/94	91	Weekly	110000	32	SOUND	N/A
C-106 (2)(3)	R-14	121	03/14/94	91	Weekly	110000	32	SOUND	N/A
SX-107	R-10	171	03/07/94	45	Monthly	42000	12	1964	10/79
SX-107	R-14	171	03/07/94	45	Monthly	42000	12	1964	10/79
SX-108	R-10	195	03/07/94	49	Monthly	45000	13	1962	8/79
SX-108	R-19	200	03/07/94	49	Monthly	45000	13	1962	8/79
SX-109 (3)	R-10	147	03/14/94	98	Weekly	50000	15	1965	5/81
SX-109 (3)	R-19	151	03/07/94	98	Weekly	50000	15	1965	5/81
SX-110	R-12	173	03/01/94	30	Monthly	42000	12	1976	8/79
SX-110	R-20	169	03/07/94	30	Monthly	42000	12	1976	8/79
SX-111	R-10	193	03/07/94	53	Monthly	44000	13	1974	7/79
SX-111	R-19	165	03/01/94	53	Monthly	44000	13	1974	7/79
SX-112	R-10	152	03/07/94	41	Monthly	43000	13	1969	7/79
SX-112	R-19	159	03/01/94	41	Monthly	43000	13	1969	7/79
SX-114	R-10	189	03/07/94	73	Monthly	58000	17	1972	7/79
SX-114	R-19	187	03/07/94	73	Monthly	58000	17	1972	7/79
10 Tanks								Legend: Tree = Thermocouple Tree	
A-105 Laterals (5)		248	03/16/94		Weekly				

Temperatures are taken in 34 thermocouples located in the laterals beneath A-105. SAR requirements (see top of table) do not apply to these temperatures; however, Westinghouse Hanford has voluntarily chosen to apply the waste temperature limits to the soil temperature for surveillance reporting.

Footnotes – see next page

TABLE A-5. SINGLE-SHELL TANKS WITH HIGH HEAT LOADS (>40,000 Btu/h)(Sheet 2 of 2)

Footnotes:

(1) High heat loads as of 1988, evaluation completed April 20, 1989 (kW = 3412 Btu/h). The predominant heat load for these tanks is from CS 137 (half life of 30 years) and SR 90 (half life of 28.1 years). Tank C-105 was re-evaluated in WHC-SD-WM-ER-189, "Thermal Analysis of Tank 241-C-105 in Support of Process Test," January 1993. Engineering Change Notice #196834, June 24, 1993, changed the status of C-105 from High Heat Load to Normal, effective July 1, 1993. Tank C-106 was re-evaluated using a revised thermal history based on the thermal transient behavior during the ventilation outage in 1992. WHC-SD-WM-ER-200 "Revised Thermal History of Tank 241-C-106," issued December 20, 1993, documents the new heat load estimate of 110,000 Btu/hr (+/-20,000 Btu/h) for this tank.

(2) Periodic water additions are required in C-106 to maintain evaporative cooling and thus prevent overheating. This tank is scheduled for partial retrieval starting in 1997, at which time cooling water additions will be discontinued. Temperatures in riser 8 are consistent at mid-150 degrees, however, temperatures in riser 14 vary between approximately 120 and 135, also consistently. Starting March 7, 1994, C-106 is undergoing a liquid-reduction process test to determine a new low level for future water addition. The process test is expected to be completed in FY-94. Cooling water is not added during the test. C-Farm thermocouple trees were connected to the Tank Monitor and Control System (TMACS) and are expected to be operational on April 4, 1994.

(3) Watch List Tanks: C-106 is on the Watch List because "without water additions (in the event of a leak) the tank could exceed structural temperature limits resulting in unacceptable structural damage." SX-109 is on the hydrogen Watch List because it has the potential for flammable gas accumulation due to other SX tanks venting through it.

(4) A-104/105/106 exhauster has been out of service from October 1, 1991, until August 20, 1992, when it was briefly restarted. Problems exist which must be resolved before the exhauster is operational. Temperatures in A-104 and A-105 are monitored weekly.

(5) Maximum lateral temperatures under A-105 increased 20 degrees F. by January 1992, but then dropped a few degrees and have remained fairly stable at current temperature. These temperatures are monitored weekly.

(6) Tanks A-104 and A-105
Two temperature probes are installed in risers in A-104, and six are installed in risers in A-105. These are individual probes. In A-104, the probes are in contact with the sludge; in A-105, they are in contact with the bottom of the tank (A-105 has a bulged bottom).

Tank C-106
Tank C-106 has six functioning thermocouples (#1 through 6) on riser 8, and 12 functioning thermocouples on riser 14.

Tanks SX-107, 108, 109, 110, 111, 112, and 114
Each of these tanks has eight thermocouple trees, with eight thermocouples on each tree, with the exception of SX-108, which has four operational thermocouples on each of two trees. Two trees are monitored in each of these SX tanks..

(7) Calculations for Total Waste Inches: see footnote (6), Table A-2 (Ferrocyanide Tanks). Waste in inches is an approximation only for temperature tables.

(8) There are 19 single-shell tanks with active ventilation (eight are on the Watch List as indicated by an asterisk):

A-104	SX-101 *	SX-107
A-105	SX-102 *	SX-108
A-106	SX-103 *	SX-109 *
C-104	SX-104 *	SX-110
C-105	SX-105 *	SX-111
C-106 *	SX-106 *	SX-112
		SX-114

TABLE A-6. NON-WATCH LIST LOW HEAT LOAD TANKS (<40,000 Btu/h)

(Page 1 of 3)

Temperatures are taken semiannually in January and July, unless otherwise indicated, in the following 95 single-shell tanks. Legend follows table.

	Tank No.	Highest Temperatures taken in waste Jul. 93	Jan. 94	Total Waste (1) Kgal	Inches	Comments
1	A-102	92	87	41	15	
2	A-103	117	114	370	135	
3	A-106	137	135	125	50	
4	AX-102	76	71	39	10	Only TC#5 working, reading in vapor space
						Control box contaminated inside
5	AX-104	98	92	7	3	
6	B-101	108	109	113	48	
7	B-102	63	63	32	19	TC#1 O/S, reading in vapor space
8	B-104	66	65	371	142	
9	B-105	66	65	306	50	
10	B-106	62	63	117	67	TC#1 & 2 O/S
11	B-107	62	60	165	41	TC#1 thru 3 O/S, reading in vapor space
12	B-108	62	64	94	54	
13	B-109	61	63	127	97	
14	B-110	68	63	246	94	TC#1 thru 4 O/S. Reading in vapor space
15	B-111	86	86	237	19	TC#1 & 2 O/S, work order issued, historical readings erratic
16	B-112	63	64	33	7	
17	B-201	60	60	29	151	
18	B-202	61	60	27	141	
19	B-203	62	61	51	263	
20	B-204	62	61	50	258	
21	BX-101	O/S	O/S	43	27	All TCs O/S, work order issued, last reading 74 F. in 11/92
22	BX-103	O/S	O/S	66	31	All TCs O/S, last reading 77 F. in 10/92
23	BX-104	O/S	O/S	99	43	(2) No TC tree per Riser Configuration document
						Last reading 87 F. in 10/80
24	BX-105	63	66	51	26	
25	BX-107	O/S	O/S	345	133	All TCs O/S, work order issued, last reading 69 F. in 10/82
26	BX-108	63	65	26	17	
27	BX-109	77	O/S	193	78	Temp reading obtained 7/93 only, 2 attempts made 1/94
						No historical readings available
28	BX-110	68	74	199	80	Readings taken weekly, pumping began, now on hold
29	BX-111	65	69	211	84	Readings taken weekly, tank being pumped
30	BX-112	62	65	165	67	
31	BY-101	75	75	387	148	Continuous readings taken on TMACS
32	BY-102	O/S	O/S	341	131	(2) No TC tree per Riser Configuration document.
						Last reading 72 F. in 4/79
33	BY-109	O/S	O/S	423	161	(2) No TC tree per Riser Configuration document.

9413279.0038

TABLE A-6. NON-WATCH LIST LOW HEAT LOAD TANKS (<40,000 Btu/h)

(Page 2 of 3)

Temperatures are taken semiannually in January and July, unless otherwise indicated, in the following 95 single-shell tanks. Legend follows table.

	Tank No.	Highest Temperatures taken in waste Jul. 93	Jan. 94	Total Waste (1) Kgal	Inches	Comments
34	C-101 (3)	88	86	88	39	
35	C-102 (3)	O/S	O/S	423	161	Broken coupling, work order issued, last reading 96 F. in 11/92
36	C-104 (3)	87	85	295	115	TC#1 thru 5 O/S, reading in vapor space
37	C-105 (3)	92	80	150	63	Monitored weekly, formerly on High Heat Load list
38	C-107 (3)	125	124	275	107	Monthly reading requirement per procedure, monitored weekly
39	C-110 (3)	65	66	187	75	TC#1 thru 4 O/S, reading in vapor space
40	C-201 (3)	61	56	2	13	
41	C-202 (3)	61	60	1	8	
42	C-203 (3)	60	59	5	29	
43	C-204	O/S	O/S	3	18	In-tank photos revealed no tree. Last reading obtained prior '91.
44	S-101	115	118	427	162	TC#1, 3, 5, & 6 O/S, work order issued
45	S-103	85	87	248	98	
46	S-104	104	108	294	114	
47	S-105	73	78	456	173	
48	S-106	78	81	543	205	
49	S-107	107	110	368	129	
50	S-108	85	89	604	227	
51	S-109	O/S	68	568	214	Readings available on TC#7 only
52	S-110	116	117	390	149	
53	SX-113	73	77	26	15	
54	SX-115	O/S	O/S	12	10	(2) No TC tree, per Riser Configuration document, last reading prior to 12/91
55	T-101	66	72	102	45	Formerly on ferrocyanide Watch List
56	T-102	O/S	O/S	32	19	(2) No TC tree per Riser Configuration document, last reading 68 F. in 2/81
57	T-103	59	62	27	17	
58	T-104	O/S	62	445	169	All TCs O/S, work order issued
59	T-105	O/S	O/S	98	43	(2) No TC tree per Riser Configuration document
60	T-106	59	60	21	15	
61	T-108	O/S	57	180	73	
62	T-109	O/S	O/S	58	29	All TCs O/S, work order issued, last reading 75 F. in 2/91
63	T-112	58	60	67	32	
64	T-201	59	60	29	150	
65	T-202	58	62	21	110	
66	T-203	75	64	35	182	
67	T-204	60	63	38	197	
68	TX-101	O/S	O/S	87	39	(2) No TC tree per Riser Configuration document
69	TX-102	O/S	O/S	113	49	Cable cut from tree

9413279.0039

TABLE A-6. NON-WATCH LIST LOW HEAT LOAD TANKS (<40,000 Btu/h)

(Page 3 of 3)

Temperatures are taken semiannually in January and July, unless otherwise indicated, in the following 95 single-shell tanks. Legend follows table.

	Tank No.	Highest Temperatures taken in waste Jul. 93	Jan. 94	Total Waste (1) Kgal	Inches	Comments
70	TX-103	55	71	157	54	Cable cut from tree, readings taken by Instrument Technician
						High reading taken 1/93 was 71 F.
71	TX-104	60	65	65	31	Cable cut from tree, readings taken by Instrument Technician
72	TX-106	59	78	453	172	Cable cut from tree, readings taken by Instrument Technician
73	TX-107	60	66	36	21	Cable cut from tree, readings taken by Instrument Technician
74	TX-108	61	68	134	56	Cable cut from tree, readings taken by Instrument Technician
75	TX-109	64	94	384	147	Cable cut from tree, readings taken by Instrument Technician
						High reading taken 1/93 was 97 F.
76	TX-110	O/S	O/S	462	175	Cable cut from tree, readings taken by Instrument Technician
77	TX-111	61	79	370	142	Cable cut from tree, readings taken by Instrument Technician
						High reading taken 1/93 was 73 F.
78	TX-112	72	67	649	243	Cable cut from tree, readings taken by Instrument Technician
79	TX-113	65	72	607	228	Dial pushed inside housing, readings taken by Instr. Tech.
80	TX-114	O/S	O/S	535	202	Cable cut from TC tree
81	TX-115	67	70	640	240	Dial pushed inside housing, readings taken by Instr. Tech.
82	TX-116	O/S	O/S	631	237	(2) Tree cut off in riser per Riser Configuration document
83	TX-117	O/S	O/S	626	235	All TCs O/S, cable cut from tree
84	TY-102	O/S	60	64	31	
85	TY-105	77	79	231	91	
86	TY-106	60	59	17	14	
87	U-101	61	67	25	17	
88	U-102	81	85	374	143	
89	U-104	O/S	O/S	122	52	(2) No TC tree per Riser Configuration document
90	U-110	72	76	186	75	
91	U-112	61	63	49	25	
92	U-201	O/S	61	5	29	
93	U-202	59	61	5	29	
94	U-203	O/S	60	3	18	
95	U-204	80	65	3	18	Selector knob not working 1/93, 7/93 readings suspect

(1) See Table A-2 (footnote 6) for waste gallons/inches calculations.

(2) Thermocouples in nine tanks (BX-104, BY-102, BY-109, SX-115, T-102, T-105, TX-101, TX-116, and U-104) are out of service due to no TC trees in these tanks, or the thermocouples have been cut off, covered over, or are otherwise unable to function, per the Riser Configuration document. (Also see comment section above)

(3) All TC trees in C-Farm connected to TMACS on 3/31/94, except for C-204 which has no tree. Scheduled to be operational 4/4/94.

LEGEND:

TC - Thermocouple
TMACS - Tank Monitor & Control System
O/S - Out of service
Riser Configuration document - WHC-SD-RE-TI-053, REV 8, "Riser Configuration Document for Single-Shell Tanks," dated September 1991

SUMMARY:

	Jul. 93	Jan. 94	Feb. 94	
Readings obtained in SSTs	71	76	75	T-111 was deleted from this list and added to the Organics Watch List on February 28, 1994
No readings (TC trees O/S - includes nine tanks with no trees - see footnote above)	25	20	20	
Total low heat load tanks	96	96	95	

9413279.0040

TABLE A-7. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS

149 TANKS (Sheet 1 of 5)

The following table indicates whether Single-Shell tank monitoring was in compliance with the requirements as specified in the applicable documents as of the last day of the applicable month:

NOTE:
All Watch List and High Heat tank temperature monitoring is in compliance. (5)
All Dome Elevation Survey monitoring is in compliance.
All Drywell monitoring is in compliance.
Psychrometrics (2)
In-tank Photographs (3)
Pressure Monitoring (6)
CAM/RAMP Monitoring (7)
Vapor Monitoring (8)

LEGEND:

(Shaded)	= in compliance with all applicable documentation
O/C	= out of compliance with documentation
-357	= WHC-SD-WM-TI-357, "Waste Storage Tank Status and Leak Detection Criteria"
POP	= Plant Operation Procedure TO-040-650, "Obtain/Record SST Temperatures"
M.T.	= Manual Tape
FIC	= Food Instrument Corporation
OSR/SAR	= Operations Safety Requirements/Safety Analysis Report, SD-WM-SAR-006, Rev 2, 2/86; -SAR-034, Rev 0, 6/81
OSD	= Operating Specifications Doc., OSD-T-151-00013, Rev D-0, 8/90
N/A	= Not applicable (i.e., no LOW, M.T., FIC installed)
O/S	= Out of Service
Neutron	= LOW readings taken by Neutron probe

Information as of March 31, 1994

Tank Number	Category		Temperature Readings (5)(6)	Surface Level Readings (1) (-357)		LOW Readings (-357) (9)	Radiation Readings		Dome Elevation Surveys (OSR/SAR)
	Watch List(6)	High Heat		M.T.	FIC	Neutron	Lateral Readings (-357)	Drywell Readings (OSR/SAR)	
A-101	X				N/A				
A-102				N/A		N/A			
A-103				N/A					
A-104		X		O/C	N/A	N/A			
A-105		X			N/A	N/A			
A-106				N/A		N/A			
AX-101	X			N/A					
AX-102					N/A	N/A			
AX-103	X			N/A		N/A			
AX-104					N/A	N/A			
B-101				N/A		N/A			
B-102				N/A		N/A			
B-103	X			N/A		N/A			
B-104					N/A				
B-105					N/A				
B-106				N/A		N/A			
B-107					N/A	N/A			
B-108				N/A		N/A			
B-109					N/A	N/A			
B-110					N/A	N/A			
B-111				N/A		N/A			
B-112				N/A		N/A			
B-201					N/A	N/A			
B-202					N/A	N/A			
B-203					N/A	N/A			
B-204					N/A	N/A			
BX-101			O/C		N/A	N/A			
BX-102	X				N/A	N/A			
BX-103			O/C	N/A		N/A			
BX-104			O/S-O/C	N/A		N/A			
BX-105				N/A		N/A			
BX-106	X			N/A		N/A			
BX-107			O/C	N/A	O/C	N/A			

TABLE A-7. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS

149 TANKS (Sheet 2 of 5)

Information as of March 31, 1994

Tank Number	Category		Temperature Readings (5)(6)	Surface Level Readings (1) (-357)		LOW Readings (-357) (9)	Radiation Readings		Dome Elevation Surveys (OSR/SAR)
	Watch List(6)	High Heat		M.T.	FIC	Neutron	Lateral Readings (-357)	Drywell Readings (OSR/SAR)	
BX-108					N/A	N/A	N/A		
BX-109			O/C	N/A		N/A	N/A		
BX-110 (4)					N/A	N/A	N/A		
BX-111 (4)					N/A		N/A		
BX-112				N/A		N/A	N/A		
BY-101 (4)				O/C	N/A		N/A		
BY-102			O/S-O/C		N/A		N/A		
BY-103	X				N/A		N/A		
BY-104	X				N/A		N/A		
BY-105	X				N/A		N/A		
BY-106	X				N/A		N/A		
BY-107	X				N/A		N/A		
BY-108	X				N/A	N/A	N/A		
BY-109			O/S-O/C	N/A			N/A		
BY-110	X				N/A		N/A		
BY-111	X				N/A		N/A		
BY-112	X				N/A	O/C	N/A		
C-101					N/A	N/A	N/A		
C-102			O/C	N/A		N/A	N/A	N/A	
C-103	X			N/A		N/A	N/A		
C-104				N/A		N/A	N/A		
C-105				N/A		N/A	N/A		
C-106 (4)	X	X		N/A		N/A	N/A		
C-107				N/A		N/A	N/A		
C-108	X			O/C (10)	N/A	N/A	N/A		
C-109	X				N/A	N/A	N/A		
C-110					N/A	N/A	N/A		
C-111	X				N/A	N/A	N/A		
C-112	X				N/A	N/A	N/A		
C-201					N/A	N/A	N/A		
C-202					N/A	N/A	N/A		
C-203					N/A	N/A	N/A		
C-204			O/C		N/A	N/A	N/A		
S-101				N/A			N/A		
S-102	X			N/A			N/A		
S-103				N/A			N/A		
S-104					N/A	N/A	N/A		
S-105				N/A			N/A		
S-106				N/A			N/A		
S-107				N/A		N/A	N/A		
S-108							N/A		
S-109				N/A			N/A		
S-110				N/A			N/A		
S-111	X			N/A			N/A		
S-112	X			N/A			N/A		
SX-101	X			N/A			N/A		
SX-102	X			N/A			N/A		
SX-103	X			N/A			N/A		
SX-104	X			N/A		O/S-O/C	N/A		
SX-105	X			N/A			O/C		
SX-106	X			N/A			N/A		
SX-107		X			N/A	N/A	O/C		
SX-108		X			N/A	N/A	O/C		

9413279.0042

TABLE A-7. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS

149 TANKS (Sheet 3 of 5)

Information as of March 31, 1994

Tank Number	Category: Watch List(6)	Category: High Heat	Temperature Readings (5)(6)	Surface Level Readings (1) (-357): M.T.	Surface Level Readings (1) (-357): FIC	LOW Readings (-357) (9): Neutron	Radiation Readings: Lateral Readings (-357)	Radiation Readings: Drywell Readings (OSR/SAR)	Dome Elevation Surveys (OSR/SAR)
SX-109 (4)	X	X			N/A	N/A	O/C		
SX-110		X			N/A	N/A	O/C		
SX-111		X			N/A	N/A	O/C		
SX-112		X			N/A	N/A	O/C		
SX-113					N/A	N/A	N/A		
SX-114		X			N/A	N/A	O/C		
SX-115			O/S - O/C		N/A	N/A	O/C		
T-101 (4)						N/A	N/A		
T-102				N/A	O/C	N/A	N/A		
T-103				N/A		N/A	N/A		
T-104			O/C		N/A		N/A		
T-105			O/S - O/C	N/A		N/A	N/A		
T-106				N/A		N/A	N/A		
T-107	X			N/A		N/A	N/A		
T-108					N/A	N/A	N/A		
T-109			O/C	N/A		N/A	N/A		
T-110	X			N/A			N/A		
T-111	X			N/A			N/A		
T-112				N/A		N/A	N/A		
T-201					N/A	N/A	N/A		
T-202					N/A	N/A	N/A		
T-203					N/A	N/A	N/A		
T-204					N/A	N/A	N/A		
TX-101			O/S - O/C	N/A		N/A	N/A		
TX-102			O/C		N/A		N/A		
TX-103				N/A		N/A	N/A		
TX-104				N/A		N/A	N/A		
TX-105	X				N/A	O/S-O/C	N/A		
TX-106					N/A		N/A		
TX-107				N/A		N/A	N/A		
TX-108				N/A			N/A		
TX-109				N/A			N/A		
TX-110			O/C		N/A		N/A		
TX-111					N/A		N/A		
TX-112					N/A		N/A		
TX-113					N/A		N/A		
TX-114			O/C		N/A		N/A		
TX-115					N/A		N/A		
TX-116			O/S O/C		N/A	N/A	N/A		
TX-117			O/C		N/A		N/A		
TX-118	X			N/A			N/A		
TY-101	X			N/A		N/A	N/A		
TY-102				N/A		N/A	N/A		
TY-103	X			N/A			N/A		
TY-104	X			N/A		N/A	N/A		
TY-105					N/A	N/A	N/A		
TY-106					N/A	N/A	N/A		
U-101					N/A	N/A	N/A		
U-102				N/A			N/A		
U-103	X			N/A			N/A		
U-104			O/S - O/C		N/A	N/A	N/A		
U-105	X			N/A			N/A		
U-106	X			N/A			N/A		

9413279.0043

TABLE A-7. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS

149 TANKS (Sheet 4 of 5)

Information as of March 31, 1994

Tank Number	Category: Watch List(6)	Category: High Heat	Temperature Readings (5)(6)	Surface Level Readings (1) (-357): M.T.	Surface Level Readings (1) (-357): FIC	LOW Readings (-357) (9): Neutron	Radiation Readings: Lateral Readings (-357)	Radiation Readings: Drywell Readings (OSR/SAR)	Dome Elevation Surveys (OSR/SAR)
U-107	X			N/A			N/A		
U-108	X			N/A			N/A		
U-109	X			N/A			N/A		
U-110				N/A		N/A	N/A		
U-111	X			N/A			N/A		
U-112					N/A	N/A	N/A		
U-201					N/A	N/A	N/A		
U-202					N/A	N/A	N/A		
U-203					N/A	N/A	N/A		
U-204					N/A	N/A	N/A		
Catch Tanks and Special Surveillance Facilities									
A-302-A	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
A-302-B	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
311-ER	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
152-AX	N/A	N/A	N/A		N/A				
151-AZ	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
154-AZ	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
BX-TK/SMP	N/A	N/A	N/A		N/A				
A-TK/SMP	N/A	N/A	N/A		N/A				
204-AR	N/A	N/A	N/A						
417-A	N/A	N/A	N/A						
Vent Sta.	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
S-302	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
S-302-A	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
S-304	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
TX-302-B	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
TX-302-C	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
U-301-B	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
UX-302-A	N/A	N/A	N/A	N/A		N/A	N/A	N/A	N/A
141-S	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
142-S	N/A	N/A	N/A		N/A	N/A	N/A	N/A	N/A
Totals: 149 tanks	46 Watch List Tanks (4)	10 High Heat Tanks (4)	O/C: 20 tanks – (semiannual monitoring frequency) (5)	O/C: 3 tanks 0 catch tank	O/C: 2 tanks 0 catch tank	O/C: 3 tanks; 58 tanks have LOWs (2 are O/S)	O/C: 9 tanks	0	0

See Footnotes on next page

9413279.0044

TABLE A-7. SINGLE-SHELL TANKS MONITORING COMPLIANCE STATUS
149 TANKS (Sheet 5 of 5)

Footnotes:

1. All SSTs have either manual tape or FIC, with the exception of S-108 and T-101, which have both. Tank 101-T also has a zip cord. All SST FICs are connected to CASS, with the exception of BX-106; however, the connection for many tanks is broken. For such cases, manual readings are taken. Manual surface level readings include readings taken by manual tape, manual FIC (not connected to CASS; BX-106), manual readings of automatic FIC (if CASS is printing "0"), or automatic FIC. In some cases, the surface level readings are taken using a zip cord. While less accurate, such readings are acceptable for meeting the surface level reading requirements.

2. High heat tanks have active exhausters; psychrometrics are taken in these tanks (A-104/105, C-105/106 [effective July 1, 1993, C-105 is no longer a high heat load tank], SX-107, 108, 109, 110, 111, 112, and 114). The exhausters on A-104/105 have been down since October 1991; no readings are being taken. Psychrometric readings have not been taken in the SX high heat load tanks since July 1993. The frequency of psychrometric readings in SSTs is determined by the Cognizant Engineers for the applicable tank farms on an "as needed" basis," with the exception of tanks C-105/106. Hanford Federal Facility Agreement and Consent Order," Washington State Department of Ecology, U. S. Environmental Protection Agency, and U. S. Department of Energy," 1992 (Tri-Party Agreement) requires psychrometric readings to be taken in C-105/106 on a monthly frequency. Psychrometric readings were taken in March 1994.

3. In-tank photographs are requested on an "as needed" basis. No in-tank photographs were taken between September 1990 and March 1993.

4. Two tanks are on both category lists (C-106 and SX-109). In July 1993, C-105 was removed from the High Heat Load list and BX-110, BX-111, BY-101 and T-101 were removed from the ferrocyanide Watch List; these tanks continue to have temperature readings taken weekly although they are only required to be taken semiannually. U-111 was added to the Organic list in August 1993. T-107 was added to the Hydrogen list in December 1993 (this tank was already on the Organics list). T-111 was added to the Organics list in February 1994.

5. Temperature readings may be regulated by OSD, -357, or POP. Additionally, high heat load tanks are regulated by OSR/SAR. Thermocouples in the nine tanks designated O/S-O/C are out of service; there are either no thermocouple trees in these tanks, or trees have been cut off, covered over, or are otherwise unable to function. The OSD does not require readings or repair of out-of service thermocouples for the 95 low heat load (<40,000 Btu/h) tanks. However, the POP requires that attempts are to be made semiannually in January and July to obtain readings for these tanks. Temperatures were taken in January 1994; a total of 20 tanks are O/C because readings could not be obtained.

6. "Safety Measures for Waste Tanks at Hanford Nuclear Reservation, Section 3137 of the National Defense Authorization Act for Fiscal Year 1991," November 5, 1990, Public Law 101-510, (the "Wyden Amendment") requires continuous pressure monitoring and temperature monitoring in Watch List tanks. WHC-EP-0422 REV 1, "A Plan to Implement Remediation of Waste Tank Safety Issues at the Hanford Site," December 1991, addresses these monitoring issues. WHC-EP-0600, "Status Report on Resolution of Waste Tank Safety Issues at the Hanford Site," issued August 1993, describes the resolution strategy for these safety issues.

   All BY-Farm tanks on the ferrocyanide watch list are on the Tank Monitor and Control System (TMACS) which continuously monitors for temperatures. In addition, all of C-Farm was added March 31, 1994, with the exception of C-204, which has no thermocouple tree, and the new tree in C-108. Readings will begin on April 4, 1994.

7. Continuous Air Monitoring (CAM) compliance and Radiation Area Monitoring Panel (RAMP) compliance are not addressed in this table.

8. Double-shell tank farm SY has the only tanks with continuous vapor/flammable gas monitoring; not addressed in this table.

9. An Engineering Change Notice was issued November 1993, changing the monitoring frequency of LOW readings by Gamma probe to be taken "by request only." The Gamma probe column has therefore been deleted.

10. Surface level measurement monitoring is out of compliance in C-108 because the manual tape was removed to install a thermocouple tree. This tank does not have an FIC. A work package is pending to re-install the manual tape.

9413279.0045

TABLE A-8. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS

28 TANKS (Sheet 1 of 2)

The following table indicates whether Double-Shell tank monitoring was in compliance with the requirements as specified in the applicable documents as of the last day of the applicable month:

NOTE:

Dome Elevation Surveys are not required for DSTs.
Psychrometrics (2)
In-tank Photographs (3)
Pressure Monitoring (6)
CAM/RAMP Monitoring (7)
Vapor Monitoring (8)

LEGEND:

(Shaded)	= In compliance with all applicable documentation
O/C	= Out of compliance with documentation
-357	= WHC-SD-WM-TI-357, "Waste Storage Tank Status and Leak Detection Criteria"
M.T.	= Manual Tape
FIC	= Food Instrument Company
OSR/SAR	= Operations Safety Requirements/Safety Analysis Report WHC-SD-WM-SAR-016, Rev 1, 5/86 WHC-SD-HS-SAR-010, Rev 1, 6/93 (Aging Waste)
OSD	= Operations Safety Doc., OSD-T-151-0007, Rev H-5, 1/92
N/A	= Not Applicable (i.e., no M.T., FIC installed)
O/S	= Out of Service
W.F.	= Weight Factor
Rad.	= Radiation

Information as of March 31, 1994

Tank Number	Watch List	Temperature Readings (4) (OSD)	Surface Level Readings (1) (-357, OSR/SAR)		Radiation Readings: Leak Detection Pits (5) (-357, OSR/SAR)		Radiation Readings: Annulus (-357)
			M.T.	FIC	W.F.	Rad.	
AN-101			N/A				
AN-102			N/A				
AN-103	X		N/A				
AN-104	X		N/A				
AN-105	X		N/A				
AN-106			N/A				
AN-107			N/A				
AP-101						O/C	
AP-102				O/S		O/C	
AP-103						O/C	
AP-104			O/S			O/C	
AP-105						O/C	
AP-106						O/C	
AP-107						O/C	
AP-108						O/C	
AW-101	X						
AW-102							
AW-103							
AW-104							
AW-105							
AW-106							
AY-101				O/S			O/C
AY-102						O/C	O/C
AZ-101				O/S			
AZ-102						O/C	
SY-101	X						
SY-102							
SY-103	X						
Totals: 28 tanks	6 Watch List Tanks	O/C: 0	O/C: 0	O/C: 0	O/C: 0	O/C: 10 tanks	O/C: 2 tanks

See footnotes next page:

TABLE A-8. DOUBLE-SHELL TANKS MONITORING COMPLIANCE STATUS
28 TANKS (Sheet 2 of 2)

Footnotes:

1. All DSTs have both manual tape and FIC, with the exception of the AN Tank Farm which has only FICs. The manual tape is used when the FIC is out of service. O/C will be shown when no readings are obtained.

2. Psychrometric readings are only taken on tanks with active exhausters; all DSTs have active exhausters. The frequency of psychrometric readings in DSTs is determined by the Cognizant Engineers for the applicable tank farms on an "as needed" basis. Currently, monthly readings are being taken on the SY-101 annulus exhaust, SY-102 tank and annulus exhaust, and SY-103 tank and annulus exhaust. SY-101 tank exhaust readings are not being taken until a port on the tank exhaust header becomes available for exhauster readings. No other psychrometric readings are currently being taken monthly.

3. In-tank photographs are requested on an "as needed" basis. Last in-tank photographs in DSTs were taken in April 1989.

4. OSD specifies DST temperature limits, gradients, etc. Tank SY-101 temperatures are obtained shiftwise with increased readings taken prior to and following gas venting.

5. Failure of both leak detection systems requires repair of at least one system within 5 working days. Failure of one system only, repair must be within 10 workdays per -357 document. If the pair of out-of-service system exceeds these timeframes, all systems are O/C. Out-of-service systems which have not exceeded these timeframes will be shown as O/S.

6. "Safety Measures for Waste Tanks at Hanford Nuclear Reservation, Section 3137 of the National Defense Authorization Act for Fiscal Year 1991," November 5, 1990, Public Law 101-510, (the "Wyden Amendment") requires continuous pressure monitoring and temperature monitoring in Watch List tanks. WHC-EP-0422 REV 1, "A Plan to Implement Remediation of Waste Tank Safety Issues at the Hanford Site," December 1991, addresses these monitoring issues. A status report on resolution of Waste Tank Safety Issues at the Hanford Site has been prepared but has not yet been cleared for public release.

7. Continuous Air Monitoring (CAM) compliance and Radiation Area Monitoring Panel (RAMP) compliance are not addressed in this table.

8. Double-shell tank farm SY has the only tanks with continuous vapor/flammable gas monitoring; not addressed in this table.

TABLE A-9. AUTOMATIC FOOD INSTRUMENT CORPORATION (FIC) GAUGES OUT OF SERVICE

March 31, 1994

Tank No.	SST/DST	Date of Last Automatic FIC Reading	Reading Status	Comments	Required Monitoring Frequency(-357)
BX-107	SST	02/09/94	No reading taken since 02/10/94	Out of compliance as of 02/10/94	Daily
T-102	SST	09/06/93	No reading taken since 09/07/93	Out of compliance as of 09/07/93	Daily
AP-108	DST	02/23/94	Taking manual FIC readings	In compliance	Daily
AW-101	DST	10/23/92	Taking manual FIC readings	In compliance	Daily
AW-103	DST	12/15/93	Taking manual FIC readings	In compliance	Daily
AY-102	DST	01/16/94	Taking manual FIC readings	In compliance	Daily
B-Farm	SST	02/18/94	Taking manual FIC readings	In compliance	Daily/Quarterly
C-107	SST	08/10/93	Taking manual FIC readings	In compliance	Quarterly
SY-101	DST	08/23/91	Taking manual FIC readings	In compliance	Daily
SY-102	DST	03/12/94	Taking manual FIC readings	In compliance	Daily
TX-107	SST	10/22/93	Taking manual FIC readings	In compliance	Quarterly
U-105	SST	11/17/92	Taking manual FIC readings	In compliance	Daily
U-107	SST	02/28/94	Taking manual FIC readings	In compliance	Daily
U-109	SST	03/17/94	Taking manual FIC readings	In compliance	Daily
AP-102	DST	01/27/93	Taking manual tape readings	In compliance	Daily
AY-101	DST	08/31/90	Taking manual tape readings	In compliance	Daily
AZ-101	DST	02/02/90	Taking manual tape readings	In compliance	Daily
Catch Tanks					
A-302-A		04/16/91	Taking manual reading	In compliance	Daily
AZ-151		07/29/93	Taking Manual FIC reading	In compliance	Daily
TX-302-C		10/22/93	Taking Manual FIC reading	In compliance	Daily

Frequency reading requirements:
Daily - Must be taken by 2 pm each day
Weekly - Must be taken by 2 pm each Monday
Quarterly - Must be taken by 2 pm on the seventh day of each quarter

LEGEND
SST = Single-Shell Tank
DST = Double-Shell Tank
-357 = WHC-SD-WM-TI-357, Waste Storage Tank Status and Leak Detection Criteria

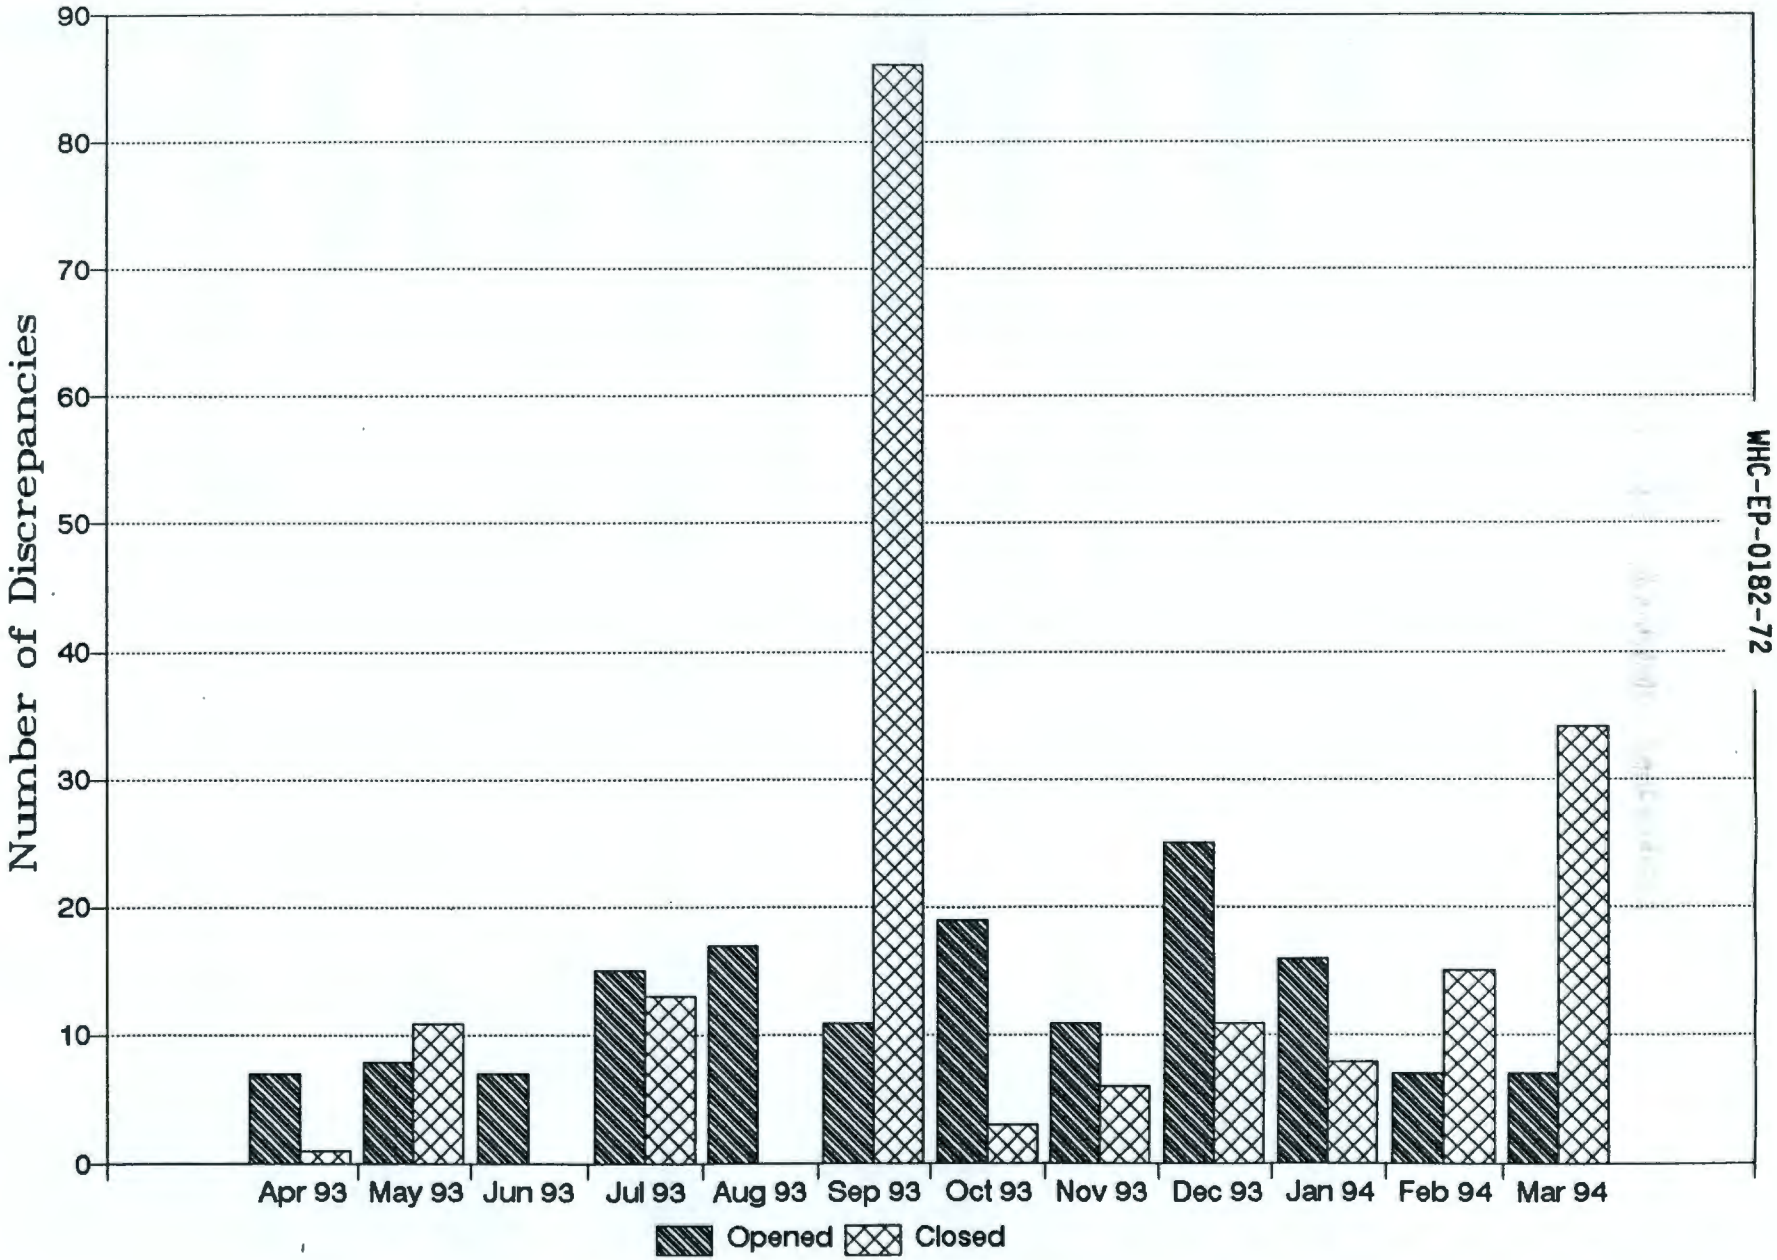

Figure 1. Discrepancy Report Status

S&DA 03/31/1994

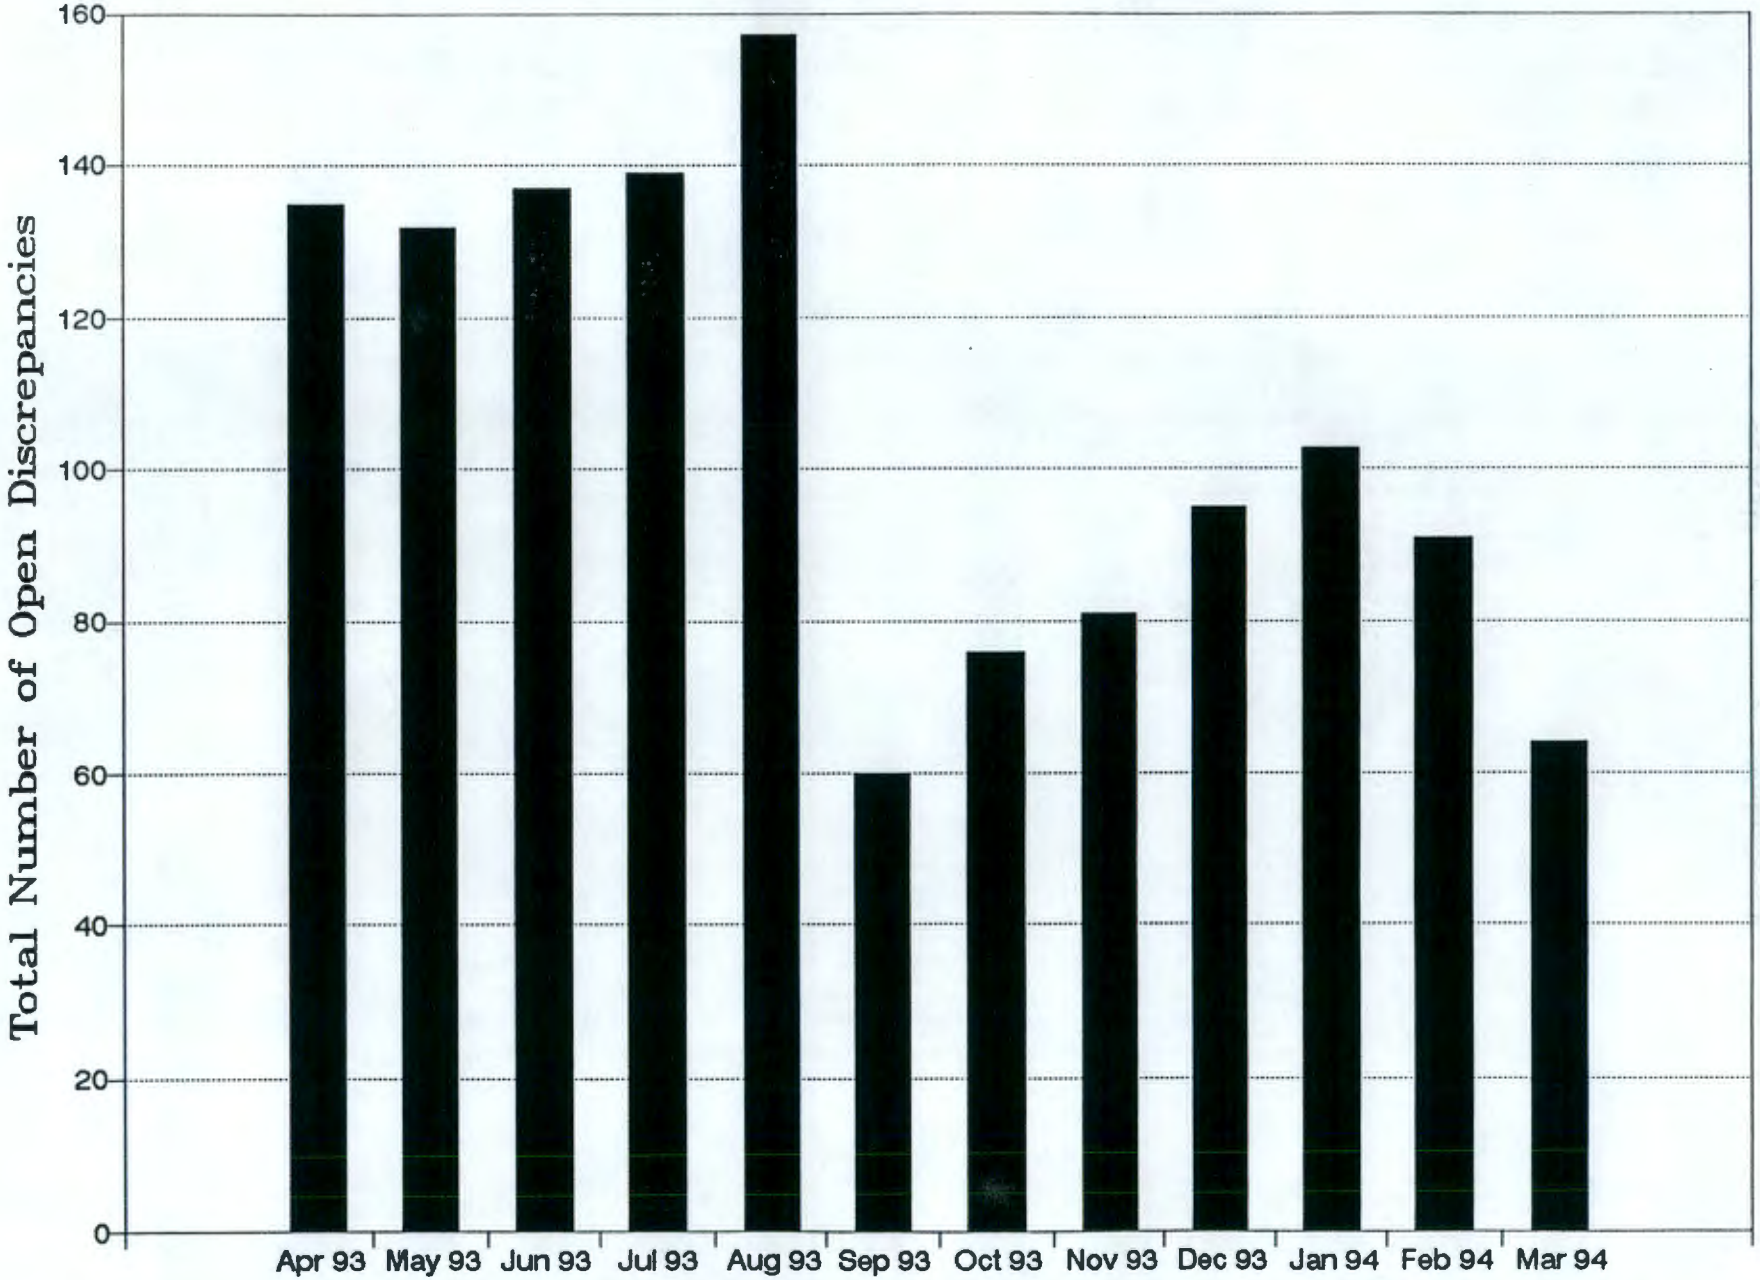

Figure 2. Open Discrepancy Reports

S&DA 03/31/1994

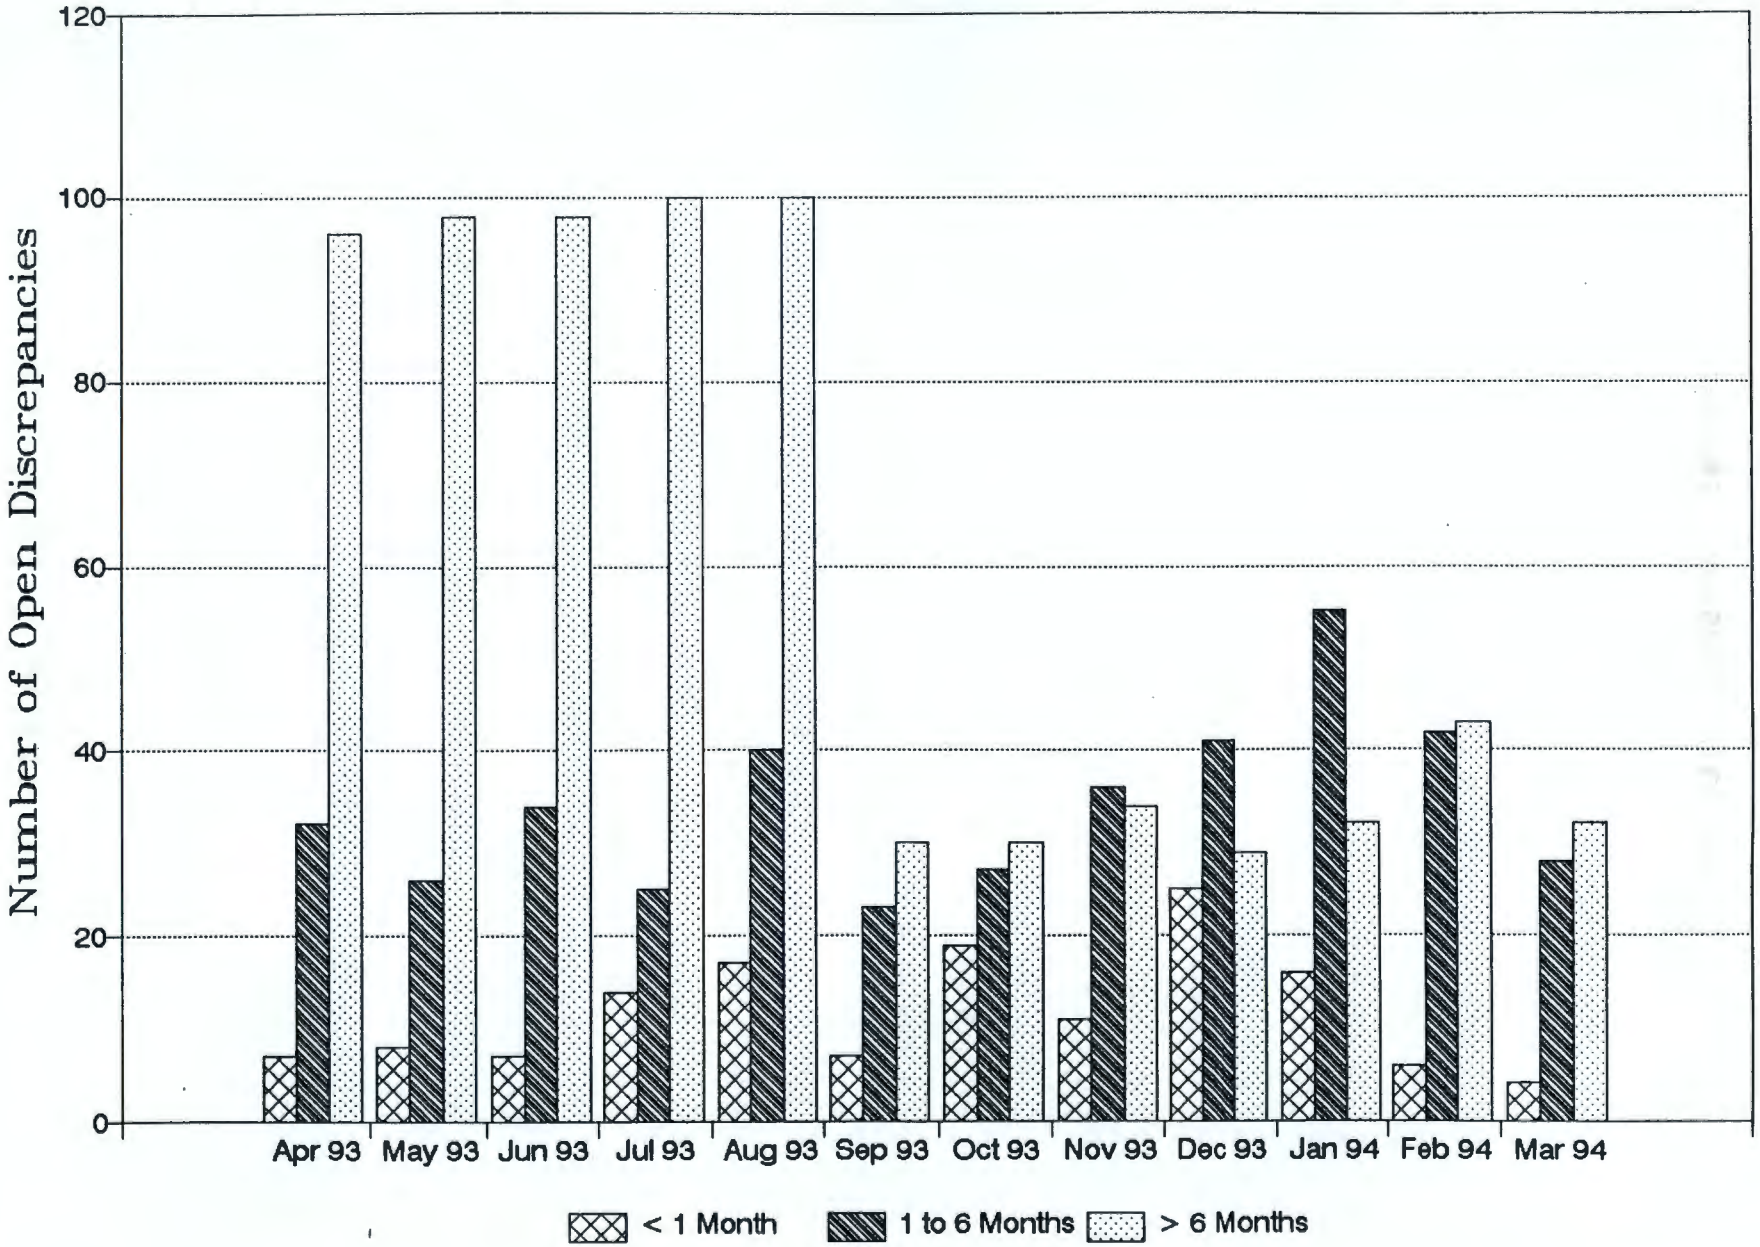

Figure 3. Discrepancy Report Status by Age

S&DA 03/31/1994

This page intentionally left blank

9413279.1052

APPENDIX B

DOUBLE SHELL TANK WASTE TYPE AND SPACE ALLOCATION

9413276.0053

This page intentionally left blank

9413279.0054

TABLE B-1. DOUBLE-SHELL TANK WASTE TYPE AND SPACE ALLOCATION
MARCH 1994

DOUBLE-SHELL TANK INVENTORY BY WASTE TYPE		SPACE DESIGNATED FOR SPECIFIC USE	
Complexant Concentrate (102-AN, 107-AN, 101-AY, 101-SY, 103-SY)	4.88 Mgal	Spare Tanks (3) (1 Aging & 1 Non-Aging Waste Tank)	2.28 Mgal
Concentrate Phosphate (102-AP,106-AN)	1.12 Mgal	Segregated Tank Space (105-AP, 101-AY, 102-AN, 107-AN, 103-AW)	1.08 Mgal
Double-Shell Slurry and Slurry Feed (103-AN, 104-AN, 105-AN, 105-AP, 101-AW)	5.09 Mgal	Watch List Tank Space (103-AN, 104-AN, 105-AN, 101-SY, 103-SY, 101-AW)	0.72 Mgal
Neutralized Current Acid Waste (101-AZ, 102-AZ)	1.23 Mgal	Priority Tank Space (2) (101-AN, 102-AW, 106-AW, 102-SY)	0.99 Mgal
Dilute Waste (1) (101-AN, 101-AP, 103-AP, 106-AP, 107-AP, 108-AP, 102-AW, 103-AW, 104-AW, 105-AW, 106-AW, 101-AY, 102-AY, 101-AZ, 102-AZ, 102-SY, 102-AP, 104-AP)	12.36 Mgal	Miscellaneous Head Space	0.19 Mgal
			5.25 Mgal
NCR and PFP Settled Solids (103-AW, 105-AW, 102-SY)	1.01 Mgal	TOTAL DOUBLE-SHELL TANK SPACE	
		24 Tanks at 1140 Kgal	27.36 Mgal
		4 Tanks at 980 Kgal	3.92 Mgal
			31.28 Mgal
Total Inventory=	**25.69 Mgal**		
		Total Available Space	**31.28 Mgal**
		Double-Shell Tank Inventory	**25.69 Mgal**
		Space Designated for Specific Use	**5.25 Mgal**
		Remaining Unallocated Space	**0.34 Mgal**

(1) Easily reduced in volume by Evaporator/LERF
(2) Reduced by Saltwell Liquid pumping, Mini Run and PFP Operations
(3) 241-101-AY: A minumum liquid level is set to provide extra protection against any bottom uplifting of the tank's steel liner. WHC-SD-WM-TI-357, "Waste Storage Tank Status and Leak Detection Criteria," specifies 64 in. as the minimum surface level measurement when the annulus system is in operation, and 18 in. if the annulus ventilation system is shut down. See also OSD-T-151-0007, "Unclassified Operation Specifications for the 241 AN, 241AP, 241AW, 241AY and 241SY Tank Farms." Because of space availablility, waste is stored in 102-AY, the aging waste spare tank. In case of a leak, the contents of 102-AY will be distributed to any other DST(s) having available space.

Note: Net change in DSTs since last month: 49 Kgal.

WVPTOT

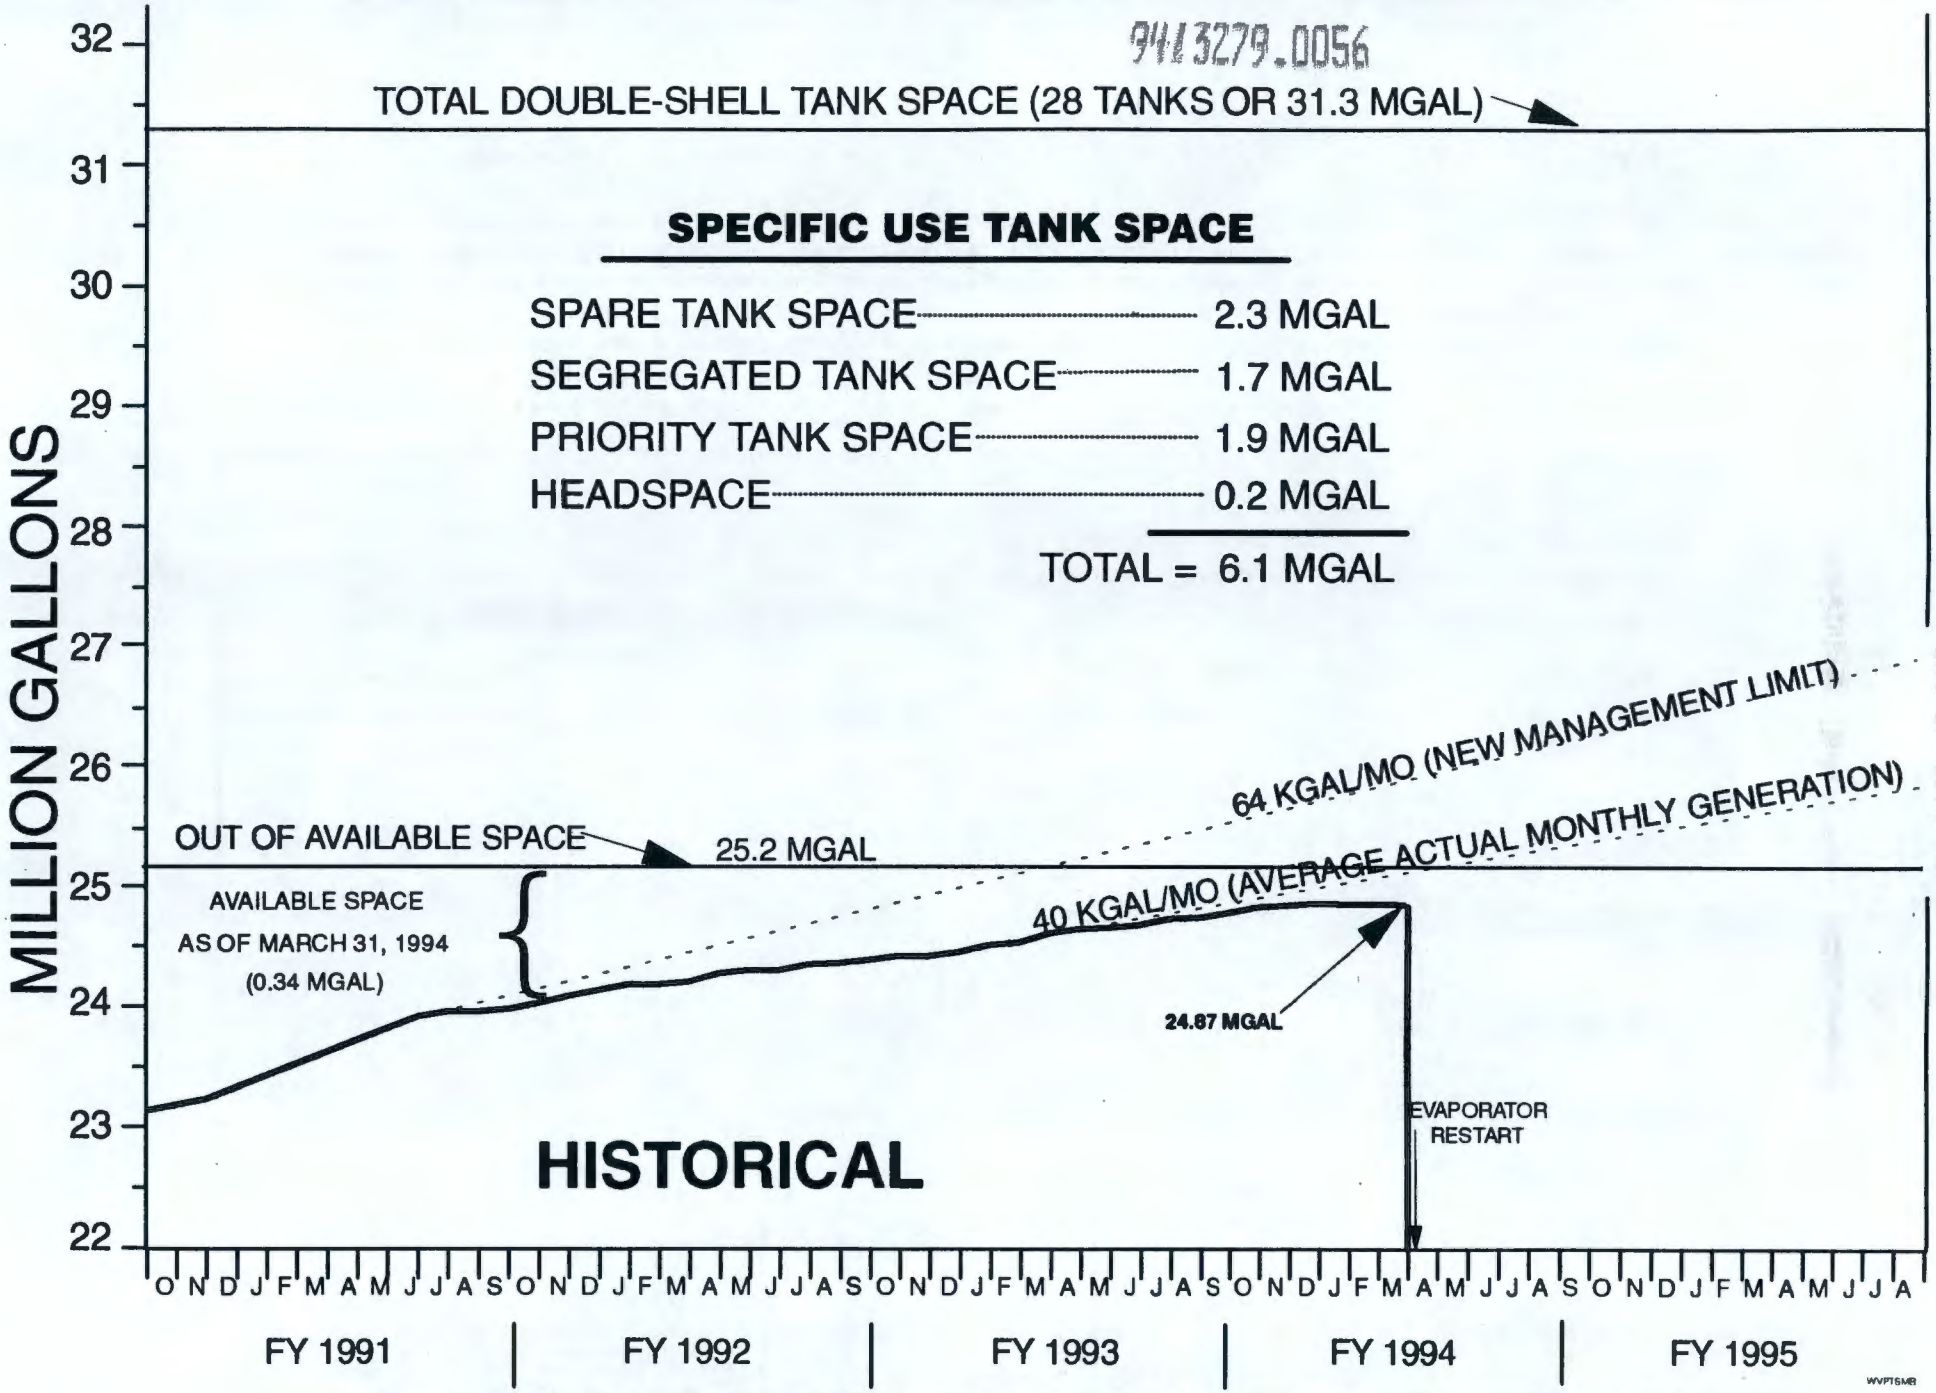

Note: Graphic does not Depict Waste Receipts or Depletions to Specific Use Tank Space

FIGURE B-1. CURRENT STATUS AND CONTINGENCY SPACE FOR THE 242-A EVAPORATOR RESTART

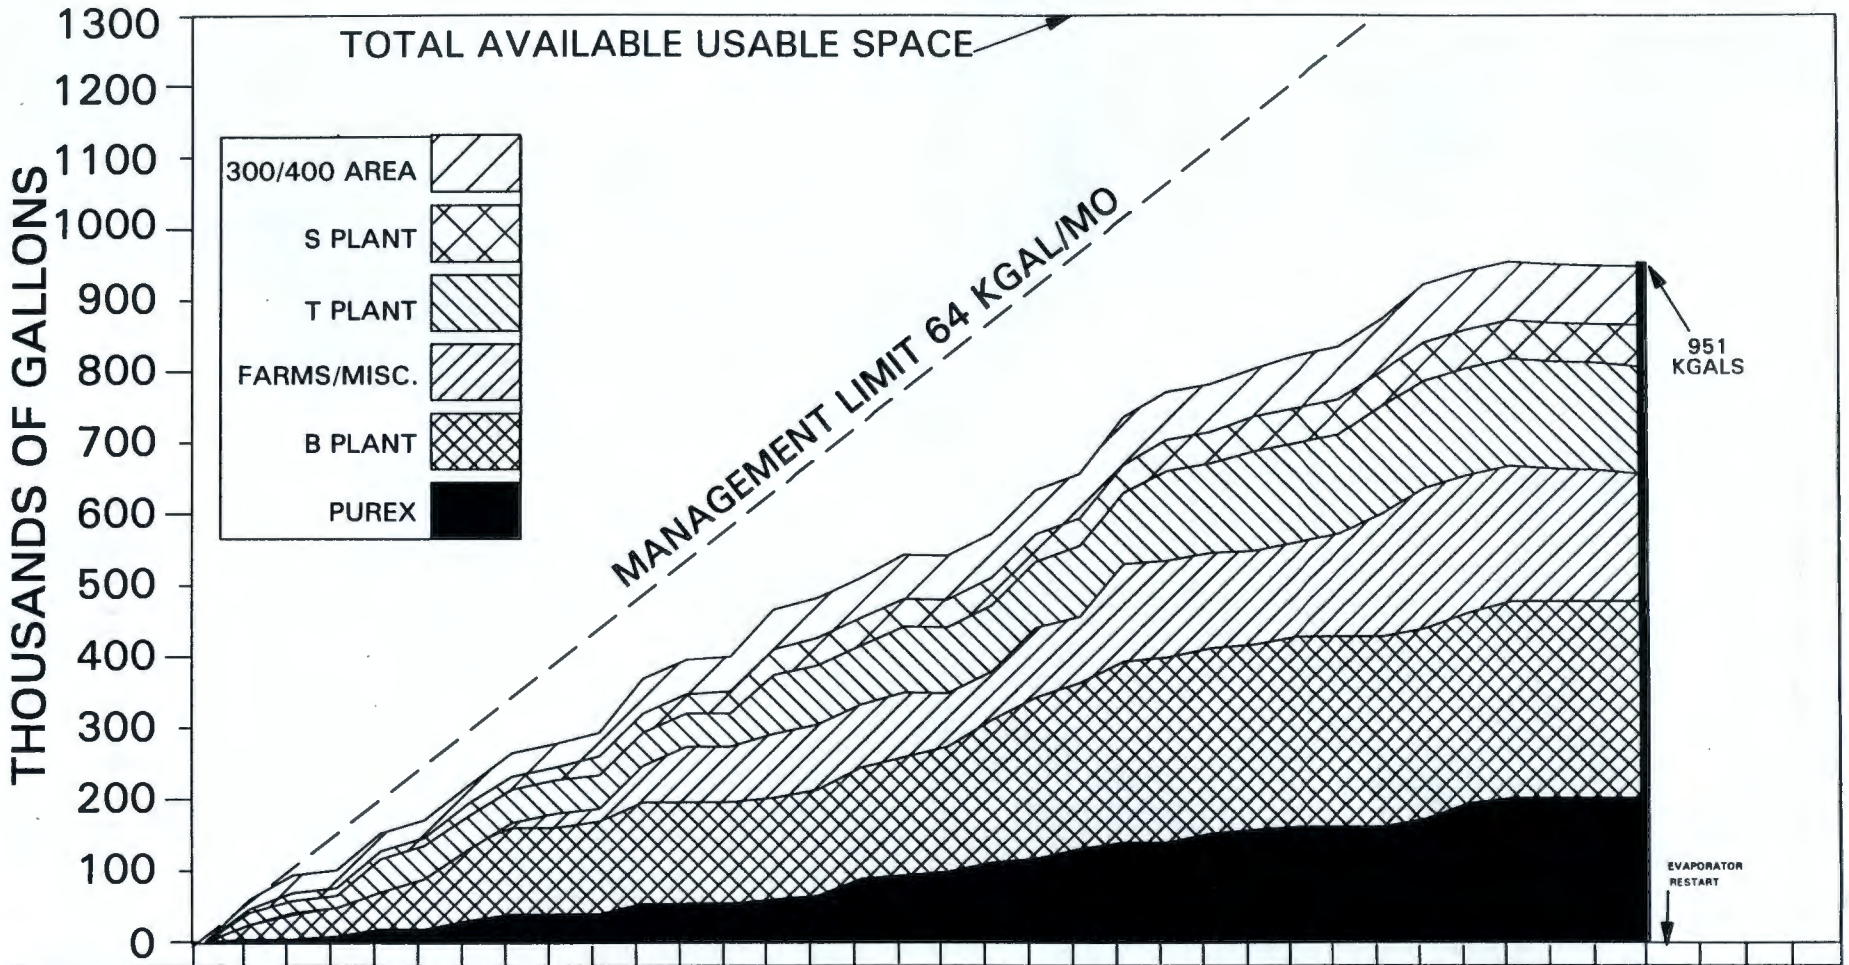

MONTHLY LIMIT		JUL 91	AUG 91	SEP 91	OCT 91	NOV 91	DEC 91	JAN 92	FEB 92	MAR 92	APR 92	MAY 92	JUN 92	JUL 92	AUG 92	SEP 92	OCT 92	NOV 92	DEC 92	JAN 93	FEB 93	MAR 93	APR 93	MAY 93	JUN 93	JUL 93	AUG 93	SEP 93	OCT 93	NOV 93	DEC 93	JAN 94	FEB 94	MAR 94	APR 94	MAY 94	JUN 94	JUL 94
300/400 AREA	5	13	12	0	0	0	0	8	0	0	16	0	0	7	0	0	6	0	0	0	0	5	0	0	0	7	12	0	8	0	0	0	0	0				
S PLANT	5	5	6	0	0	0	0	0	0	9	0	0	4	5	3	0	0	0	0	0	0	0	5	0	5	0	0	0	5	0	0	0	0	5				
T PLANT	6	17	0	0	30	0	0	0	0	0	0	0	0	36	0	0	10	0	0	0	7	0	26	0	14	0	0	11	0	0	0	0	0	0				
MISC\TANK FARM	NA	0	2	-4	-10	-2	6	14	13	4	33	27	0	12	2	-3	2	-16	-7	30	-5	44	1	-2	-2	1	0	28	24	-4	-3	-4	-2	-4				
B PLANT	23	20	14	7	22	21	23	15	0	9	12	0	0	0	6	7	10	10	25	26	7	21	6	0	0	7	0	0	0	0	9	0	0	0				
PUREX	15	3	0	4	10	0	12	9	0	0	15	0	0	6	5	24	5	5	13	5	14	9	0	13	5	4	0	0	12	22	7	0	0	0				

NOTE: THIS GRAPHIC DEPICTS "USABLE SPACE" DEPLETION AND NOT THE TOTAL RECEIPTS TO DSTs.

WVPFACIL

FIGURE B-2. TOTAL AVAILABLE USABLE TANK SPACE

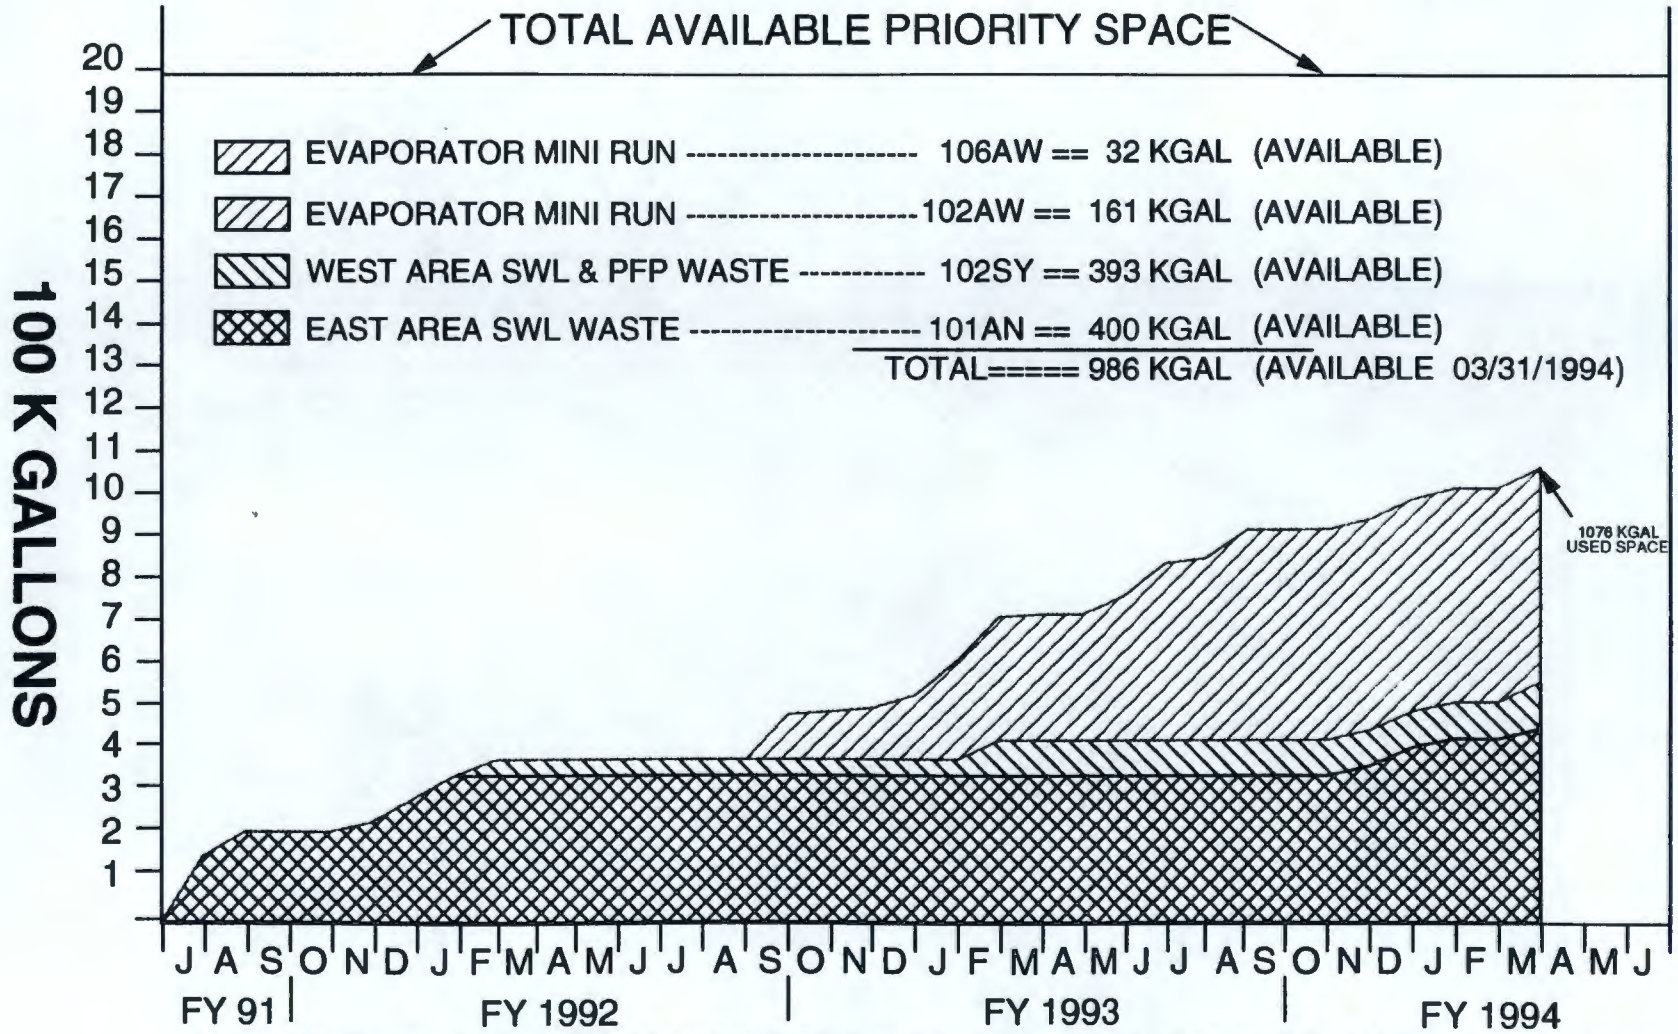

FIGURE B-3. PRIORITY SPACE AVAILABILITY AND USAGE

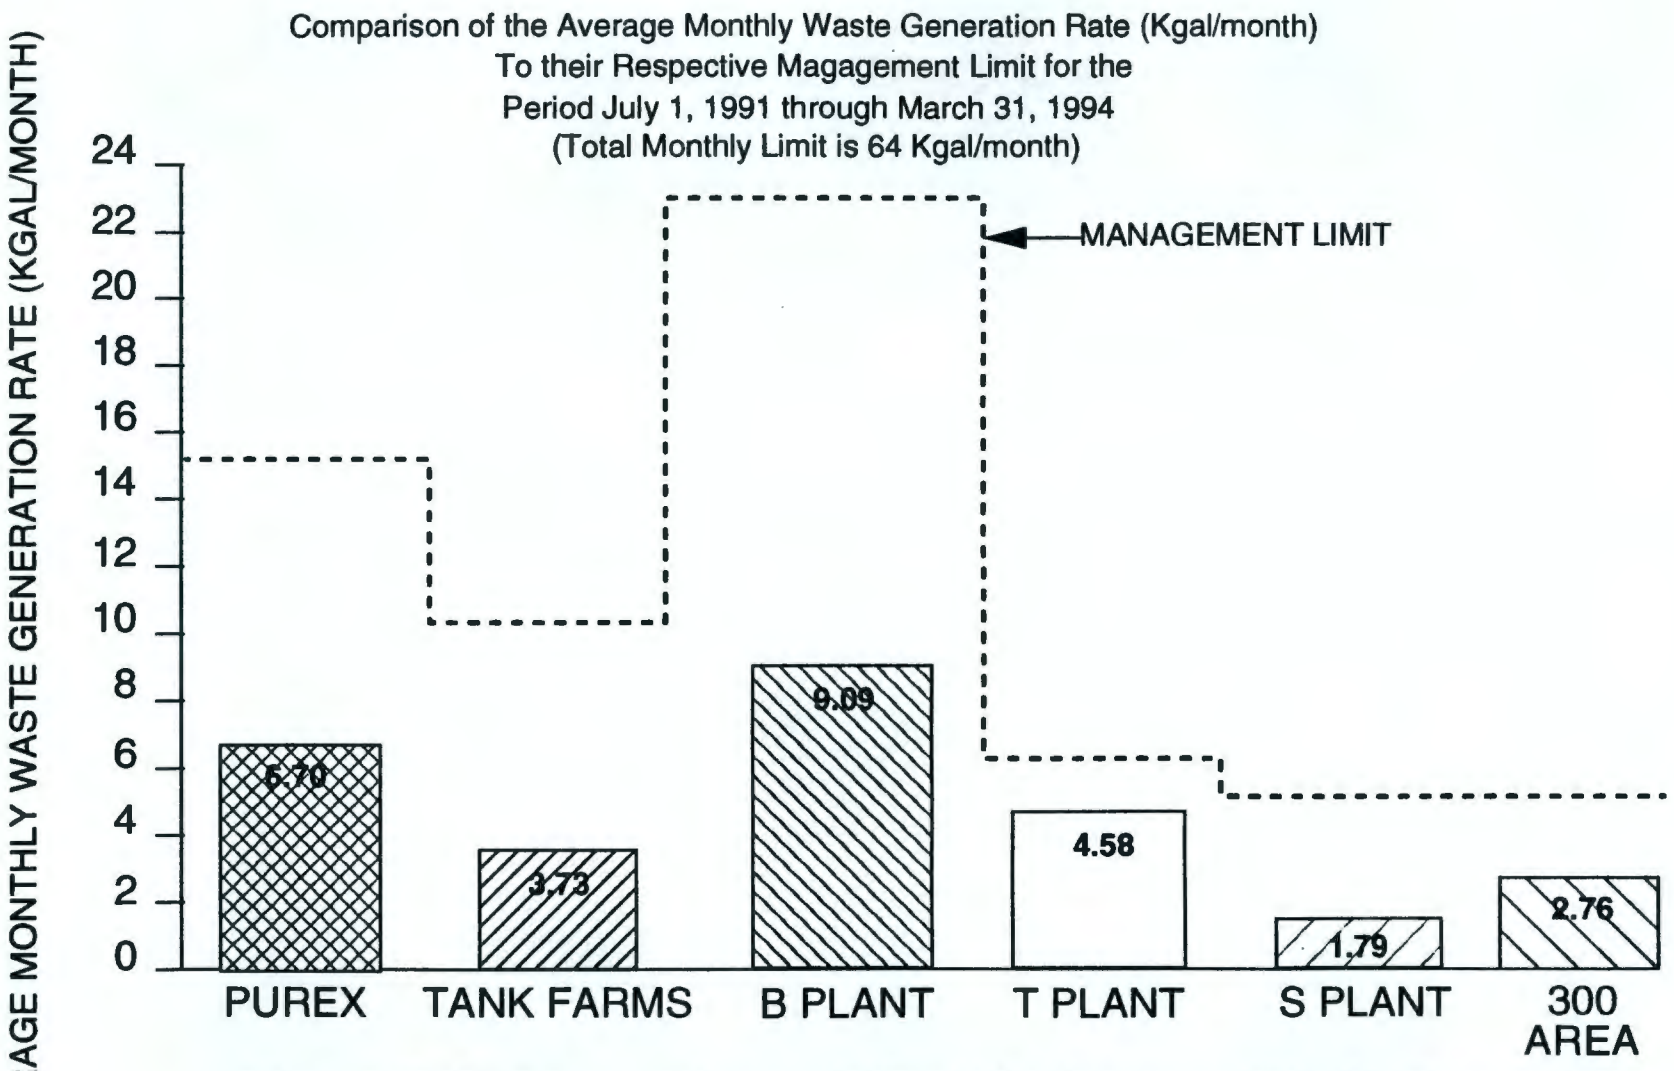

Figure B-4. Comparison of Monthly Average Waste Generation to Management Limit by Facility

WVPAVE

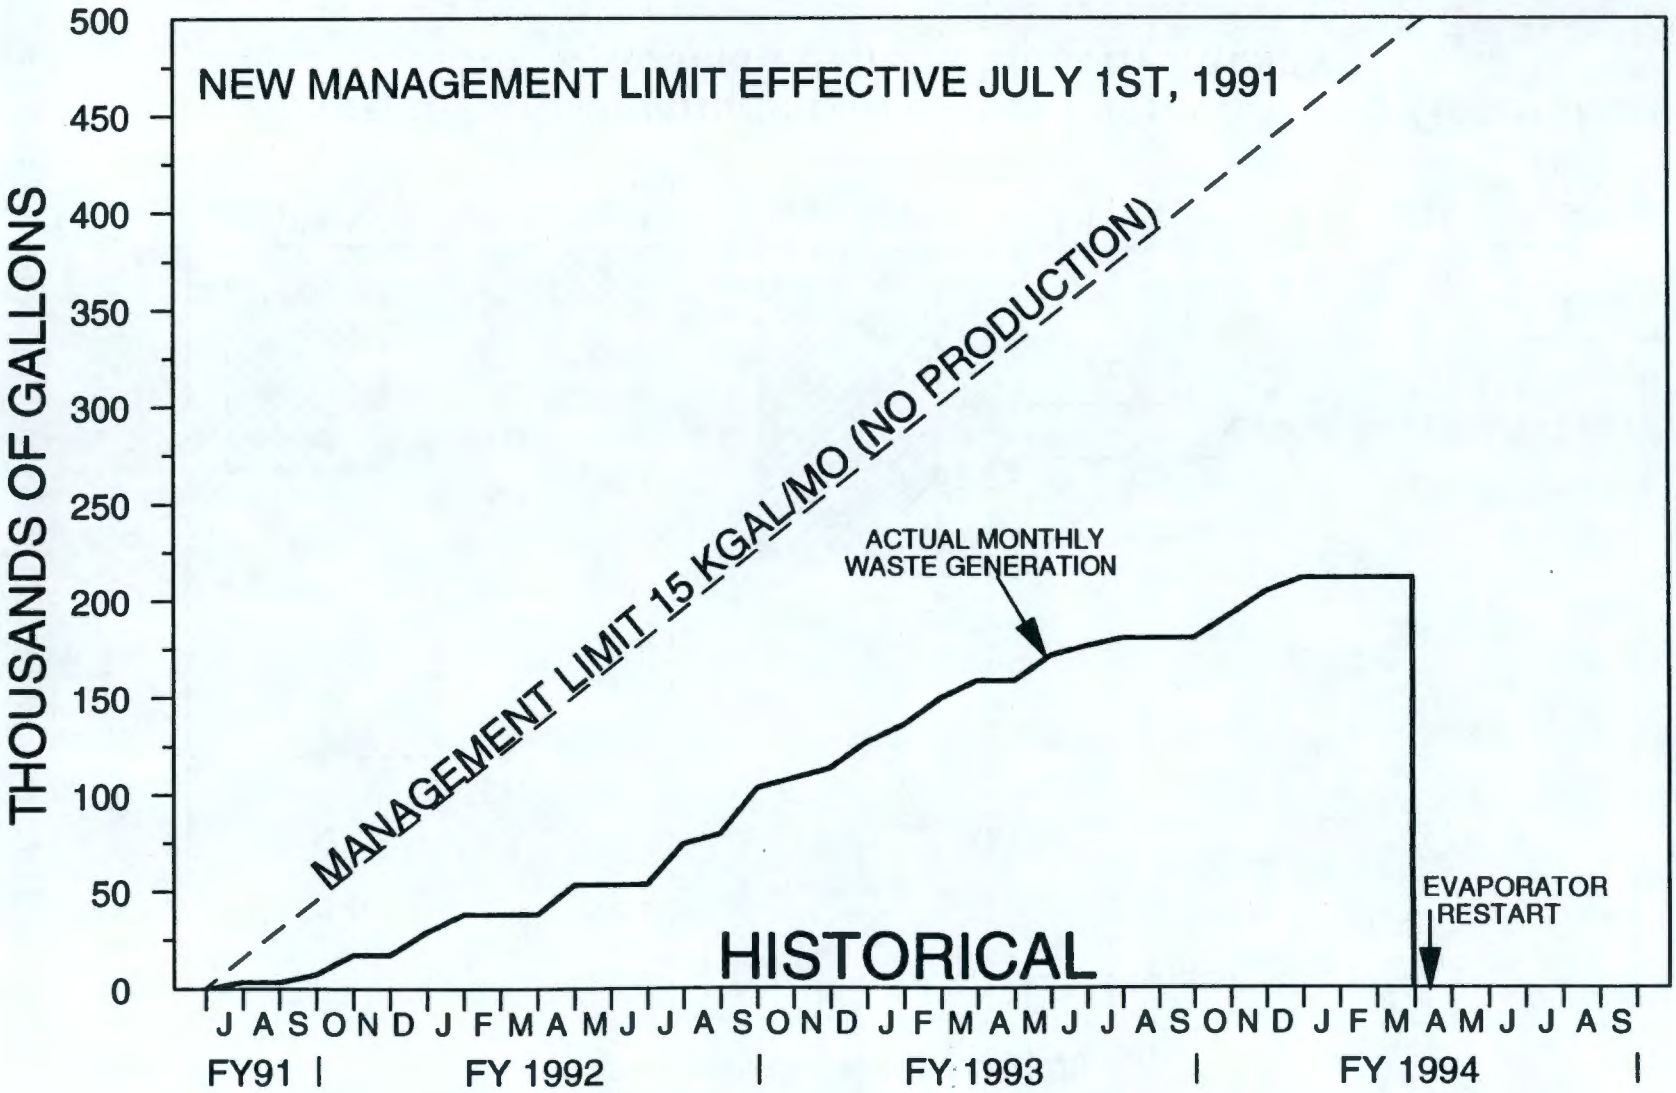

FIGURE B-5. PUREX MONTHLY WASTE GENERATIONS

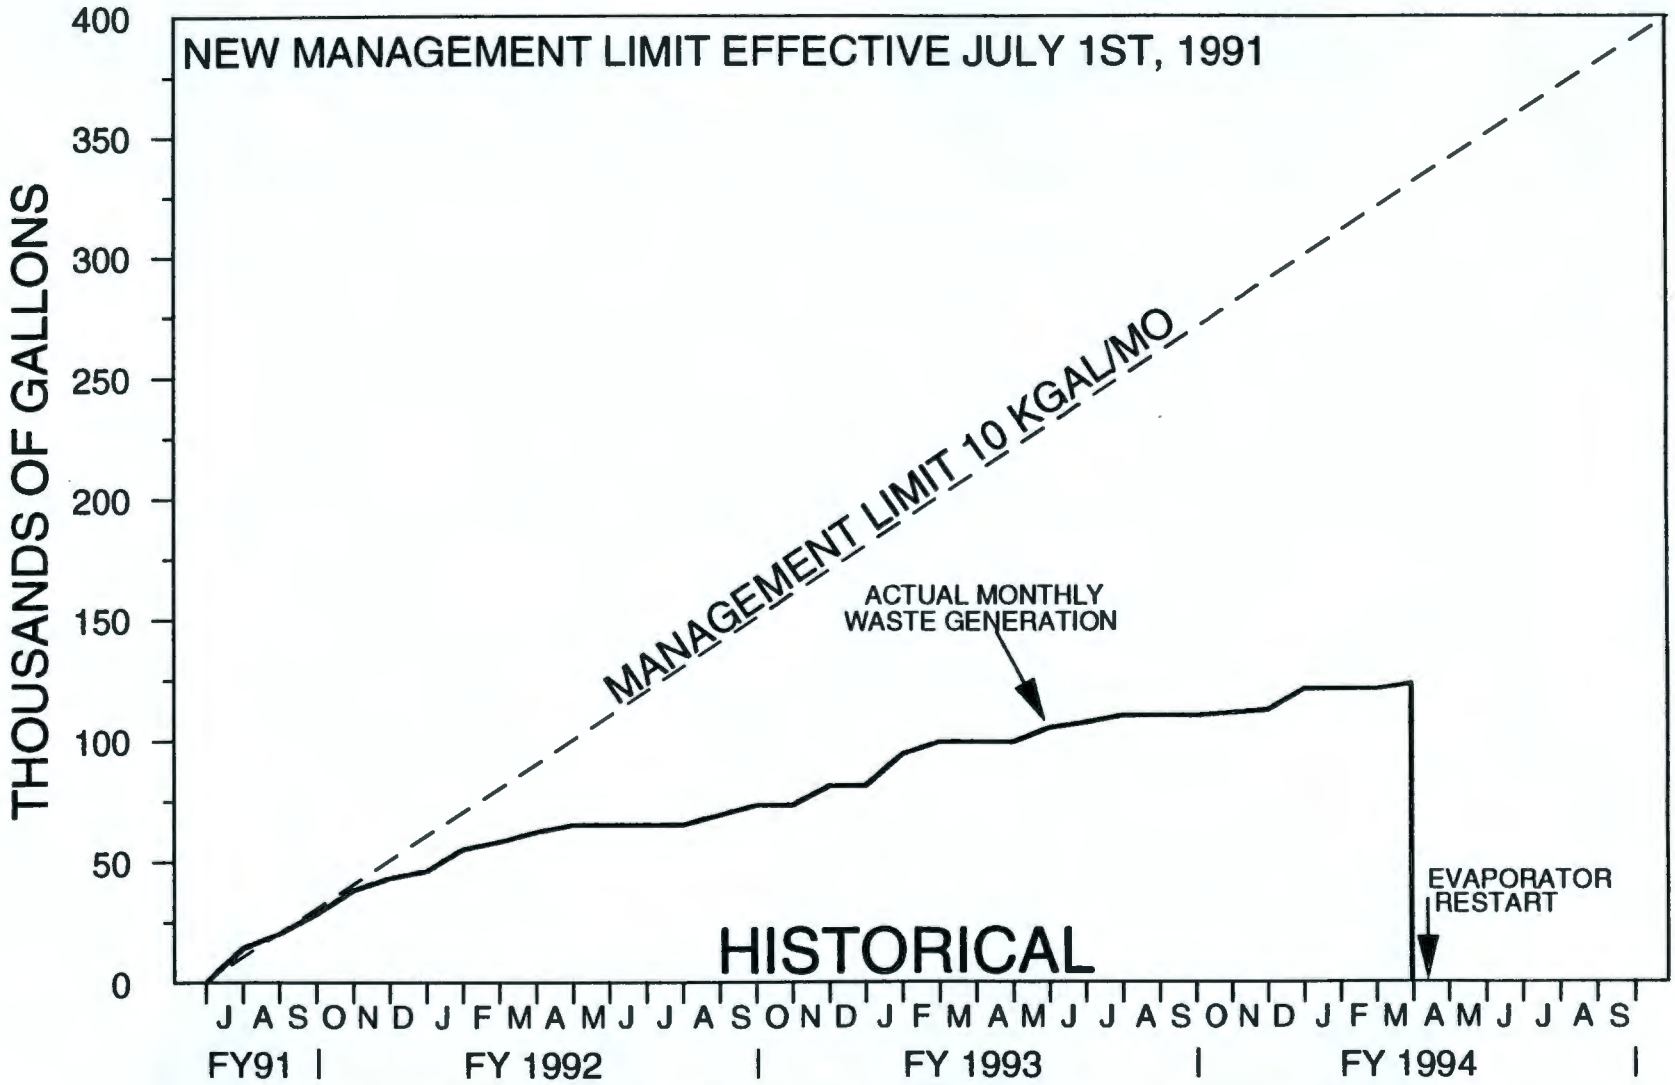

FIGURE B-6. TANK FARMS MONTHLY WASTE GENERATIONS

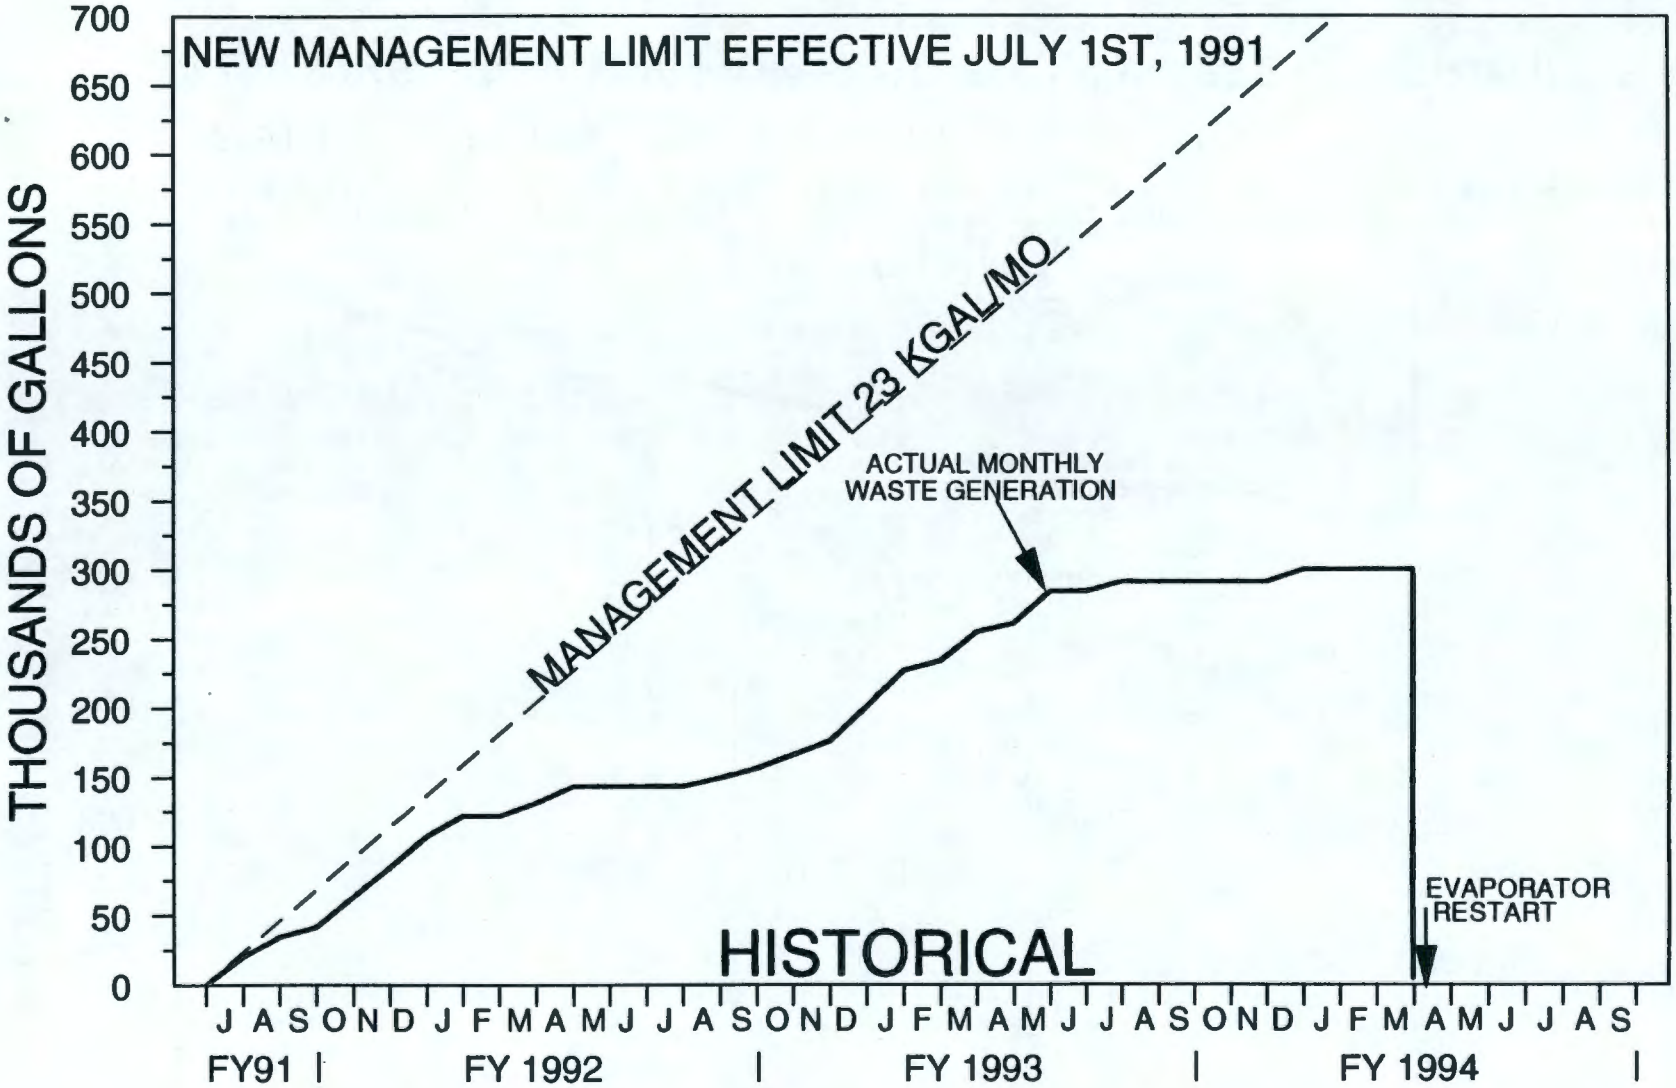

FIGURE B-7. B PLANT MONTHLY WASTE GENERATIONS

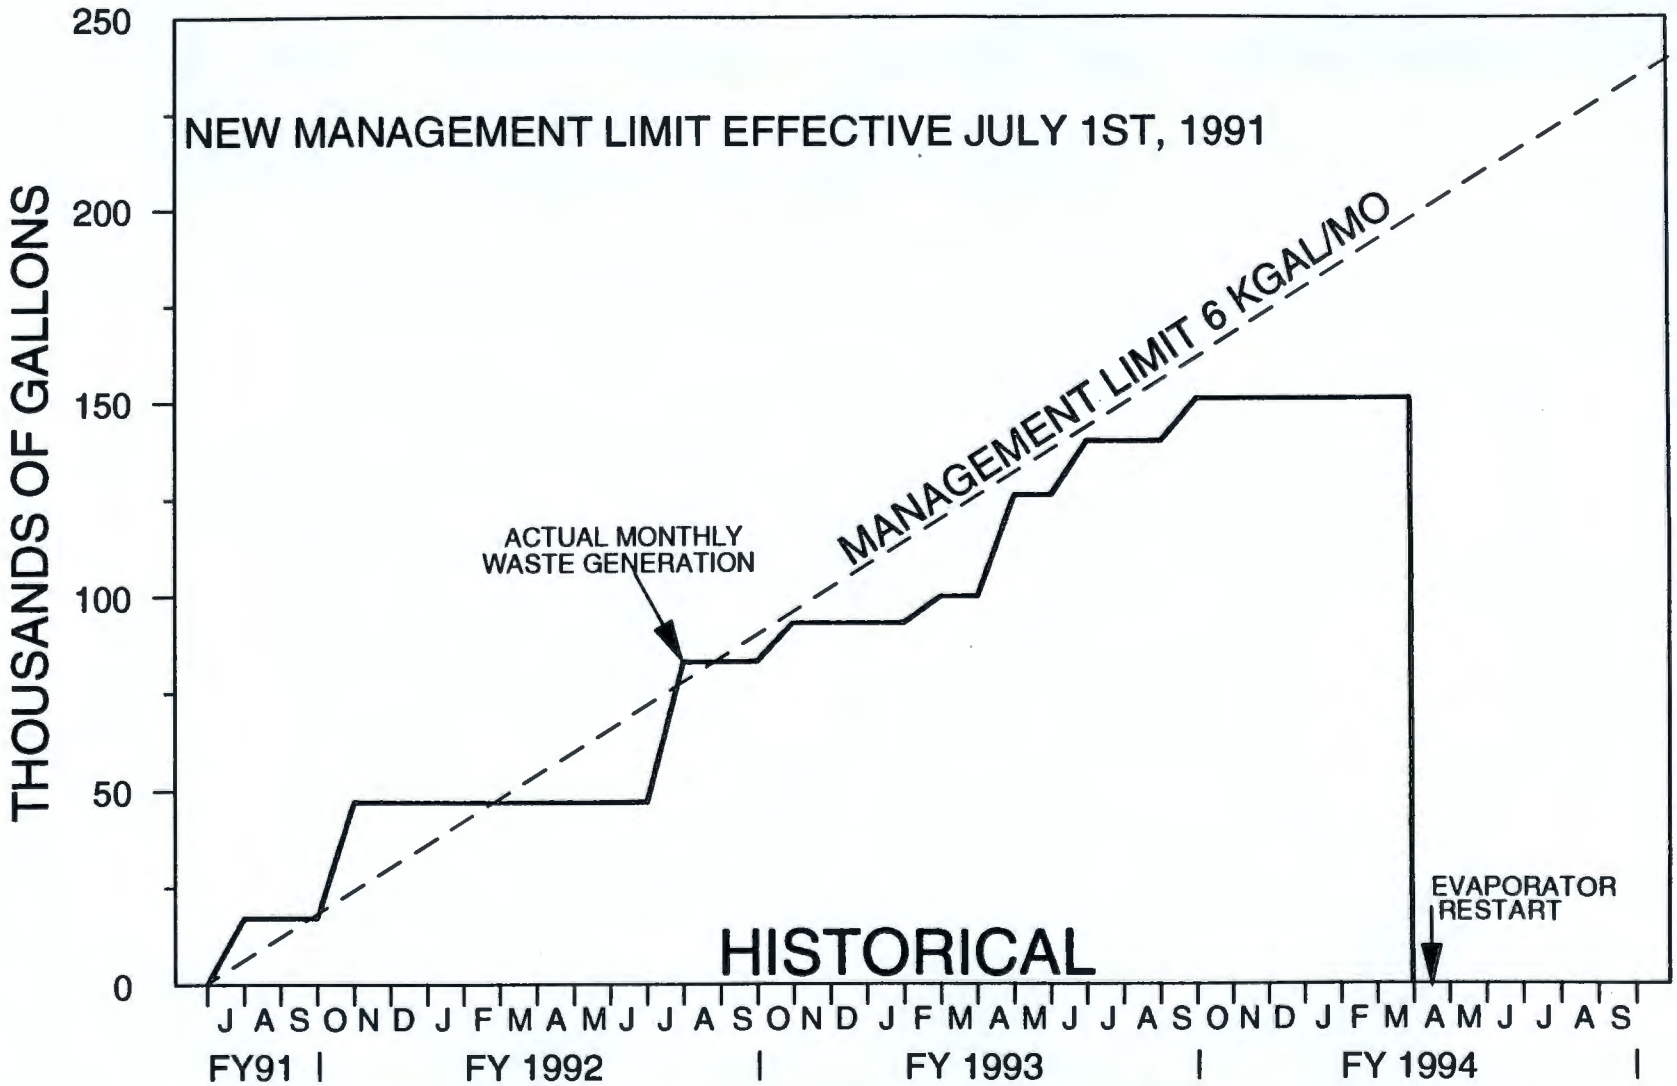

FIGURE B-8. T PLANT MONTHLY WASTE GENERATIONS

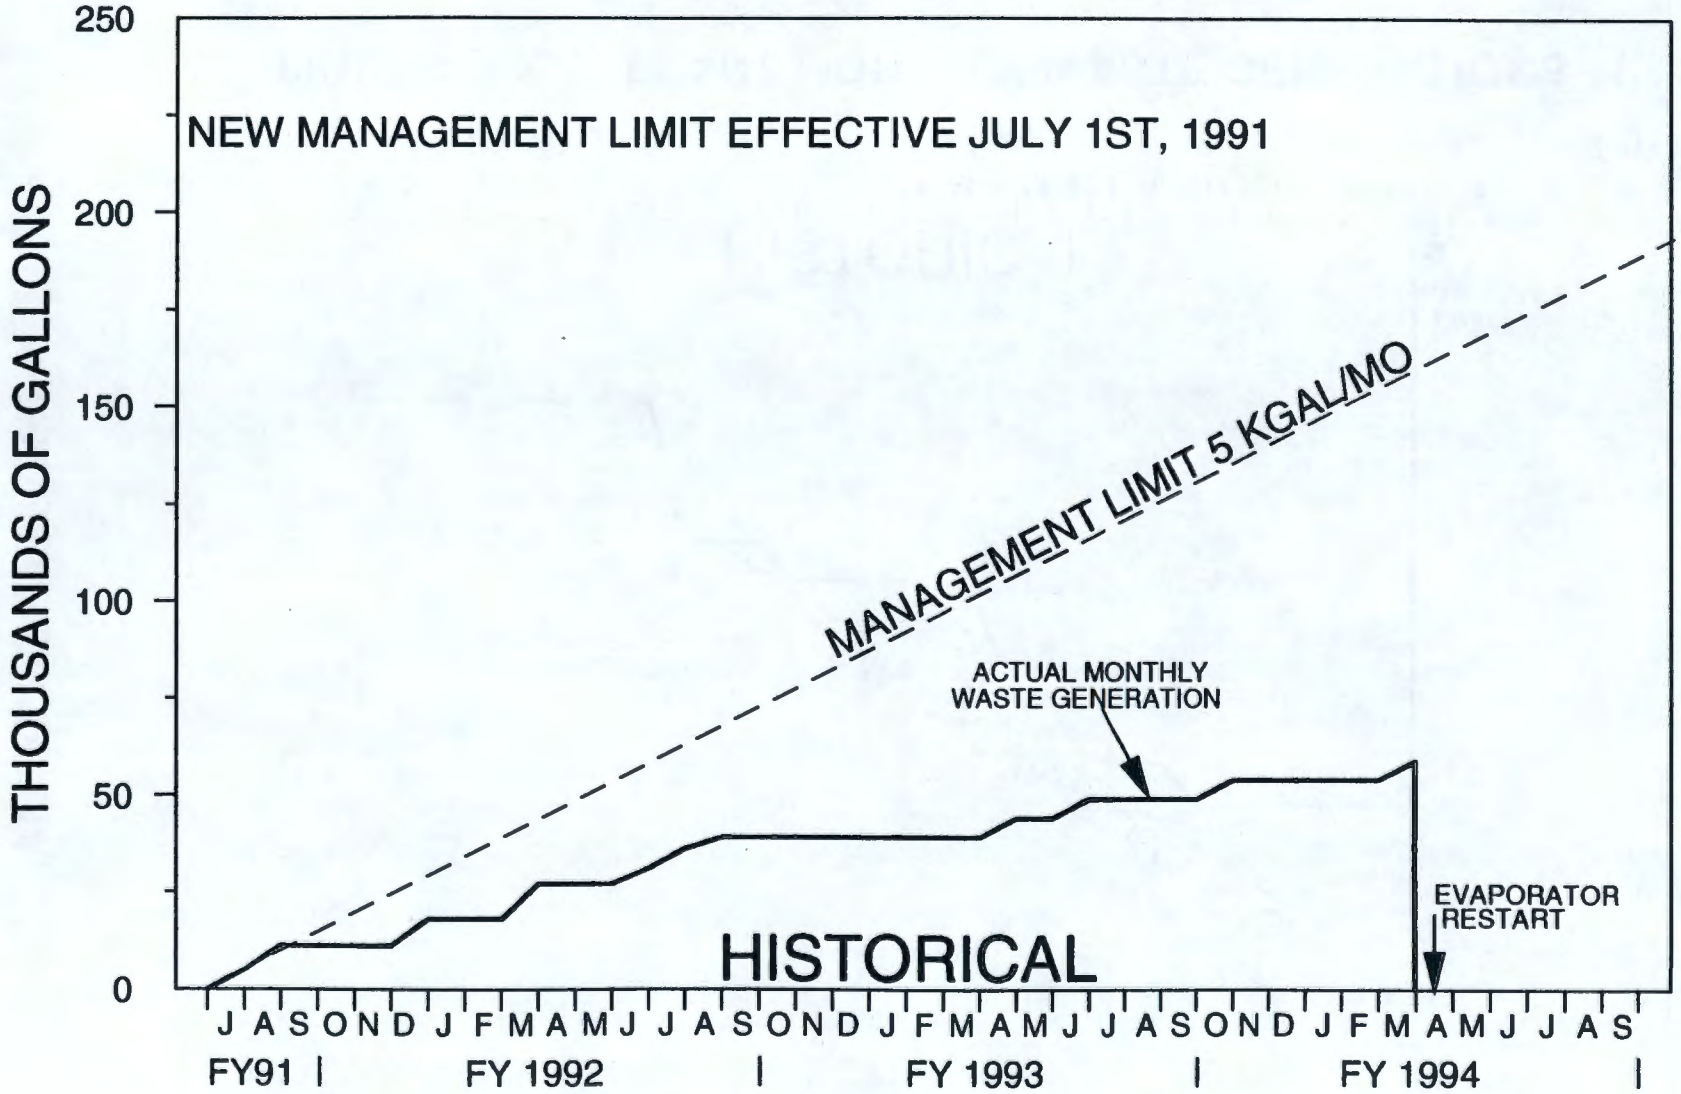

FIGURE B-9. S PLANT MONTHLY WASTE GENERATIONS

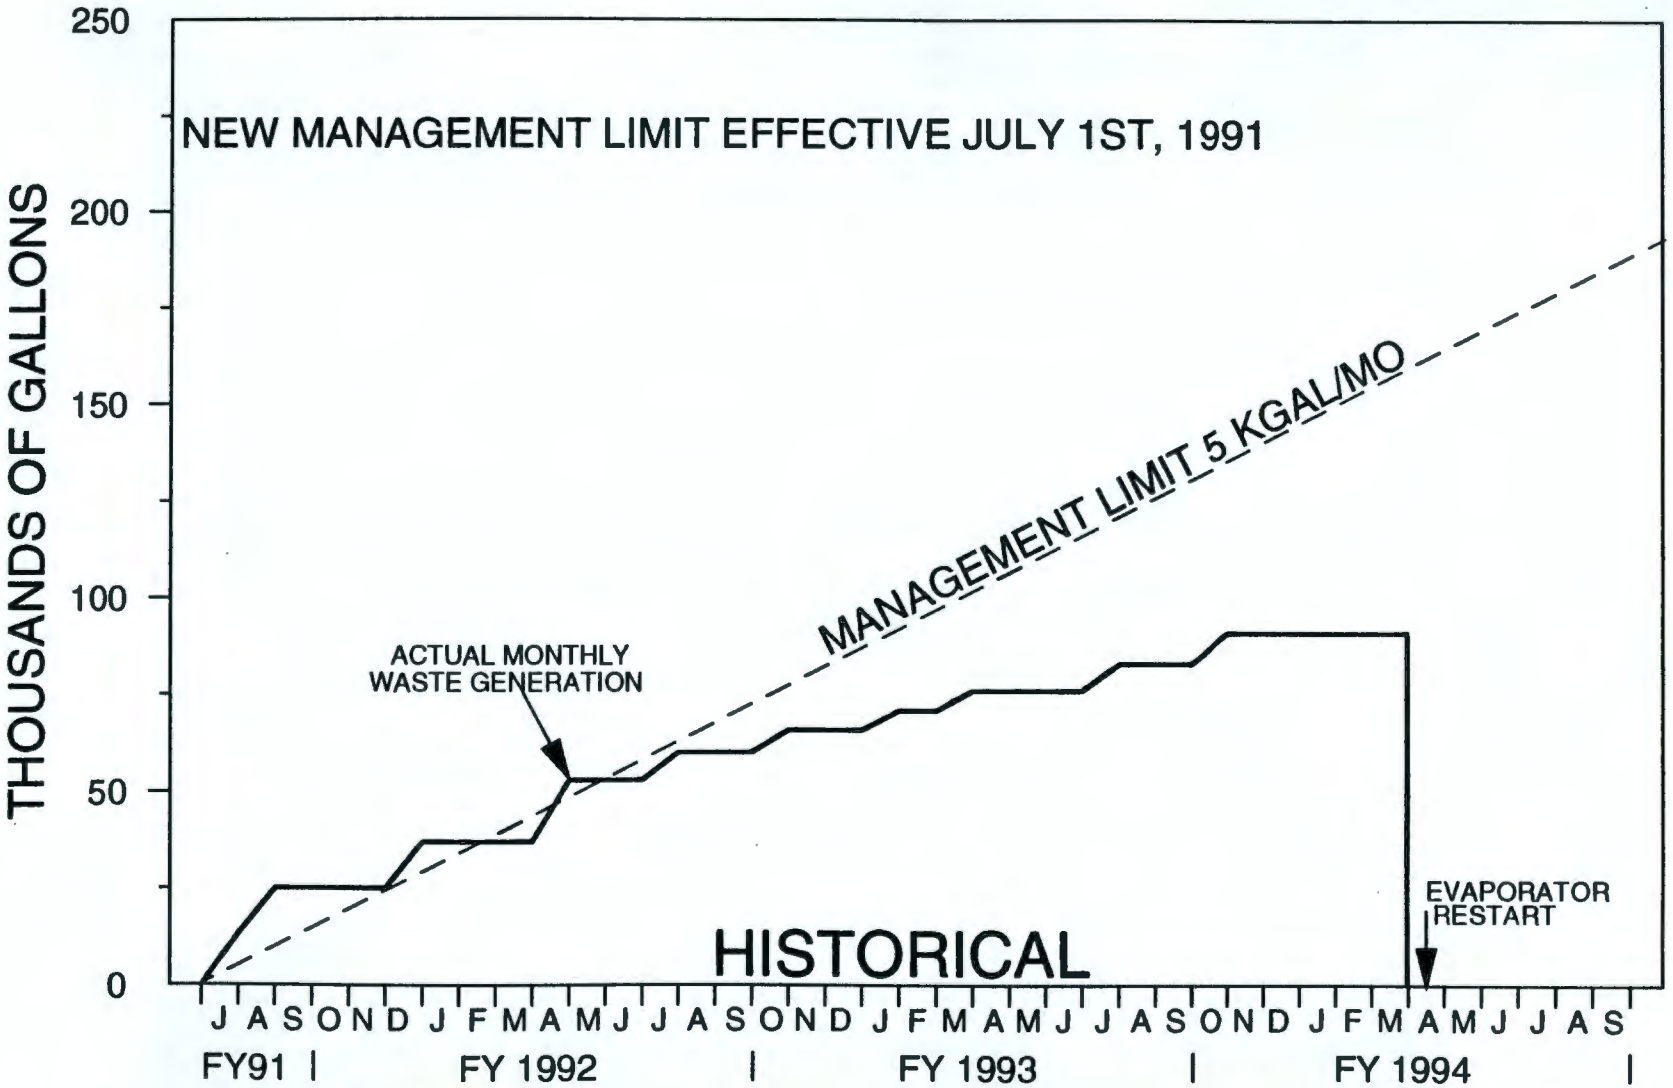

FIGURE B-10. 300 AREA MONTHLY WASTE GENERATIONS

Table B-2. Double Shell Tank Waste Inventory for March 31, 1994 (page 1 of 2)

TANKS	INVENTORY	SOLIDS	TYPE	LEFT
101AW=	1139	84	DSSF	1
102AW=	979	3	DN	161
103AW=	646	487	NCRW	494
104AW=	1123	267	DN	17
105AW=	1040	388	NCRW	100
106AW=	1108	211	DN	32
101AY=	881	83	DC	99
102AY=	711	32	DN	269
101AZ=	960	35	NCAW	20
102AZ=	963	95	NCAW	17
101AN=	740	0	DN	400
102AN=	1090	89	CC	50
103AN=	953	373	DSS	187
104AN=	1056	264	DSSF	84
105AN=	1130	0	DSSF	10
106AN=	21	17	CP	1119
107AN=	1063	134	CC	77
101SY=	1100	560	CC	40
102SY=	747	133	PT/DN	393
103SY=	744	4	CC	396
101AP=	1060	0	DN	80
102AP=	1103	0	CP	37
103AP=	1131	0	DN	9
104AP=	18	0	DN	1122
105AP=	820	0	DSSF	320
106AP=	1127	0	DN	13
107AP=	1110	0	DN	30
108AP=	1131	0	DN	9
TOTAL=	25694		TOTAL	5586

SEGREGATED SPACE	
* 101AW=	1
103AW=	494
102AP=	37
105AP=	320
* 101SY=	40
* 103SY=	396
101AY=	99
102AN=	50
* 103AN=	187
* 104AN=	84
* 105AN=	10
107AN=	77
TOTAL=	1795

* WATCHLIST TANKS

PRIORITY SPACE	
102SY=	393
101AN=	400
102AW=	161
106AW=	32
TOTAL=	986

MISC. HEADSPACE	
101AP=	80
103AP=	9
106AP=	13
107AP=	30
104AW=	17
101AZ=	20
102AZ=	17
TOTAL=	186

USABLE SPACE	
104AP=	1122
108AP=	9
105AW=	100
102AY=	269
106AN=	1119
TOTAL=	2619
SPARES	-2280
USABLE	339

TOTAL SPACE AVAILABLE	
NON-AGING	27360
AGING =	3920
TOTAL=	31280

TOTAL INVENTORY	
02/94 TOTAL	25645
03/94 TOTAL	25694
INCREASE	49

USEABLE SPACE	
02/94 TOTAL	340
03/94 TOTAL	339
DECREASE	-1

PRIORITY SPACE	
02/94 TOTAL	1030
03/94 TOTAL	986
DECREASE	-44

Inventory Calculation by Waste Type:

COMPLEXED CONCENTRATE (CC)		
102AN=	1090	(CC)
107AN=	1063	(CC)
101SY=	1100	(CC & DSS)
103SY=	744	(CC, DSS & SWL)
101AY=	881	(DC)
TOTAL=	4878	

NCRW			
103AW=	159	SOLIDS=	487
105AW=	652	SOLIDS=	388
TOTAL=	811	TOTAL=	875

WEST AREA WASTE (DN/PD)			
102SY=	614	SOLIDS=	133
TOTAL=	614	TOTAL=	133

CONC. PHOSPHATE (CP)	
106AN=	21
102AP=	1103
TOTAL=	1124

DILUTE WASTE (DN)	
101AP=	1060
103AP=	1131
106AP=	1127
107AP=	1110
108AP=	1131
101AN=	740
102AW=	979
104AW=	1123
106AW=	1108
102AY=	711
104AP=	18
TOTAL=	12361

NCAW (AGING WASTE (@ 5M Na)	
101AZ=	791
102AZ=	434
TOTAL=	1225
DN=	698

DSS/DSSF	
105AP=	820
103AN=	953
104AN=	1056
105AN=	1130
101AW=	1139
TOTAL=	5098

GRAND TOTALS	
CC=	3997
DC=	881
NCRW=	875
CP=	1124
NCAW=	1225
DSS/DSS	5098
PFP=	133
DILUTE=	12361
TOTAL=	25694

WVPINV93

NOTE: All Values are in Kilogallons.

9413279.0066

Table B-2. Double Shell Tank Waste Inventory for March 31, 1994 (page 2 of 2)

TOTAL AVAILABLE SPACE AS OF MARCH 31, 1994:			**5586**	**KGALS**
SEGREGATED TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE	
	* 101-AW	DSSF	1	KGALS
(*)Watch List Tanks	103-AW	NCRW	494	KGALS
	102-AP	CP	37	KGALS
	105-AP	DSSF	320	KGALS
	* 101-SY	CC/DSS	40	KGALS
	* 103-SY	CC/DSS	396	KGALS
	101-AY	DC	99	KGALS
	102-AN	CC	50	KGALS
	* 103-AN	DSS	187	KGALS
	* 104-AN	DSSF	84	KGALS
	* 105-AN	DSSF	10	KGALS
	107-AN	CC	77	KGALS
		TOTAL=	**1795**	**KGALS**
		AVAILABLE TANK SPACE=	5586	KGALS
		MINUS SEGREGATED SPACE=	-1795	KGALS
TOTAL AVAILABLE SPACE AFTER SEGREGATION=			**3791**	**KGALS**
PRIORITY TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE	
SWL/PFP	102-SY	DN	393	KGALS
NON-COMPLEXED SWL RECEIVER	101-AN	DN	400	KGALS
EVAPORATOR START-UP	102-AW	DN	161	KGALS
EVAPORATOR START-UP	106-AW	DN	32	KGALS
		TOTAL=	**986**	**KGALS**
		AVAILABLE SPACE AFTER SEGREGATION=	3791	KGALS
		MINUS PRIORITY SPACE=	-986	KGALS
TOTAL AVAILABLE SPACE AFTER PRIORITY=			**2805**	**KGALS**
MISCELLANEOUS HEADSPACE:	TANK	WASTE TYPE	AVAILABLE SPACE	
	101-AP	DN	80	KGALS
	103-AP	DN	9	KGALS
	106-AP	DN	13	KGALS
	107-AP	DN	30	KGALS
	104-AW	DN	17	KGALS
	101-AZ	AW	20	KGALS
	102-AZ	AW	17	KGALS
		TOTAL=	**186**	**KGALS**
		AVAILABLE SPACE AFTER PRIORITY=	2805	KGALS
		MINUS MISCELLANEOUS HEADSPACE=	-186	KGALS
TOTAL AVAILABLE SPACE AFTER HEADSPACE=			**2619**	**KGALS**
REALISTIC USABLE TANK SPACE:	TANK	WASTE TYPE	AVAILABLE SPACE	
	104-AP	DN	1122	KGALS
	108-AP	DN	9	KGALS
	105-AW	NCRW	100	KGALS
	102-AY	DN	269	KGALS
	106-AN	CP	1119	KGALS
		TOTAL=	**2619**	**KGALS**
		TOTAL AVAILABLE SPACE AFTER UNUSABLE DEPLETION=	2619	KGALS
		MINUS SPARE TANK SPACE=	-2280	KGALS
TOTAL TANK SPACE AVAILABLE AFTER SPARE SPACE=			**339**	**KGALS**

WVPBE061

9413279.0067

This page intentionally left blank

9413270.0068

9413279.0069

APPENDIX C

TANK AND EQUIPMENT CODE AND STATUS DEFINITIONS

This page intentionally left blank

9413279.0070

C. TANK AND EQUIPMENT CODE/STATUS DEFINITIONS
March 31, 1994

1. TANK STATUS CODES

WASTE TYPE

AGING	Aging Waste (Neutralized Current Acid Waste [NCAW])
CC	Complexant Concentrate Waste
CP	Concentrated Phosphate Waste
DC	Dilute Complexed Waste
DN	Dilute Non-Complexed Waste
DSS	Double-Shell Slurry
DSSF	Double-Shell Slurry Feed
NCPLX	Non-Complexed Waste
PD/PN	Plutonium-Uranium Extraction (PUREX) Neutralized Cladding Removal Waste (NCRW), transuranic waste (TRU)
PT	Plutonium Finishing Plant (PFP) TRU Solids

TANK USE (DOUBLE-SHELL TANKS ONLY)

CWHT	Concentrated Waste Holding Tank
DRCVR	Dilute Receiver Tank
EVFD	Evaporate Feed Tank
SRCVR	Slurry Receiver Tank

2. SOLID AND LIQUID VOLUME DETERMINATION METHODS

F	Food Instrument Company (FIC) Automatic Surface Level Gauge
M	Manual Tape Surface Level Gauge
P	Photo Evaluation
S	Sludge Level Measurement Device

3. DEFINITIONS

WASTE TANKS - GENERAL

Waste Tank Safety Issue
A potentially unsafe condition in the handling of waste material in underground storage tanks that requires corrective action to reduce or eliminate the unsafe condition.

Watch List Tank
An underground storage tank containing waste that requires special safety precautions because it may have a serious potential for release of high level radioactive waste because of uncontrolled increases in temperature or pressure. Special restrictions have been placed on these tanks by "Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the *National Defense Authorization Act for Fiscal Year 1991*, November 5, 1990, Public Law 101-510, (also known as the Wyden Amendment).

9413279.0071

9413279.0072

WASTE TYPES

Aging Waste (AGING)
High level, first cycle solvent extraction waste from the PUREX plant (NCAW)

Concentrated Complexant (CC)
Concentrated product from the evaporation of dilute complexed waste.

Concentrated Phosphate Waste (CP)
Waste originating from the decontamination of the N Reactor in the 100 N Area. Concentration of this waste produces concentrated phosphate waste.

Dilute Complexed Waste (DC)
Characterized by a high content of organic carbon including organic complexants:

ethylenediaminetetra-acetic acid (EDTA), citric acid, and hydroxyethyl-ethylenediaminetriacetic acid (HEDTA), being the major complexants used. Main sources of DC waste in the DST system are saltwell liquid inventory (from SSTs).

Dilute Non-Complexed Waste (DN)
Low activity liquid waste originating from T and S Plants, the 300 and 400 Areas, PUREX facility (decladding supernatant and miscellaneous wastes), 100 N Area (sulfate waste), B Plant, saltwells, and PFP (supernate).

Double-Shell Slurry (DSS)
Waste that exceeds the sodium aluminate saturation boundary in the evaporator without exceeding receiver tank composition limits. For reporting purposes, DSS is considered a solid.

Double-Shell Slurry (DSSF)
Waste concentrated just before reaching the sodium aluminate saturation boundary (of 6.5 molar hydroxide) in the evaporator without exceeding receiver tank composition limits. This form is not as concentrated as DSS.

Non-complexed (NCPLX)
General waste term applied to all Hanford Site (NCPLX) liquors not identified as complexed.

PUREX Decladding (PD/PN)
PUREX Neutralized Cladding Removal Waste (NCRW) is the solids portion of the PUREX plant neutralized cladding removal waste stream; received in Tank Farms as a slurry. NCRW solids are classified as transuranic (TRU) waste.

PFP TRU Solids (PT)
TRU solids fraction from PFP Plant operations.

Drainable Interstitial Liquid (DIL)
Interstitial liquid that is not held in place by capillary forces, and will therefore migrate or move by gravity. (See also Section 4)

Supernate
The liquid above the solids in waste storage tanks. (See also Section 4)

Ferrocyanide
A compound of iron and cyanide commonly expressed as FeCN. The actual formula for the ferrocyanide anion is $[Fe(CN)_6]^{-4}$.

WASTE STATUS

In-Service Tank
The waste classification of a tank being used, or planned for use, for the storage of liquid (in excess of a minimum supernatant liquid heel) in conjunction with production and/or waste processing.

Out-of-Service Tank
A tank which does not meet the definition of an in-service tank. Before September 1988, these tanks were defined as inactive in this report. (Note: All single-shell tanks are out of service.)

INTERIM STABILIZATION (Single-Shell Tanks only)

Interim Stabilized (IS)
A tank which contains less than 50,000 gal of drainable interstitial liquid and less than 5,000 gal of supernatant liquid. If the tank was jet pumped to achieve interim stabilization, then the jet pump flow must also have been at or below 0.05 gpm before interim stabilization criteria is met.

Jet Pump
The jet pump system includes 1) a jet assembly with foot valve mounted to the base of two pipes that extend from the top of the well to near the bottom of the well casing inside the saltwell screen, 2) a centrifugal pump to supply power fluid to the down-hole jet assembly, 3) flexible or rigid transfer jumpers, 4) a flush line, and 5) a flowmeter. The jumpers contain piping, valves, and pressure and limit switches.

The centrifugal pump and jet assembly are needed to pump the interstitial liquid from the saltwell screen into the pump pit, nominally a 40-foot elevation rise. The power fluid passes through a nozzle in the jet assembly and acts to convert fluid pressure head to velocity head, thereby reducing the pressure in the jet assembly chamber. The reduction in pressure allows the interstitial liquid to enter the jet assembly chamber and mix with the power fluid. Velocity head is converted to pressure head above the nozzle, lifting power fluid, and interstitial liquid to the pump pit. Pumping rates vary from 0.05 gal to about 4 gal/min.

9413279.0073

Saltwell Screen

The saltwell system is a 10-inch diameter saltwell casing consisting of a stainless steel saltwell screen welded to a Schedule 40 carbon steel pipe. The casing and screen are to be inserted into the 12-inch tank riser located in the pump pit. The stainless steel screen portion of the system will extend through the tank waste to near the bottom of the tank. The saltwell screen portion of the casing is an approximately 10-foot length of 300 Series, 10-inch diameter, stainless steel pipe with screen openings (slots) of 0.05 inches.

Emergency Pumping Trailer

A 45-foot Tractor-Type trailer is equipped to provide storage space and service facilities for emergency pumping equipment: this consists of two dedicated jet pump jumpers and two jet pumps, piping and dip tubes for each, two submersible pumps and attached piping, and a skid-mounted Weight Factor Instrument Enclosure (WFIE) with an air compressor and electronic recording instruments. The skid also contains a power control station for the pumps, pump pit leak detection, and instrumentation. A rack for over 100 feet of overground double-contained piping is also in the trailer.

9413279.0074

INTRUSION PREVENTION (ISOLATION) Single-Shell Tanks only

Partially Interim Isolated (PI)

The administrative designation reflecting the completion of the physical effort required for Interim Isolation except for isolation of risers and piping that is required for jet pumping or for other methods of stabilization.

Interim Isolated (II)

The administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. In June 1993, Interim Isolation was replaced by Intrusion Prevention.

Intrusion Prevention (IP)

Intrusion Prevention is the administrative designation reflecting the completion of the physical effort required to minimize the addition of liquids into an inactive storage tank, process vault, sump, catch tank, or diversion box. Under no circumstances are electrical or instrumentation devices disconnected or disabled during the intrusion prevention process (with the exception of the electrical pump), in accordance with WHC-SD-WM-SAR-006 REV 2, *Single-Shell Tank Isolation Safety Analysis Report*, March 1986.

TANK INTEGRITY

Sound

The integrity classification of a waste storage tank for which surveillance data indicate no loss of liquid attributed to a breach of integrity.

Assumed Leaker
The integrity classification of a waste storage tank for which surveillance data indicate a loss of liquid attributed to a breach of integrity.

Assumed Re-Leaker
A condition that exists after a tank has been declared as an "assumed leaker" and then the surveillance data indicates a new loss of liquid attributed to a breach of integrity.

TANK INVESTIGATION

Intrusion
A term used to describe the infiltration of liquid into a waste tank.

SURVEILLANCE INSTRUMENTATION

Drywells
Drywells are vertical boreholes with 6-in. (internal diameter) carbon steel casings positioned radially around SSTs. Periodic monitoring is done by gamma radiation or neutron sensors to obtain scan profiles of radiation or moisture in the soil as a function of well depth, which could be indicative of tank leakage. These wells range between 50 and 250 ft in depth, and are monitored between the range of 50 to 150 ft. The wells are sealed when not in use. They are called drywells because they do not penetrate to the water table and are therefore usually "dry." There are 759 drywells which are monitored on various frequencies.

Laterals
Laterals are horizontal drywells positioned under single-shell waste storage tanks to detect radionuclides in the soil which could be indicative of tank leakage. These drywells are monitored by radiation detection probes. Laterals are 4-in. inside diameter steel pipes located 8 to 10 ft below the tank's concrete base. There are three laterals per tank. Laterals are located only in A and SX farms.

Surface Levels
The surface level measurements in all waste storage tanks are monitored by manual or automatic conductivity probes, and recorded and transmitted or entered into the Computer Automated Surveillance System (CASS).

Automatic FIC
An automatic waste surface level measurement device is manufactured by the Food Instrument Company (FIC). The instrument consists of a conductivity electrode (plummet) connected to a calibrated steel tape, a steel tape reel housing and a controller that automatically raises and lowers the plummet to obtain a waste surface level reading. The controller can provide a digital display of the data

9413279.0075

and also transmit the reading to the CASS. Some tanks have gauges connected to CASS and others are read manually.

Annulus

The annulus is the space between the inner and outer shells on DSTs only. Drain channels in the insulating and/or supporting concrete carry any leakage to the annulus space where conductivity probes are installed. Alarms from the annunciators are received by CASS. Continuous Air Monitoring (CAM) alarms are also located in the annulus. The annulus conductivity probes and radiation detectors are the primary means of leak detection for all DSTs.

Liquid Observation Well (LOW)

In-tank liquid observation wells are used for monitoring the interstitial liquid level (ILL) in single-shell waste storage tanks. The wells are usually constructed of fiberglass or TEFZEL*-reinforced epoxy-polyester resin. There are a few LOWs constructed of steel. LOWs are sized to extend to within 1 in. of the bottom of the waste tank, are sealed at their bottom ends and have a nominal outside diameter of 3.5 in. Two probes are used to monitor changes in the ILL; gamma and neutron, which can indicate intrusions or leakage by increases or decreases in the ILL. There are 58 LOWs (56 are in operation) installed in SSTs that contain or are capable of containing greater than 50,000 gal of drainable interstitial liquid, and in two DSTs only. The LOWs installed in two DSTs, (102-SY and 103-AW Tanks), are constructed of steel and are used for special, rather than routine, surveillance purposes only.

Thermocouple (TC)

A thermocouple is a thermoelectric device used to measure temperature. More than one thermocouple on a device (probe) is called a thermocouple tree. In DSTs there may be one or more thermocouple trees in risers in the primary tank. In addition, in DSTs only, there are thermocouple elements installed in the insulating concrete, the lower primary tank knuckle, the secondary tank concrete foundation, and in the outer structural concrete. These monitor temperature gradients within the concrete walls, bottom of the tank, and the domes. In SSTs, one or more thermocouples may be installed directly in a tank, although some SSTs do not have any trees installed. A single thermocouple (probe) may be installed in a riser, or lowered down an existing riser or LOW. There are also four thermocouple laterals beneath Tank 105-A in which temperature readings are taken in 34 thermocouples.

In-tank Photography

In-tank photographs may be taken to aid in resolving in-tank measurement anomalies and determine tank integrity. Photographs help determine sludge and liquid levels by visual examination.

---

*TEFZEL, a trademark of E. I. du Pont de Nemours & Company

9413279.0079

TERMS/ACRONYMS

CASS	Computer Analysis Surveillance System
OSD	Operating Specifications Document
OSR	Operational Safety Requirements (OSRs are sections in SARs - see below)
SAR	Safety Analysis Reports
TMACS	Tank Monitor and Control System
TPA	Hanford Federal Facility Consent and Compliance Order, "Washington State Department of Ecology, U. S. Environmental Protection Agency, and U. S. Department of Energy," 1992 (Tri-Party Agreement)
USQ	Unreviewed Safety Question
Wyden Amendment	"Safety Measures for Waste Tanks at Hanford Nuclear Reservation," Section 3137 of the National Defense Authorization Act for Fiscal Year 1991, November 5, 1990, Public Law 101-510.

9413279.0077

4. INVENTORY AND STATUS BY TANK - VOLUME CALCULATIONS/DEFINITIONS FOR TABLE E-5 (SINGLE-SHELL TANKS)

COLUMN HEADING	VOLUME CALCULATIONS/DEFINITIONS
Total Waste	Solids volume plus Supernatant liquid. Solids include sludge and saltcake (see definitions below)
Supernatant Liquid	Drainable Liquid Remaining minus Drainable Interstitial. Supernate is the clear liquid floating on the surface of the waste. Supernate is usually derived by subtracting the solids, level measurement from the liquid level measurement. In some cases, the supernatant volume includes floating solid crusts because their volume cannot be measured. Photographs are useful in estimating the liquid volumes; the are of solids covered and the average depth can be estimated.

COLUMN HEADING	VOLUME CALCULATIONS/DEFINITIONS
Drainable Interstitial Liquid	Drainable Liquid Remaining minus Supernate. Drainable interstitial liquid is calculated based on the saltcake and sludge volumes, using average porosity values or actual data for each tank, when available. Interstitial liquid is liquid that fills the interstitial spaces of the solids waste. Drainable interstitial liquid is calculated based on the saltcake and sludge volumes in the tank. The sum of the interstitial liquid contained in saltcake and sludge is the initial volume of drainable interstitial liquid. The volume reported as Drainable Interstitial Liquid is the initial volume of drainable interstitial liquid minus interstitial liquid removed by pumping.
Pumped This Month	Net total gallons of liquid pumped from the tank during the month. If supernate is present, pump production is first subtracted from the supernatant volume. The remainder is then subtracted from the drainable interstitial liquid volume. The total pumped volume is subtracted from drainable liquid remaining and pumpable liquid remaining. Pump production takes into account the amount of water added to the tank during the month (if any).
Total Pumped	Cumulative net total gallons of liquid pump from 1979 to date.
Drainable Liquid Remaining	Supernate plus Drainable Interstitial. (See Supernatant Liquid and Drainable Interstitial Liquid above for definitions). The total Drainable Liquid Remaining is the sum of drainable interstitial liquid and supernate minus total gallons pumped.
Pumpable Liquid Remaining	Drainable Liquid Remaining minus undrainable heel volume. (Dish bottom tanks have a "heel" where liquids can collect: flat bottom tanks do not). (See Drainable Liquid Remaining and Pumped this Month for definitions). Not all drainable interstitial liquid is pumpable. It is assumed that drainable interstitial liquid on top of the undrainable heel in sludge or saltcake, is not jet pumpable. Therefore, pumpable interstitial liquid is the initial volume of drainable interstitial liquid minus the amount of interstitial liquid on top of the heel. The volume shown as Pumpable Liquid Remaining is the sum of pumpable interstitial liquid and supernate minus total gallons pumped.

9413279.0078

COLUMN HEADING	VOLUME CALCULATIONS/DEFINITIONS
Sludge	Solids formed during sodium hydroxide additions to waste. Sludge usually was in the form of suspended solids when the waste was originally received in the tank from the waste generator. In-tank photographs may be used to estimate the volume.
Saltcake	Results from crystallization and precipitation after concentration of liquid waste, usually in an evaporator. If saltcake is layered over sludge, it is only possible to measure total solids volume. In-tank photographs may be used to estimate the saltcake volume.
Solids Volume Update	Indicates the latest update of any change in the solids volume.
Solids Update Source - See Footnote	Indicates the source or basis of the latest solids volume update.
Last Photo Date	Date of latest in-tank photographs taken.
See Footnotes for These Changes	Indicates any change made the previous month. A footnote explanation for the change follows the Inventory and Status by Tank section (Table E-5).

9413279.0079

This page intentionally left blank.

9413279.0080

APPENDIX D

TANK FARM CONFIGURATION, STATUS, AND FACILITY CHARTS

9413279.0081

This page intentionally left blank.

9413279.0082

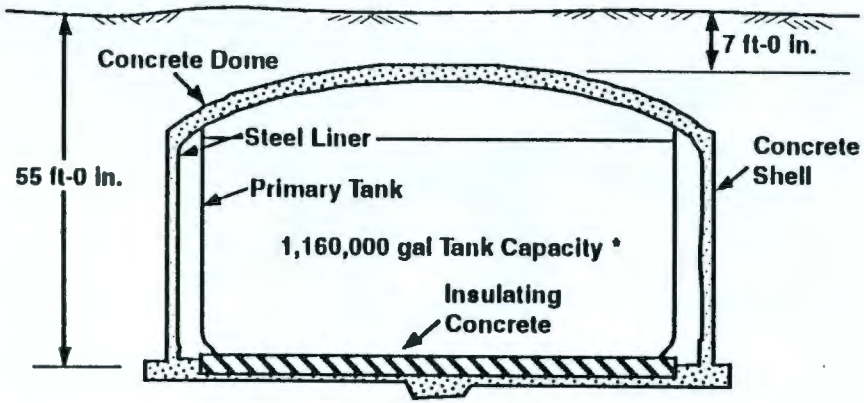

75 ft Diameter Double-Shell Tank
Tank Farms: AN, AP, AW, AY, AZ, SY

* AY and AZ Have a Tank Capacity of 1,000,000 gal

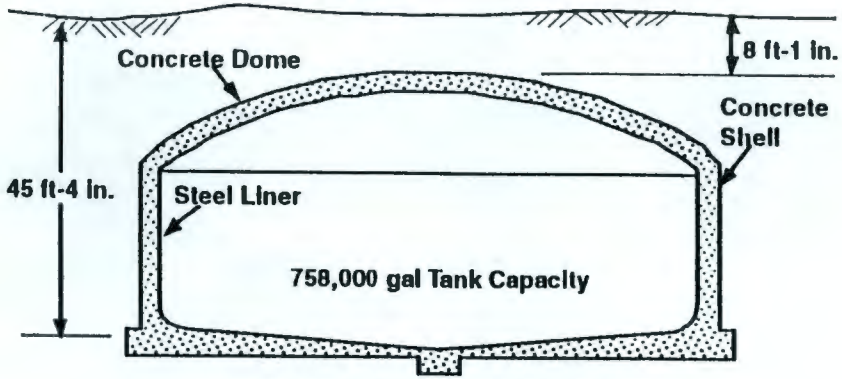

75 ft Diameter Single-Shell Tank
Tank Farms: BY, S, TX, TY

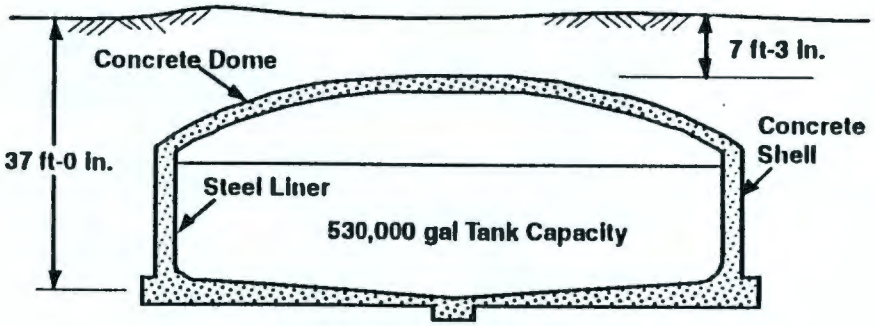

75 ft Diameter Single-Shell Tank
Tank Farms: B, BX, C, T, U

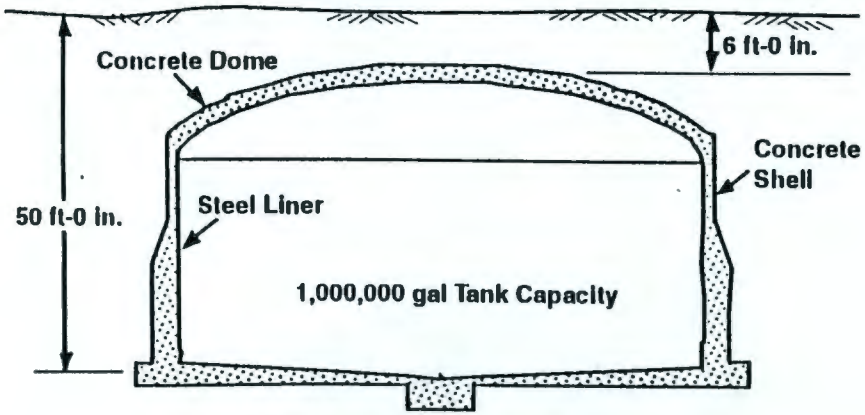

75 ft Diameter Single-Shell Tank
Tank Farms: A*, AX*, SX

* A and AX have flat bottoms

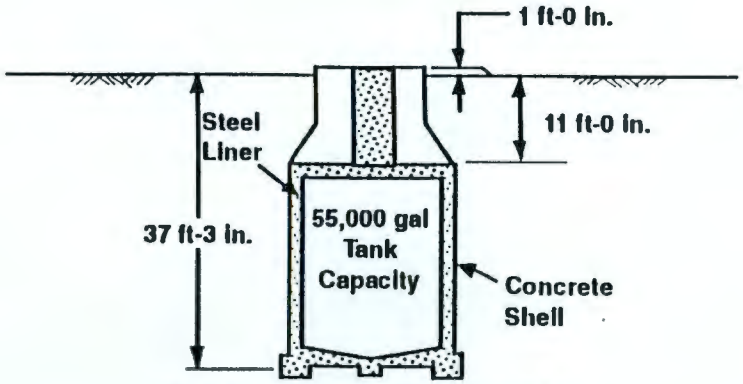

20 ft Diameter Single-Shell Tank
Tank Farms: B, C, T, U

Figure D-1. High-Level Waste Tank Configuration

29103062.1a

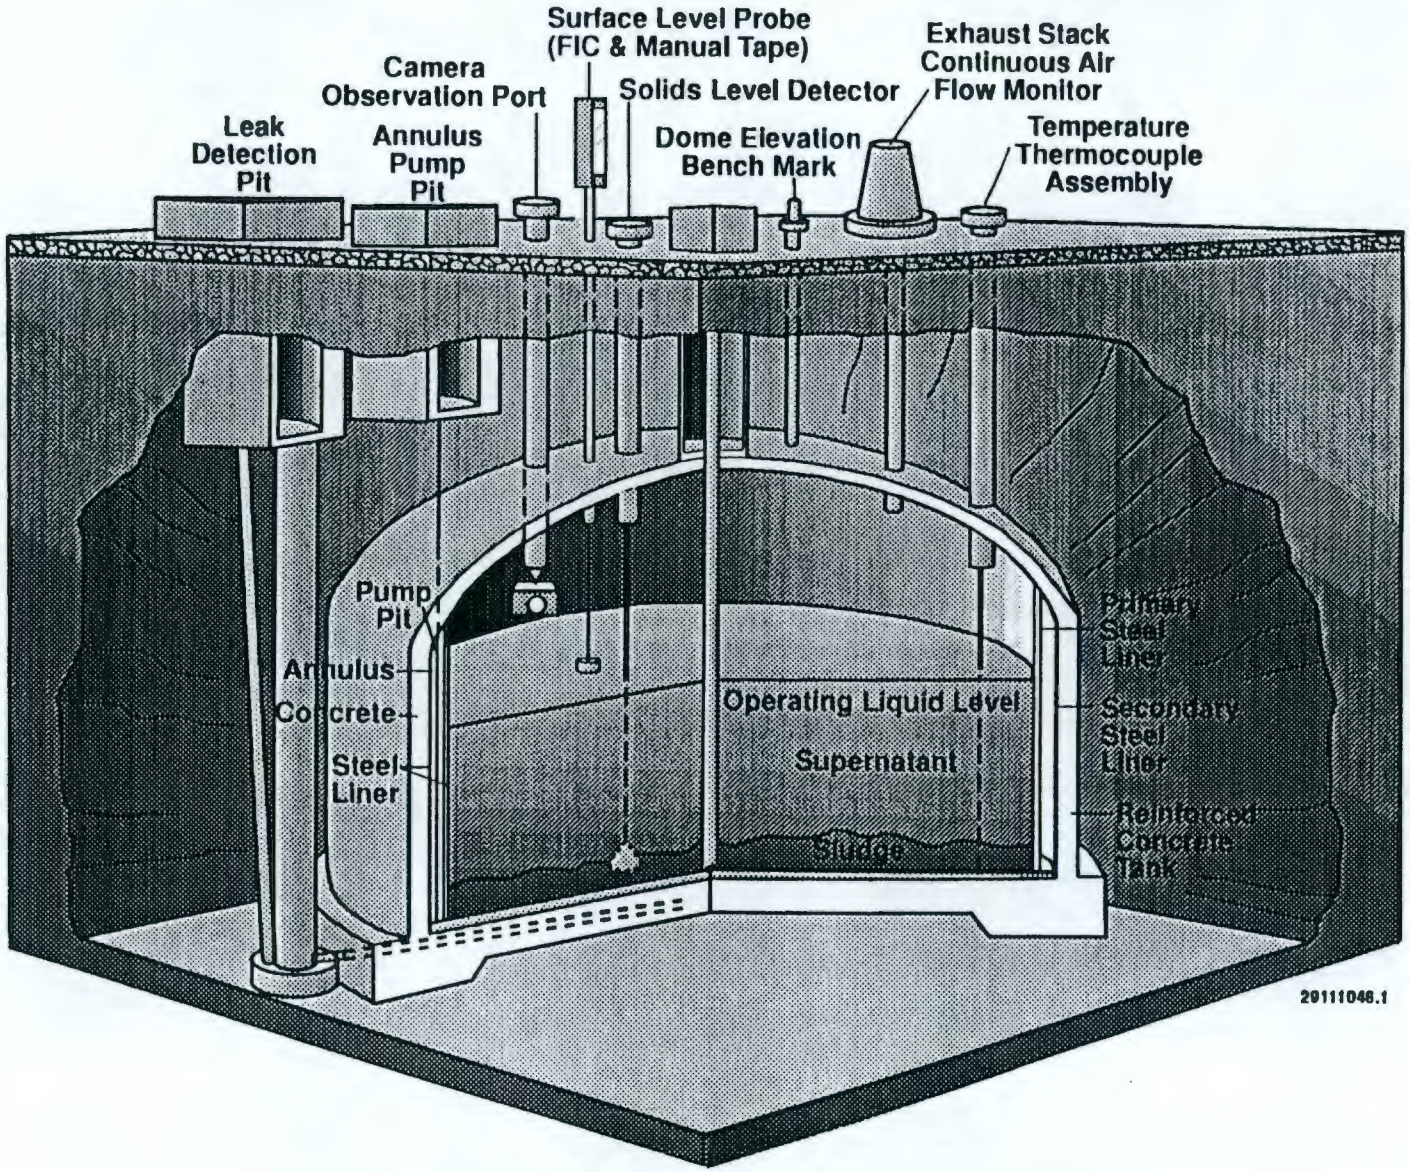

Figure D-2. Double-Shell Tank Instrumentation Configuration

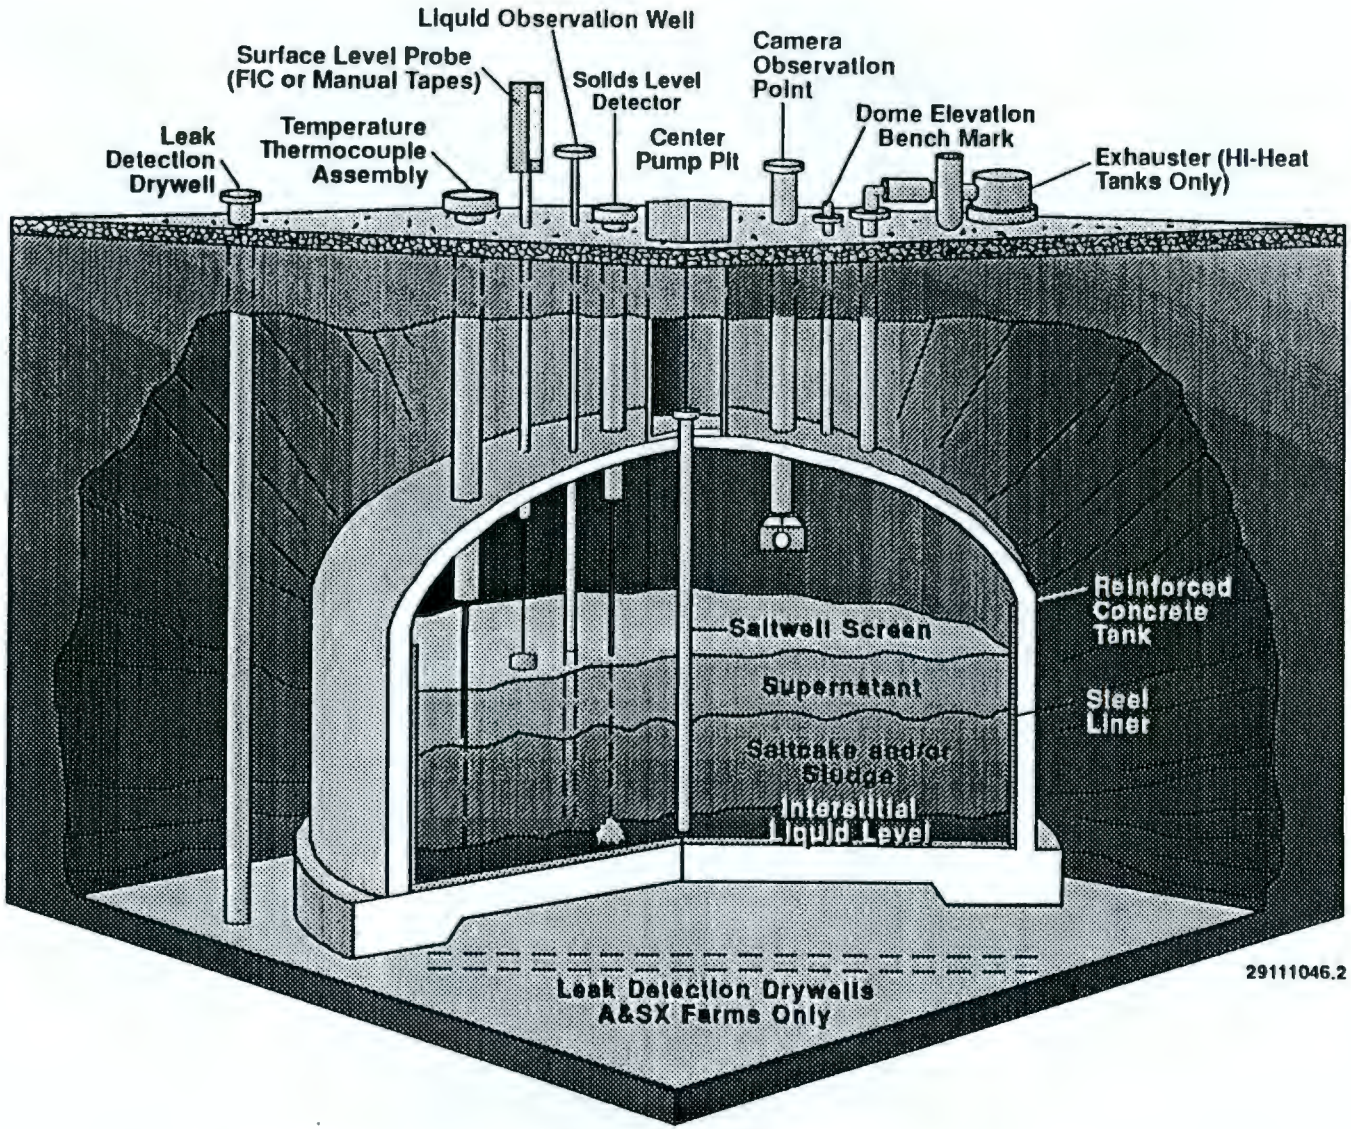

Figure D-3. Single-Shell Tank Instrumentation Configuration

This page intentionally left blank

9413279.0086

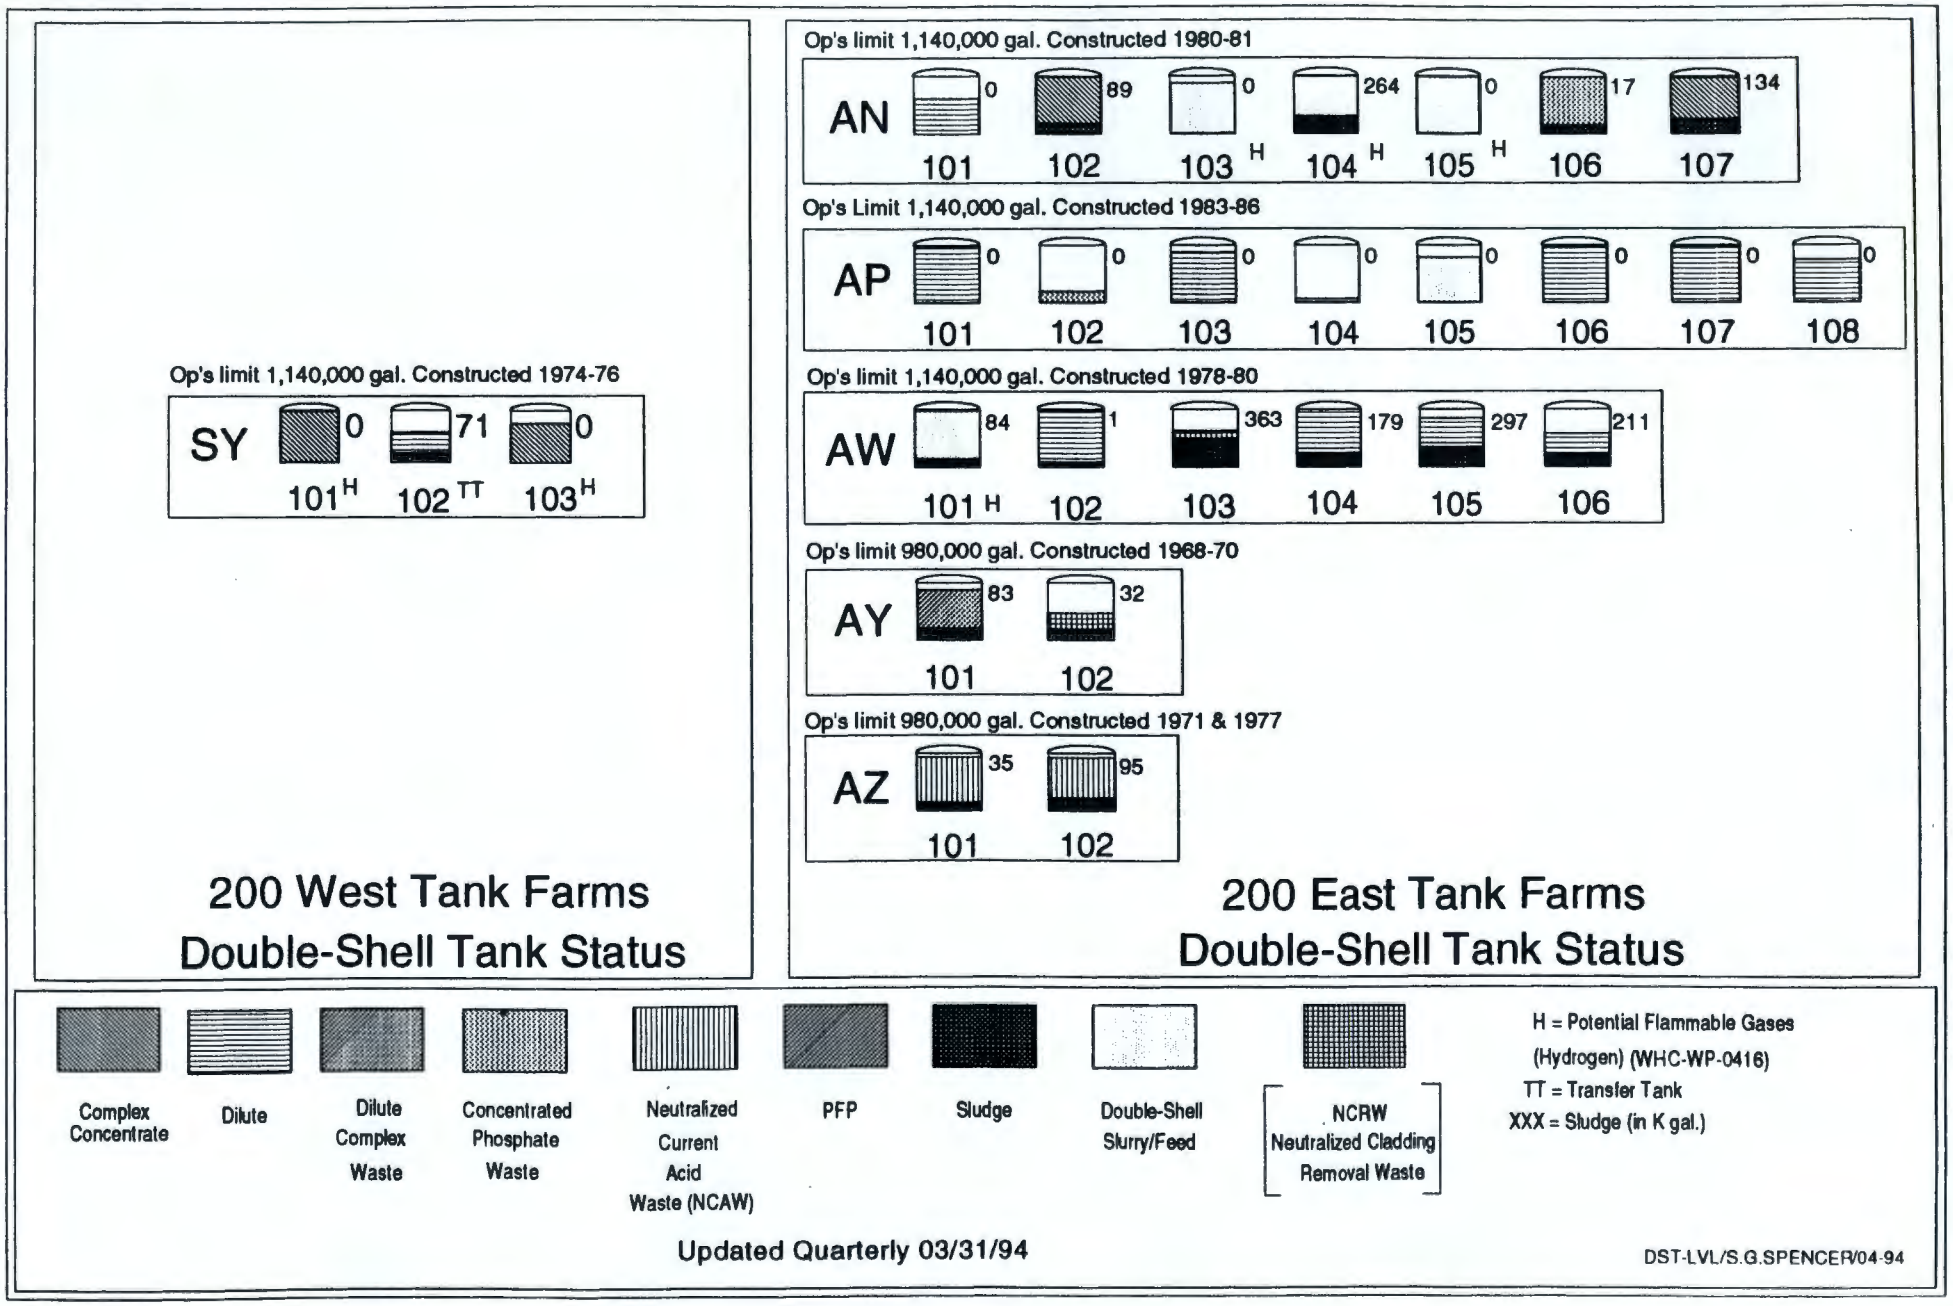

Figure D-4. Double-Shell Tank Status

THIS PAGE INTENTIONALLY
LEFT BLANK

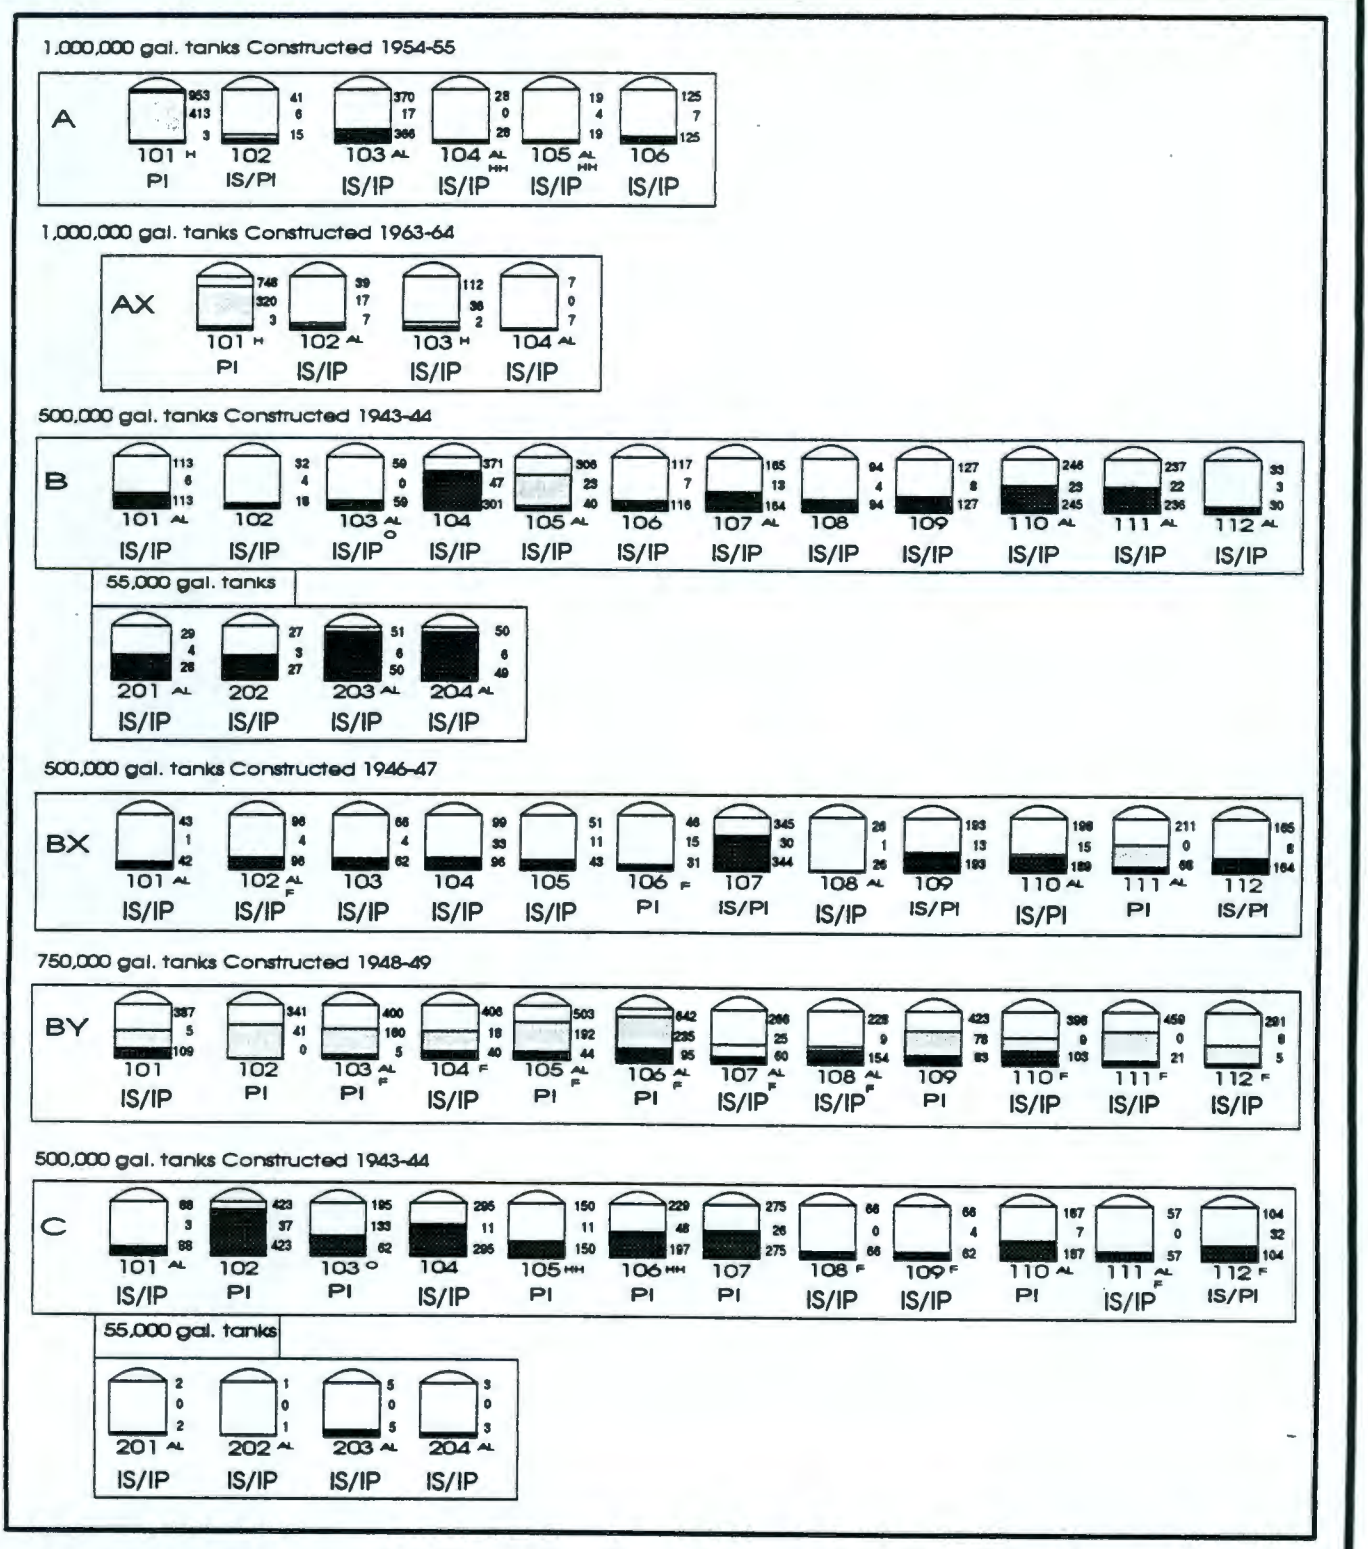

Figure D-5. 200E Single-Shell Tank Status

THIS PAGE INTENTIONALLY
LEFT BLANK

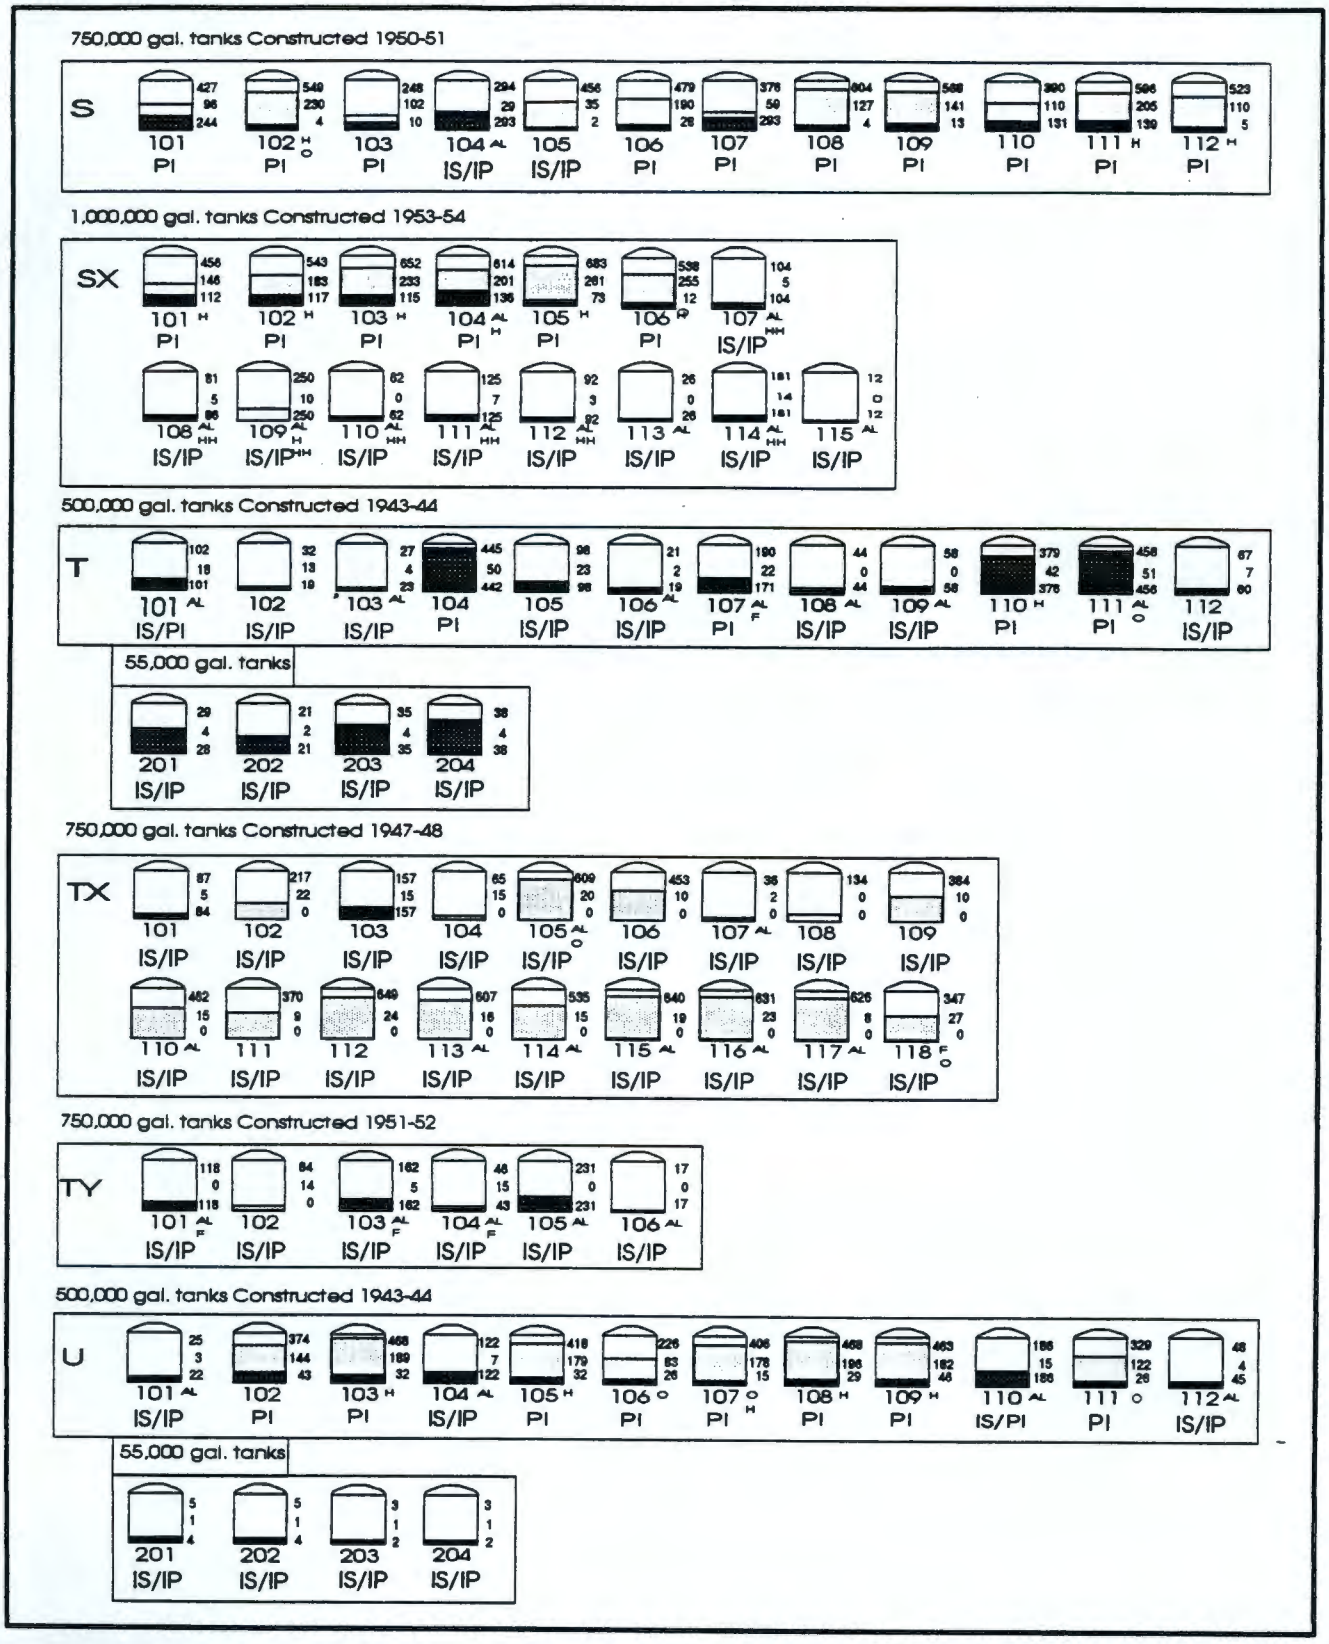

Fig. D-6. 200W Single-Shell Tank Status

9413279.0089

THIS PAGE INTENTIONALLY
LEFT BLANK

Hanford Tank Farm Facilities

200 East

Note: All single-shell tanks were removed from service (not allowed to receive waste) on or before November 21, 1980

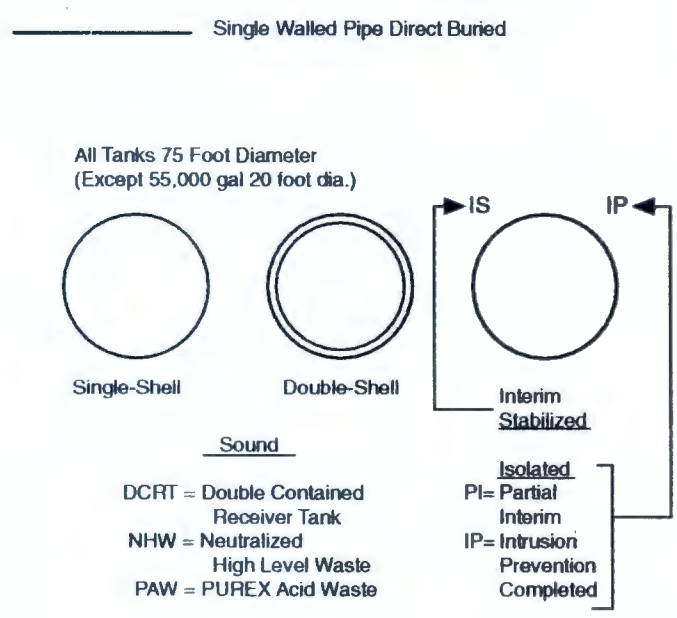

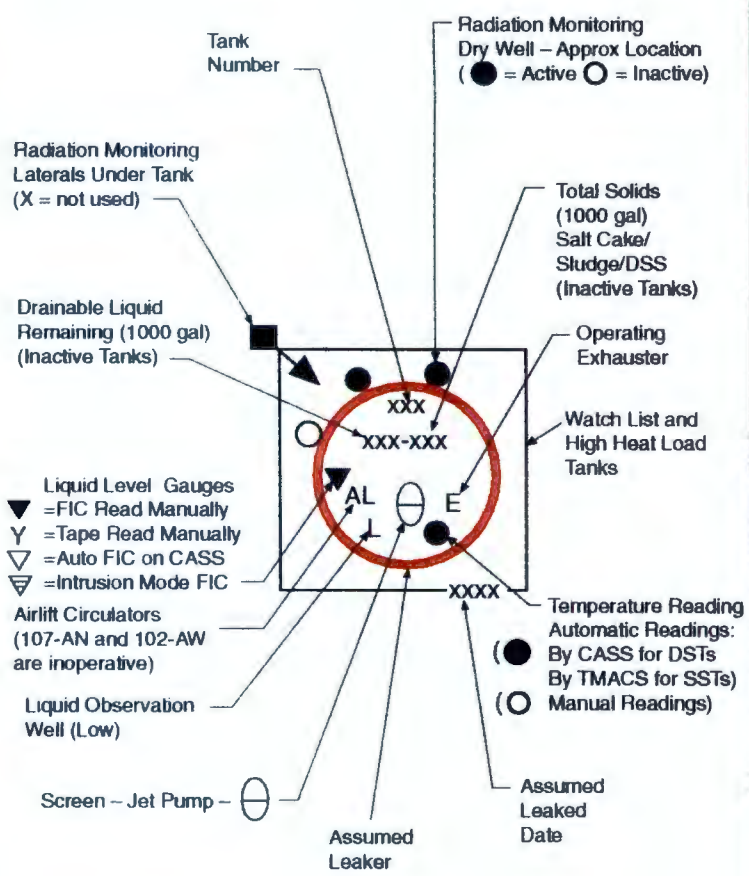

Watch List Tanks

- Ferrocyanide
- H2/Flammable gases (109-SX has potential only-other tanks vent thru it)
- Organics
- High Heat - 106-C only on Watch List (cooling water added)

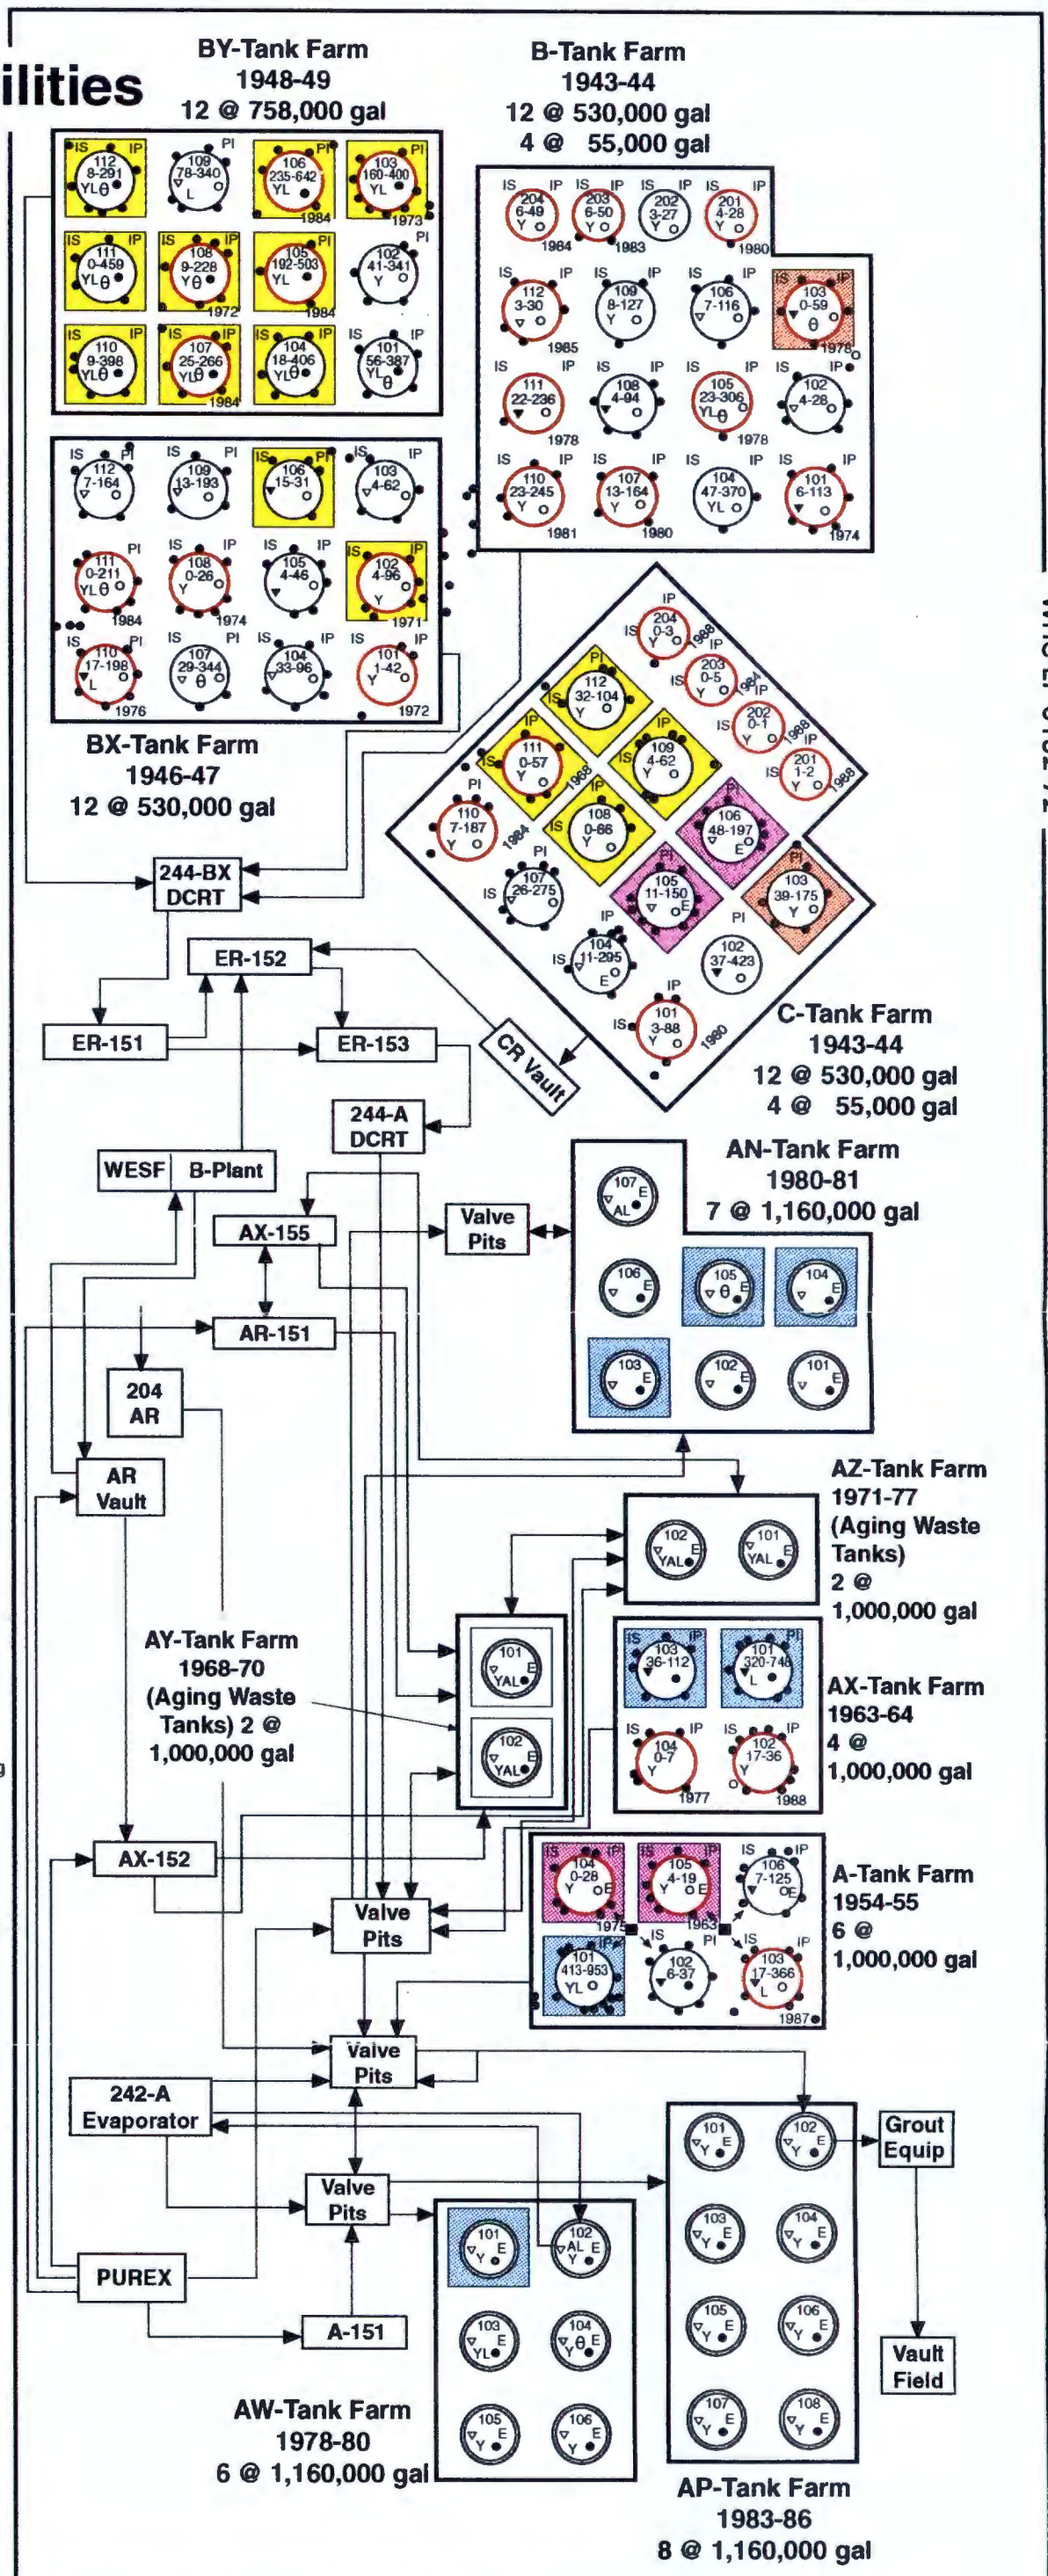

Status as of March 31, 1994 - Updated Monthly
Issued by WHC/WTPE

29310073.2C

THIS PAGE INTENTIONALLY
LEFT BLANK

Hanford Tank Farm Facilities

200 West

Note: All single-shell tanks were removed from service (not allowed to receive waste) on or before November 21, 1980

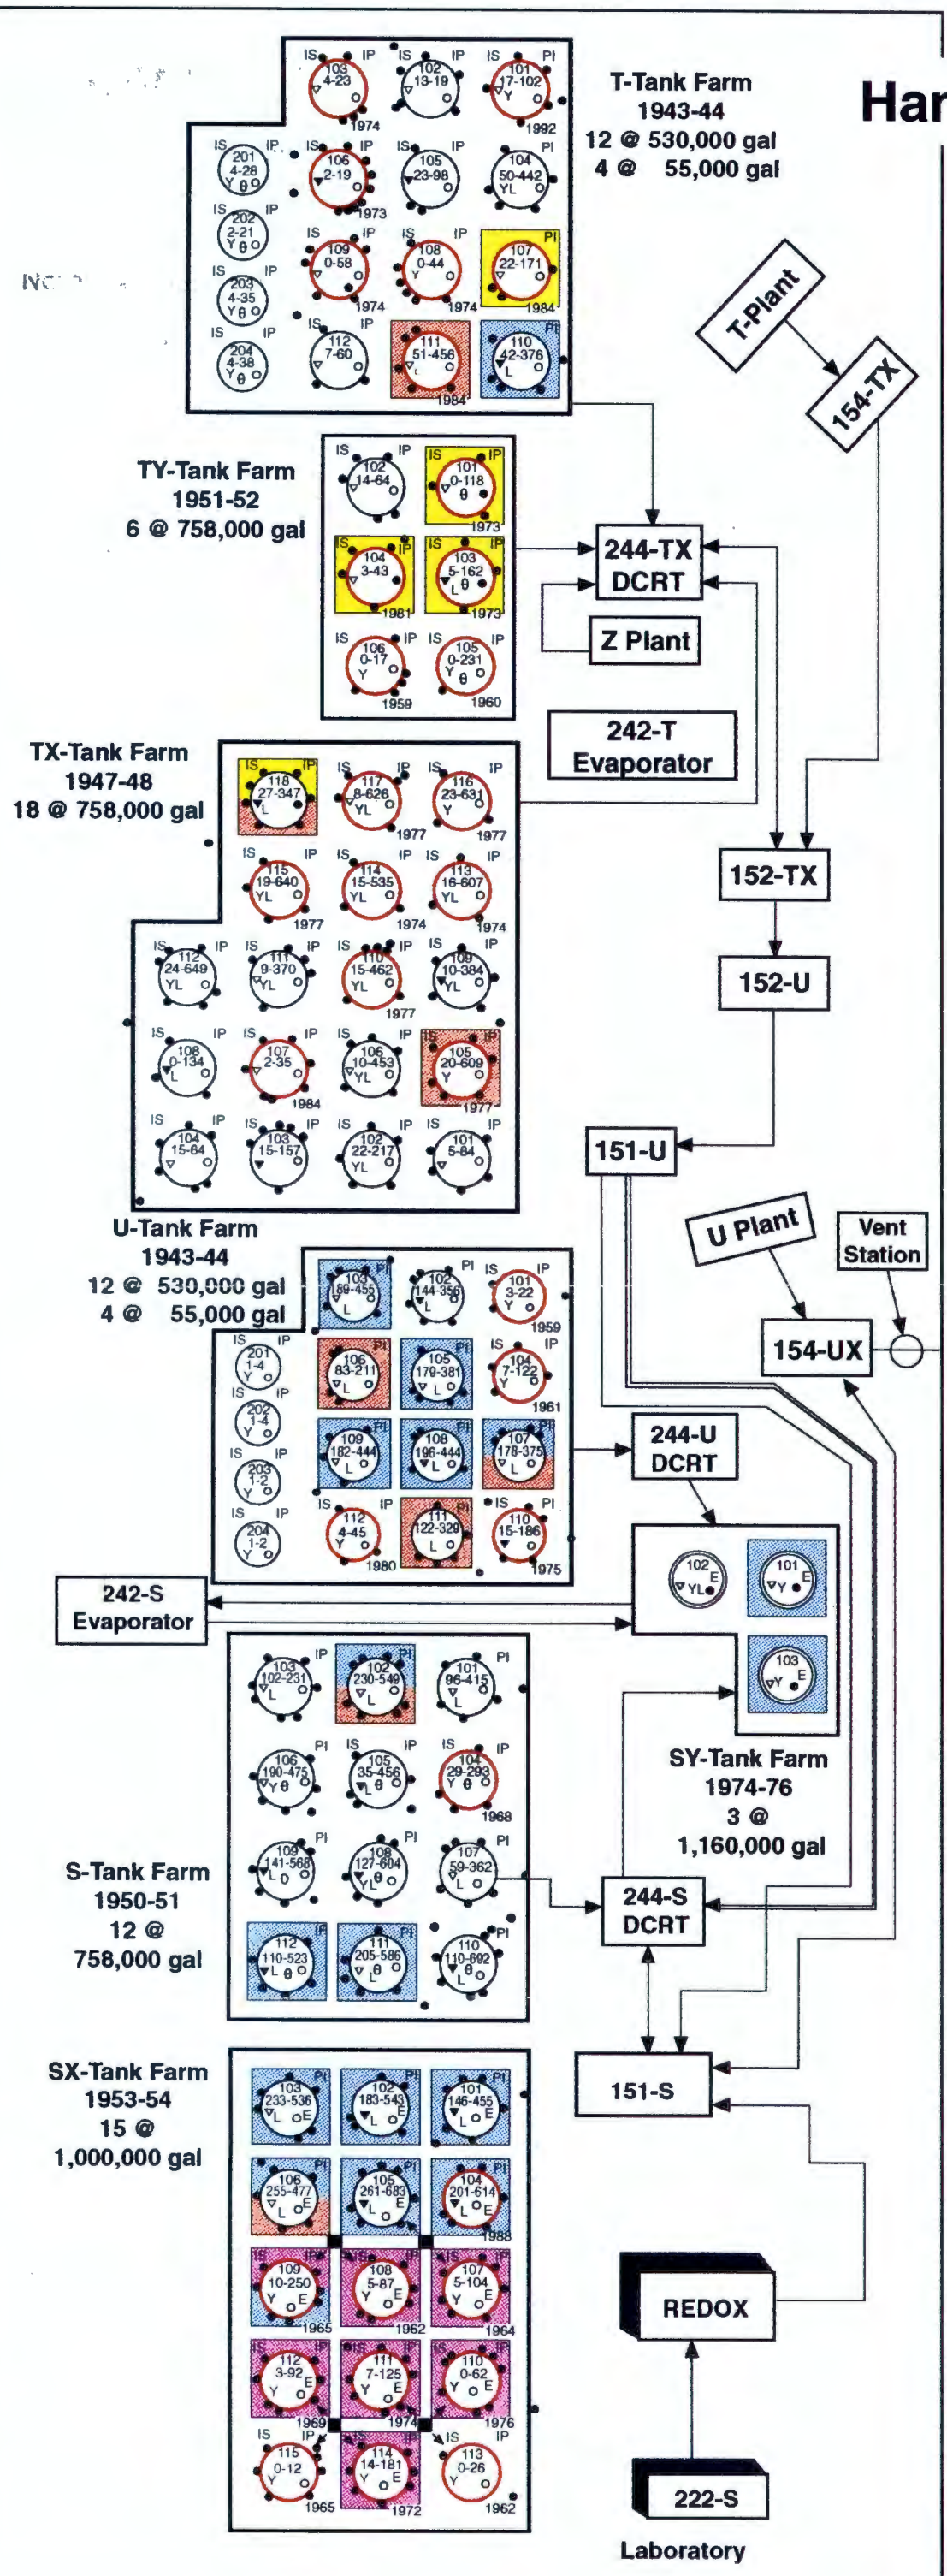

Double Walled Pipe

Single Walled Pipe Direct Buried

All Tanks 75 Foot Diameter
(Except 55,000 gal 20 foot dia.)

Single-Shell | Double-Shell | Interim Stabilized

Sound

DCRT = Double Contained Receiver Tank
NHW = Neutralized High Level Waste
PAW = PUREX Acid Waste

Isolated
PI= Partial Interim
IP= Intrusion Prevention Completed

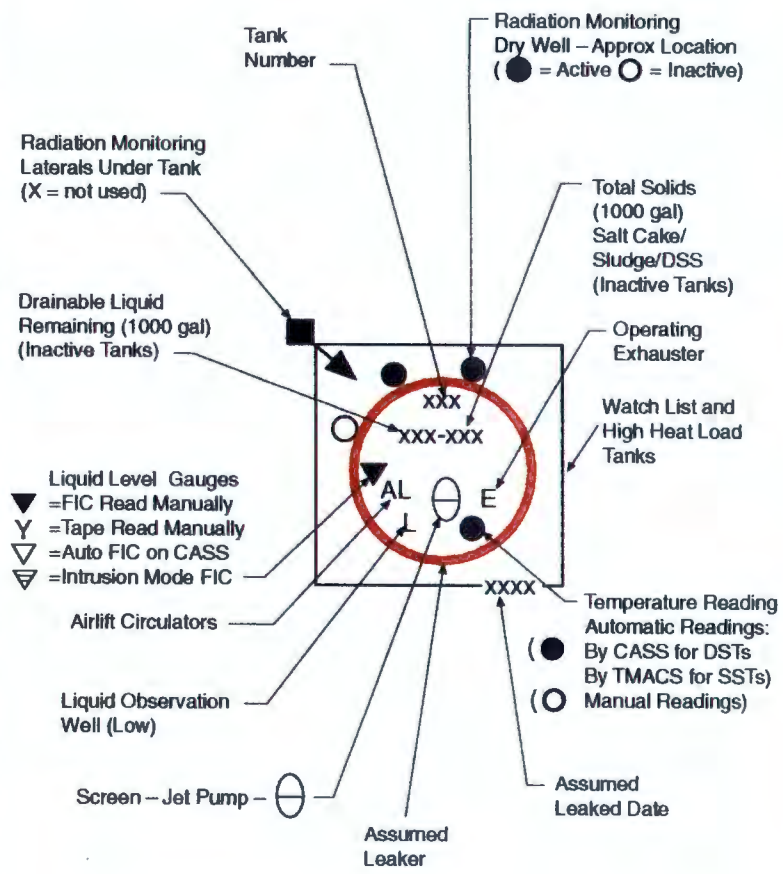

Watch List Tanks

- Ferrocyanide
- H2/Flammable gases (109-SX has potential only-other tanks vent thru it)
- Organics
- High Heat - 106-C only on Watch List (cooling water added)

Status as of March 31, 1994 - Updated Monthly
Issued by WHC/WTPE

29310073.1C

THIS PAGE INTENTIONALLY
LEFT BLANK

APPENDIX E

MONTHLY SUMMARY
TANK USE SUMMARY
INVENTORY SUMMARY BY TANK FARM
INVENTORY AND STATUS BY TANK

9413279.0092

This page intentionally left blank.

9413279.0093

TABLE E-1. MONTHLY SUMMARY

TANK STATUS

March 31, 1994

	200 EAST AREA	200 WEST AREA	TOTAL
IN SERVICE	25	3	28 (2)
OUT OF SERVICE	66	83	149
SOUND	59	51	110
ASSUMED LEAKER	32	35	67
INTERIM STABILIZED	51	55	106 (1)
ISOLATED			
PARTIAL INTERIM	21	30	51
INTRUSION PREVENTION COMPLETED	45	53	98

WASTE VOLUMES (Kgallons)

		200 EAST AREA	200 WEST AREA	TOTAL	SST TANKS	DST TANKS	TOTAL
SUPERNATANT							
AGING	Aging waste	1793	0	1793	0	1793	1793
CC	Complexant concentrate waste	1933	177	2110	3	2107	2110
CP	Concentrated phosphate waste	1107	0	1107	0	1107	1107
DC	Dilute complexed waste	798	1	799	1	798	799
DN	Dilute non-complexed waste	9619	0	9619	0	9619	9619
DN/PD	Dilute non-complex/PUREX TRU solids	1026	0	1026	0	1026	1026
DN/PT	Dilute non-complex/PFP TRU solids	0	676	676	0	676	676
DSSF	Double-shell slurry feed	3822	48	3870	57	3813	3870
NCPLX	Non-complexed waste	214	293	507	507	0	507
TOTAL SUPERNATANT		20312	1195	21507	568	20939	21507
SOLIDS							
Double-shell slurry		937	1103	2040	0	2040	2040
Sludge		8206	5930	14136	12181	1955	14136
Saltcake		6577	17529	24106	23346	760	24106
TOTAL SOLIDS		15720	24562	40282	35527	4755	40282
TOTAL WASTE		36032	25757	61789	36095	25694	61789
AVAILABLE SPACE IN TANKS		4757	829	5586	0	5586 (2)	5586
DRAINABLE INTERSTITIAL		2205	4492	6697	6258	439	6697
DRAINABLE LIQUID REMAINING		22519	5687	28206	6828	21378	28206

(1) Includes six tanks that do not meet current established supernatant and interstitial liquid stabilization criteria, B-104, 110, 111, T-102, T-112, and U-110.
(2) Includes six double-shell tanks on Hydrogen Watch List not currently allowed to receive waste, 103-AN, 104-AN, 105-AN, 101-AW, 101-SY, and 103-SY.
Note: +/- 1 Kgal differences are the result of computer rounding

TABLE E-2. TANK USE SUMMARY

March 31, 1994

TANK FARMS	IN SERVICE	OUT OF SERVICE	SOUND	ASSUMED LEAKER	ISOLATED TANKS PARTIAL INTERIM	ISOLATED TANKS INTRUSION PREVENTION	INTERIM STABILIZED TANKS
EAST							
A	0	6	3	3	2	4	5
AN	7 (2)	0	7	0	0	0	0
AP	8	0	8	0	0	0	0
AW	6 (2)	0	6	0	0	0	0
AX	0	4	2	2	1	3	3
AY	2	0	2	0	0	0	0
AZ	2	0	2	0	0	0	0
B	0	16	6	10	0	16	16 (1)
BX	0	12	7	5	6	6	10 (1)
BY	0	12	7	5	5	7	7
C	0	16	9	7	7	9	10
Total	25	66	59	32	21	45	51
WEST							
S	0	12	11	1	10	2	2
SX	0	15	5	10	6	9	9
SY	3 (2)	0	3	0	0	0	0
T	0	16	9	7	5	11	12 (1)
TX	0	18	10	8	0	18	18
TY	0	6	1	5	0	6	6
U	0	16	12	4	9	7	8 (1)
Total	3	83	51	35	30	53	55
TOTAL	28	149	110	67	51	98	106

(1) Includes six tanks that do not meet current established supernatant and interstitial liquid stabilization criteria (B-104, 110, 111, T-102, 112, and U-110).

(2) Six Double-Shell Tanks on the Hydrogen Tank Watch List are not currently in service (AN-103, 104, 105, AW-101, SY-101 and 103).

TABLE E-3. INVENTORY SUMMARY BY TANK FARM

March 31, 1994

TANK FARM	TOTAL WASTE	AVAIL SPACE	SUPERNATANT LIQUID VOLUMES (Kgallons) AGING	CC	CP	DC	DN	DN/PD	DN/PT	DSSF	NCPLX	TOTAL	SOLIDS VOLUME DSS	SLUDGE	SALT CAKE	TOTAL
EAST																
A	1537	0	0	0	0	0	0	0	0	9	0	9	0	556	972	1528
AN	6053	1927	0	1930	4	0	740	0	0	1938	0	4612	937	504	0	1441
AP	7500	1620	0	0	1103	0	5577	0	0	820	0	7500	0	0	0	0
AW	6035	805	0	0	0	0	2623	1026	0	1055	0	4704	0	1135	196	1331
AX	906	0	0	3	0	0	0	0	0	0	0	3	0	19	884	903
AY	1592	368	0	0	0	798	679	0	0	0	0	1477	0	115	0	115
AZ	1923	37	1793	0	0	0	0	0	0	0	0	1793	0	130	0	130
B	2057	0	0	0	0	0	0	0	0	0	15	15	0	1697	345	2042
BX	1539	0	0	0	0	0	0	0	0	0	30	30	0	1354	155	1509
BY	4744	0	0	0	0	0	0	0	0	0	0	0	0	719	4025	4744
C	2146	0	0	0	0	0	0	0	0	0	169	169	0	1977	0	1977
Total	36032	4757	1793	1933	1107	798	9619	1026	0	3822	214	20312	937	8206	6577	15720
WEST																
S	5510	0	0	0	0	0	0	0	0	17	41	58	0	1166	4286	5452
SX	4425	0	0	0	0	1	0	0	0	0	62	63	0	1254	3108	4362
SY	2591	829	0	177	0	0	0	0	676	0	0	853	1103	71	564	1738
T	2034	0	0	0	0	0	0	0	0	0	45	45	0	1989	0	1989
TX	7009	0	0	0	0	0	0	0	0	0	5	5	0	241	6763	7004
TY	638	0	0	0	0	0	0	0	0	0	3	3	0	571	64	635
U	3550	0	0	0	0	0	0	0	0	31	137	168	0	638	2744	3382
Total	25757	829	0	177	0	1	0	0	676	48	293	1195	1103	5930	17529	24562
TOTAL	61789	5586	1793	2110	1107	799	9619	1026	676	3870	507	21507	2040	14136	24106	40282

Note: +/- 1 Kgal differences are the result of computer rounding

TABLE E-4. INVENTORY AND STATUS BY TANK
DOUBLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME			VOLUME DETERMINATION				
TANK	WASTE MATL	TANK INTEGRTY	TANK USE	EQUIVALENT WASTE INCHES	TOTAL WASTE (Kgal)	AVAIL SPACE (Kgal)	SUPERNATANT LIQUID (Kgal)	DRAINABLE INTERSTIT. (Kgal)	DRAINABLE LIQUID REMAIN (Kgal)	PUMPABLE LIQUID REMAIN (Kgal)	DSS SLUDGE (Kgallons)	SALT CAKE	LIQUID VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
								AN TANK FARM STATUS									
AN-101	DN	SOUND	DRCVR	269.1	740	400	740	0	740	740	0	0	0	FM	S	08/22/89	0/ 0/ 0	
AN-102	CC	SOUND	CWHT	396.4	1090	50	1001	3	1004	1001	0	89	0	FM	S	08/22/89	0/ 0/ 0	
AN-103	DSS	SOUND	CWHT	346.5	953	187	16	0	16	16	937	0	0	FM	S	08/22/89	10/29/87	
AN-104	DSSF	SOUND	CWHT	384.0	1056	84	792	25	817	795	0	264	0	FM	S	08/22/89	08/19/88	
AN-105	DSSF	SOUND	CWHT	410.9	1130	10	1130	0	1130	1130	0	0	0	FM	S	10/22/84	01/26/88	
AN-106	CP	SOUND	CWHT	7.6	21	1119	4	0	4	4	0	17	0	FM	S	08/22/89	0/ 0/ 0	
AN-107	CC	SOUND	CWHT	386.5	1063	77	929	9	938	929	0	134	0	FM	S	08/22/89	09/01/88	
7 DOUBLE-SHELL TANKS				TOTALS:	6053	1927	4612	37	4649	4615	937	504	0					
								AP TANK FARM STATUS									
AP-101	DN	SOUND	DRCVR	385.5	1060	80	1060	0	1060	1060	0	0	0	FM	S	05/01/89	0/ 0/ 0	
AP-102	CP	SOUND	GRTFD	401.1	1103	37	1103	0	1103	1103	0	0	0	FM	S	07/11/89	0/ 0/ 0	
AP-103	DN	SOUND	DRCVR	411.3	1131	9	1131	0	1131	1131	0	0	0	FM	S	10/13/88	0/ 0/ 0	
AP-104	DN	SOUND	GRTFD	6.5	18	1122	18	0	18	18	0	0	0	FM	S	10/13/88	0/ 0/ 0	
AP-105	DSSF	SOUND	CWHT	298.2	820	320	820	0	820	820	0	0	0	FM	S	02/02/89	0/ 0/ 0	
AP-106	DN	SOUND	DRCVR	409.8	1127	13	1127	0	1127	1127	0	0	0	FM	S	10/13/88	0/ 0/ 0	
AP-107	DN	SOUND	DRCVR	403.6	1110	30	1110	0	1110	1110	0	0	0	FM	S	10/13/88	0/ 0/ 0	
AP-108	DN	SOUND	DRCVR	411.3	1131	9	1131	0	1131	1131	0	0	0	FM	S	10/13/88	0/ 0/ 0	
8 DOUBLE-SHELL TANKS				TOTALS:	7500	1620	7500	0	7500	7500	0	0	0					

TABLE E-4. INVENTORY AND STATUS BY TANK
DOUBLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME			VOLUME DETERMINATION				
TANK	WASTE MATL	TANK INTEGRTY	TANK USE	EQUIVA-LENT WASTE INCHES	TOTAL WASTE (Kgal)	AVAIL SPACE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	DSS SLUDGE (Kgallons)	SALT CAKE	LIQUID VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
								AW TANK FARM STATUS									
AW-101	DSSF	SOUND	CWHT	414.2	1139	1	1055	2	1057	1055	0	84	0	FM	S	10/22/84	03/17/88	
AW-102	DN	SOUND	EVFD	356.0	979	161	978	0	978	978	0	1	0	FM	S	02/29/84	02/02/83	
AW-103	DN/PD	SOUND	DRCVR	234.9	646	494	283	37	320	298	0	363	0	FM	S	02/01/89	0/ 0/ 0	
AW-104	DN	SOUND	DRCVR	408.4	1123	17	833	49	882	860	0	179	111	FM	S	03/05/87	02/02/83	
AW-105	DN/PD	SOUND	DRCVR	378.2	1040	100	743	29	772	750	0	297	0	FM	S	03/05/87	0/ 0/ 0	
AW-106	DN	SOUND	SRCVR	402.9	1108	32	812	42	854	832	0	211	85	FM	S	01/31/92	02/02/83	
6 DOUBLE-SHELL TANKS				TOTALS:	6035	805	4704	159	4863	4773	0	1135	196					
								AY TANK FARM STATUS									
AY-101	DC	SOUND	DRCVR	320.4	881	99	798	2	800	798	0	83	0	FM	S	02/02/87	12/28/82	
AY-102	DN	SOUND	DRCVR	258.5	711	269	679	0	679	679	0	32	0	FM	S	02/10/88	04/28/81	
2 DOUBLE-SHELL TANKS				TOTALS:	1592	368	1477	2	1479	1477	0	115	0					
								AZ TANK FARM STATUS									
AZ-101	AGING	SOUND	CWHT	349.1	960	20	925	0	925	925	0	35	0	FM	S	09/30/90	08/18/83	
AZ-102	AGING	SOUND	DRCVR	350.2	963	17	868	4	872	868	0	95	0	FM	S	06/04/92	12/24/84	
2 DOUBLE-SHELL TANKS				TOTALS:	1923	37	1793	4	1797	1793	0	130	0					

TABLE E-4. INVENTORY AND STATUS BY TANK
DOUBLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME			VOLUME DETERMINATION				
TANK	WASTE MATL	TANK INTEGRTY	TANK USE	EQUIVALENT WASTE INCHES	TOTAL WASTE (Kgal)	AVAIL SPACE (Kgal)	SUPERNATANT LIQUID (Kgal)	DRAINABLE INTERSTIT. (Kgal)	DRAINABLE LIQUID REMAIN (Kgal)	PUMPABLE LIQUID REMAIN (Kgal)	DSS SLUDGE (Kgallons)	SALT CAKE	LIQUID VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
SY TANK FARM STATUS																	
SY-101	CC	SOUND	CWHT	400.0	1100	40	10	237	247	241	530	0	560	FM	S	01/31/92	04/12/89
SY-102	DN/PT	SOUND	DRCVR	271.6	747	393	676	0	676	676	0	71	0	FM	S	05/12/87	04/29/81
SY-103	CC	SOUND	CWHT	270.5	744	396	167	0	167	167	573	0	4	FM	S	10/22/84	10/01/85
3 DOUBLE-SHELL TANKS				TOTALS:	2591	829	853	237	1090	1084	1103	71	564				
GRAND TOTAL					25694	5586	20939	439	21378	21242	2040	1955	760				

Note: +/- 1 Kgal differences are the result of computer rounding

Tank Farms	Available Space Calculations Used In This Document (Most Conservative)	Document SD-WM-TI-357* Operating Limit	Document SD-WM-TI-357* Tank Capacity	OSD-T-151-00007** Specification Limit
AN, AP, AW, SY	1,140,000 gal (414.5 in.)	1,144,000 gal (416 in.)	1,160,000 gal (421.8 in.)	1,160,500 gal (422 in.)
AY, AZ (Aging Waste)	980,000 gal (356.4 in.)	990,000 gal (360 in.)	1,000,000 gal (363.6 in.)	1,001,000 gal (364 in.)

* WHC-SD-WM-TI-357, "Waste Storage Tank Status and Leak Detection Criteria."
**WHC-OSD-T-151-00007, "Operating Specifications for 241-AN, AP, AW, AY, AZ, & SY Tank Farms."

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++ A FARM STATUS ++++++												
A-101	DSSF	SOUND	/PI	953	0	413	0.0	0.0	413	390	3	950	P	F	11/21/80		08/21/85	
A-102	DSSF	SOUND	IS/PI	41	4	2	0.0	39.5	6	0	15	22	P	FP	07/27/89	(1)	07/20/89	
A-103	DSSF	ASMD LKR	IS/IP	371	5	15	0.0	111.0	20	0	366	0	-	FP	06/03/88	(1)	12/28/88	
A-104	NCPLX	ASMD LKR	IS/IP	28	0	0	0.0	0.0	0	0	28	0	M	PS	01/27/78		06/25/86	
A-105	NCPLX	ASMD LKR	IS/IP	19	0	4	0.0	0.0	4	0	19	0	P	MP	08/23/79	(1)	08/20/86	
A-106	CP	SOUND	IS/IP	125	0	7	0.0	0.0	7	0	125	0	P	M	09/07/82		08/17/86	
6 SINGLE-SHELL TANKS			TOTALS	1537	9	441	0.0	150.5	450	390	556	972						
						++++++ AX FARM STATUS ++++++												
AX-101	DSSF	SOUND	/PI	748	0	320	0.0	0.0	320	298	3	745	P	F	05/06/82		08/18/87	
AX-102	CC	ASMD LKR	IS/IP	39	3	14	0.0	13.0	17	3	7	29	F	S	09/06/88		06/05/89	
AX-103	CC	SOUND	IS/IP	112	0	36	0.0	0.0	36	3	2	110	F	S	08/19/87		08/13/87	
AX-104	NCPLX	ASMD LKR	IS/IP	7	0	0	0.0	0.0	0	0	7	0	P	M	04/28/82		08/18/87	
4 SINGLE-SHELL TANKS			TOTALS:	906	3	370	0.0	13.0	373	304	19	884						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++ B FARM STATUS ++++++												
B-101	NCPLX	ASMD LKR	IS/IP	113	0	6	0.0	0.0	6	0	113	0	P	F	04/28/82		05/19/83	
B-102	NCPLX	SOUND	IS/IP	32	4	0	0.0	0.0	4	0	18	10	P	F	08/22/85	(1)	08/22/85	
B-103	NCPLX	ASMD LKR	IS/IP	59	0	0	0.0	0.0	0	0	59	0	F	F	02/28/85	(1)	10/13/88	
B-104	NCPLX	SOUND	IS/IP	371	1	46	0.0	0.0	47	40	301	69	M	M	06/30/85	(1)	10/13/88	
B-105	NCPLX	ASMD LKR	IS/IP	306	0	23	0.0	0.0	23	0	40	266	P	MP	12/27/84	(1)	05/19/88	
B-106	NCPLX	SOUND	IS/IP	117	1	6	0.0	0.0	7	0	116	0	F	F	03/31/85	(1)	02/28/85	
B-107	NCPLX	ASMD LKR	IS/IP	165	1	12	0.0	0.0	13	7	164	0	M	M	03/31/85	(1)	02/28/85	
B-108	NCPLX	SOUND	IS/IP	94	0	4	0.0	0.0	4	0	94	0	F	F	05/31/85	(1)	05/10/85	
B-109	NCPLX	SOUND	IS/IP	127	0	8	0.0	0.0	8	0	127	0	M	M	04/08/85	(1)	04/02/85	
B-110	NCPLX	ASMD LKR	IS/IP	246	1	22	0.0	0.0	23	17	245	0	MP	MP	02/28/85	(1)	03/17/88	
B-111	NCPLX	ASMD LKR	IS/IP	237	1	21	0.0	0.0	22	16	236	0	F	F	06/28/85	(1)	06/26/85	
B-112	NCPLX	ASMD LKR	IS/IP	33	3	0	0.0	0.0	3	0	30	0	F	F	05/31/85	(1)	05/29/85	
B-201	NCPLX	ASMD LKR	IS/IP	29	1	3	0.0	0.0	4	0	28	0	M	M	04/28/82		11/12/86	
B-202	NCPLX	SOUND	IS/IP	27	0	3	0.0	0.0	3	0	27	0	P	M	05/31/85	(1)	05/29/85	
B-203	NCPLX	ASMD LKR	IS/IP	51	1	5	0.0	0.0	6	0	50	0	PM	PM	05/31/84	(1)	11/13/86	
B-204	NCPLX	ASMD LKR	IS/IP	50	1	5	0.0	0.0	6	0	49	0	P	M	05/31/84	(1)	10/21/87	
16 SINGLE-SHELL TANKS			TOTALS	2057	15	164	0.0	0.0	179	80	1697	345						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++	BX FARM	STATUS	++++++									
BX-101	NCPLX	ASMD LKR	IS/IP	43	1	0	0.0	0.0	1	0	42	0	P	M	04/28/82		11/24/88	
BX-102	NCPLX	ASMD LKR	IS/IP	96	0	4	0.0	0.0	4	0	96	0	P	M	04/28/82		09/18/85	
BX-103	NCPLX	SOUND	IS/IP	66	4	0	0.0	0.0	4	0	62	0	P	F	11/29/83		10/31/86	
BX-104	NCPLX	SOUND	IS/IP	99	3	30	0.0	17.4	33	27	96	0	F	F	09/22/89	(1)	09/21/89	
BX-105	NCPLX	SOUND	IS/IP	51	5	6	0.0	15.0	11	4	43	3	F	S	09/03/86	(1)	10/23/86	
BX-106	NCPLX	SOUND	/PI	46	15	0	0.0	0.0	15	15	31	0	MP	PS	04/28/82		05/19/88	
BX-107	NCPLX	SOUND	IS/PI	345	1	29	0.0	23.1	30	23	344	0	MP	P	09/18/90	(2)	09/11/90	
BX-108	NCPLX	ASMD LKR	IS/IP	26	0	1	0.0	0.0	1	0	26	0	M	PS	07/31/79	(1)	10/23/86	
BX-109	NCPLX	SOUND	IS/PI	193	0	13	0.0	8.2	13	8	193	0	FP	P	09/17/90	(2)	09/11/90	
BX-110	NCPLX	ASMD LKR	IS/PI	198	0	15	4.0	4.0	17	6	189	9	MP	M	08/22/85	(1)	07/31/85	
BX-111	NCPLX	ASMD LKR	/PI	211	0	0	7.2	79.3	0	0	68	143	M	M	07/26/77		07/16/93	(a)
BX-112	NCPLX	SOUND	IS/PI	165	1	7	0.0	4.1	8	2	164	0	FP	P	09/17/90	(2)	09/11/90	
12 SINGLE-SHELL TANKS			TOTALS:	1539	30	105	11.2	151.1	137	85	1354	155						
						++++++	BY FARM	STATUS	++++++									
BY-101	NCPLX	SOUND	IS/IP	387	0	5	0.0	35.8	5	0	109	278	P	M	05/30/84		09/19/89	
BY-102	NCPLX	SOUND	/PI	341	0	41	0.0	123.3	41	22	0	341	MP	M	08/30/91	(2)	09/11/87	
BY-103	NCPLX	ASMD LKR	/PI	400	0	160	0.0	78.5	160	137	5	395	MP	M	04/03/90	(2)	09/07/89	
BY-104	NCPLX	SOUND	IS/IP	406	0	18	0.0	329.5	18	0	40	366	P	M	04/28/82		04/27/83	
BY-105	NCPLX	ASMD LKR	/PI	503	0	192	0.0	0.0	192	169	44	459	P	MP	04/28/82		07/11/86	
BY-106	NCPLX	ASMD LKR	/PI	642	0	235	0.0	0.0	235	213	95	547	P	MP	04/28/82		11/04/82	
BY-107	NCPLX	ASMD LKR	IS/IP	266	0	25	0.0	56.4	25	0	60	206	P	MP	04/28/82		10/15/86	

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
BY-108	NCPLX	ASMD LKR	IS/IP	228	0	9	0.0	27.5	9	0	154	74	MP	M	04/28/82		10/15/86	
BY-109	NCPLX	SOUND	/PI	423	0	78	0.0	93.5	78	57	83	340	F	PS	08/30/91	(2)	10/15/86	
BY-110	NCPLX	SOUND	IS/IP	398	0	9	0.0	213.3	9	0	103	295	M	S	09/10/79		07/26/84	
BY-111	NCPLX	SOUND	IS/IP	459	0	0	0.0	313.2	0	0	21	438	P	M	04/28/82		10/31/86	
BY-112	NCPLX	SOUND	IS/IP	291	0	8	0.0	116.4	8	0	5	286	P	M	04/28/82		04/14/88	
12 SINGLE-SHELL TANKS			TOTALS:	4744	0	780	0.0	1387.4	780	598	719	4025						
						++++++ C FARM STATUS ++++++												
C-101	NCPLX	ASMD LKR	IS/IP	88	0	3	0.0	0.0	3	0	88	0	M	M	11/29/83		11/17/87	
C-102	DC	SOUND	/PI	423	0	37	0.0	11.6	37	19	423	0	F	FP	04/28/82		05/18/76	
C-103	NCPLX	SOUND	/PI	195	133	0	0.0	0.0	133	133	62	0	F	S	10/22/90	(2)	07/28/87	
C-104	CC	SOUND	IS/IP	295	0	11	0.0	0.0	11	5	295	0	FP	P	09/22/89	(1)	07/25/90	
C-105	NCPLX	SOUND	/PI	150	0	11	0.0	0.0	11	4	150	0	F	S	05/31/85		03/13/94	
C-106	NCPLX	SOUND	/PI	229	32	16	0.0	0.0	48	42	197	0	F	PS	04/28/82		04/05/79	
C-107	DC	SOUND	/PI	275	0	26	0.0	16.3	26	20	275	0	F	S	01/30/92	(2)	00/00/00	
C-108	NCPLX	SOUND	IS/IP	66	0	0	0.0	0.0	0	0	66	0	M	S	02/24/84	(1)	12/05/74	
C-109	NCPLX	SOUND	IS/IP	66	4	0	0.0	0.0	4	0	62	0	M	PS	11/29/83		01/30/76	
C-110	DC	ASMD LKR	/PI	187	0	7	0.0	8.9	7	5	187	0	F	FMP	03/01/92	(2)	08/12/86	
C-111	NCPLX	ASMD LKR	IS/IP	57	0	0	0.0	0.0	0	0	57	0	M	S	04/28/82		02/25/70	
C-112	NCPLX	SOUND	IS/PI	104	0	32	0.0	0.0	32	26	104	0	M	PS	09/18/90	(2)	09/18/90	

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
C-201	NCPLX	ASMD LKR	IS/IP	2	0	0	0.0	0.0	0	0	2	0	P	MP	03/31/82		12/02/86	
C-202	EMPTY	ASMD LKR	IS/IP	1	0	0	0.0	0.0	0	0	1	0	P	M	01/19/79		12/09/86	
C-203	NCPLX	ASMD LKR	IS/IP	5	0	0	0.0	0.0	0	0	5	0	P	MP	04/28/82		12/09/86	
C-204	NCPLX	ASMD LKR	IS/IP	3	0	0	0.0	0.0	0	0	3	0	P	MP	04/28/82		12/09/86	
16 SINGLE-SHELL TANKS			TOTALS:	2146	169	143	0.0	36.8	312	254	1977	0						
						++++++ S FARM STATUS ++++++												
S-101	NCPLX	SOUND	/PI	427	12	84	0.0	0.0	96	90	244	171	F	PS	09/16/80		03/18/88	
S-102	DSSF	SOUND	/PI	549	0	230	0.0	0.0	230	208	4	545	P	FP	04/28/82		03/18/88	
S-103	DSSF	SOUND	/PI	248	17	85	0.0	0.0	102	79	10	221	M	S	11/20/80		06/01/89	
S-104	NCPLX	ASMD LKR	IS/IP	294	1	28	0.0	0.0	29	23	293	0	M	M	12/20/84	(1)	12/12/84	
S-105	NCPLX	SOUND	IS/IP	456	0	35	0.0	114.3	35	13	2	454	MP	S	09/26/88		04/12/89	
S-106	NCPLX	SOUND	/PI	479	4	186	0.0	97.0	190	168	28	447	P	FP	12/31/93		03/17/89	
S-107	NCPLX	SOUND	/PI	376	14	45	0.0	0.0	59	52	293	69	F	PS	09/25/80		03/12/87	
S-108	NCPLX	SOUND	/PI	604	0	127	0.0	151.6	127	105	4	600	P	MP	04/28/82		03/12/87	
S-109	NCPLX	SOUND	/PI	568	0	141	0.0	111.0	141	119	13	555	F	PS	09/30/75		08/24/84	
S-110	NCPLX	SOUND	/PI	390	0	110	0.0	185.9	110	103	131	259	F	PS	05/14/92		03/12/87	
S-111	NCPLX	SOUND	/PI	596	10	195	0.0	3.3	205	134	139	447	P	FP	04/28/82		08/10/89	
S-112	NCPLX	SOUND	/PI	523	0	110	0.0	125.1	110	107	5	518	P	FP	12/31/93		03/24/87	
12 SINGLE-SHELL TANKS			TOTALS:	5510	58	1376	0.0	788.2	1434	1201	1166	4286						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++	SX FARM	STATUS	++++++									
SX-101	DC	SOUND	/PI	456	1	145	0.0	0.0	146	124	112	343	P	FP	04/28/82		03/10/89	
SX-102	DSSF	SOUND	/PI	543	0	183	0.0	0.0	183	177	117	426	P	M	04/28/82		01/07/88	
SX-103	NCPLX	SOUND	/PI	652	1	232	0.0	0.0	233	211	115	536	F	S	07/15/91		12/17/87	
SX-104	DSSF	ASMD LKR	/PI	614	0	201	0.0	113.2	201	195	136	478	F	S	07/07/89		09/08/88	
SX-105	DSSF	SOUND	/PI	683	0	261	0.0	0.0	261	238	73	610	P	F	04/28/82		06/15/88	
SX-106	NCPLX	SOUND	/PI	538	61	194	0.0	0.0	255	233	12	465	F	PS	10/28/80		06/01/89	
SX-107	NCPLX	ASMD LKR	IS/IP	104	0	5	0.0	0.0	5	0	104	0	P	M	04/28/82		03/06/87	
SX-108	NCPLX	ASMD LKR	IS/IP	87	0	5	0.0	0.0	5	0	87	0	P	M	12/31/93		03/06/87	
SX-109	NCPLX	ASMD LKR	IS/IP	250	0	10	0.0	0.0	10	0	0	250	P	M	10/05/93		05/21/86	
SX-110	NCPLX	ASMD LKR	IS/IP	62	0	0	0.0	0.0	0	0	62	0	M	PS	10/06/76		02/20/87	
SX-111	NCPLX	ASMD LKR	IS/IP	125	0	7	0.0	0.0	7	0	125	0	M	PS	05/31/74		03/10/87	
SX-112	NCPLX	ASMD LKR	IS/IP	92	0	3	0.0	0.0	3	0	92	0	P	M	04/28/82		03/10/87	
SX-113	NCPLX	ASMD LKR	IS/IP	26	0	0	0.0	0.0	0	0	26	0	P	M	04/28/82		03/18/88	
SX-114	NCPLX	ASMD LKR	IS/IP	181	0	14	0.0	0.0	14	0	181	0	P	M	04/28/82		02/26/87	
SX-115	NCPLX	ASMD LKR	IS/IP	12	0	0	0.0	0.0	0	0	12	0	P	M	04/28/82		03/31/88	
15 SINGLE-SHELL TANKS			TOTALS:	4425	63	1260	0.0	113.2	1323	1178	1254	3108						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++ T FARM STATUS ++++++												
T-101	NCPLX	ASMD LKR	IS/PI	102	1	16	0.0	25.3	17	0	101	0	F	S	04/14/93		04/07/93	
T-102	NCPLX	SOUND	IS/IP	32	13	0	0.0	0.0	13	13	19	0	P	FP	08/31/84		06/28/89	
T-103	NCPLX	ASMD LKR	IS/IP	27	4	0	0.0	0.0	4	0	23	0	F	FP	11/29/83	(1)	07/02/84	
T-104	NCPLX	SOUND	/PI	445	3	47	0.0	0.0	50	44	442	0	P	MP	04/28/82		06/29/89	
T-105	NCPLX	SOUND	IS/IP	98	0	23	0.0	0.0	23	17	98	0	P	F	05/29/87		05/14/87	
T-106	NCPLX	ASMD LKR	IS/IP	21	2	0	0.0	0.0	2	0	19	0	P	FP	04/28/82		06/29/89	
T-107	NCPLX	ASMD LKR	/PI	180	9	13	0.0	0.0	22	16	171	0	P	FP	08/31/84		07/12/84	
T-108	NCPLX	ASMD LKR	IS/IP	44	0	0	0.0	0.0	0	0	44	0	P	M	04/28/82		07/17/84	
T-109	NCPLX	ASMD LKR	IS/IP	58	0	0	0.0	0.0	0	0	58	0	M	M	12/30/84	(1)	02/25/93	
T-110	NCPLX	SOUND	/PI	379	3	39	0.0	0.0	42	36	376	0	P	FP	04/28/82		07/12/84	
T-111	NCPLX	ASMD LKR	/PI	458	2	49	0.0	0.0	51	45	456	0	P	FP	04/28/82		08/02/84	
T-112	NCPLX	SOUND	IS/IP	67	7	0	0.0	0.0	7	7	60	0	P	FP	04/28/82		08/01/84	
T-201	NCPLX	SOUND	IS/IP	29	1	3	0.0	0.0	4	0	28	0	M	PS	05/31/78		04/15/86	
T-202	NCPLX	SOUND	IS/IP	21	0	2	0.0	0.0	2	0	21	0	FP	P	07/12/81		07/06/89	
T-203	NCPLX	SOUND	IS/IP	35	0	4	0.0	0.0	4	0	35	0	M	PS	01/31/78		08/03/89	
T-204	NCPLX	SOUND	IS/IP	38	0	4	0.0	0.0	4	0	38	0	FP	P	07/22/81		08/03/89	
16 SINGLE-SHELL TANKS			TOTALS:	2034	45	200	0.0	25.3	245	178	1989	0						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++	TX FARM	STATUS	++++++									
TX-101	NCPLX	SOUND	IS/IP	87	3	2	0.0	0.0	5	0	84	0	F	P	02/02/84	(1)	10/24/85	
TX-102	NCPLX	SOUND	IS/IP	217	0	22	0.0	94.4	22	0	0	217	M	S	08/31/84		10/31/85	
TX-103	NCPLX	SOUND	IS/IP	157	0	15	0.0	68.3	15	0	157	0	F	S	08/14/80		10/31/85	
TX-104	NCPLX	SOUND	IS/IP	65	1	14	0.0	3.6	15	0	0	64	F	FP	04/06/84		10/16/84	
TX-105	NCPLX	ASMD LKR	IS/IP	609	0	20	0.0	121.5	20	0	0	609	M	PS	08/22/77		10/24/89	
TX-106	NCPLX	SOUND	IS/IP	453	0	10	0.0	134.6	10	0	0	453	M	S	08/29/77		10/31/85	
TX-107	NCPLX	ASMD LKR	IS/IP	36	1	1	0.0	0.0	2	0	0	35	FP	FP	01/20/84	(1)	10/31/85	
TX-108	NCPLX	SOUND	IS/IP	134	0	0	0.0	13.7	0	0	0	134	P	FP	05/30/83		09/12/89	
TX-109	NCPLX	SOUND	IS/IP	384	0	10	0.0	72.3	10	0	0	384	F	PS	05/30/83		10/24/89	
TX-110	NCPLX	ASMD LKR	IS/IP	462	0	15	0.0	115.1	15	0	0	462	M	PS	05/30/83		10/24/89	
TX-111	NCPLX	SOUND	IS/IP	370	0	9	0.0	98.4	9	0	0	370	M	PS	07/26/77		09/12/89	
TX-112	NCPLX	SOUND	IS/IP	649	0	24	0.0	94.0	24	0	0	649	P	PS	05/30/83		11/19/87	
TX-113	NCPLX	ASMD LKR	IS/IP	607	0	16	0.0	19.2	16	0	0	607	M	PS	05/30/83		04/11/83	
TX-114	NCPLX	ASMD LKR	IS/IP	535	0	15	0.0	104.3	15	0	0	535	M	PS	05/30/83		04/11/83	
TX-115	NCPLX	ASMD LKR	IS/IP	640	0	19	0.0	99.1	19	0	0	640	M	S	03/25/83		06/15/88	
TX-116	NCPLX	ASMD LKR	IS/IP	631	0	23	0.0	23.8	23	0	0	631	M	PS	03/31/72		10/17/89	
TX-117	NCPLX	ASMD LKR	IS/IP	626	0	8	0.0	54.3	8	0	0	626	M	PS	12/31/71		04/11/83	
TX-118	NCPLX	SOUND	IS/IP	347	0	27	0.0	89.1	27	0	0	347	F	S	11/17/80		12/19/79	
18 SINGLE-SHELL TANKS			TOTALS:	7009	5	250	0.0	1205.7	255	0	241	6763						

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
						++++++ TY FARM STATUS ++++++												
TY-101	NCPLX	ASMD LKR	IS/IP	118	0	0	0.0	8.2	0	0	118	0	P	F	04/28/82		08/22/89	
TY-102	NCPLX	SOUND	IS/IP	64	0	14	0.0	6.6	14	0	0	64	P	FP	06/28/82		07/07/87	
TY-103	NCPLX	ASMD LKR	IS/IP	162	0	5	0.0	11.5	5	0	162	0	P	FP	07/09/82		08/22/89	
TY-104	NCPLX	ASMD LKR	IS/IP	46	3	12	0.0	0.0	15	0	43	0	P	FP	06/27/90	(1)	11/03/87	
TY-105	NCPLX	ASMD LKR	IS/IP	231	0	0	0.0	3.6	0	0	231	0	P	M	04/28/82		09/07/89	
TY-106	NCPLX	ASMD LKR	IS/IP	17	0	0	0.0	0.0	0	0	17	0	P	M	04/28/82		08/22/89	
6 SINGLE-SHELL TANKS			TOTALS:	638	3	31	0.0	29.9	34	0	571	64						
						++++++ U FARM STATUS ++++++												
U-101	NCPLX	ASMD LKR	IS/IP	25	3	0	0.0	0.0	3	0	22	0	P	MP	04/28/82		06/19/79	
U-102	NCPLX	SOUND	/PI	374	18	126	0.0	0.0	144	122	43	313	P	MP	04/28/82		06/08/89	
U-103	NCPLX	SOUND	/PI	468	13	176	0.0	0.0	189	166	32	423	P	FP	04/28/82		09/13/88	
U-104	NCPLX	ASMD LKR	IS/IP	122	0	7	0.0	0.0	7	0	122	0	P	MP	04/28/82		08/10/89	
U-105	NCPLX	SOUND	/PI	418	37	142	0.0	0.0	179	157	32	349	FM	PS	09/30/78		07/07/88	
U-106	NCPLX	SOUND	/PI	226	15	68	0.0	0.0	83	61	26	185	F	PS	12/30/83		07/07/88	
U-107	DSSF	SOUND	/PI	406	31	147	0.0	0.0	178	156	15	360	F	S	12/30/83		10/27/88	
U-108	NCPLX	SOUND	/PI	468	24	172	0.0	0.0	196	174	29	415	F	S	12/30/83		09/12/84	
U-109	NCPLX	SOUND	/PI	463	19	163	0.0	0.0	182	160	48	396	F	F	11/13/77		07/07/88	
U-110	NCPLX	ASMD LKR	IS/PI	186	0	15	0.0	0.0	15	9	186	0	M	M	12/30/84	(1)	12/11/84	
U-111	DSSF	SOUND	/PI	329	0	122	0.0	0.0	122	99	26	303	PS	FPS	04/28/82		06/23/88	
U-112	NCPLX	ASMD LKR	IS/IP	49	4	0	0.0	0.0	4	0	45	0	P	MP	02/10/84	(1)	08/03/89	

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES
U-201	NCPLX	SOUND	IS/IP	5	1	0	0.0	0.0	1	0	4	0	M	S	08/15/79		08/03/89	
U-202	NCPLX	SOUND	IS/IP	5	1	0	0.0	0.0	1	0	4	0	M	S	08/15/79		08/08/89	
U-203	NCPLX	SOUND	IS/IP	3	1	0	0.0	0.0	1	0	2	0	M	S	08/15/79		06/13/89	
U-204	NCPLX	SOUND	IS/IP	3	1	0	0.0	0.0	1	0	2	0	M	S	08/15/79		06/13/89	
16 SINGLE-SHELL TANKS			TOTALS:	3550	168	1138	0.0	0.0	1306	1104	638	2744						
GRAND TOTAL				36095	568	6258	11	3901	6828	5372	12181	23345						

NOTES: +/- 1K gal differences are the result of rounding
Total Waste is calculated as the sum of Sludge and Saltcake plus Supernate.
The category "Interim Isolated" (II) was changed to "Intrusion Prevention" (IP) in June 1993. See section C. "Tank and Equipment Code and Status Definitions"

(1) WHC-SD-RE-TI-178 SST STABILIZATION RECORD, latest revision
(2) TANK FARMS SST ENGINEER MONTHLY INPUT (Retained 10 yr in Monthly Summary Report author's office)

See next page for footnotes

TABLE E-5. INVENTORY AND STATUS BY TANK
SINGLE-SHELL TANKS
March 31, 1994

TANK STATUS				LIQUID VOLUME							SOLIDS VOLUME		VOLUME DETERMINATION					
TANK	WASTE MATERIAL	TANK INTEGRITY	STABIL/ ISOLATION STATUS	TOTAL WASTE (Kgal)	SUPER-NATANT LIQUID (Kgal)	DRAIN-ABLE INTER-STIT. (Kgal)	PUMPED THIS MONTH (Kgal)	TOTAL PUMPED (Kgal)	DRAIN-ABLE LIQUID REMAIN (Kgal)	PUMP-ABLE LIQUID REMAIN (Kgal)	SLUDGE (Kgal)	SALTCAKE (Kgal)	LIQUIDS VOLUME METHOD	SOLIDS VOLUME METHOD	SOLIDS VOLUME UPDATE	SOLIDS UPDATE SOURCE SEE FOOTNOTE	LAST PHOTO DATE	SEE FOOTNOTES FOR THESE CHANGES

Footnote:

(a) BX-111 - Following information from SST Cognizant Engineer:
Recheck of data sheets for January 1994 revealed incorrect totalizer reading was used in the calculations. Recalculations for January and February resulted in the following corrections:

	Jan 94 Kgal	Feb 94 Kgal	
Pumped this Month	15.80	1.50	
Total Pumped	70.50	72.10	(+/- .1 Kgal resulting from rounding)

(DLR and PLR are being reflected as "0" because the gallons pumped have exceeded the estimate of the gallons remaining when pumping began. DLR and PLR will be re-estimated when pumping is completed).

This page intentionally left blank

9413279.0111

9413279.0112

APPENDIX F

PERFORMANCE SUMMARY

This page intentionally left blank.

9413279.0163

TABLE F-1. PERFORMANCE SUMMARY (Sheet 1 of 2)

WASTE VOLUMES (Kgallons)

March 31, 1994

INCREASES/DECREASES IN WASTE VOLUMES STORED IN DOUBLE-SHELL TANKS

SOURCE		THIS MONTH	FY1994 TO DATE
B PLANT		0	9
PUREX TOTAL (1)		0	41
PFP (1)		4	4
T PLANT (1)		0	0
S PLANT (1)		5	10
300/400 AREAS (1)		0	8
SULFATE WASTE -100 N (2)		0	0
MINI-RUN (14)		0	67
TANK FARMS & SALTWELL LIQUID (6)		43	134
OTHER GAINS		31	151
Slurry increase (3)	3		
Condensate	28		
Instrument change (7)	0		
Unknown (5)	0		
OTHER LOSSES		-34	-237
Slurry decrease (3)	-3		
Evaporation (4)	-18		
Instrument change (7)	-4		
Unknown (5)	-9		
EVAPORATED		0	0
GROUTED		0	0
Total		49	187

Note: +/-1 Kgal differences are the result of rounding

* 2936 gallons of water added to C-106 on March 4. Starting March 7, C-106 is undergoing a liquid-reduction process test to determine a new low level for future water addition. The process test is expected to be completed FY-94. No cooling water is added during the test.

INCREASES/DECREASES IN WASTE VOLUMES STORED IN SINGLE-SHELL TANKS

SOURCE		THIS MONTH	FY1994 TO DATE
106-C (8)	Gains	3	24
	Losses	-6	-33
Total		-3 *	-9

CUMULATIVE EVAPORATION - 1950 TO PRESENT WASTE VOLUME REDUCTION

FACILITY	
242-B EVAPORATOR (9)	7172
242-T EVAPORATOR (1950's) (9)	9181
IN-TANK SOLIDIFICATION UNIT 1 (10)	11876
IN-TANK SOLIDIFICATION UNIT 2 (10)	15295
IN-TANK SOLID. UNIT 1 & 2 (10)	7965
(after conversion of Unit 1 to a cooler for Unit 2)	
242-T (Modified) (9)	24471
242-S EVAPORATOR (11)	41983
242-A EVAPORATOR (12)	65227
B PLANT (Cell 23) (13)	1185
REDOX (12)	12393
Total	196748

TOTAL THROUGHPUT

FACILITY	
242-A EVAPORATOR (12)	182437
242-S EVAPORATOR (11)	134587
Total	317024

Footnotes: See Next Page

TABLE F-1. PERFORMANCE SUMMARY
(Sheet 2 of 2)

Footnotes:

INCREASES/DECREASES IN WASTE VOLUMES

(1) Including Flush

(2) Sulfate waste is generated from ion exchange backflushing and sand filter clean out, resulting in sulfate waste (Na_2SO_4).

(3) Slurry increase/growth is caused by gas generation within the waste. The gas which is trapped in the waste expands in the tank causing the surface level and volume to increase. Slurry decrease results from the periodic release of gas in the waste.

(4) Aging waste tanks

(5) Unknown waste gains or losses may be the result of rounding calculations, clean water slowly leaking through a valve, changes in levels (expansion/contraction) because of ambient temperature changes, different measuring devices being used by Tank Farm operators, transfers taking place during the end of the month, Tank Farm activities such as miscellaneous water additions not associated with facility waste generation, or the addition of water which is added to aging waste tanks and then evaporated off.

(6) Includes Tank Farms miscellaneous flushes (flushes are used to "clean out" pipelines and reduce personnel exposure, reduce potential for waste incompatibility, prevent line plugging, and reduce waste content of potential spills or leaks), and saltwell liquid, which results from pumping of single-shell tanks to double-shell tanks.

(7) Liquid level measurement instrument changes from the automatic FIC to manual tape (and vice versa) result in unusual gains or losses because the manual tape may rest on an uneven crust surface giving a different reading from that of the automatic FIC. These instrument changes are made when the automatic FIC is out of service and the reading from the manual tape is used for reporting purposes. The reported reading reverts back to the automatic FIC when it is repaired.

(8) Water is periodically added 106-C to provide evaporative cooling. Losses due to evaporation are calculated assuming all losses are evaporative losses. Some drywells are monitored weekly and some are monitored every two weeks on tank 106-C. If there are any indications of a leak from this tank, the assumption that all losses are due to evaporation will be reevaluated.

WASTE VOLUME REDUCTION

(9) Currently inoperative. These evaporator systems (242-B and 242-T) were installed in 1952 in each of the two operating areas to remove water from the waste, and ran for approximately 4 yr after which both units were shut down. The 242-T Evaporator was reactivated in December 1965, and shut down again in April 1976.

(10) Currently inoperative. These two in-tank solidification (ITS) units provided in-tank heating to promote in-tank boiling or evaporation. The ITS Unit 1 started up March 1965, and ITS Unit 2 started up February 1968. In August 1971, ITS Unit 1 was converted from an evaporator to a cooler for ITS Unit 2. Both units were shut down June 1974.

(11) Currently inoperative. The 242-S Evaporator-Crystallizer was started up November 1973, and shut down March 1980, when its processing campaign was completed. It is in standby mode with no future mission. This evaporator operates under a vacuum, employing evaporative concentration with subsequent crystallization and precipitation of salt crystals.

(12) Currently inoperative. The 242-A Evaporator-Crystallizer was started up March 1977, and shut down April 1989 because of regulatory issues, and has remained shut down for subsequent upgrading. This evaporator operates under a vacuum, employing evaporative concentration with subsequent crystallization and precipitation of salt crystals (forming saltcake). Start up for this evaporator is expected to be April 1994.

(13) Currently inoperative. Additional concentration of wastes was completed by using the concentrators at REDOX and B Plant. The REDOX concentrator was used from July 1967 to June 1972, while the B Plant concentrator was used from July 1967 to February 1968.

(14) Waste generated for training and testing purposes prior to Evaporator restart.

9413279.0115

9413279.0116

APPENDIX G

PUMPING RECORD
LIQUID STATUS AND PUMPABLE LIQUID
REMAINING IN TANKS

This page intentionally left blank.

9413279.0117

TABLE G-1. PUMPING RECORD

March 31, 1994
(Kgallons)

TANK FARMS	PUMPED THIS MONTH	PUMPED FY TO DATE	CUMULATIVE TOTAL PUMPED 1979 TO DATE
EAST			
A	0.0	0.0	150.5
AN	N/A	N/A	N/A
AP	N/A	N/A	N/A
AW	N/A	N/A	N/A
AX	0.0	0.0	13.0
AY	N/A	N/A	N/A
AZ	N/A	N/A	N/A
B	0.0	0.0	0.0
BX	7.2	79.3	151.1 (b)
BY	0.0	0.0	1387.4 (a)
C	0.0	0.0	36.8
Total	7.2	79.3	1738.8
WEST			
S	0.0	0.0	791.0
SX	0.0	0.0	113.2
SY	N/A	N/A	N/A
T	0.0	0.0	25.3
TX	0.0	0.0	1205.7
TY	0.0	0.0	29.9
U	0.0	0.0	0.0
Total	0.0	0.0	2165.1
TOTAL	7.2	79.3	3903.9

NA = Not Applicable

(a) The total volume pumped was adjusted by the Single-Shell Tanks Cognizant Engineer to account for the 14% miscalibration of the constant velocity transmitter and the amount of flush water used. DIL, DLR and PLR volumes were recalculated, based on the observed porosity in 102 and 109-BY.

(b) Recheck of data sheets for January 1994 revealed incorrect totalizer reading was used in the calculations. Recalculation corrections by Single-Shell Tanks Cognizant Engineer for January and February are included in above volumes.

TABLE G-2. LIQUID STATUS AND PUMPABLE LIQUID REMAINING IN TANKS

March 31, 1994

Waste Volumes (Kgallons)

TANK FARMS	SUPERNATANT LIQUID	DRAINABLE INTERSTITIAL LIQUID	DRAINABLE LIQUID REMAINING	PUMPABLE LIQUID REMAINING
EAST				
A	9	441	450	390
AN	4612	37	4649	N/A
AP	7500	0	7500	N/A
AW	4704	159	4863	N/A
AX	3	370	373	304
AY	1477	2	1479	N/A
AZ	1793	4	1797	N/A
B	15	164	179	80
BX	30	105	137	85
BY	0	780	780	598
C	169	143	312	254
Total	20312	2205	22519	1711
WEST				
S	58	1376	1434	1201
SX	63	1260	1323	1178
SY	853	237	1090	N/A
T	45	200	245	178
TX	5	250	255	0
TY	3	31	34	0
U	168	1138	1306	1104
Total	1195	4492	5687	3661
TOTAL	21507	6697	28206	5372 (1)

(1) Volume based on 12.5% (sludge waste) and 45% (saltcake waste) liquid in solid (porosity) value. This is a conservative (high) estimate.

Note: +/- 1 Kgal differences are the result of computer rounding

N/A = Not applicable

9413279.0120

APPENDIX H

CATCH TANKS AND SPECIAL SURVEILLANCE FACILITIES

This page intentionally left blank.

9413279.0121

TABLE H-1. EAST AND WEST AREA CATCH TANKS AND SPECIAL SURVEILLANCE FACILITIES

ACTIVE – still running transfers through the associated diversion boxes or pipeline encasements

March 31, 1994

FACILITY	LOCATION	PURPOSE (receives waste from:)	VOLUME OF CONTENTS (Gallons)	MONITORED BY	REMARKS
EAST AREA					
241-A-302-A	A FARM	A-151 DB	1583	CASS/FIC	PUMPED 08/11/92
241-ER-311	B PLANT	ER-151, ER-152 DB	7937	CASS/FIC	PUMPED 05/29/91
241-AX-152	AX FARM	AX-152 DB	6179	MANUALLY	DIAL O/S, USING ZIP CORD, PUMPED 08/29/92
241-AZ-151	AZ FARM	AZ-152 DB, AZ LOOP SEAL	2870	CASS/FIC	VOLUME CHANGES DAILY
241-AZ-154	AZ FARM	AZ-102 HTG COIL STEAM CONDENSATE	0	CASS/MT	AUTOMATIC PUMP
244-BX-TK/SMP	BX COMPLEX	DCRT - RECEIVES FROM SEVERAL FARMS	13982	MANUALLY	USING MANUAL TAPE FOR TANK
244-A-TK/SMP	A COMPLEX	DCRT - RECEIVES FROM SEVERAL FARMS	6949	MCS	
AR-204	AY FARM	RR CARS DURING TRANSFER TO REC. TKS	195	DIP TUBE	ALARMS ON CASS
A-417	A FARM	A-702 PROCESS CONDENSATE	31860	DIP TUBE	
Vent Station Catch Tank		CROSS COUNTRY TRANSFER LINE	619	MT	
WEST AREA					
241-TX-302-C	TX FARM	TX-154 DB	3898	CASS/FIC	FIC REPAIRED
241-U-301-B	U FARM	U-151, U-152, U-153, U-252 DB	6762	CASS/FIC	RETURNED TO SERVICE 12/30/93
241-UX-302-A	U PLANT	UX-154 DB	11831	CASS/MFIC	
241-S-304	S FARM	S-151 DB	2070	RS	OPERATIONAL 10/91, REPLACED S-302-A
244-S-TK/SMP	S FARM	DCRT - RECEIVES FROM SEVERAL FARMS	11082	MANUALLY	CWF
244-TX-TK/SMP	TX FARM	DCRT - RECEIVES FROM SEVERAL FARMS	11387	MANUALLY	MT

Total active facilities 16

LEGEND:
- DB - Diversion Box
- DCRT - Double-Contained Receiver Tank
- TK - Tank
- SMP - Sump
- R - Usually denotes replacement
- FIC - Food Instrument Corporation measurement device
- RS - Robert Shaw Instrument measurement device
- MFIC - Manual FIC
- MT - Manual Tape
- CWF - Weight Factor/SpG = Corrected Weight Factor
- CASS - Computer Automated Surveillance System
- MCS - Monitor and Control System
- O/S - Out of Service

TABLE H-2. EAST AREA CATCH TANKS AND SPECIAL SURVEILLANCE FACILITIES

INACTIVE - no longer receiving waste transfers

March 31, 1994

FACILITY	LOCATION	RECEIVED WASTE FROM:	VOLUME OF CONTENTS (Gallons)	MONITORED BY	REMARKS
241-A-302-B	A FARM	A-152 DB	4150	CASS/MT	ISOLATED 1985, PROJECT B-138 INTERIM STABILIZED 1990
241-B-301-B	B FARM	B-151, B-152, B-153, B-252 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-B-302-B	B FARM	B-154 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-BX-302-A	BX FARM	BR-152, BX-153, BXR-152, BYR-152 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-BX-302-B	BX FARM	BX-154 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-BX-302-C	BX FARM	BX-155 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-C-301-C	C FARM	C-151, C-152, C-153, C-252 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-CX-70	HOT SEMI-	TRANSFER LINES	UNKNOWN	NM	ISOLATED, DECOMMISSION PROJ.
241-CX-72	WORKS	TRANSFER LINES	UNKNOWN	NM	SEE DWG H-2-95-501, 2/5/87
244-AR	A COMPLEX	DCRT - RECEIVES FROM SEVERAL FARMS	UNKNOWN	NM	BEING UPGRADED
244-BXR-TK/SMP-001	BX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED 1985(1)
244-BXR-TK/SMP-002	BX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED 1985(1)
244-BXR-TK/SMP-003	BX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED 1985(1)
244-BXR-TK/SMP-011	BX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED 1985(1)
361-B-TANK	B PLANT	DRAINAGE FROM B-PLANT	UNKNOWN	NM	INTERIM STABILIZED 1985(1)

Total East Area Inactive facilities 15

LEGEND:
- DB - Diversion Box
- DCRT - Double-Contained Receiver Tank
- MT - Manual Tape
- CASS - Computer Automated Surveillance System
- TK - Tank
- SMP - Sump
- R - Usually denotes replacement
- NM - Not Monitored

(1) SOURCE: WASTE STORAGE TANK STATUS & LEAK DETECTION CRITERIA document

TABLE H-3. WEST AREA CATCH TANKS AND SPECIAL SURVEILLANCE FACILITIES

INACTIVE – no longer receiving waste transfers

March 31, 1994

FACILITY	LOCATION	RECEIVED WASTE FROM:	VOLUME OF CONTENTS (Gallons)	BY	REMARKS
241-S-302	S FARM	240-S-151 DB	2276	CASS/FIC *	ASSUMED LEAKER EPDA 85-04
241-S-302-A	S FARM	241-S-151 DB		CASS/FIC *	ASSUMED LEAKER TF-EFS-90-042
			* FIC in Intrusion mode		Partially filled with grout 2/91, determined still assumed leaker after leak test
241-S-302-B	S FARM	S ENCASEMENTS	UNKNOWN	NM	ISOLATED 1985(1)
241-SX-304(302)	SX FARM	SX-152 TRANSFER BOX, SX-151 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-TX-302	TX FARM	TX-153 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-TX-302-X-B	TX FARM	TX ENCASEMENTS	UNKNOWN	NM	ISOLATED 1985(1)
241-TX-302-B	TX FARM	TX-155 DB	1460	CASS/MT	NEW MT INSTALLED 7/16/93
241-TY-302-A	TY FARM	TX-153 DB	UNKNOWN	NM	ISOLATED 1985(1)
241-TY-302-B	TY FARM	TY ENCASEMENTS	UNKNOWN	NM	ISOLATED 1985(1)
244-U-TK/SMP	U FARM	DCRT - RECEIVES FROM SEVERAL FARMS	UNKNOWN	NM	NOT YET IN USE
244-UR VAULT	U FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1985(1)
244-UR-TK/SMP-001	U FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1985(1)
244-UR-TK/SMP-002	U FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1985(1)
244-UR-TK/SMP-003	U FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1985(1)
244-TXR VAULT	TX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1984(1)
244-TXR-TK/SMP-001	TX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1984(1)
244-TXR-TK/SMP-002	TX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1984(1)
244-TXR-TK/SMP-003	TX FARM	TRANSFER LINES	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1984(1)
361-T-TANK	T PLANT	DRAINAGE FROM T-PLANT	UNKNOWN	NM	ISOLATED 1985(1)
361-U-TANK	U PLANT	DRAINAGE FROM U-PLANT	UNKNOWN	NM	INTERIM STABILIZED, MT REMOVED 1985(1)

Total West Area inactive facilities 20

LEGEND:
DB - Diversion Box
DCRT - Double-Contained Receiver Tank
TK - Tank
SMP - Sump
R - Usually denotes replacement
FIC - Food Instrument Corporation
MT - Manual Tape
O/S - Out of Service
CASS - Computer Automated Surveillance System
NM - Not Monitored

(1) SOURCE: WASTE STORAGE TANK STATUS & LEAK DETECTION CRITERIA document

This page intentionally left blank.

9413279.0125

9413229.0126

APPENDIX I

LEAK VOLUME ESTIMATES

This page intentionally left blank.

9413279.0127

TABLE I-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (4) (Sheet 1 of 6)

Tank No.	Date Declared Confirmed or Assumed Leaker (3)	Volume (2)(4) (Gallons)	Associated KiloCuries 137 cs (10)	Interim Stabilized Date (12)	Leak Estimate Updated	Leak Estimate Reference
241-A-103	1987	5500 (9)		6/88	1987	(j)
241-A-104	1975	500 to 2500	0.8 to 1.8 (q)	9/78	1983	(a) (q)
241-A-105 (1)	1963	10000 to 277000	85 to 760 (b)	7/79	1991	(b),(c)
241-AX-102	1988	3000 (9)		9/88	1989	(h)
241-AX-104	1977	-- (7)		8/81	1989	(g)
241-B-101	1974	-- (7)		3/81	1989	(g)
241-B-103	1978	-- (7)		2/85	1989	(g)
241-B-105	1978	-- (7)		12/84	1989	(g)
241-B-107	1980	8000 (9)		3/85	1986	(d),(f)
241-B-110	1981	10000 (9)		3/85	1986	(d)
241-B-111	1978	-- (7)		6/85	1989	(g)
241-B-112	1978	2000		5/85	1989	(g)
241-B-201	1980	1200 (9)		8/81	1984	(e),(f)
241-B-203	1983	300 (9)		6/84	1986	(d)
241-B-204	1984	400 (9)		6/84	1989	(g)
241-BX-101	1972	-- (7)		9/78	1989	(g)
241-BX-102	1971	70000	50 (l)	11/78	1986	(d)
241-BX-108	1974	2500	0.5 (l)	7/79	1986	(d)
241-BX-110	1976	-- (7)		8/85	1989	(g)
241-BX-111	1984	-- (7)		N/A	1993	(g),(r)
241-BY-103	1973	<5000		N/A	1983	(a)
241-BY-105	1984	-- (7)		N/A	1989	(g)
241-BY-106	1984	-- (7)		N/A	1989	(g)
241-BY-107	1984	15100 (9)		7/79	1989	(g)
241-BY-108	1972	<5000		2/85	1983	(a)
241-C-101	1980	20000 (9,11)		11/83	1986	(d)
241-C-110	1984	2000		N/A	1989	(g)
241-C-111	1968	5500 (9)		3/84	1989	(g)
241-C-201 (5)	1988	550		3/82	1987	(i)
241-C-202 (5)	1988	450		8/81	1987	(i)
241-C-203	1984	400 (9)		3/82	1986	(d)
241-C-204 (5)	1988	350		9/82	1987	(i)
241-S-104	1968	24000 (9)		12/84	1989	(g)
241-SX-104	1988	6000 (9)		N/A	1988	(k)
241-SX-107	1964	<5000		10/79	1983	(a)
241-SX-108 (6)	1962	2400 to 35000	17 to 140 (m) (q)	8/79	1991	(m) (q)
241-SX-109 (6)	1965	<10000	<40 (n)	5/81	1992	(n)
241-SX-110	1976	5500 (9)		8/79	1989	(g)
241-SX-111	1974	500 to 2000	0.6 to 2.4 (l) (q)	7/79	1986	(d) (q)
241-SX-112	1969	30000	40 (l)	7/79	1986	(d)
241-SX-113	1962	15000	8 (l)	11/78	1986	(d)
241-SX-114	1972	-- (7)		7/79	1989	(g)
241-SX-115	1965	50000	21 (o)	9/78	1992	(o)
241-T-101	1992	7500 (9)		4/93	1992	(p)
241-T-103	1974	<1000 (9)		11/83	1989	(g)
241-T-106	1973	115000 (9)	40 (l)	8/81	1986	(d)
241-T-107	1984	-- (7)		N/A	1989	(g)
241-T-108	1974	<1000 (9)		11/78	1980	(f)
241-T-109	1974	<1000 (9)		12/84	1989	(g)
241-T-111 (5)(13)	1984	<1000 (9)		N/A	1980	(f)
241-TX-105	1977	-- (7)		4/83	1989	(g)
241-TX-107	1984	2500		10/79	1986	(d)
241-TX-110	1977	-- (7)		4/83	1989	(g)
241-TX-113	1974	-- (7)		4/83	1989	(g)
241-TX-114	1974	-- (7)		4/83	1989	(g)
241-TX-115	1977	-- (7)		9/83	1989	(g)
241-TX-116	1977	-- (7)		4/83	1989	(g)
241-TX-117	1977	-- (7)		3/83	1989	(g)
241-TY-101	1973	<1000 (9)		4/83	1980	(f)
241-TY-103	1973	3000	0.7 (l)	2/83	1986	(d)
241-TY-104	1981	1400 (9)		11/83	1986	(d)
241-TY-105	1960	35000	4 (l)	2/83	1986	(d)
241-TY-106	1959	20000	2 (l)	11/78	1986	(d)
241-U-101	1959	30000	20 (l)	9/79	1986	(d)
241-U-104	1961	55000	0.09 (l)	10/78	1986	(d)
241-U-110	1975	5000 to 8100 (9)	0.05 (q)	12/84	1986	(d) (q)
241-U-112	1980	8500 (9)		9/79	1986	(d)
67 Tanks		<600,000 - 900,000 (8)				

N/A = not applicable (not yet interim stabilized)

FOOTNOTES: SEE NEXT PAGE

9413279.0128

TABLE I-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 2 of 4)

Footnotes:

(1) Current estimates (see reference b) are that 610 Kgal of cooling water was added to Tank 241-A-105 from November 1970 to December 1978 to aid in evaporative cooling. In accordance with Dangerous Waste Regulations (Washington Administrative Code 173-303-070 (2)(a)(ii), as amended, Washington State Department of Ecology, 1990, Olympia, Washington), any of this cooling water that has been added and subsequently leaked from the tank must be classified as a waste and should be included in the total leak volume. In August 1991, the leak volume estimate for this tank was updated in accordance with the WAC regulations. Previous estimates excluded the cooling water leaks from the total leak volume estimates because the waste content (concentration) in the cooling water which leaked should be much less than the original liquid waste in the tank (the sludge is relatively insoluble). The total leak volume estimate in this report (10 Kgal to 277 Kgal) is based on the following (see References).

1. Reference (b) contains an estimate of 5 Kgal to 15 Kgal for the initial leak prior to August 1968.

2. Reference (b) contains an estimate of 5 Kgal to 30 Kgal for the leak while the tank was being sluiced from August 1968 to November 1970.

3. Reference (b) contains an estimate of 610 Kgal of cooling water added to the tank from November 1970 to December 1978 but it was estimated that the leakage was small during this period. This reference contains the statement "Sufficient heat was generated in the tank to evaporate most, and perhaps nearly all, of this water." This results in a low estimate of zero gallons leakage from November 1970 to December 1978.

4. Reference (c) contains an estimate that 378 to 410 Kgal evaporated out of the tank from November 1970 to December 1978. Subtracting the minimum evaporation estimate from the cooling water added estimate provides a range from 0 to 232 Kgal of cooling water leakage from November 1970 to December 1978.

	Low Estimate	High Estimate
Prior to August 1968	5,000	15,000
August 1968 to November 1970	5,000	30,000
November 1970 to December 1978	0	232,000
Totals	10,000	277,000

(2) These leak volume estimates do not include (with some exceptions), such things as: (a) cooling/raw water leaks, (b) intrusions (rain infiltration) and subsequent leaks, (c) leaks inside the tank farm but not through the tank liner (surface leaks, pipeline leaks, leaks at the joint for the overflow or fill lines, etc.), and (d) leaks from catch tanks, diversion boxes, encasements, etc.

(3) In many cases, a leak was suspected long before it was identified or confirmed. For example, reference (d) shows that Tank 241-U-104 was suspected of leaking in 1956. The leak was "confirmed" in 1961. This report lists the "assumed leaker" date as 1961. Using present standards, Tank 241-U-104 would have been declared as assumed leaker in 1956. In 1984, the criteria designations of "suspected leaker," "questionable integrity," "confirmed leaker," "declared leaker," "borderline," and "dormant," were merged into one category now reported as "assumed leaker." See reference (f) for explanation of when, how long, and how fast some of the tanks leaked. It is highly likely that there have been undetected leaks from single-shell tanks because of the nature of their design and instrumentation.

(4) There has been an effort in the past two years to reevaluate these leak volume estimates. During the FY 1993 funding reviews, this reevaluation of leak volumes was given a priority which resulted in this activity no longer being funded. The priority versus funding will be reevaluated as part of the prior to FY 1994 budget planning.

(5) The leak volume estimate date for these tanks is before the "declared leaker" date because the tank was in a "suspected leaker" or "questionable integrity" status; however, a leak volume had been estimated prior to the tank being reclassified.

(6) The increasing radiation levels in drywells and laterals associated with these three tanks could be indicative of a continuing leak or movement of existing radionuclides in the soil. There is no conclusive way to confirm these observations.

(7) Methods were used to estimate the leak volumes from these 19 tanks based on the assumption that their cumulative leakage is approximately the same as for 18 of the 24 tanks identified in footnote (10). For more details see reference (g). The total leak volume estimate for these tanks is 150 Kgal (rounded to the nearest 10 Kgal), for an average of approximately 8 Kgal for each of the 19 tanks.

9413279.0129

TABLE I-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES
(Sheet 3 of 4)

(8) The total has been rounded to the nearest 50 Kgal. Upperbound values were used in many cases in developing these estimates. It is likely that some of these tanks have not actually leaked.

(9) Leak volume estimate is based solely on observed liquid level decreases in these tanks. This is considered to be the most accurate method for estimating leak volumes.

(10) The curie content listed is as listed in the reference document and is not decayed to a consistent date; therefore, a cumulative total is inappropriate.

(11) Tank 241-C-101 experienced a liquid level decrease in the late 1960s and was taken out of service and pumped to a "minimum heel" in December 1969. In 1970, the tank was classified as a "questionable integrity" tank. Liquid level data show decreases in level throughout the 1970s and the tank was saltwell pumped during the 1970s, ending in April 1979. The tank was reclassified as a "confirmed leaker" in January 1980. See reference (q) and (s): refer to reference (s) for information on the potential for there to have been leaks from other C-farm tanks (specifically, C-102, C-103, and C-109).

(12) These dates indicate when the tanks were declared to be interim stabilized. In some cases, the official interim stabilization documents were issued at a later date. Also, in some cases, the field work associated with interim stabilization was completed at an earlier date.

(13) Tank 241-T-111 was built in 1944 and placed into service in 1945. The tank was in service, receiving waste from T-Plant, when an unexplained 0.30 inch level decrease was observed in 1974. The tank was then declared "Questionable Integrity" and removed from service. In 1976, 13,000 gallons were transferred to T-101. Inactive saltwell pumping continued to 12/78. It is estimated that 5,000 gallons were removed from the tank. The tank was reclassified as an Assumed Leaker in 1979. The level is known to have increased from at least 160.9 inches in 1979 to 162.6 inches in January 1993. That same month the level decreased sharply to 161.9 inches by the end of the month. From February to July 1993, the rate of decrease slowed until the level reached 161.5 inches. The rate of decrease then accelerated, reaching 161.1 inch by January 1994. Off Normal Occurrence Report RL-WHC-TANKFARM-1994-0009, was issued February 24, 1994. Tank T-111 was declared an assumed re-leaker on February 28, 1994.

9413279.0130

TABLE I-1. SINGLE-SHELL TANK LEAK VOLUME ESTIMATES (Sheet 4 of 4)

References:

(a) Murthy, K.S., et al, June 1983, Assessment of Single-Shell Tank Residual Liquid Issues at Hanford Site, Washington, PNL-4688, Pacific Northwest Laboratory, Richland, Washington.

(b) WHC, 1991a, Tank 241-A-105 Leak Assessment, WHC-MR-0264, Westinghouse Hanford Company, Richland, Washington.

(c) WHC, 1991b, Tank 241-A-105 Evaporation Estimate 1970 Through 1978, WHC-EP-0410, Westinghouse Hanford Company, Richland, Washington.

(d) Smith, D. A., January 1986, Single-Shell Tank Isolation Safety Analysis Report, SD-WM-SAR-006, Rev. 1, Westinghouse Hanford Company, Richland, Washington.

(e) McCann, D. C., and T. S. Vail, September 1984, Waste Status Summary, RHO-RE-SR-14, Rockwell Hanford Operations, Richland, Washington.

(f) Catlin, R. J., March 1980, Assessment of the Surveillance Program of the High-Level Waste Storage Tanks at Hanford, Hanford Engineering Development Laboratory, Richland, Washington.

(g) Baumhardt, R. J., May 15, 1989, Letter to R. E. Gerton, U.S. Department of Energy-Richland Operations Office, Single-Shell Tank Leak Volumes, Westinghouse Hanford Company, Richland, Washington.

(h) WHC, 1990a, Occurrence Report, Surface Level Measurement Decrease in Single-Shell Tank 241-AX-102, WHC-UO-89-023-TF-05, Westingnouse Hanford Company, Richland, Washington.

(i) Groth, D. R., July 1, 1987, Internal Memorandum to R. J. Baumhardt, Liquid Level Losses in Tanks 241-C-201, -202 and -204, 65950-87-517, Westinghouse Hanford Company, Richland, Washington.

(j) Groth, D. R. and G. C. Owens, May 15, 1987, Internal Memorandum to J. H. Roecker, Tank 103-A Integrity Evaluation, Westinghouse Hanford Company, Richland, Washington.

(k) Campbell, G. D., July 8, 1988, Internal Memorandum to R. K. Welty, Engineering Investigation: Interstitial Liquid Level Decrease in Tank 241-SX-104, 13331-88-416, Westinghouse Hanford Company, Richland, Washington.

(l) ERDA, 1975, Final Environmental Statement Waste Management Operations, Hanford Reservation, Richland, Washington, ERDA-1538, 2 vols., U.S. Energy Research and Development Administration, Washington, D.C.

(m) WHC, 1992a, Tank 241-SX-108 Leak Assessment, WHC-MR-0300, Westinghouse Hanford Company, Richland, Washington.

(n) WHC, 1992b, Tank 241-SX-109 Leak Assessment, WHC-MR-0301, Westinghouse Hanford Company, Richland, Washington.

(o) WHC, 1992c, Tank 241-SX-115 Leak Assessment, WHC-MR-0302, Westinghouse Hanford Company, Richland, Washington.

(p) WHC, 1992d, Occurrence Report, "Apparent Decrease in Liquid Level in Single Shell Underground Storage Tank 241-T-101, Leak Suspected; Investigation Continuing," RL-WHC-TANKFARM-1992-0073, Westinghouse Hanford Company, Richland, Washington.

(q) WHC-1990b, A History of the 200 Area Tank Farms, WHC-MR-0132, Westinghouse Hanford Company, Richland, Washington.

(r) WHC, 1993, Occurrence Report, Single-Shell Underground Waste Storage Tank 241-BX-111 Surface Level Decrease and Change From Steady State Condition, RL-WHC-TANKFARM-1993-0035, Westinghouse Hanford Company, Richland, Washington.

(s) WHC, 1993a, Assessment of Unsaturated Zone Radionuclide Contamination Around Single-Shell Tanks 241-C-105 and 241-C-106, WHC-SD-EN-TI-185, REV OA, Westinghouse Hanford Company, Richland, Washington.

9413279.0131

9413279.0132

APPENDIX J

INTERIM STABILIZATION STATUS

This page intentionally left blank.

9413279.0133

TABLE J-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (Sheet 1 of 2)

March 31, 1994

Tank Number	Tank Integrity	Interim Stabilized Date (1)	Stabilized Method (2)(3)	Tank Number	Tank Integrity	Interim Stabilized Date (1)	Stabilized Method (2)(3)	Tank Number	Tank Integrity	Interim Stabilized Date (1)	Stabilized Method (2)(3)
A-101	SOUND	N/A		C-101	ASMD LKR	11/83	AR	T-108	ASMD LKR	11/78	AR
A-102	SOUND	08/89	SN	C-102	SOUND	N/A		T-109	ASMD LKR	12/84	AR
A-103	ASMD LKR	06/88	AR	C-103	SOUND	N/A		T-110	SOUND	N/A	
A-104	ASMD LKR	09/78	AR	C-104	SOUND	09/89	SN	T-111	ASMD LKR	N/A	
A-105	ASMD LKR	07/79	AR	C-105	SOUND	N/A		T-112	SOUND	03/81	AR
A-106	SOUND	08/82	AR	C-106	SOUND	N/A		T-201	SOUND	04/81	AR
AX-101	SOUND	N/A		C-107	SOUND	N/A		T-202	SOUND	08/81	AR
AX-102	ASMD LKR	09/88	SN	C-108	SOUND	03/84	AR	T-203	SOUND	04/81	AR
AX-103	SOUND	08/87	AR	C-109	SOUND	11/83	AR	T-204	SOUND	08/81	AR
AX-104	ASMD LKR	08/81	AR	C-110	ASMD LKR	N/A		TX-101	SOUND	02/84	AR
B-101	ASMD IKR	03/81	SN	C-111	ASMD LKR	03/84	SN	TX-102	SOUND	04/83	JET
B-102	SOUND	06/85	SN	C-112	SOUND	09/90	AR	TX-103	SOUND	06/83	JET
B-103	ASMD IKR	02/85	SN	C-201	ASMD LKR	03/82	AR	TX-104	SOUND	09/79	SN
B-104	SOUND	06/85	SN	C-202	ASMD LKR	08/81	AR	TX-105	ASMD LKR	04/83	JET
B-105	ASMD IKR	12/84	AR	C-203	ASMD LKR	03/82	AR	TX-106	SOUND	06/83	JET
B-106	SOUND	03/85	SN	C-204	ASMD LKR	09/82	AR	TX-107	ASMD LKR	10/79	AR
B-107	ASMD LKR	03/85	SN	S-101	SOUND	N/A		TX-108	SOUND	03/83	JET
B-108	SOUND	05/85	SN	S-102	SOUND	N/A		TX-109	SOUND	04/83	JET
B-109	SOUND	04/85	SN	S-103	SOUND	N/A		TX-110	ASMD LKR	04/83	JET
B-110	ASMD LKR	12/84	AR	S-104	ASMD LKR	12/84	AR	TX-111	SOUND	04/83	JET
B-111	ASMD LKR	06/85	SN	S-105	SOUND	09/88	JET	TX-112	SOUND	04/83	JET
B-112	ASMD LKR	05/85	SN	S-106	SOUND	N/A		TX-113	ASMD LKR	04/83	JET
B-201	ASMD LKR	08/81	AR	S-107	SOUND	N/A		TX-114	ASMD LKR	04/83	JET
B-202	SOUND	05/85	AR	S-108	SOUND	N/A		TX-115	ASMD LKR	06/83	JET
B-203	ASMD LKR	06/84	AR	S-109	SOUND	N/A		TX-116	ASMD LKR	04/83	JET
B-204	ASMD LKR	06/84	AR	S-110	SOUND	N/A		TX-117	ASMD LKR	03/83	JET
BX-101	ASMD LKR	09/78	AR	S-111	SOUND	N/A		TX-118	SOUND	04/83	JET
BX-102	ASMD LKR	11/78	AR	S-112	SOUND	N/A		TY-101	ASMD LKR	04/83	JET
BX-103	SOUND	11/83	AR	SX-101	SOUND	N/A		TY-102	SOUND	09/79	AR
BX-104	SOUND	09/89	SN	SX-102	SOUND	N/A		TY-103	ASMD LKR	02/83	JET
BX-105	SOUND	03/81	SN	SX-103	SOUND	N/A		TY-104	ASMD LKR	11/83	AR
BX-106	SOUND	N/A		SX-104	ASMD LKR	N/A		TY-105	ASMD LKR	02/83	JET
BX-107	SOUND	09/90	JET	SX-105	SOUND	N/A		TY-106	ASMD LKR	11/78	AR
BX-108	ASMD LKR	07/79	SN	SX-106	SOUND	N/A		U-101	ASMD LKR	09/79	AR
BX-109	SOUND	09/90	JET	SX-107	ASMD LKR	10/79	AR	U-102	SOUND	N/A	
BX-110	ASMD LKR	08/85	SN	SX-108	ASMD LKR	08/79	AR	U-103	SOUND	N/A	
BX-111	ASMD LKR	N/A		SX-109	ASMD LKR	05/81	AR	U-104	ASMD LKR	10/78	AR
BX-112	SOUND	09/90	JET	SX-110	ASMD LKR	08/79	AR	U-105	SOUND	N/A	
BY-101	SOUND	05/84	JET	SX-111	ASMD LKR	07/79	SN	U-106	SOUND	N/A	
BY-102	SOUND	N/A		SX-112	ASMD LKR	07/79	AR	U-107	SOUND	N/A	
BY-103	ASMD LKR	N/A		SX-113	ASMD LKR	11/78	AR	U-108	SOUND	N/A	
BY-104	SOUND	01/85	JET	SX-114	ASMD LKR	07/79	AR	U-109	SOUND	N/A	
BY-105	ASMD LKR	N/A		SX-115	ASMD LKR	09/78	AR	U-110	ASMD LKR	12/84	AR
BY-106	ASMD LKR	N/A		T-101	ASMD LKR	04/93	SN	U-111	SOUND	N/A	
BY-107	ASMD LKR	07/79	JET	T-102	SOUND	03/81	AR	U-112	ASMD LKR	09/79	AR
BY-108	ASMD LKR	02/85	JET	T-103	ASMD LKR	11/83	AR	U-201	SOUND	08/79	AR
BY-109	SOUND	N/A		T-104	SOUND	N/A		U-202	SOUND	08/79	SN
BY-110	SOUND	01/85	JET	T-105	SOUND	06/87	AR	U-203	SOUND	08/79	AR
BY-111	SOUND	01/85	JET	T-106	ASMD LKR	08/81	AR	U-204	SOUND	08/79	SN
BY-112	SOUND	06/84	JET	T-107	ASMD LKR	N/A					

LEGEND:
AR = Administratively interim stabilized
JET = Saltwell jet pumped to remove drainable interstitial liquid
SN = Supernate pumped (Non-Jet pumped)
N/A = Not yet interim stabilized
ASMD LKR = Assumed Leaker

Interim Stabilized Tanks	106
Not Yet Interim Stabilized	43
Total Single-Shell Tanks	149

Footnotes: See next page

9413279.0134

TABLE J-1. SINGLE-SHELL TANKS INTERIM STABILIZATION STATUS (sheet 2 of 2)

Footnotes:

(1) These dates indicate when the tanks were actually interim stabilized. In some cases, the official interim stabilization documents were issued at a later date.

(2) The following six tanks do not meet current established supernatant and interstitial liquid interim stabilization criteria, but did meet the criteria in existence when they were declared interim stabilized :

B-104, 110, 111
T-102, 112
U-110

(3) Interim Stabilization data are missing on four tanks. These tanks were Administratively Interim Stabilized.

B-201, T-102, 112, 201

9413279.0135

TPA SST STABILIZATION SCHEDULE
(START OF PUMPING/COMPLETION OF PUMPING)

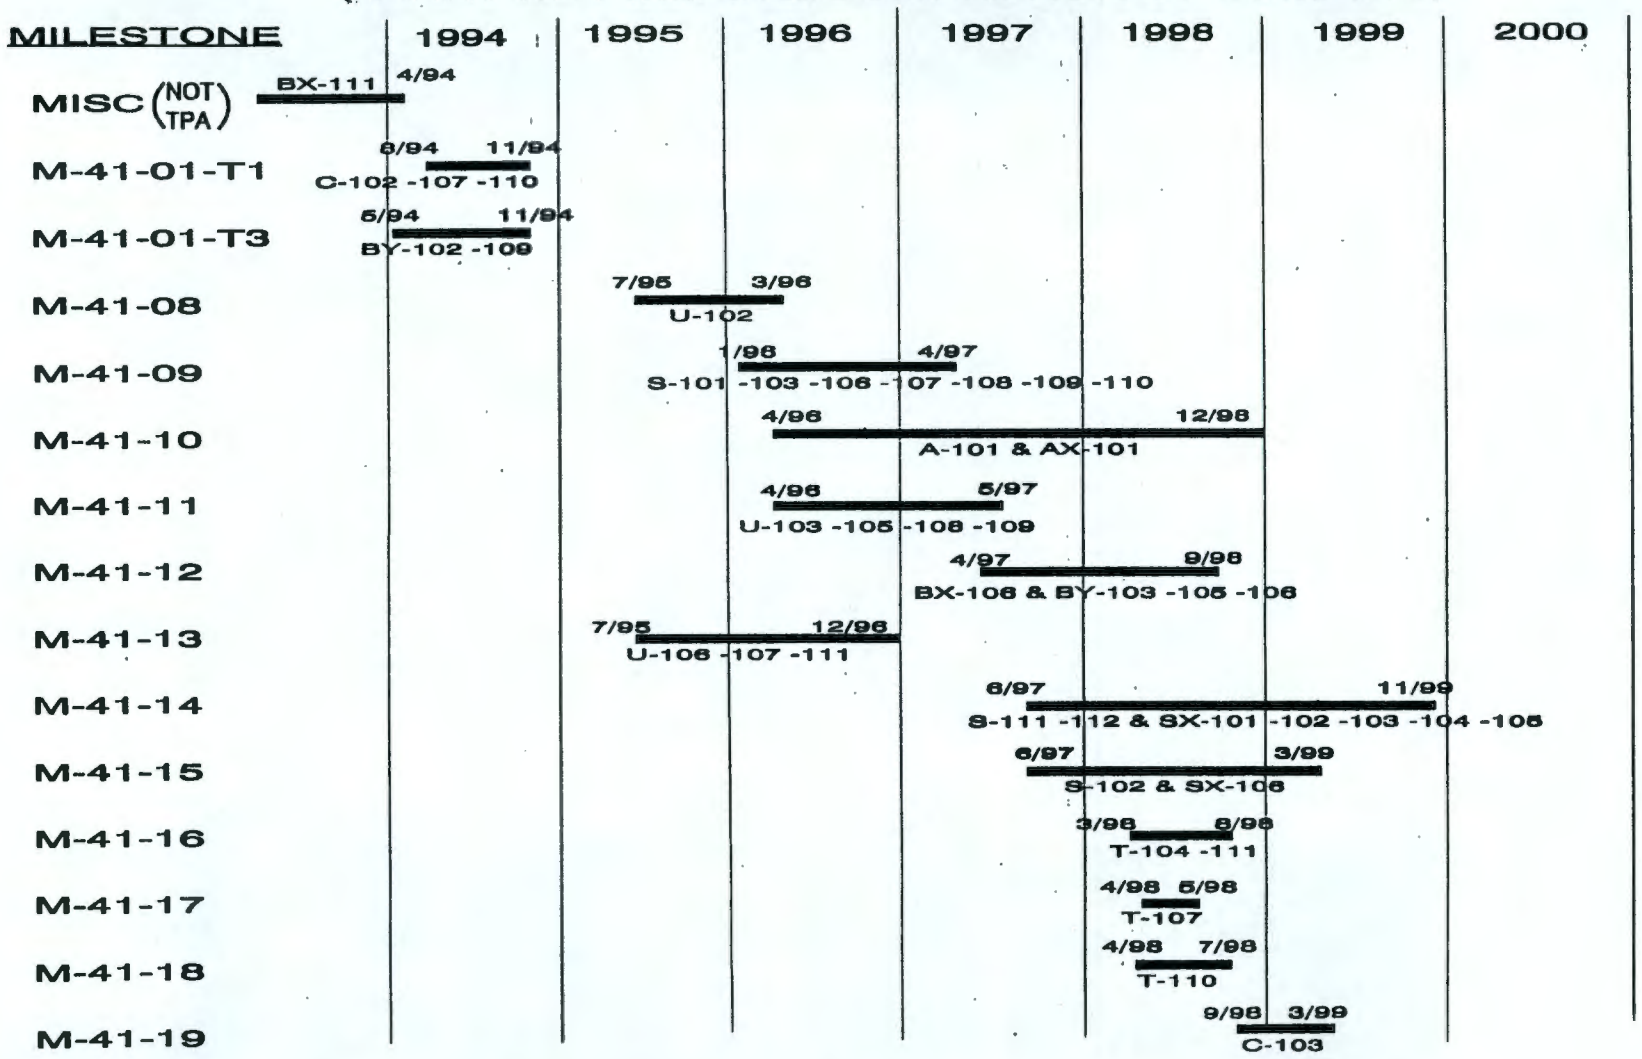

NOTE: C-105 & C-106 NOT INCLUDED IN THIS SCHEDULE

This page intentionally left blank

9413279.0132

9413229.0138

APPENDIX K

TANK FARM OPERATIONS SAMPLING SCHEDULE STATUS

This page intentionally left blank

9413279.0139

TABLE K-1. TANK FARM OPERATIONS SAMPLING SCHEDULE STATUS (Sheet 1 of 2)

ACTIVITY ID	ACTIVITY DESCRIPTION		EARLY START	EARLY FINISH	OBS1
VS55-4	TAKE SAMPLES SJ-4/SJ-4\5 Vapor C-103		12NOV93A	16NOV93A	1
VS46-4	C-103 VAPOR SAMPLE INS PROBE. TAKE SAMPLES-SJ-6		14DEC93A	15DEC93A	2
VS36-4	C-103 VAPOR SAMPLE Using VSS Truck - SJ-6b		25JAN94A	25JAN94A	3
VS03-4	C-105/106 VAPOR SAMPLE (B, C)		14FEB94A	17FEB94A	4
VS99-4	C-104 VAPOR SAMPLE (B, C)		22FEB94A	3MAR94A	5
GS11-4	T-111 GRAB SAMPLE (EMERGENT WORK)		5MAR94A	5MAR94A	6
GS01-4	SY-102 GRAB SAMPLE (EMERGENT WORK)		10MAR94A	10MAR94A	7
VS98-4	BY-108 VAPOR SAMPLE FeCn		24MAR94A	25MAR94A	8
VS97-4	BY-107 VAPOR SAMPLE FeCn		25MAR94A	28MAR94A	9
PS01-4	C-111 PUSH MODE SAMPLING Samples 2-3 Seg 2	222S	31MAR94A	27APR94	10
VS47-4	C-103 VAPOR SAMPLE - SJ-7a		8APR94A	8APR94A	11
TC05-4	BY-107 FeCN THERMOCOUPLE INSTALLATION		12APR94A	12APR94A	12
VS74-4	BY RISER INSP BY103\104\105\106\111 VS (A)		21APR94A	3MAY94	13
GS03-4	TX-244 GRAB SAMPLE (EMERGENT WORK)		26APR94	26APR94	14
TC09-4	BY-108 FeCN THERMOCOUPLE INSTALLATION	222S	26APR94	27APR94	15
PS11-4	C-108 PUSH MODE SAMPLE (B)	222S	3MAY94	9MAY94	16
VSA8-4	C RISER INSP C101\108\C105\C110\C112 VS (A)		13NOV93A	11MAY94	17
GS54-4	S-110 PROCESS GRAB SAMPLE		4MAY94	5MAY94	18
TC26-4	C-111 FeCN THERMOCOUPLE INSTALLATION		11MAY94	12MAY94	19
GS51-4	AP-108 GRAB SAMPLE/EVAPORATOR FEED		21MAR94A	16MAY94	20
AS01-4	SY-103 AUGER SAMPLE Samples 3	222S	13MAY94	20MAY94	21
GS55-4	AN-107 SLUDGE SAMPLING		16MAY94	17MAY94	22
GS21-4	AN-102 GRAB SAMPLING RCRA	325	19MAY94	20MAY94	23
GS52-4	AY-102 PROCESS GRAB SAMPLE		12MAY94	13MAY94	24
AS07-4	BX-108 AUGER SAMPLING Sample 1 Segments 1	222S	23MAY94	24MAY94	25
GS15-4	BY-106 PROCESS GRAB SAMPLING		23MAY94	24MAY94	26
TC14-4	TY-104 FeCN THERMOCOUPLE INSTALLATION		23MAY94	24MAY94	27
VS22-4	TY RISER INSPECTION TY101\103\104 VS (A)		24MAY94	31MAY94	28
VS34-4	U RISERS INSPECTION\ U-106\107\111 VS (A)		24MAY94	31MAY94	29
AS08-4	BX-105 AUGER SAMPLING Sample 1 Segments 4		25MAY94	26MAY94	30
GS24-4	T-111 SLUDGE PROCESS SAMPLE		25MAY94	26MAY94	31
AS03-4	BX-101 AUGER SAMPLING Samples 1 Segments 1	325	27MAY94	31MAY94	32
GS06-4	AZ-102 RCRA GRAB SAMPLE		27MAY94	31MAY94	33
AS05-4	B-102 AUGER SAMPLING Sample 1 Segments 1	325	1JUN94	2JUN94	34
RS02-4	C-106 ROTARY SAMPLING Samples 2 Seg 5	325	2JUN94	15JUN94	35
TC15-4	TY-101 FeCN THERMOCOUPLE INSTALLATION		2JUN94	3JUN94	36
AS10-4	AX-102 AUGER SAMPLING Sample 1 Segment 1	325	7JUN94	8JUN94	37
AS99-4	C-102 AUGER SAMPLING Samples 1 Segments 1		7JUN94	8JUN94	38
AS04-4	AN-101 AUGER SAMPLING Sample 1 Segments 1	222S	9JUN94	10JUN94	39
AS09-4	TX-118 AUGER SAMPLE		9JUN94	10JUN94	40
GS10-4	T-104 PROCESS GRAB SAMPLE		13JUN94	14JUN94	41
GS18-4	T-102 PROCESS GRAB SAMPLING		13JUN94	14JUN94	42
PS08-4	C-104 PUSH SAMPLING Sample 2 Segments 6	222S	13JUN94	24JUN94	43
TC34-4	U-106 VAPOR (A) THERMOCOUPLE\VAPOR TUBE INSTALL		13JUN94	14JUN94	44
VS13-4	BX-104\BX106 VAPOR SAMPLE (A)		13JUN94	14JUN94	45
RS03-4	BY-104 ROTARY MODE Samples 2 Segments 8		16JUN94	15JUL94	46
GS41-4	BY-103 PROCESS GRAB SAMPLE (PROCESS) BY-103		21JUN94	27JUN94	47
VS04-4	C-108 VAPOR SAMPLE (B)		22JUN94	23JUN94	48
VS89-4	U-106 VAPOR SAMPLE (B) (FOLLOWS VAPOR TUBE INS)		22JUN94	23JUN94	49

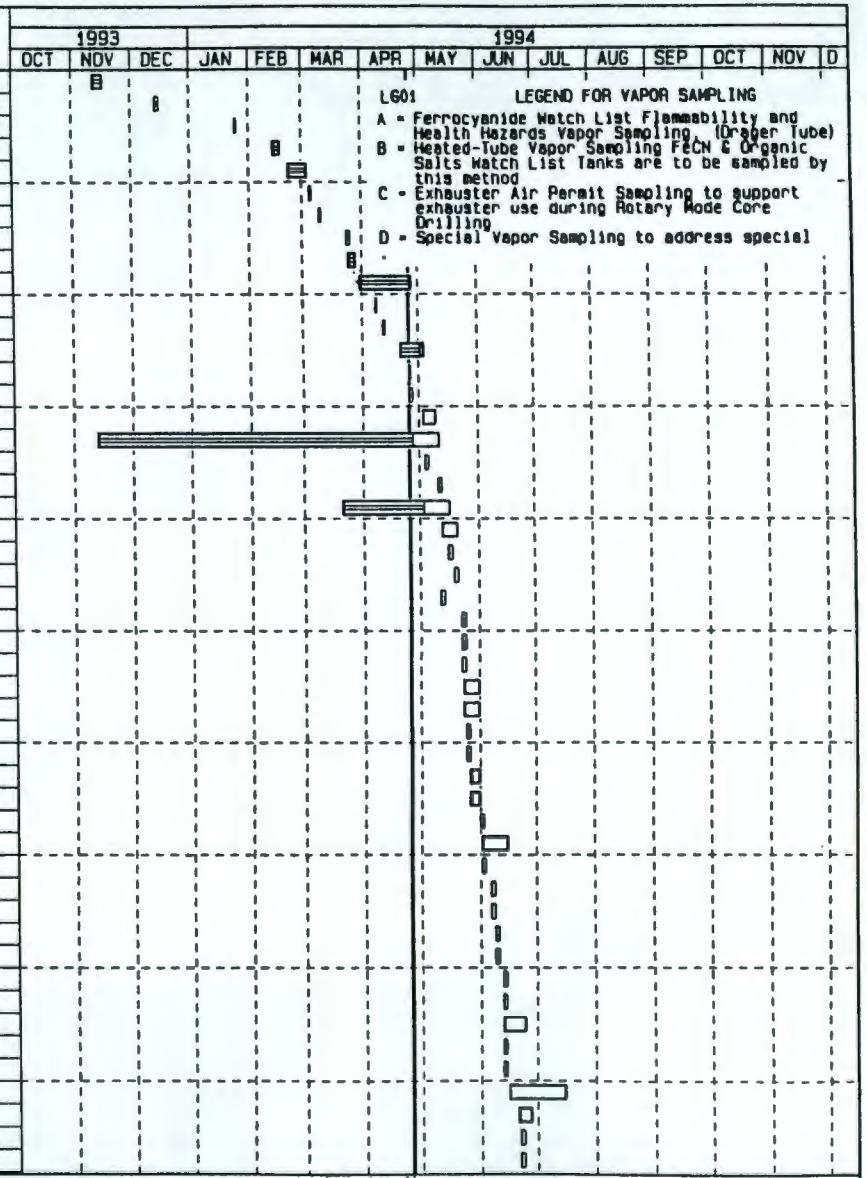

Plot Date 25APR94
Data Date 26APR94
Project Start 10OCT93
Project Finish 10JUL96

(c) Primavera Systems, Inc.

Activity Bar/Early Dates
Critical Activity
Progress Bar
Milestone/Flag Activity

DMS

TANK FARMS OPERATIONS DATA DATE 4\19
PREL DRAFT REBASELINE SCHED
Summary Field Work Sched Sort ES

Sheet 1 of 2

DA Healey 372-3698 for D. Hamilton 373-0259

Date	Revision	Checked	Approved

TABLE K-1. TANK FARM OPERATIONS SAMPLING SCHEDULE STATUS (Sheet 2 of 2)

ACTIVITY ID	ACTIVITY DESCRIPTION	EARLY START	EARLY FINISH	OBS1
PS05-4	C-103 PUSH SAMPLING Sample 1 Segments 22	27JUN94	1JUL94	50
TC39-4	U-111 THERMOCOUPLE\VAPOR TUBE INSTALLATION	27JUN94	28JUN94	51
VS06-4	BY-104\105\106 VAPOR SAMPLE (A, B, HCN)	27JUN94	6JUL94	52
GS02-4	BY-105 PROCESS GRAB SAMPLING	28JUN94	29JUN94	53
VS67-4	TX-118 VAPOR SAMPLE (A, HCN)	28JUN94	29JUN94	54
VS23-4	T RISER INSPECTION T-107\111 VS (A)	29JUN94	28JUL94	55
GS05-4	AW-104 RCRA GRAB SAMPLING RCRA 325	30JUN94	1JUL94	56
GS53-4	T-112 PROCESS GRAB SAMPLE	30JUN94	1JUL94	57
GS07-4	T-107 PROCESS GRAB SAMPLING	1JUL94	6JUL94	58
TC21-4	T-107 FeCN VAPOR SAMPLE & THERMOCOUPLE INS (A)	1JUL94	6JUL94	59
VS52-4	BY-111 VAPOR SAMPLE (HCN)	1JUL94	6JUL94	60
VS76-4	C-109 VAPOR SAMPLING (A, B)	1JUL94	6JUL94	61
AS06-4	AX-104 AUGER SAMPLING Sample 1 Segments 1	6JUL94	7JUL94	62
PS25-4	C-105 Sludge VS & Push Mode Sample 1 Segment 3	6JUL94	12JUL94	63
VS66-4	U-111 VAPOR SAMPLE (B) (FOLLOWS VAPOR TUBE INS)	8JUL94	11JUL94	64
PS20-4	AN107 OH Consumer VS & Push Mode Samp 1 Seg 21	13JUL94	19JUL94	65
RS04-4	BY-106 ROTARY MODE Samples 2 Segments 12	18JUL94	12AUG94	66
VS12-4	C-111 VAPOR SAMPLING (B)	19JUL94	20JUL94	67
PS24-4	AY101 D.NCX VS & Push Mode Sample 1 Segment 2	20JUL94	26JUL94	68
TC16-4	TY-103 FeCN THERMOCOUPLE INSTALLATION	26JUL94	27JUL94	69
PS23-4	AZ102 Aging Waste VS & Push Mode Samp 1 Seg	27JUL94	2AUG94	70
GS33-4	BX-106 GRAB SAMPLE	1AUG94	2AUG94	71
GS44-4	AY-101 VAPOR SAMPLE (A) AND GRAB SAMPLE RCRA	1AUG94	2AUG94	72
AS11-4	A-104 AUGER SAMPLING Sample 1 Segment 1	3AUG94	4AUG94	73
PS02-4	SY-103 PUSH SAMPLING Samples 1 Segments 15	3AUG94	9AUG94	74
VS35-4	C-112 VAPOR SAMPLE (A, B)	3AUG94	4AUG94	75
PS06-4	AY-102 PUSH MODE CORE SAMPLING Sample 1 Segm 1	10AUG94	16AUG94	76
GS14-4	S-102 GRAB SAMPLE VAPOR SAMPLE (A)	15AUG94	16AUG94	77
RS01-4	BY-105 ROTARY MODE Samples 2 Segments 1	15AUG94	12SEP94	78
TC43-4	BY-103 FeCN VAPOR SAMPLE & THERMOCOUPLE INS (A)	15AUG94	16AUG94	79
VS02-4	C-101 VAPOR SAMPLE (B)	15AUG94	16AUG94	80
PS22-4	T-101 FeCN VS & Push Mode Sample 2 Segment 3	17AUG94	30AUG94	81
GS13-4	BX-106 VAPOR SAMPLE (A) PROCESS GRAB SAMPLE	29AUG94	30AUG94	82
TC36-4	BX-102 FeCN VAPOR SAMPLE (HCN) THERMOCOUPLE INS	29AUG94	30AUG94	83
VS33-4	BX RISER INSP BX-102\104\106\110\111 VS (A)	29AUG94	29AUG94	84
PS21-4	BX102 FeCN VS & Push Mode Sample 2 Segment 2	31AUG94	14SEP94	85
AS12-4	U-107 AUGER SAMPLING Sample 1 Segment 1	1SEP94	2SEP94	86
GS08-4	U-107 VAPOR SAMPLE (A) GRAB SAMPLING	1SEP94	2SEP94	87
GS07-4	AN-107 GRAB SAMPLE/RCRA	1SEP94	2SEP94	88
VS01-4	C-102 VAPOR SAMPLE (B)	1SEP94	2SEP94	89
GS09-4	U-106 PROCESS GRAB SAMPLE	6SEP94	7SEP94	90
RS05-4	U-111 ROTARY SAMPLING Samples 2 Segments 3	13SEP94	10OCT94	91
VS19-4	C-107 VAPOR SAMPLING (B)	15SEP94	16SEP94	92
RS06-4	U-106 ROTARY SAMPLING Sample 3 Segments 5	11OCT94	21NOV94	93
TC38-4	U-107 THERMOCOUPLE INSTALLATION	2NOV94	3NOV94	94
VS45-4	B-103 VAPOR SAMPLE (A) (B)	17NOV94	18NOV94	95
RS07-4	S-106 ROTARY SAMPLING	22NOV94	21DEC94	96
TC31-4	B-103 THERMOCOUPLE INSTALLATION	28NOV94	29NOV94	97

Plot Date 25APR94
Data Date 26APR94
Project Start 10CT93
Project Finish 10JUL96

(c) Primavera Systems, Inc.

Activity Bar/Early Dates
Critical Activity
Progress Bar
Milestone/Flag Activity

CHA1

TANK FARMS OPERATIONS DATA DATE 4\19
PREL DRAFT REBASELINE SCHED
Summary Field Work Sched Sort ES

Sheet 2 of 2

DA Healey 372-3698 for D. Hamilton 373-0259

Date	Revision	Checked	Approved

DISTRIBUTION

Number of copies

OFFSITE - USA

3 **Congress of the United States**
House of Representatives
1111 Longworth Building
Washington, DC 20515-3703

Ron Wyden, Member of Congress, 3rd District
Josh Kardon, Legislative Director

House of Representatives
1431 Longworth House Office Building
Washington D. C. 20515

Jay Inslee, Member of Congress, 4th District
Atten: Louis J. Alex, Legislative Assistant

19 **U. S. Department of Energy-Headquarters**
1000 Independence Avenue, SW
Washington, D. C. 20585

Jim Antizzo	EM-36	TREV II/364
Emile Bernard	EM-50	TREV II
H. Calley	EM-36	TREV II
H. Eckert	EM-37	TREV II
Teresa Fryberger	EM-542	TREV II
Sherry Gibson	EM-55	TREV II
A. Griffith	EM-36	TREV II/341
L. Gunn	EM-36	TREV II
D. Gupta	EM-36	TREV II
Kenneth Lang	EM-36	TREV II
J. C. Lehr	EM-442	TREV II/160
G. Mellinger	EM-36	TREV II
C. O'Dell	EM-36	TREV II
D. Pepson	EM-36	TREV II
J. C. Tseng	EM-36	TREV II/364
S. Woodbury	EH-222	FORS/3G-092

19901 Germantown Rd,
Germantown, MD 20585

R. Lasky	EH-32.1	GTN/G-115
J. Psaras	NS-20 GTN	
P. Worthington	NS-20 GTN	

1 **U. S. Department of Energy - Oak Ridge Operations Office**
P. O. Box 2001
Oak Ridge, TN 37831

W. D. Adams EW-40

9413279.0142

Distribution - continued

7 **U. S. Department of Energy - Savannah River Site**
P. O. Box A
Aiken, SC 29808

C. Anderson	707-H
Michael Chandler	703-H
Mazen Shurrab	704-H
T. C. Temple	
L. Sjostrom	
W. R. West	704-8H
V. Wheeler	704-S

1 **U. S. Environmental Protection Agency**
Region 10
712 Swift Boulevard, Suite 5
Richland, WA 99352

D. R. Sherwood

8 **Washington State Department of Ecology**
Nuclear & Mixed Waste Management Program
P.O. Box 47600
Olympia, WA 98504-7600

M. T. Gordon
M. Lerchan
Scott McKinney
R. Stanley
Library

7601 W. Clearwater #102
Kennewick, WA 99336

S. V. Moore
G. T. Tebb
Office Library

1 **Washington State Department of Health**
Radiation Protection Section
Industrial Park Building 5, LE-13
Olympia, WA 98504

A. Conklin

1 **General Accounting Office**
P. O. Box 321
Richland, WA 99352

C. R. Abraham

9413279.0143

Distribution - continued

1 **Oregon State Department of Energy**
625 Marion St. N.E.
Salem, OR 97310

Janet Franco

1 **Oregon State Water Resources Department**
Ground Water Hanford Studies
3850 Portland Road
Salem, OR 97310

R. O. Patt

1 **Lawrence Livermore National Laboratory**
Box 808, East Avenue
Livermore, CA 94550

B. C. Hudson L-221

5 **Oak Ridge National Laboratory**
P. O. Box 2009
Oak Ridge, TN 37831-6385

C. Forsberg MS-6495
T. S. Kress MS-8088
Bldg 9108

Chemical Technology Division
P. O. Box 2008

Emory D. Collins
C. Phil McGinnis
Dr. Jack Watson

7 **Los Alamos National Laboratory**
P. O. Box 1663
Los Alamos, NM 87545

Stephen Agnew
Group INC-14 C-346
Phyllis Baca J-514
T. Larson C-915
Sylvia Lee K-557
A. Nuels N-6
H. Sullivan N-6
Dr. Reed Jensen J-565

9413279.0144

Distribution - continued

5 **Brookhaven National Laboratory**
Upton, NY 11973

K. K. Bandyopadhyay, Bldg 475-C
M. K. Kaisser, Bldg 475-C
P. D. Kalb, Bldg. 703
M. Reich, Bldg 475-C
J. R. Weeks, Bldg 197-C

1 **Brookhaven National Laboratory**
1409 Jan Drive
Wilmington, DE 19803

Michael Streicher

2 **Argonne National Laboratory**
9700 South Cass Avenue
Argonne, IL 60439

Dr. Martin Steindler
Dr. George Vandergrift

5 **Sandia National Laboratories**
1515 Eubank, NE
P. O. Box 5800
Albuquerque, NM 87185

Scott Slezak, Division 6471
Leon D. Chapman, Program Manager
Industrial Waste Reduction Program
Dr. Margaret Chu, Organ #6622
Elmer Klavetter, Mail Stop 0709
Norman E. Brown, Mail Stop 0728

1 **Massachusetts Institute of Technology**
77 Massachusetts Avenue
Cambridge, MA 02139

Mujid S. Kazimi
Professor and Head
Department of Nuclear Engineering

2 **BDM International, Inc.**
20030 Century Blvd, Suite 101
Germantown, MD 20874

P. Kiang
K. J. Mahoney

9413279.0145

Distribution - continued

7 **SAIC**
Trevion 1, Suite 300
20300 Century Blvd.
Germantown, MD 20874

J. Bunting
J. R. Pearring
R. A. Wullaert

102 Windham Road
Oak Ridge, TN 37830

D. O. Campbell

1845 Terminal Drive, Suite 130
Richland, WA 99352

J. Mishima

555 Quince Orchard Road
Gaithersburg, MD 20878

Paul Szerszen

507 Knight Street, Suite B
Richland, WA 99352

Pete Lowry

1 **Harvard University**
295 Upland Avenue
Newton Highlands, MA 02161

Melvin First

1 **Syracuse University**
334 Hinds Hall
Chemical Engineering & Materials Science Department
Syracuse, NY 13244

Dr. Larry Tavlarides

1 **University of Washington**
Chemical Engineering Department
Benson Hall, BF-10
Seattle, WA 98195

Professor Gene Woodruff

9410.6279.0146

Distribution - continued

1 **Washington State University**
Department of Mechanical & Materials Engineering
Pullman, WA 99164-2920

Dr. Steve Antolovich, Chairman

1 **Confederated Tribes, Umatilla Indian Reservation**
P. O. Box 638
Pendleton, OR 97801

Rick George

5 **West Valley Nuclear Services Co.**
P. O. Box 191
West Valley, NY 14171

K. K. Gupta	MS-49
S. Ketola	MS-191
D. K. Ploetz	MS-305
Ram Shukla	
Don Stroud	

1 **K & M Engineering & Consulting Corporation**
Suite 500
2001 L St. NW
Washington, D. C. 20036

Ryan Gill

5 **Defense Nuclear Facilities Safety Board**
625 Indiana Ave, N. W., Suite 700
Washington, D. C. 20004

Ralph Arcaro	
Lester Clemons	Suite 700
Steven Stokes	
Richard Tontodonato	
Dermot Winters	

3 **Westinghouse Idaho Nuclear Corporation**
P. O. Box 4000
Idaho Falls, ID 83404-4000

B. Griebenow	MS-5104
A. P. Hoskins	MS-5217
Dr. Terry Todd	

1 C. Abrams
1987 Virginia Drive
Idaho Falls, ID 83404

9413279.0147

Distribution - continued

1 Fred N. Carlson
6965 North 5th West
Idaho Falls, ID 83401

1 Dr. A. Veletsos
Department of Civil Engineering
Rice University
P. O. Box 1892
Houston, TX 77252

2 Westinghouse Electric Corporation
1801 K Street NW, 8th floor
Washington DC, 20006

Kevin Billings

6 Gateway Center
Pittsburgh, PA 15222

Steve Green, Manager
Westinghouse Environmental Affairs

1 Westinghouse Materials Company of Ohio
P. O. Box 398704
Cincinnati OH 45239-8704

David L. Jacoboski
Senior Engineer, Technology Demonstration

6 Westinghouse Savannah River Company
P. O. Box 616
Aiken, SC 29802

D. M. Barnes, 773-41A
J. R. Chandler, 703-H
P. d'Entremont
F. G. McNatt, 704-8A
Dr. Major Thompson

1991 S. Centennial Ave.
Aiken, SC 29803

L. A. Wooten

1 Institute for Energy and Environmental Reseach
6935 Laurel Avenue
Takoma Park, MD 20912

Dr. Arjun Makhijani, President

9413279.0148

Distribution - continued

1 **SPAR Aerospace Ltd.**
20 Avon Meadow Lane, Suite 220
Avon, CT 06001

Peter W. Kruse
Advanced Technology Systems Division

1 **Redzone Robotics, Inc.**
2425 Liberty Ave
Pittsburgh, PA 15222-4639

David W. White

6 **National Research Council, National Academy of Sciences**
2101 Constitution Ave., N. W.
Washington D. C. 20418

Robert S. Andrews, Senior Staff Officer
Board on Radioactive Waste Management

1 **Converse Consultants**
18 W. Mercer Street, Suite 300
Seattle, WA 98119

David Stanley

1 **Brown & Caldwell**
100 W. Harrison
Seattle, WA 98119

Hal Cooper

1 **Benton County Department of Emergency Management**
P.O. Box 6144
Kennewick, WA 99336

Gary Pira

1 **BOVAY Northwest Inc.**
660 Swift, Suite D
Richland, WA 99352

T. J. McLaughlin

1 **Omega Environmental Technology**
655 Montgomery Street, Suite 1000
San Francisco, CA 94111

Mike Bailey

9413279.0149

Distribution - continued

1 <u>Schilling Development, Inc.</u>
1632 DaVinci Court
Davis, CA 95616

Wes Gerriets

1 T. S. Elleman
North Carolina State University
Department of Nuclear Energy
P. O. Box 7909
Raleigh, NC 27606

1 Mike Lingle
Stone & Webster
7677 E. Berry Ave
Englewood, CA 80111

1 Bryant Mather
Corps of Engineers
WESSV-Z
3909 Halls Ferry Rd
Vicksburg, MS 39180-6199

1 Paul Shewmon
Prof. Metallurgical Engineer
Ohio State University
2477 Lytham Road
Columbus, OH 43220

8 <u>Waste Management External Advisory Committee Members</u>

Dr. Frank L. Parker
Professor of Environmental and Water Resources Engineering
Vanderbilt University
P. O. Box 1596, Station B
Nashville, TN 37235

Dr. Bruce R. Kowalski
Professor of Chemistry, Co-director of Center for Process
Analytical Chemistry
University of Washington
Chemistry Department, Bldg 10
Seattle, WA 98195

Dr. Greg R. Choppin
Professor of Chemistry
Florida State University
Department of Chemistry, B-164
Tallahassee, FL 32306

9413279.0150

Distribution - continued

Dr. Chester Grelecki
President, Chief Scientist
Hazards Research Corporation
200 Valley Road, Suite 301
Mt. Arlington, NJ 07856

Dr. Alfred Schneider
Professor Meritus of Nuclear Engineering
Georgia Institute of Technology
5005 Hidden Branches Dr.
Dunwoody, GA 30338

Dr. Gary Powers
President
Design Science, Inc.
163 Witherow Road
Sewickley, PA 15143

Joseph S. Byrd
University of South Carolina
Department of Electrical and Computer Engineering
Swearingen Engineering Center
Columbia, SC 29208

William R. Prindle
1556 Crestline Drive
Santa Barbara, CA 93105

3 <u>Ames Laboratory</u>
7 Spedding Hall
Iowa State University
Ames, IA 50011

Bill Haas
R. B. Thompson
Dr. Paul Wang

1 <u>RKK Ltd.</u>
16404 Smokey Pt. Blvd, Suite 303
Arlington, WA 98223

Chris Reno

1 <u>MACTEC</u>
8320 Centerbrook Place
Alexandria, VA 22308

Stan Blacker

9413279.0159

Distribution - continued

1 **Engineering-Science, Inc.**
1955 Jadwin Ave, Suite 470
Richland, WA 99352

Matt Sakach

1 **EBASCO Services,Inc.**
1201 Jadwin Avenue, Suite 202
Richland, WA 99352-3429

F. J. Young

1 **MTL Systems, Inc.**
3481 Dayton-Xenia Road
Dayton, OH 45431-0299

E. McDaniel

1 **Nuclear Consulting Services, Inc.**
7000 Huntley Road
P. O. Box 29151
Columbus, OH 43229

Dr. J. Louis Kovach

1 **Battelle Laboratories**
505 King Avenue
Columbus, OH 43201-2693

Rob Taylor Jr., P.E.
Rm 13-6-016

1 **Portland General Electric Co.**
121 S. W. Salmon St.
Portland, OR 97204-2991

Wayne Lei, 3WTCBR05

3 **RUST Geotech Inc.**
P. O. Box 14000
Grand Junction, CO 81502-5504

Brian Mathis
Michael C. Butherus
John R. Duray

1 **ICF Kaiser Engineers**
1800 Harrison St.
Oakland, CA 94612-3430

Chris G. Whipple, Ph.D

9413279.0152

Distribution - continued

1 **Neptune & Company**
1505 15th St., Suite B
Los Alamos, NM 87544
Randy Ryti

1 **John Hopkins University**
1714 Eutaw Place
Baltimore, MD 21217

Morton Corn

1 **Roberts Engineering Services, INC.**
1980 East Ocean Boulevard
Stuart, FL 34916

Dr. Paul Roberts

1 **Columbia River United Technical Consultant**
P. O. Box 912
Bingen, WA 98605

Gregory de Bruler

1 **Government Accountability Project**
West Coast Office
1402 Third Avenue, Suite 1215
Seattle, WA 98101

Thomas E. Carpenter, Director

1 **Heart of America Northwest**
1305 Fourth Avenue
Cobb Building Suite 208
Seattle, WA 98101

Gerald M. Pollet, Executive Director

1 Dr. Viorica Lopez-Avila
Midwest Research Institute
625-B Clyde Ave
Mountain View, CA 94043

1 **Los Alamos Technical Associates**
8633 W. Gage Blvd.
Kennewick, WA 99336

D. S. Delorenzo

9413279.0153

Distribution - continued

OFFSITE - FOREIGN

1 **British Nuclear Fuels Ltd**
Risley Warrington
Cheshire WA3 6AS
United Kingdom

Howard A. Edwards

1 **Ricardo Hitec Ltd**
Club street Works, Bamber Bridge
Preston, PR5 6FN
United Kingdom

P. K. J. Smith

1 **Telerobot**
Consorzio Telerobot
Via Hermada 6
16154 Genova, Italy

Bruno Sessarego

4 **SGN**
1, rue des Herons, Montigny-le-Bretonneux
78182 Saint-Quentin-en-Yvelines Cedex,
France

Serge Merlin
Gilles Clement
Bernard Tousant
Eric Tchemitcheff

2 **CEA - Saclay**
DCC/DIR
Ba't 121
91190 GIF/Yvette Cedex
France

G. Baudin
R. Atabek

1 **SDMS-Chaudronnerie Blanche**
B.P. 4-F-38160 Saint-Romans
France

Phillipe Monneau

9413279.0154

Distribution - continued

1 **GEA-Cadarache**
SGDC/STDE
Boite Pastale 313
13115 Saint Paul Les Durance
France

Magali Ranchoux

1 **Hans Walischmiller GmbH**
D-7778 Markdorf/Bodensee
Germany

Wolfgang Walischmiller

ONSITE

25 **U. S. Department of Energy-Richland Operations Office**

G. E. Bishop	R3-72
K. W. Bracken	R3-73
S. T. Burnum	R3-74
R. C. Cullison	A5-55
J. J. Davis	R3-74
L. Erickson	R3-74
R. E. Gerton	R3-72
M. Glasper	R3-72
W. F. Hendrickson	R3-72
R. L. Higgins	R3-72
R. D. Hildebrand	A5-55
A. Hon	R3-72
P. E. LaMont	R3-74
T. Noble	R3-72
M. S. Peck	T4-07
L. E. Petersen	R3-72
G. W. Rosenwald	R3-72
G. H. Sanders	R3-74
T. R. Sheridan	R3-73
A. B. Sidpara	R3-73
A. D. Toth	R3-72
D. L. Vieth	R3-73
D. J. Williams	R3-72
J. K. Yerxa	A5-15
Reading Room	A1-65

1 **BNFL INC.**

Dr. Mike McKeon G3-02

1 **Stone & Webster Engineering Co.**

E. L. Richards R2-83

9413279.0155

Distribution - continued

2	**MACTEC**	
	J. Janus	G6-18
	L. Soler	A4-35
1	**EBASCO**	
	C. T. Anderson	G3-02
1	**Yakima Indian Nation**	
	John Brodeur	G1-02
44	**Pacific Northwest Laboratories**	
	D. N. Anderson	K7-34
	W. J. Apley	K1-73
	D. B. Baird	K7-34
	R. M. Bean	P8-08
	D. W. Bennett	K5-17
	P. R. Bredt	P7-25
	J. C. Brown	K7-22
	S. A. Bryan	P7-25
	L. L. Burger	P7-25
	J. B. Colson	K5-10
	J. M. Creer	G6-01
	P. G. Eller	B1-40
	J. F. Fletcher	K7-97
	E. A. Flores	K3-08
	L. K. Holton Jr.	P7-43
	V. L. Hunter	K7-94
	P. R. Hrma	P8-37
	J. Janata	K2-12
	B. M. Johnson	K1-78
	E. O. Jones	P8-38
	D. E. Larson	G3-02
	S. G. McKinley	P7-22
	B. D. McVeety	K6-63
	I. C. McVeety	K7-22
	P. J. Mellinger	P7-22
	B. E. Opitz	K6-79
	M. D. Patridge	K7-94
	M. S. Peffers	K7-94
	R. K. Quinn	K1-73
	W. G. Richmond	P7-41
	J. M. Robbins	P7-22
	R. D. Scheele	P7-25
	E. A. Schmieman	B1-40
	R. C. Schrotke	P7-18
	P. A. Scott	P7-19
	D. A. Seaver	K1-73
	J. C. Spanner	K2-05
	J. L. Straalsund	K1-79

Distribution - continued

K. L. Steinmaus		K6-84
J. L. Swanson		P7-25
K. M. Tominey		K7-97
R. S. Wegeng		K7-97
P. D. Whitney		K7-34
T. W. Wood		K6-47

348 **Westinghouse Hanford Company/Boeing Computer Sciences Richland/ICF Kaiser Hanford Company**

L. K. Ahrens		H6-07
A. T. Alstad		R1-49
W. T. Alumkal		R2-52
R. P. Anantatmula		R2-11
J. D. Anderson		N3-11
J. N. Appel		S4-58
I. J. Austin		T4-01
H. Babad		R2-78
J. J. Badden		S5-12
J. K. Bajwa		H4-63
R. A. Ballou		S4-58
T. J. Bander		H0-33
A. D. Bates		T3-01
L. L. Barry		R1-67
G. D. Bazinet		L4-71
D. B. Bechtold		T6-09
D. L. Becker		H5-57
L. Bedford		S5-07
K. E. Bell		R1-12
R. V. Berg		R4-02
M. V. Berriochoa		B3-30
P. K. Bhatia		S4-58
B. D. Biddle	(6)	S5-14
K. R. Birney		H0-40
D. L. Bjorklund		S6-01
J. E. Bjorklund		R1-62
R. J. Blanchard		R1-17
D. C. Board		S1-57
K. D. Boomer		H5-49
G. L. Borsheim		R2-11
V. C. Boyles		R1-49
D. A. Bragg		R1-49
D. R. Bratzel		L5-31
W. R. Brooksher		L4-01
T. M. Brown		R2-12
R. G. Brown		R2-14
J. H. Bussell		L7-06
J. A. Caggiano Jr		H6-06
J. W. Carey		S5-07
K. G. Carothers		R1-51
B. C. Carpenter		R1-12
R. J. Cash		R2-78
T. Chiao		L0-06

9413279.0157

Distribution - continued

G. Christensen	H4-21
K. L. Chubb	L6-86
G. J. Coleman	T4-07
J. C. Conner	H4-61
R. B. Conrad	H5-09
W. L. Cowley	H4-61
D. W. Craig	S5-07
C. Crawford	R3-01
N. R. Croskrey	R1-30
G. M. Crummel	R1-51
J. M. Cruse	L5-63
D. S. Cunningham	S0-02
J. E. Daniels	S4-65
S. A. Davidson	K6-26
J. S. Davis	H4-64
S. J. Dechter	R2-54
C. DeFigh-Price	R2-31
J. L. Deichman	H4-19
T. A. Demitruk	H5-36
C. J. Denson	L4-95
D. R. Dickinson	L5-31
S. E. Dieterle	S2-20
L. F. Dougherty	H4-62
J. G. Douglas	L5-55
G. L. Dunford	R1-51
R. F. Eggers	S4-58
D. R. Ellingson	H5-37
F. W. Ellis	B4-52
D. B. Engelman	R2-18
R. W. Ewert	R1-19
S. D. Estey	R2-11
W. G. Farley	H4-62
J. E. Fasso Jr.	S3-10
G. W. Faulk	T3-28
K. O. Fein	H4-63
L. A. Fort	S4-57
K. D. Fowler	R2-11
S. B. Fowler	L0-24
C. R. Fox	S4-60
G. L. Fox, Jr.	L5-01
H. P. Fox	R2-88
G. T. Frater	R1-51
E. A. Fredenburg	S4-55
J. R. Freeman-Pollard	H6-03
R. T. French	E6-61
J. C. Fulton	R2-31
L. A. Gaddis	G7-57
K. A. Gasper	G3-20
G. J. Gauck	R1-51
C. J. Geier	R2-50
P. W. Gibbons	S4-58
R. L. Gilchrist	L5-63
D. A. Gilles	S2-14

Distribution - continued

S. D. Godfrey	R1-51
D. E. Good	S3-97
A. Greenberg	S2-66
P. R. Golberg	B4-08
P. Greenbaum	S5-20
J. M. Grigsby	H4-62
R. D. Gustavson	R1-51
J. H. Haberman	R1-30
K. D. Haggerty	T4-09
L. E. Hall	E6-25
V. W. Hall	R2-85
C. S. Haller	G6-04
D. W. Hamilton	S7-03
K. L. Hampsten	S4-53
B. M. Hanlon (40)	R1-80
J. M. Hanson	R2-85
H. D. Harmon	R2-52
M. S. Harrington	B4-53
J. P. Harris III	S4-55
G. A. Harvey	B4-52
F. J. Heard	H0-34
D. A. Healey	T4-07
J. M. Henderson	S4-55
D. W. Hendrickson	L5-55
E. G. Hess	R3-09
M. C. Higginson	A4-25
M. J. Holm	R1-80
C. S. Homi	R2-12
G. P. Hopkins	N2-40
J. D. Hopkins	R2-11
B. K. Horsager	B5-24
J. H. Huber	R1-49
J. L. Huckaby	R2-78
J. V. Hurley	R4-02
J. J. Huston	S1-54
J. E. Irvin	R2-85
M. N. Islam	R3-08
M. T. Jansky	H6-26
T. D. Jarecki	S7-12
P. Jennings	P6-72
G. D. Johnson	R2-78
J. L. Juette	G6-56
R. A. Karnesky	H0-39
D. L. Kelly	S5-20
R. A. Kirkbride	S4-58
P. F. Kison	S2-45
C. A. Kuhlman	B3-30
N. W. Kirch	R2-11
D. B. Klos	S0-14
A. G. Krasopoulos	A5-55
M. Kummerer	H4-62
M. J. Kupfer	H5-49
E. C. Ladd	R1-19

9413279.0159

Distribution - continued

D. R. Lance	S0-09
J. L. Lee	R2-36
J. M. Light	B4-08
D. C. Lini	H3-56
B. H. Lueck Jr.	R3-12
P. J. Mackey	B3-15
G. T. MacLean	S4-58
M. K. Mahaffey	L4-73
R. M. Marusich	H4-60
V. D. Maupin	N1-73
T. B. McCall	H0-33
J. D. McCormack	L5-31
K. S. McCullough	H4-70
M. H. McGrath	S4-58
M. A. McLaughlin	H5-09
J. P. Menard	R2-40
W. C. Miller	S4-55
N. J. Milliken	H4-63
W. J. Millsap	H5-68
G. J. Miskho	R2-50
J. R. Mobley	H5-49
T. Moleff	R1-30
S. R. Morgan	R2-50
P. M. Morant	H4-19
K. L. Morris	H5-09
J. P. Mullally	B5-24
L. D. Muhlestein	H4-64
R. L. Nelson (4)	R2-36
R. L. Newell	E6-31
D. J. Newland	R2-36
R. Ni	S5-07
T. W. Oden	R2-18
P. C. Ohl	H1-30
P. A. Olsen	R3-12
D. L. Osowski	L6-10
V. M. Pacheco	R1-51
A. L. Pajunen	H5-49
R. B. Pan	H5-53
L. D. Parchen	B3-63
G. L. Parsons	S4-57
M. A. Payne	R2-50
L. T. Pedersen	X5-52
L. D. Pennington	T4-07
C. E. Petersen	R1-30
S. R. Pierce	R1-51
R. S. Popielarczyk	R1-30
E. A. Porter	R2-88
R. L. Powers	R1-49
T. B. Powers	H4-65
R. K. P'Pool	T1-30
G. R. Priddy Jr.	R3-12
T. E. Rainey	R4-02
G. F. Raphael	R2-12

Distribution - continued

R. E. Raymond (3)	R2-54
R. W. Reed	R1-51
I. E. Reep	R2-08
M. A. Rezvani	H5-55
D. Richardson	R2-31
S. K. Rifaey	S6-12
W. E. Ross	S5-07
J. A. Ryan	H5-55
P. Sathyanarayana	R2-12
C. C. Scaief	L7-06
F. A. Schmorde	B2-18
R. D. Schreiber	R2-12
C. P. Schroeder	L7-06
K. V. Scott	H5-52
N. J. Scott-Proctor	R1-80
O. Serrano	T4-01
L. K. Severud	R2-50
M. H. Shannon	H4-61
J. E. Shapley	H4-68
T. N. Shaw	S4-55
R. A. Shea	L8-16
E. M. Sheen	L7-03
E. J. Shen	S4-58
P. K. Shen	H0-39
D. J. Sherwood	R2-78
A. T. Shook	S2-01
E. R. Siciliano	H0-39
R. B. Simmons	R2-12
K. P. Slape	S0-11
C. M. Smith	H6-30
S. G. Spencer	R1-30
S. M. Stahl	H4-61
E. G. Stephan	A3-74
B. E. Stapley	R4-02
R. R. Stickney	R4-02
J. N. Strode	R2-11
D. G. Sutherland	L4-72
J. P. Summerhays	R2-88
M. J. Sutey	T4-08
S. L. Swaney	T4-08
L. M. Swanson	H5-49
C. L. Thomas	H4-19
J. F. Thompson	H5-68
J. D. Thomson	R1-30
S. R. Tifft	H6-26
J. A. Tilden (2)	L6-12
H. Toffer	H0-38
T. T. Tran	L7-04
J. W. Tritz	B1-32
D. P. Trott	R2-86
D. A. Turner	R2-78
L. A. Tusler	R2-11
C. J. Udell	L6-12

9413279.0161

Distribution - continued

B. D. Valenzuela	R2-12
R. E. Van der Cook	L4-75
R. J. Van Vleet	H4-63
A. O. Vance	H5-33
N. J. Vermeulen	R1-80
D. T. Vladimiroff	G7-01
J. A. Voogd	R4-03
G. R. Walker	B2-16
O. S. Wang	R2-78
D. L. Wegener	R1-62
R. K. Welty	R1-80
G. T. Wells	H6-26
K. A. White	R1-51
R. Whitman	H5-49
R. S. Whittman	B1-59
J. H. Wicks	T4-07
D. D. Wiggins	R1-49
L. S. Williams	S4-53
C. R. Wilson	H5-52
G. R. Wilson	R2-31
M. E. Witherspoon	E6-61
D. D. Wodrich	R2-85
K. L. Woodard	R4-02
R. D. Wojtasek	H6-27
W. R. Wrzesinski	R3-74
P. A. Young	R2-14
F. A. Zak	R3-01
B. D. Zimmerman	L0-06
SDPC Docket File (2)	H5-36
272-AW Shift Office	S5-04
Central Files (2)	L8-04
Tank Farms Info Center	R1-20
Information Release Administration (3)	R1-08
Env Data Mgmt Center	H4-22
RL/TWRS Library	R3-72

9413279.0162

THIS PAGE INTENTIONALLY
LEFT BLANK

Distribution - continued

H. Toffer	H0-38
T. T. Tran	L7-04
J. W. Tritz	B1-32
D. P. Trott	B1-32
D. A. Turner	R2-78
L. A. Tusler	R2-11
C. J. Udell	L6-12
B. D. Valenzuela	R2-12
R. E. Van der Cook	L4-75
R. J. Van Vleet	H4-62
D. T. Vladimiroff	G7-01
J. A. Voogd	R4-03
G. R. Walker	B2-16
O. S. Wang	R2-78
D. L. Wegener	R1-62
R. K. Welty	R1-80
G. T. Wells	H6-26
R. Whitman	H5-49
J. H. Wicks	T4-07
D. D. Wiggins	R1-49
L. S. Williams	S4-53
C. R. Wilson	H5-52
G. R. Wilson	R2-31
M. E. Witherspoon	E6-61
D. D. Wodrich	R2-85
K. L. Woodard	R4-02
R. D. Wojtasek	H6-27
W. R. Wrzesinski	R3-74
P. A. Young	R2-14
F. A. Zak	R3-01
B. D. Zimmerman	L0-06
SDPC Docket File (2)	H5-36
272-AW Shift Office	S5-04
Central Files (2)	L8-04
Tank Farms Info Center	R1-20
Information Release Administration (3)	R1-08
Env Data Mgmt Center	H4-22 H6-07
RL/TWRS Library	R3-72

9413279.0163

THIS PAGE INTENTIONALLY
LEFT BLANK
