CPCC-2603957
Revision 0

200 AREA PROJECT MANAGERS MEETING (PMM) JULY 16, 2026

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Contractor for the U.S. Department of Energy
Hanford Field Office under Contract 89303320DEM000030

P.O. Box 1464
Richland, Washington 99352

Approved for Public Release;
Further Dissemination Unlimited

CPCC-2603957
Revision 0

200 AREA PROJECT MANAGERS MEETING (PMM) JULY 16, 2026

Date Published
August 2026

Prepared for the U.S. Department of Energy
Assistant Secretary for Environmental Management

Contractor for the U.S. Department of Energy
Hanford Field Office under Contract 89303320DEM000030

CPCCo
Central Plateau
Cleanup Company
P.O. Box 1464
Richland, Washington 99352

APPROVED
By Susan Natalie Molina at 2:14 pm, Aug 25, 2026

Release Approval Date

Approved for Public Release;
Further Dissemination Unlimited

TRADEMARK DISCLAIMER

Reference herein to any specific commercial product, process, or service by tradename, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors.

This report has been reproduced from the best available copy.

Printed in the United States of America

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MEETING MINUTES APPROVAL
MAY - JUNE 2026 DATA
JULY 16, 2026

SIGNATURES:

In accordance with the Tri-Party Agreement Section 4.1, Project Manager Role, any agreements and commitments resulting from the meeting will be prepared and signed by all parties as soon as possible after the meeting. The undersigned indicate by their signatures (or their delegate's signature) that these meeting minutes reflect the actual discussion during this meeting. Signatures denote concurrence with the agreements and commitments resulting from this meeting and do not imply agreement with statements made during this meeting. Attachments to these meeting minutes are provided for informational purposes only.

APPROVAL: NAOMI JASCHKE Digitally signed by NAOMI JASCHKE Date: 2026.08.06 08:03:37 -07'00' **DATE:** _____
200 Area Project Manager, HFO

APPROVAL: Manuel L. Lopez Digitally signed by MANUEL LOPEZ-LOPEZ Date: 2026.08.06 13:27:26 -07'00' **DATE:** _____
200 Area Project Manager, HFO

APPROVAL: Debra J. Alexander 2026.08.06 15:11:07 -07'00' **DATE:** _____
200 Area Project Manager, Ecology

APPROVAL: Digitally signed by GEOFF SCHRAMM Date: 2026.08.19 04:25:17 -07'00' **DATE:** _____
200 Area Project Manager, EPA

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
May - June 2026 DATA
JULY 16, 2026

Agenda

- 200-BC-1 and 200-WA-1 Remedial Actions (Jason Capron)
- 200-IA-1 Remedial Actions (Patrick Brice)
- 200-DV-1 Response Actions (Celia Onishi)
- 200-SW-2 Remedial Actions (Jason Capron)
- 200-EA-1 Remedial Actions (Jason Capron)
- 200-PW-1/3/6 and 200-CW-5 Remedial Actions (Mohammed Gorashi)
- 200-IS-1 Remedial Actions (Jason Capron)
- 200-OA-1, Outer Area, 200-CW-1, and 200-CW-3 Remedial Actions (Manny Lopez-Lopez)
- 200-SW-1 Remedial Actions (Manny Lopez-Lopez)
- 200-CB-1 (B Plant) Remedial Actions (Naomi Jaschke)
- 200-CP-1 (PUREX) Remedial Actions (Jason Capron)
- 200-CR-1 (REDOX) Remedial Actions (Naomi Jaschke)
- 200 Area Removal Action Activities (Mohammed Gorashi)
- Integrated Disposal Facility – IDF (Manny Lopez-Lopez)
- Environmental Restoration Disposal Facility – ERDF (Manny Lopez-Lopez)
- 200-BP-5 and 200-PO-1 Remedial Actions (Celia Onishi)
- 200-UP-1 Remedial Actions (Celia Onishi)
- 200-ZP-1 Remedial Actions (Celia Onishi)
- 200 West Pump & Treat Facility Supporting Remedial Actions (Patrick Brice)
- Hanford Annual Groundwater Sampling Program Performance (Kaitlyn Nelson)
- Well Installation Status (Kaitlyn Nelson)
- Central Plateau Milestone Status
- Documents for the Administrative Record

Action Items

Closing Comments

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MAY - JUNE 2026 DATA
JULY 16, 2026

NAME	ORGANIZATION	EMAIL
Mohammad Gorashi	DOE	
Celia Onishi	DOE	
Kaitlyn Nelson	DOE	
Doug H. Hebrand	ANL	rhildebrand@anl.gov
Patrick Brich	DOE	—
Manuel Lopez	DOE	—
Anne McCartney	EPA	—
GEOFF SCHRAMM	EPA	SCHRAMM.GEOFF@EPA.GOV
Roberto A. Armijo	EPA	—
Jason Capron	DOE	—
Elyse Frahling	CPCCO	Elyse_E_frahling@rl.gov

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Attendance List
May - June 2026 Data
July 16, 2026

NAME	ORGANIZATION	EMAIL
ALEXANDER, DEB	ECY	DEBRA.ALEXANDER@ECY.WA.GOV
ARMIJO, ROBERTO	EPA	ARMIJO.ROBERTO@EPA.GOV
AROLA, CRAIG	CPCC	CRAIG_C_AROLA@RL.GOV
AUKERMAN, LAURA	DOH	LAURA.AUKERMAN@DOH.WA.GOV
BAKER, MORGAN	ECY	MOJO461@ECY.WA.GOV
BALLINGER, KIMBERLY	DOE	KIMBERLY.BALLINGER@HANFORD.GOV
BOHNEE, GABRIEL	HNRTC	GABEB@NEZPERCE.ORG
BOUNDS, CYNTHIA	HMIS	CYNTHIA_L_BOUNDS@RL.GOV
BOYD, ALICIA	ECY	ABOY461@ECY.WA.GOV
BRANTON, EVON	HMIS	EVON_R_BRANTON@RL.GOV
BRASHER, STEPHANIE	HMIS	STEPHANIE_L_BRASHER@RL.GOV
BRECKON, DEANNA	HMIS	DEANNA_BRECKON@RL.GOV
BRICE, PATRICK	DOE	PATRICK.BRICE@HANFORD.GOV
BROZE, ELLIOT	CPCC	ELLIOT_A_BROZE@RL.GOV
CALDWELL, COLE	ECY	COLE.CALDWELL@ECY.WA.GOV
CAPRON, JASON	DOE	JASON.CAPRON@HANFORD.GOV
CARR, SEAN	DOE	SEAN.CARR@HANFORD.GOV
CARTER, RYAN	CPCC	RYAN_M_CARTER@RL.GOV
CLINE, KATE	DOE	KATE.CLINE@HANFORD.GOV
COLTON, INGRID	DOE	INGRID.COLTON@HANFORD.GOV
COWIN, BEN	HMIS	BENJAMIN_J_COWIN@RL.GOV
CUTTER, STACY	CPCC	STACY_L_CUTTER@RL.GOV
DENTON, ERIC	CPCC	ERIC_T_DENTON@RL.GOV
DURKEE, MATT	ECY	MDUR461@ECY.WA.GOV
DURANCEAU, DAVID	CPCC	DAVID_A_DURANCEAU@RL.GOV
EBERT, KELLY	DOE	KELLY.EBERT@HANFORD.GOV
EDWARDS, DAN	PNNL	DANIEL.EDWARDS@PNNL.GOV
FREEMAN, CHASE	CPCC	CHASE_M_FREEMAN@RL.GOV
FROHLING, ELYSE	CPCC	ELYSE_E_FROHLING@RL.GOV
GALASSOIRISH, CASCADE	EPA	GALASSOIRISH.CASCADE@EPA.GOV

Tri-Party Agreement (TPA)
200 AREA PROJECT MANAGERS MEETING
Attendance List
May - June 2026 Data
July 16, 2026

NAME	ORGANIZATION	EMAIL
JASCHKE, NAOMI	DOE	NAOMI.JASCHKE@HANFORD.GOV
LEPAGE, JANE	DOH	JANE.LEPAGE@DOH.WA.GOV
LIEBRECHT, TABITHA	ECY	TLIE461@ECY.WA.GOV
LYNCH, MATT	NREL	MATTL@NEZPERCE.ORG
MACDONALD, EMILLY	CPCC	EMILY_M_MACDONALD@RL.GOV
MEDINA, AHTZIRY	YN	AMEDINA@YNERWM.COM
MORGANS, DONNA	CPCC	DONNA_L_MORGANS@RL.GOV
PECK, GEORGE	ECY	GEPE461@ECY.WA.GOV
PERKINS, MEGAN	DOH	MEGAN.PERKINS@DOH.WA.GOV
SADLER, KASEY	CPCC	KASEY_L_SADLER@RL.GOV
SICILIA, TOM	ODOE	TOM.SICILIA@ENERGY.OREGON.GOV
SINGLETON, DEBORAH	CPCC	DEBORAH_G_SINGLETON@RL.GOV
SMITH, ANTHONY	HNRTC	ASMITH@NEZPERCE.ORG
STILES, KYLE	CPCC	KYLE_K_STILES@RL.GOV
TOSCH, MCCLURE	YN	MTOSCH@YNERWM.COM
TURNER, MICHAEL	HMIS	MICHAEL_J_TURNER@RL.GOV
WANG, LI	YN	LWANG@YNERWM.COM

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OU STATUS
May - June 2026 DATA
JULY 16, 2026

200-BC-1 and 200-WA-1 Remedial Actions

EPA Lead
HFO – Jason Capron, CPCCo – Elyse Frohling

Regulatory Document Status:

- DOE/HFO-2025-25, Rev. 0, *Supplemental Characterization Plan for the 200-BC-1 Operable Unit*, has been published.

Recent Accomplishments and Upcoming Work:

- Borehole planning efforts for 200-BC-1 supplemental characterization per DOE/HFO-2025-25 are underway.

Regulatory Agency Comments: None

200-IA-1 Remedial Actions

EPA and Ecology Joint Lead
HFO – Patrick Brice, CPCCo – David Becker

Regulatory Document Status:

- DOE/RL-2020-51, Draft B, *200-IA-1 OU Focused Feasibility Study* in development.
- DOE/RL-2022-04, Draft A, *Proposed Plan for Remediation of the 200-IA-1 Operable Unit* in development.

Recent Accomplishments and Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-DV-1 Response Actions

Ecology Lead
HFO – Celia Onishi, CPCCo – Elyse Frohling/Ryan Carter

Regulatory Document Status:

- None for this reporting period.

Recent Accomplishments and Upcoming Work:

- Continuing perched water treatment (Table 1).

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OU STATUS
May - June 2026 DATA
JULY 16, 2026

Table 1. Perched Water Treatment for the 200-DV-1 OU [a]

Period	Volume (kgal)	Chromium (kg) [b]	Nitrate (as NO_3) (kg) [c]	Technetium-99 (Ci)	Uranium (kg)
May 2026	26.1	0.00058	0	0.0024	3.55
June 2026	23.0	0.00011	0	0.0021	3.13
CY 2026	99.6	0.00250	0	0.0089	13.47
Cumulative Since 2017 [a]	2,867	0.353	2,945	0.397	557

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.

a. The 200-DV-1 extraction system was connected to the 200 West P&T system in February 2017. Prior to connection to the 200 West P&T system, the 200-DV-1 extraction system operated from August 2011 through December 2016, extracting 1.364 million L (0.360 million gal) of perched water with 778 kg of nitrate, 2.47 g (0.0420 Ci) of tehnetium-99, and 79.7 kg of uranium, which are not included with the above totals (Table 5-9 in DOE/RL-2016-69, *Calendar Year 2016 Annual Summary Report for the 200-ZP-1 and 200-UP-1 Operable Unit Pump-and-Treat Operations*).

b. Chromium treatment since October 2019 (when biological treatment was suspended) reflects incidental removal by the IX resins for the extraction wells with discharge processed through the radiological treatment building. Prior to suspension of biological treatment, chromium was treated for all extraction wells.

c. Biological treatment for nitrate was suspended in October 2019.

CY: calendar year

IX: ion exchange

OU: operable unit

Regulatory Agency Comments: None

200-SW-2 Remedial Actions

Ecology Lead
HFO – Jason Capron, CPCCo – Craig Arola

Regulatory Document Status/Recent Accomplishments/Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-EA-1 Remedial Actions

Ecology Lead
HFO – Jason Capron, CPCCo – Elyse Frohling

Regulatory Document Status:

- DOE/RL-2016-58, Rev, 0, *200-EA-1 Operable Unit Waste Site RCRA Facility Investigation/Corrective Measures Study and Remedial Investigation/Feasibility Study Work Plan* has been published.

Recent Accomplishments and Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-PW-1/3/6 and 200-CW-5 Remedial Actions

EPA Lead
HFO – Mohammed Gorashi, CPCCo – Deborah Singleton

Regulatory Document Status:

- Draft inputs for remedial design/remedial work plan update have been prepared to be discussed with EPA to determine next steps.

Recent Accomplishments and Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: Please note that EPA has not agreed to any delays in this schedule and expects the RD/RAWP schedule to be followed since it is an enforceable part of the remedial action work plan. Any proposed changes to the schedule need to be discussed in a timely manner.

200-IS-1 Remedial Actions

Ecology Lead
HFO – Jason Capron, CPCCo – Craig Arola

Regulatory Document Status/Recent Accomplishments/Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-OA-1, Outer Area, 200-CW-1, and 200-CW-3 Remedial Actions

EPA Lead
HFO – Manny Lopez-Lopez, CPCCo – Travis Creach

Regulatory Document Status/Recent Accomplishments/Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-SW-1 Remedial Actions

Ecology Lead
HFO – Manny Lopez-Lopez, CPCCo – Bob Bullock

Regulatory Document Status:

- Approval of Change Control Form M-37-26-02 was done on 6/03/2026 extended the due date of Milestone M-037-31 from 8/31/2026 to 10/31/2030.

Recent Accomplishments and Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-CB-1 (B Plant) Remedial Actions

Ecology Lead
HFO – Naomi Jaschke, CPCCo – Deborah Singleton

Regulatory Document Status/Recent Accomplishments/Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-CP-1 (PUREX) Remedial Actions

Ecology Lead
HFO – Jason Capron, CPCCo – Deborah Singleton

Regulatory Document Status:

- The RI/FS Work Plan is being prepared for final Rev. 0 pending update for Chapter 6 “Project Schedule.”

Recent Accomplishments and Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200-CR-1 (REDOX) Remedial Actions

EPA Lead

HFO – Naomi Jaschke, CPCCo – Deborah Singleton

Regulatory Document Status/Recent Accomplishments/Upcoming Work:

- None for this reporting period.

Regulatory Agency Comments: None

200 Area Removal Action Activities

EPA/Ecology Lead

HFO – Mohammed Gorashi, CPCCo – Deborah Singleton

Regulatory Document Status:

- DOE/RL-2020-56, Revision 1 *Action Memorandum for the 200 West Area Tier 2 Buildings/Structures* was updated to incorporate the addition of 242-T-135. This is in process of transmittal from DOE to EPA.

Recent Accomplishments and Upcoming Work:

- Completed development of a site setup work package and started mobilizing equipment and materials to the Reduction Oxidation (REDOX) facility in preparation for ventilation pre-filter replacement.
- Continued development of additional REDOX work packages, including pre-filter replacement, and installation of receptacles to support filter maintenance
- Continued large-scale vegetation removal, posting/fencing relocation, and application of fixatives in the 216-Z-1A contamination area (Figure 1). Stabilization activities were suspended at the end of June due to off road fire restrictions; work will resume after fire restrictions are lifted.

Figure 1. 216-Z-1A Stabilization

- D4ES Waste Operations is sorting and segregating chemicals in the 212-Z Lag Yard for compliant storage and has compiled a comprehensive legacy chemical inventory to support future disposition.

Planned Work:

- None for this reporting period.

Regulatory Agency Comments: None

Integrated Disposal Facility – IDF

Ecology Lead
HFO – Manny Lopez-Lopez, CPCCo – Tim Wintle/Travis Dill/Bob Bullock

Regulatory Document Status:

- IDF (PCN-IDF-2026-02): The Class 1 permit modification to update drawings numbers and documents in Appendix C, C3, and C9 to account for the truck loadout pad extension.

Recent Accomplishments and Upcoming Work:

- Placed 85 immobilized low-activity glass (ILAW) glass logs in IDF Cell 1 while no ILAW pallets await placement in the receiving pad.
- Completed our first leachate load out campaign and shipped 120,000 gallons of leachate to Effluent Treatment Facility (ETF).

Regulatory Agency Comments: None

Environmental Restoration Disposal Facility – ERDF

EPA Lead
HFO – Manny Lopez-Lopez, CPCCo – Dave Duranceau/Travis Dill

Regulatory Document Status:

- None to report.

Recent Accomplishments and Upcoming Work:

- Continuing to dispose of waste, primarily from 100-K. Approximately 13,333 tons of waste have been disposed of from the 100-K projects since starting earlier this year.
- Placed first pour of high strength grout on the latest 11 standard waste boxes (SWBs) received from the Central Waste Complex (CWC) for disposal. The first pour anchors the SWBs in place.
- Continuing work on placement of primary and secondary liner following admix placement.
- A leachate collection tank from Trenches 31/34 is being planned for disposal at ERDF.

Regulatory Agency Comments: None

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OU STATUS
May - June 2026 DATA
JULY 16, 2026

200-BP-5 and 200-PO-1 Remedial Actions

Ecology Lead
HFO – Celia Onishi, CPCCo – Elyse Frohling

Regulatory Document Status:

- DOE/RL-2014-31, Rev. 0, *Sampling and Analysis Plan for the 200-PO-1 Groundwater Operable Unit* has been finalized.
- DOE/RL-2014-33, Rev. 1, *Sampling and Analysis Plan for the 200-BP-5 Groundwater Operable Unit* has been finalized.

Recent Accomplishments and Ongoing Work:

- Hydraulic pumping tests for 299-E27-157 and 299-E25-240 are complete and data analysis and evaluation are ongoing.
- Groundwater treatment values for the B Complex area (in the 200-BP-5 OU) and the A-AX and C Farm area (in the 200-BP-5 and 200-PO-1 OUs) are presented in Tables 2 and 3.

Table 2. Groundwater Treatment for the B Complex Area[a]

Period	Volume (kgal)	Nitrate (as NO_3) (kg)[b]	Technetium-99 (Ci)	Uranium (kg)
May 2026	6,973	0	0.069	1.73
June 2026	3,583	0	0.029	0.96
CY 2026	20,346	0	0.193	5.42
Cumulative Since 2015	763,337	209,480	10.7	301

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.
a. The B Complex area extraction system began operating in September 2015.
b. Biological treatment for nitrate was suspended in October 2019 such that nitrate no longer is treated.
CY: calendar year
OU: operable unit

Table 3. Groundwater Treatment for the A-AX and C Tank Farm Area[a]

Period	Volume (kgal)	Technetium-99 (Ci)
May 2026	7,092	0.080
June 2026	1	0.000
CY 2026	13,055	0.132
Cumulative Since 2025	23,362	0.2

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.
a. The A-AX and C Tank Farm area extraction system began operating on October 28, 2025.
COC: contaminant of concern
CY: calendar year

Table 3. Groundwater Treatment for the A-AX and C Tank Farm Area[a]

Period	Volume (kgal)	Technetium-99 (Ci)

OU: operable unit

Regulatory Agency Comments: None

200-UP-1 Remedial Actions

EPA Lead
HFO – Celia Onishi, CPCCo – Ryan Carter

Regulatory Document Status:

- None for this reporting period.

Recent Accomplishments and Upcoming Work:

- Continued rebound study at extraction well 299-W22-92 downgradient of WMA S-SX to determine if there is stranded technetium-99 in the vadose zone. This extraction well no longer captures the downgradient portion of the WMA S-SX technetium-99 plume.
- Continue to determine path forward at extraction well 299-W19-123 to increase uranium removal efficiency.
- Groundwater treatment values for the 200-UP-1 OU are presented in Table 4.

Table 4. Groundwater Treatment for the 200-UP-1 OU[a]

Period	Volume (kgal)	Carbon Tetrachloride (kg)	Chromium (kg)[b]	Nitrate (as NO_3) (kg)[c]	Technetium-99 (Ci)	Trichloroethene (kg)	Uranium (kg)
May 2026	10,952	1.30	0.033	0	0.028	0.021	0.533
June 2026	7,943	0.93	0.004	0	0.022	0.016	0.427
CY 2026	38,870	4.61	0.140	0	0.096	0.077	1.985
Cumulative Since 2012	1,377,529	319	51.7	131,665	6.22	5.10	108

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.

a. For the 200-UP-1 OU, the WMA S-SX extraction system began operating in August 2012, and the U Plant area extraction system began operating in September 2015.

b. Chromium treatment since October 2019 (when biological treatment was suspended) reflects incidental removal by the IX resins for the extraction wells with discharge processed through the radiological treatment building. Prior to suspension of biological treatment, chromium was treated for all extraction wells.

c. Biological treatment for nitrate was suspended in October 2019 such that nitrate no longer is treated.

CY: calendar year

IX: ion exchange

OU: operable unit

Regulatory Agency Comments: None

200-ZP-1 Remedial Actions

EPA Lead
HFO – Celia Onishi, CPCCo – Ryan Carter

Regulatory Document Status:

- TPA-CN-0981 for the *Performance Monitoring Plan for the 200-ZP-1 Groundwater Operable Unit Remedial Action*, Revision 3B (DOE/RL-2009-115) is currently being drafted to update sampling collection frequencies.

Recent Accomplishments and Upcoming Work:

- New carbon tetrachloride extraction wells (299-W12-6 and 299-W11-116) are currently pumping and Tc-99 WMA T-TX/TY extraction wells (299-W11-117, 299-W11-118, and 299-W14-35) will commence pumping by the end of July.
- Continued implementing the DOE/RL-2019-38, Rev. 0, *200-ZP-1 Operable Unit Optimization Study Plan* to collect the data needed to evaluate remedy performance enhancements and remedy configuration changes associated with P&T operations.
- Quarterly sampling for total and free cyanide continues at wells within the ZP-1 OU and at the 200 West P&T. Monitoring wells which historically have been above 200 µg/L federal MCL for total cyanide continue to be sampled.
- The 200-ZP-1 extraction well pumping continued at an average flow rate of approximately 2,635 gpm and 2,866 gpm for May and June, respectively.
- Groundwater treatment values for the 200-ZP-1 OU are presented in Table 5.

Table 5. Groundwater Treatment for the 200-ZP-1 OU[a]

Period	Volume (kgal)	Carbon Tetrachloride (kg)	Chromium (kg)[b]	Nitrate (as NO_3) (kg)[c]	Technetium-99 (Ci)	Trichloroethene (kg)
May 2026	117,640	136	0.326	0	0.061	0.92
June 2026	123,825	157	0.357	0	0.058	1.00
CY 2026	673,837	800	1.246	0	0.308	5.60
Cumulative Since 2012	13,336,915	26,491	504	1,842,668	7.43	153

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.

a. The 200-ZP-1 extraction system began operating in July 2012.

b. Chromium treatment since October 2019 (when biological treatment was suspended) reflects incidental removal by the IX resins for the extraction wells with discharge processed through the radiological treatment building. Prior to suspension of biological treatment, chromium was treated for all extraction wells.

c. Biological treatment for nitrate was suspended in October 2019 such that nitrate no longer is treated.

CY: calendar year

IX: ion exchange

OU: operable unit

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OU STATUS
May - June 2026 DATA
JULY 16, 2026

Regulatory Agency Comments: None

200 West Pump & Treat Facility Supporting Remedial Actions

EPA Lead
HFO – Patrick Brice, CPCCo – Ryan Carter

Regulatory Document Status:

- The 200W P&T O&M Plan status was reported above in 200-ZP-1.

Recent Accomplishments and Upcoming Work:

- Completed uranium resin transfer from the 2nd vessel to the new Y-29 IX train and scheduled Tc-99 resin change to September.
- Completed all necessary corrective and preventive maintenance activities to maintain safe and compliant operation of the 200 West P&T facility.
- Pumping continued at the 200 West P&T with average flow rates of 3,133 gal/min in May 2026 and 3,270 gal/min in June 2026 (Figure 2).

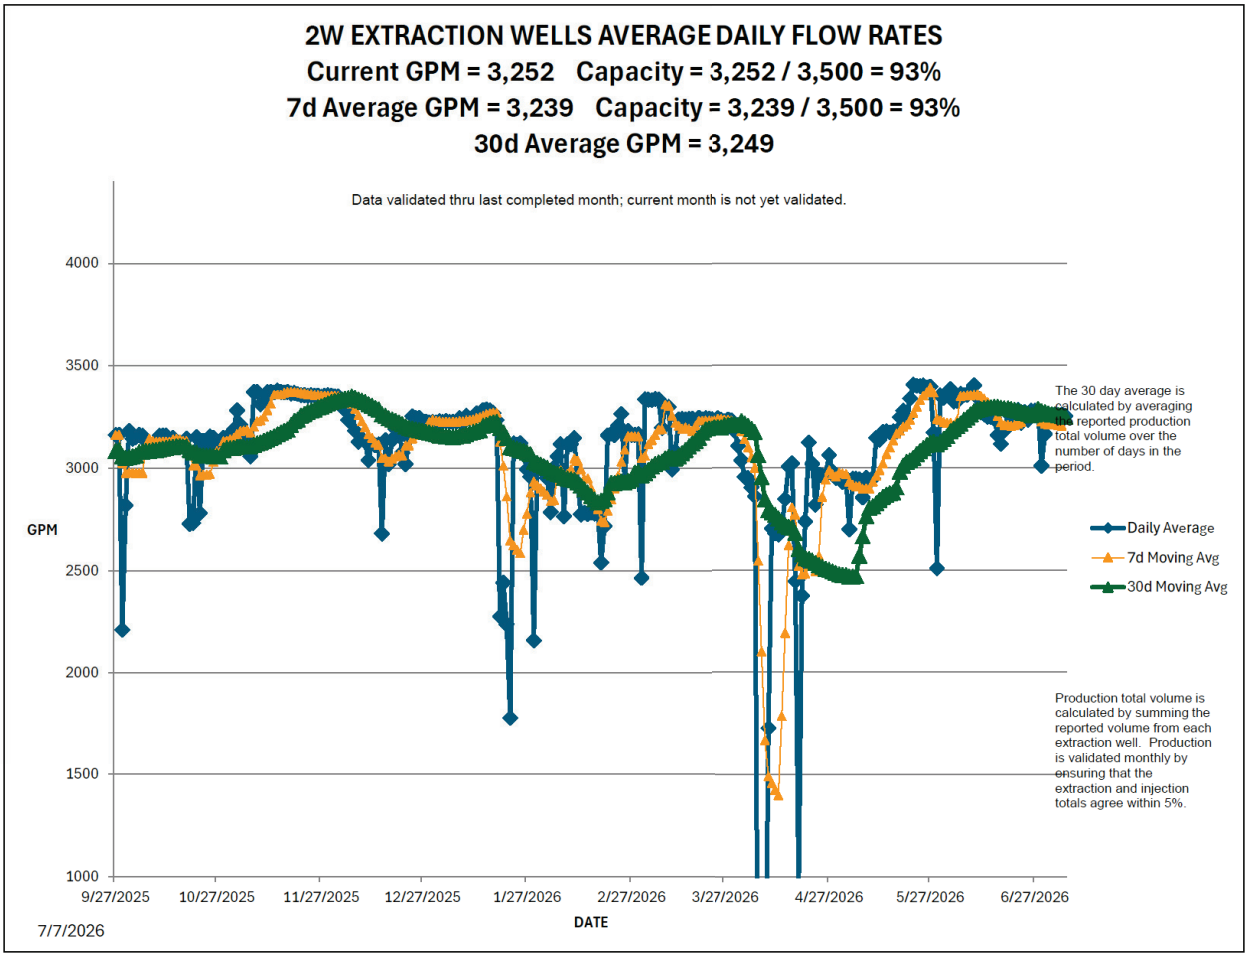

Figure 2. 2W Extraction Wells Average Daily Flow Rates

- Groundwater and perched water treatment values for the 200 West P&T facility are presented in Table 6.

Table 6. Groundwater and Perched Water Treatment by the 200 West P&T Facility

Period	Volume (kgal)	Carbon Tetrachloride (kg)	Chromium (kg) a	Nitrate (as NO3) (kg) b	Technetium-99 (Ci)	Trichloroethene (kg)	Uranium (kg)
May 2026	143,181	146	0.129	0	0.234	1.09	5.81
June 2026	106,561	114	0.016	0	0.095	0.87	4.51
CY 2026	504,742	527	0.523	0	0.610	3.96	20.87
Cumulative Since 2012	15,262,502	26,533	563	2,186,758	24.8	157	967

Contaminant treatment calculated using linear concentration interpolation between extraction well and effluent sampling events; as additional concentration data become available, values may be updated.

a. Chromium treatment since October 2019 (when biological treatment was suspended) reflects incidental removal by the IX resins for the extraction wells with discharge processed through the radiological treatment building. Prior to suspension of biological treatment, chromium was treated for all extraction wells.

b. Biological treatment for nitrate was suspended in October 2019 such that nitrate no longer is treated.

CY: calendar year

IX: ion exchange

Regulatory Agency Comments: None

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OU STATUS
May - June 2026 DATA
JULY 16, 2026

Hanford Annual Groundwater Sampling Program Performance

HFO – Kaitlyn Nelson, CPCCo – Craig Arola

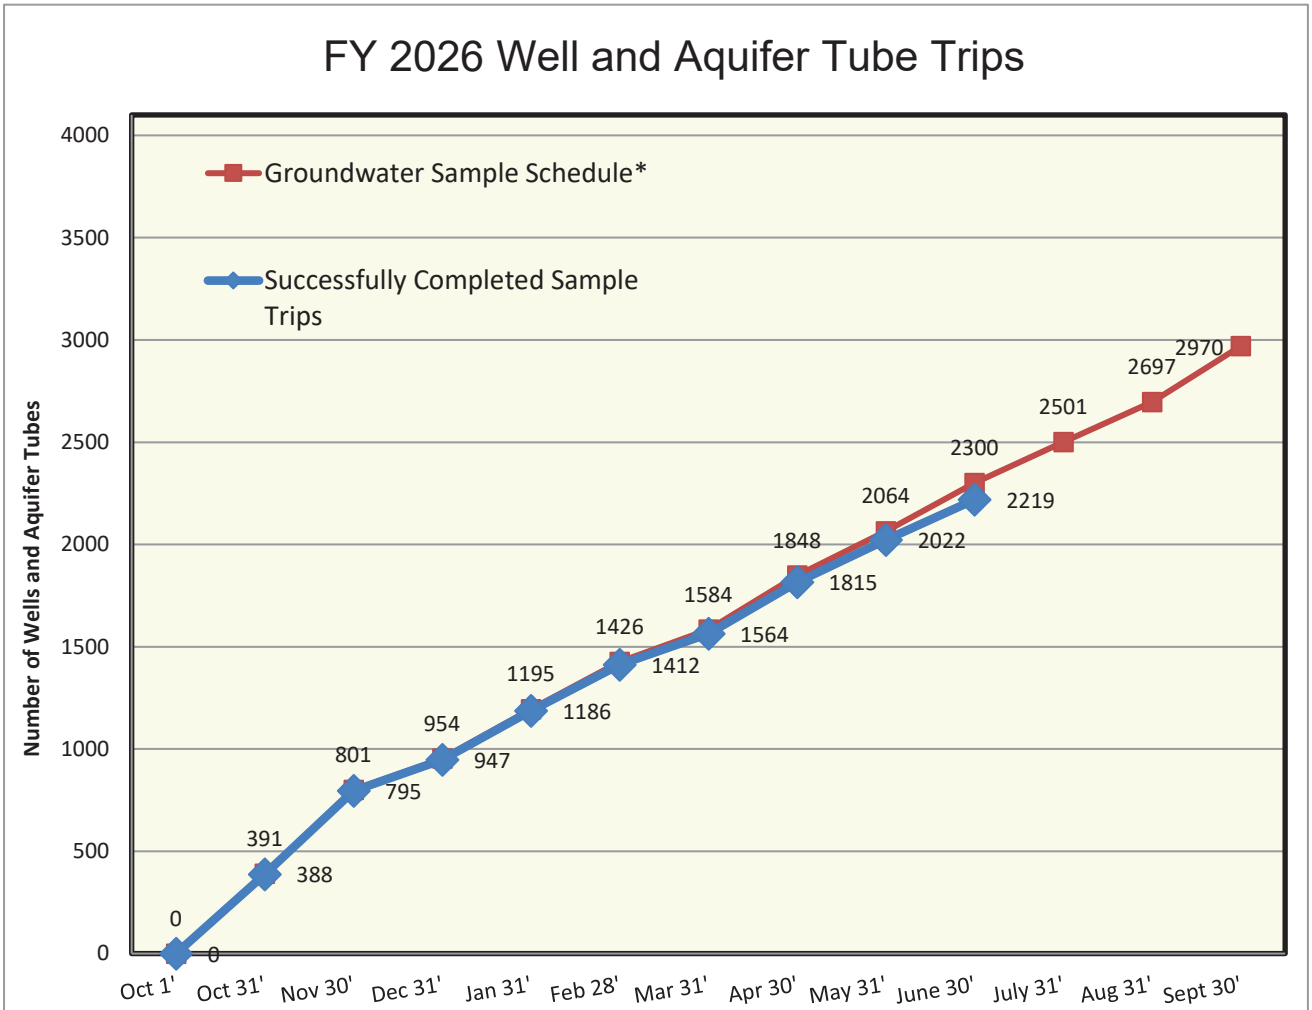

*The groundwater schedule is a living number of planned sample events. It represents sampling events from the beginning of the fiscal year as altered by approved sample cancellations and SAP revisions/TPA change notices.

Regulatory Agency Comments: None

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OPERABLE UNIT STATUS
MAY - JUNE 2026 DATA
JULY 16, 2026

Well Installation Status

Ecology Lead
HFO – Kaitlyn Nelson, CPCCo - Jennifer Richart

Regulatory Document Status:

- Drafting of SGW-73315, *Field Summary Report for the Installation of Monitoring Well 299-E17-59 (D0438) in the 200-PO-1 Groundwater Operable Unit* is ongoing.
- Drafting of SGW-73388, *Field Summary Report for the Installation of Monitoring Well 299-E25-256 (D0234) in the 200-PO-1 Groundwater Operable Unit* and SGW-73461, *Field Summary Report for the Installation of Monitoring Well 699-43-45B (D0689) in the 200-PO-1 Groundwater Operable Unit* is ongoing.

Recent Accomplishments and Upcoming Work:

- Continued the installation of four extraction wells in the 100-HR-3 groundwater operable unit. Extraction well 199-H3-41 (D0461) is under construction and extraction well 199-H6-10 (D0266) is currently being drilled.

Other Upcoming Planned Work:

- Installation of monitoring well 699-76-54 (D0439) will begin mobilizing to start drilling work the first week of August 2026.

Regulatory Agency Comments: None

Central Plateau Milestone Status

Milestone	Title	Due Date
M-015-00	Complete the RI/FS (or RFI/CMS) Process for All Non-Tank Farm Operable Units	Deleted
M-015-38B	Submit FS/PP for 200-CW-1, 200-CW-3 and 200-OA-1 OUs	Deleted
M-015-84	Complete RI of 200-WA-1 and 200-BC-1 Waste Sites in Accordance with RI/FS Work Plan	Deleted
M-015-91B	Submit FS/PP for the 200-BC-1 and 200-WA-1 OUs to EPA	Deleted
M-015-91D	Submit Draft CCF to Establish Schedule for Activities in the 200-WA-1 & 200-BC-1 OUs RI/FS Work Plan	Deleted
M-015-92B	Submit RFI/CMS, RI/FS Study report and Proposed CAD/PP for 200-EA-1	Deleted
M-015-92C	Submit RFI/CMS & RI/FS Report and PCAD/PP for 200-IS-1 OU to Ecology	Deleted
M-015-92E	Submit Draft CCF to Establish Schedule for Activities in the 200-EA-1 OU RFI/CMS/RI/FS Work Plan	Deleted
M-015-92F	Submit Draft CCF with Date for Milestone M-015-112 for Submittal of 200-IS-1 OU RFI/CMS/RI/FS WP	Deleted
M-015-93B	Submit RFI/CMS & RI/FS Report and Proposed CAD/PP for 200-SW-2 OU	Deleted

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OPERABLE UNIT STATUS
MAY - JUNE 2026 DATA
JULY 16, 2026

Milestone	Title	Due Date
M-015-93C	Initiate Characterization Field Work for the 200-SW-2 OU Landfills	Deleted
M-015-98	Complete Remedial Investigation of U Plant Related Waste Sites located in 200-WA-1 in accordance with the WA-1 RI/FS Work Plan	Deleted
M-015-99	Complete Remedial Investigation of PFP Related Waste Sites located in 200-WA-1 in accordance with the 200-WA-1 and 200-BC-1 RI/FS Work Plan.	Deleted
M-015-110B	Submit CMS & FS and PCAD/PP for 200-DV-1 OU	Deleted
M-015-112	Submit Draft B 200-IS-1 RFI/CMS/RI/FS Work Plan to Ecology with Schedule Dates	Deleted
M-016-87E	Submit Annual Evaluation of Results of Enhanced Groundwater Monitoring Near the 618-11 Burial Ground	Deleted
M-016-89	Submit to EPA the RD/RA Work Plan with Updated Schedule for Remediating the 618-11 Burial Ground	Deleted
M-016-200B	Complete U Plant (221 U Facility) barrier construction	Deleted
M-024-58S	Initiate Discussions of Well Commitments	6/01/2026 Completed
M-024-58T	Initiate Discussions of Well Commitments	6/01/2027 On Schedule
M-024-58U	Initiate Discussions of Well Commitments	6/01/2028 On Schedule
M-024-77	Complete the Construction of All Wells Listed for CY26 and Before	12/31/2026 On Schedule
M-024-77-T01	Conclude discussions of well commitments initiated under M-024-58	8/01/2026 On Schedule
M-024-78	Complete the Construction of All Wells Listed for CY27 and Before	12/31/2027 On Schedule
M-024-78-T01	Conclude discussions of well commitments initiated under M-024-58	8/01/2027 On Schedule
M-024-79	Complete the Construction of All Wells Listed for CY28 and Before	12/31/2028 On Schedule
M-024-79-T01	Conclude Discussions of Well Commitments Initiated Under M-024-58	8/01/2028 On Schedule
M-037-20*	Submit Coordinated Closure Proposal for the 4 Specified TSDs if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-92B
M-037-22*	Submit Coordinated Closure Proposal for the 2 Specified TSDs if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-38B
M-037-25*	Submit Coordinated Closure Proposal for Inactive SST Components Outside WMAs if Requesting Alternative Closure Requirements	Submit concurrently with M-015-92C

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OPERABLE UNIT STATUS
MAY - JUNE 2026 DATA
JULY 16, 2026

Milestone	Title	Due Date
M-037-26*	Submit Coordinated Closure Proposal for Green Island TSDs in LLBG if Requesting Use of Alternative Closure Requirements	Submit concurrently with M-015-93B
M-037-31**	Submit PMR with 90% Design for Final Landfill Cover, Including Closure Schedule for NRDWL and SWL	10/31/2030 On Schedule
M-037-32	Submit PMR with Updated Post-Closure Plan, Including Groundwater Monitoring Plan for NRDWL and SWL	Due date is 180 days after Ecology's approval of the 90% cover design submitted in Milestone M-037-31 On Schedule
M-085-01	Submit change package to establish a date for Major Milestone M-085-00	Deleted
M-085-70	Submit to Ecology a RI/FS Work Plan for 200-CB-1	Deleted
M-085-76	Initiate response actions for the B Plant geographic area	Deleted
M-085-84	Initiate response actions for the PUREX Operable Unit	Deleted
M-085-84C	Complete Infrastructure Upgrades to Support Demolition Preparation of the PUREX Complex	Deleted
M-085-84D	Initiate Utility System Isolations for the PUREX Complex	Deleted
M-085-86	Submit a Modification to the PUREX RAWP a Schedule for White Powder Removal	Deleted
M-085-90	Submit Remedial Investigation/Feasibility Study Work Plan for 200-CR-1 to EPA	Deleted
M-100-01A	Adaptive Milestone Process: Initiate Discussions to Support Completion of TPA Interim Milestone M-100-02	01/15/2027
M-100-01B	Adaptive Milestone Process: Initiate Discussions to Support Completion of TPA Interim Milestone M-100-02	01/15/2028
M-100-01C	Adaptive Milestone Process: Initiate Discussions to Support Completion of TPA Interim Milestone M-100-02	01/15/2029
M-100-02A	Adaptive Milestone Process: Conclude Annual Review and Submit Draft CCF Documenting Completion of Discussions/Decisions	05/31/2027
M-100-02B	Adaptive Milestone Process: Conclude Annual Review and Submit Draft CCF Documenting Completion of Discussions/Decisions	05/31/2028
M-100-02C	Adaptive Milestone Process: Conclude Annual Review and Submit Draft CCF Documenting Completion of Discussions/Decisions	05/31/2029
M-100-15	Central Plateau Decision-Making: Issue Signed Record of Decision for 200-IA-1 OU	10/31/2029
M-100-15-T01	Central Plateau Decision-Making: Submit Draft B Focused Feasibility Study and Draft A Proposed Plan for 200-IA-1 OU	10/31/2027
M-100-16	Central Plateau Decision-Making: Complete Field Sampling for 200-DV-1 OU	09/30/2030
M-100-17	Central Plateau Decision-Making: Provide Recommendations for 200-BC-1 OU Remedial Action Decision-Making	03/31/2028

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OPERABLE UNIT STATUS
MAY - JUNE 2026 DATA
JULY 16, 2026

Milestone	Title	Due Date
M-100-18-T01	Central Plateau Decision-Making: Initiate 200-WA-1 OU Field Characterization	06/30/2030
M-100-19	Central Plateau Decision-Making: Provide Plan Addressing Sequence of Activities per RAWP for PUREX Complex	09/30/2028

NOTES:

- On May 18, 2026, the M-016 and M-085 milestone series were deleted with approval of TPA Change Control Forms (CCF) M-16-25-02 and M-85-25-01 and the new M-100 milestone series was established via approved CCF M-100-25-01.
- *Parties are working to update the M-037 coordinated closure milestones to align with updates from adaptive milestone planning, including deletion of previously associated M-015 milestones and establishment of M-100 milestones for the adaptive milestone process.
- **Approval of CCF M-37-26-02 on 6/03/2026 extended the due date of Milestone M-037-31 from 8/31/2026 to 10/31/2030

Regulatory Agency Comments: None

Documents Submitted to the Administrative Record

Document Number	Title	Clearance Date/Signed	Referencing Document Number	Referencing Document Title
HNF-9162, Rev. 0	CSER 01-012: Cleanup of Criticality Mass Lab in 209-E Building	5/7/2003	DOE/RL-2020-51	200-IA-1 Focused Feasibility Study
RHO-CD-1048	Current Status of Outdoor Radiation Areas in the 200 Areas	9/11/1980	DOE/RL-2020-51	200-IA-1 Focused Feasibility Study
WHC-SD-DD-AP-013 Rev.0	UN-216-W-31 Unplanned Release Site Interim Stabilization Plan and Alternatives Evaluation	12/23/1991	DOE/RL-2020-51	200-IA-1 Focused Feasibility Study
SGW-72650, Rev.0	D0118 and D0119 Drilling DUA	4/21/2026	N/A	N/A
SGW-70501, Rev.0	221-T Railroad Cut RCRA Clean Closure Samples Data Usability Assessment	5/12/2026	N/A	N/A
ECF-200E-26-0002, Rev. 0	Groundwater Elevation Mapping for 200 East Area: Quarter 4 Calendar Year 2025	4/22/2026	N/A	N/A
ECF-200W-26-0003, Rev. 0	Groundwater Elevation Mapping for 200 West Area: Quarter 4 Calendar Year 2025	4/22/2026	N/A	N/A
ECF-HANFORD-26-0001, Rev. 0	Hydraulic Gradient and Average Linear	4/22/2026	N/A	N/A

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MILESTONES AND OPERABLE UNIT STATUS
MAY - JUNE 2026 DATA
JULY 16, 2026

Document Number	Title	Clearance Date/Signed	Referencing Document Number	Referencing Document Title
	Groundwater Velocity Calculation - Quarter 3 Calendar Year 2025			
ECF-200IA1-25-0036, Rev. 0	200-IA-1 Operable Unit Human Health Risk Assessment	5/27/2026	DOE/RL-2020-51	200-IA-1 OU Focused Feasibility Study
ECF-200IA1-25-0084, Rev. 0	200-IA-1 Operable Unit Ecological Risk Assessment	5/27/2026	DOE/RL-2020-51	200-IA-1 OU Focused Feasibility Study
CPCC-SRP-00041, Rev.0	211-T Pad DUA	6/8/2026	N/A	N/A

Regulatory Agency Comments: None

TRI-PARTY AGREEMENT (TPA)
200 AREA PROJECT MANAGERS MEETING
MAY - JUNE 2026 DATA
JULY 16, 2026

Action Items

Action Number	Action	Assigned to	Owed to	Assigned Date	Due Date	Status
203	Capture the updated M-100 milestone series	DOE	All	05/21/2026	07/16/2026	Closed. Milestone table has been updated to reflect both deleted milestones as well as the addition of the M-100 milestone series.
204	Add ERDF section	DOE	All	05/21/2026	07/16/2026	Closed. This section has been added.
