

START



0013439
9101347

Department of Energy


Richland Operations Office
P.O. Box 550
Richland, Washington 99352

91-ERB-061

MAR 26 1991

Mr. Paul T. Day
Hanford Project Manager
U. S. Environmental Protection Agency
712 Swift Boulevard, Suite 5
Richland, Washington 99352

Mr. Timothy L. Nord
Hanford Project Manager
State of Washington
Department of Ecology
Mail Stop PV-11
Olympia, Washington 98504-8711



Dear Messrs. Day and Nord:

200-BP-1 OPERABLE UNIT INTERIM STABILIZATION

Per a request by the U. S. Environmental Protection Agency, this letter documents the schedule for performing the 200-BP-1 Remedial Investigation (RI) field activities and the interim stabilization activities within the operable unit. The RI field activities will not be impacted by the interim stabilization activities.

Attached is an integrated schedule showing Radiation Area Remediation Action (RARA) interim stabilization activities and RI Task 3 and 4 field activities. Task 3 Near Surface Soil Sampling coupled with RARA site preparation is completed prior to site stabilization, followed by Task 4 vadose sampling. These activities have been coordinated such that the start of Task 4 vadose zone samples is not impacted by RARA program activities. Task 4 vadose zone sampling will be initiated upon completion of the required hazard assessment safety documentation estimated to be completed by the end of April 1991. Should this be completed sooner, Task 4 work would be initiated at the B-57 crib first. This is facilitated by phasing the RARA program stabilization activities at the B-57 crib followed by cribs B-43 through B-50.

If you have any questions or need further information, please contact Ms. Julie K. Erickson on (509) 376-3603.

Sincerely,

James E. Rasmussen
for Steven H. Wisness
Hanford Project Manager



ERD:JKE


Attachment

cc w/att:
R. E. Lerch, WHC

9 2 1 2 5 3 0 3 5 3

9 2 1 2 5 8 3 0 3 5 4

200-BP-1 Interim Stabilization

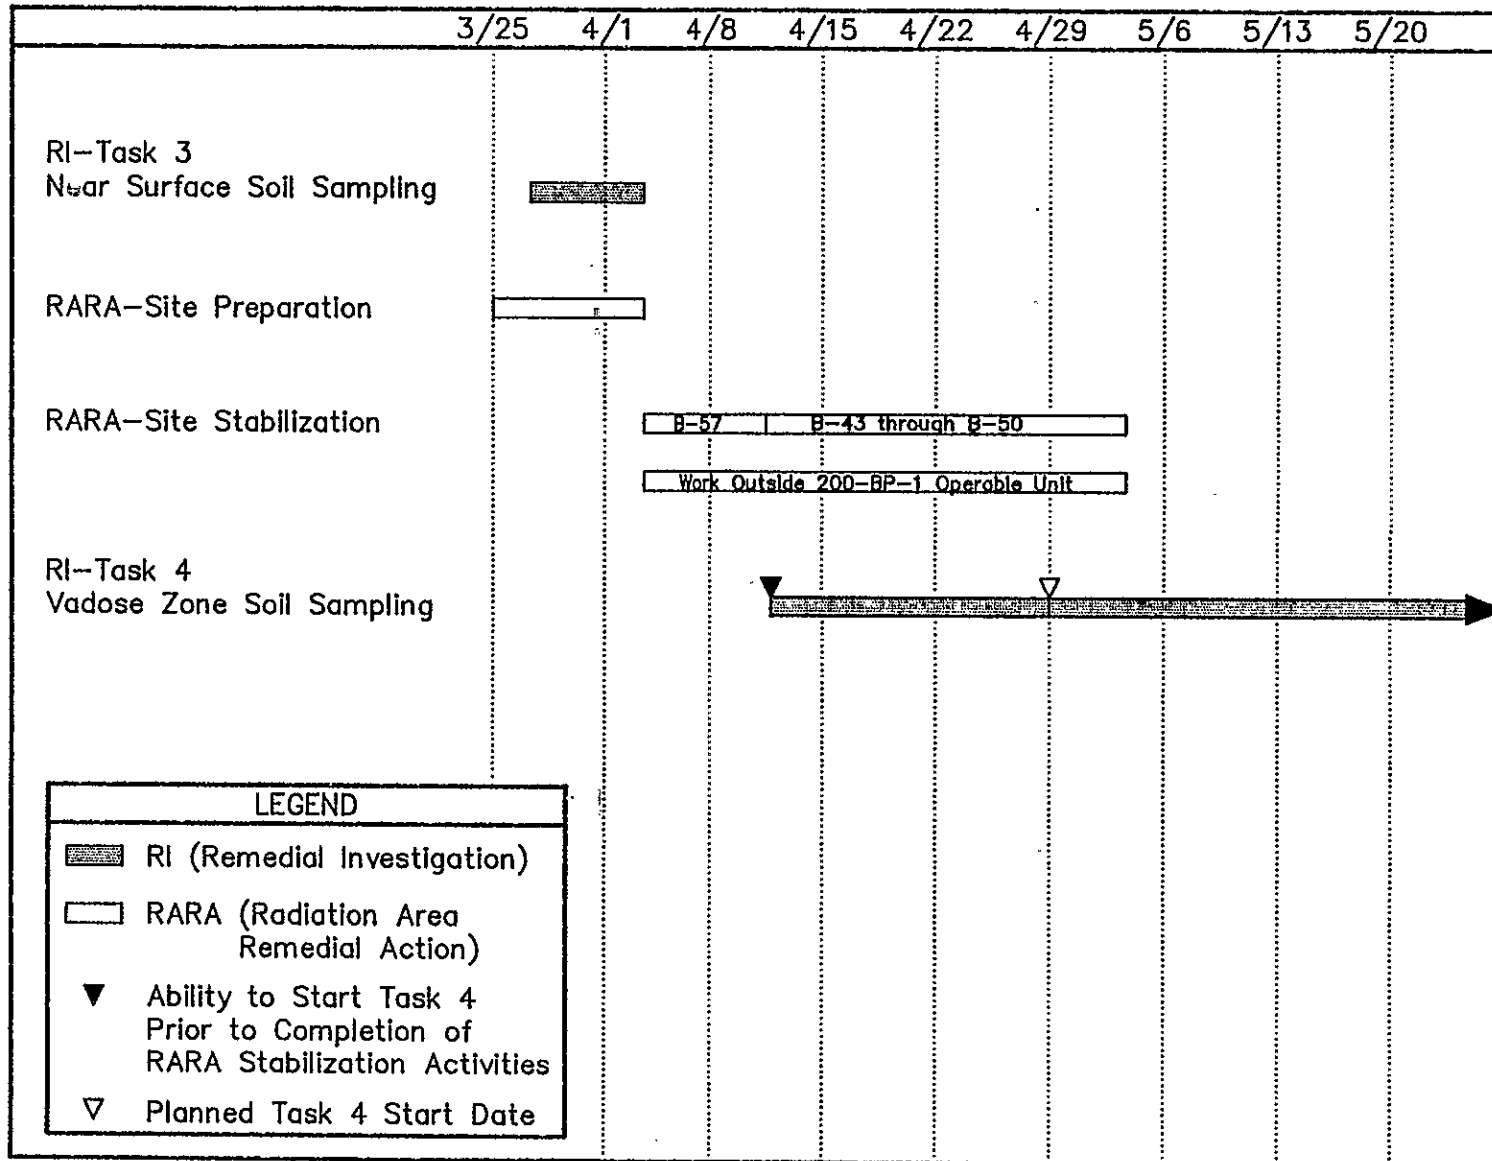

DISTRIBUTION COVERSHEET

Author
SH Wisness/DOE-RL


Addressee
PT Day/U.S. EPA
TL Nord/Dept. of Ecology

Incoming Correspondence No.
9101347

Subject 200-BP-1 Operable Unit Interim Stabilization

Internal Distribution

Approval	Date	Name	Location	w/att
		Correspondence Control	A3-01	X
		MR Adams	H4-55	X
		BA Austin	B2-14	X
		LC Brown	H4-51	X
		KR Fecht	H4-56	X
		VW Hall	L4-88	X
		KL Hoewing		X
		WL Johnson	H4-55	X
		KN Jordan	L4-92	X
		KR Jordan		X
		RE Lerch (Assignee)		X
		HE McGuire		X
		K Parnell	H4-18	X
		LL Powers	B2-35	X
		TB Veneziano	B2-35	X
		TM Wintczak	L4-92	X
		RD Wojtasek	L4-92	X
		EDMC	H4-22	X
		TPAI File (DH)	B2-35	X



DISTRIBUTION CORRECTIONS SHOULD BE SENT OR CALLED TO MARIAN CRAM
LIST 1

54-6000-117 (09/88)

A3-01 6-4123 or CC Mail

92125830355
