

START

0013960 //

April 15, 1991

Meeting Minutes Transmittal/Approval
Unit Managers Meeting: 100-FR-1
450 Hills St., Room 47
Richland, Washington
March 20, 1991


From/ Appvl.: James D. Goodenough Date: _____
James D. Goodenough, R.I. Coordinator, DOE-RL (A6-95)
Appvl.: Pamela L. Innis Date: 4-16-91
Pamela Innis, Unit Manager, EPA (B5-01)
Appvl.: Larry Goldstein Date: 4/16/91
Larry Goldstein, CERCLA Unit Supervisor, Washington Dept. of Ecology

The purpose of this meeting was to discuss the status of the 100-FR-1 operable unit.

Meeting Minutes are attached. Minutes are comprised of the following:

- Attachment #1 - Meeting Summary/Summary of Commitments and Agreements
- Attachment #2 - Attendance List
- Attachment #3 - Presentation on Work Plan Status

Prepared by: Doug Fassett Date: 4/16/91
SWEC GSSC
Concurrence by: John Stewart Date: 4/16/91
USACE Unit Manager



Distribution

Unit Managers Meeting: 100-FR-1
March 20, 1991

Dave Einan, EPA (B5-01)
Pamela Innis, EPA (B5-01)
Doug Sherwood, EPA (B5-01)
Dan Duncan, EPA, Region 10, RCRA
Chuck Cline, WDOE (two copies)
R.O. Patt, Oregon Water Resources Dept.
Ward Staubitz, USGS
Donna Lacombe, PRC
Doug Fassett, SWEC (A4-35)
Jim Goodenough, DOE-RL (A6-95)
Mary Harmon, DOE-HQ (EM-442)
Bob Stewart, DOE-RL (A6-95)
John Stewart, USACE
KaeRae Parnell, WHC (H4-18)
Jim Patterson, WHC (B2-15)
Linda Powers, WHC (B2-35)

ADMINISTRATIVE RECORDS: 100-FR-1, Care of Susan Wray, WHC (H4-51C)

Please inform Doug Fassett (SWEC) of deletions or additions to the distribution list.

Attachment #1

Meeting Summary and Summary of Commitments and Agreements
100-FR-1 Unit Managers Meeting
March 20, 1991

1. Tetra-Tech started the preparation of the 100-FR-1 work plan in mid-February. The corps will begin review of a draft of the work plan between March 26 and March 29. Two informal copies will be distributed next week, one to Jim Goodenough and one to Pam Innis. Draft A of the work plan will be presented to DOE-RL on April 15, 1991; review by DOE and the regulators will be concurrent. Attachment #3 contains information on the operable unit and schedules for developing and finalizing the work plan.
2. Jim Goodenough said a letter from Leo Duffy states that all primary regulatory documents must be provided to DOE-HQ 60 days prior to distribution to the regulators. Compliance on this 60-day provision will not fit the given schedule. There is no way to be in compliance with the TPA and with the requirement for 60-day approval time for DOE-HQ.

ATTACHMENT #2

Attendance List
100-FR-1 Unit Managers Meeting
March 20, 1991


Name	Org.	O.U.	Phone
Murray, David	B & C	Ecology Support	(503) 244-7005
Goodenough, Jim	DOE-RL	DOE O.U.	(509) 376-7078
Stewart, John	DOE-RL	DOE backup	(509) 376-6192
Cline, Chuck	Ecology	CERCLA Unit	(206) 438-7556
Hibbard, Richard	Ecology	CERCLA Unit	(206) 493-9367
Moore, Clyde	PMX	Ecology Support	(206) 455-2550
LaCombe, Donna	PRC	EPA Cont.	(206) 624-2692
Collins, Carol	SWEC	GSSC	(509) 376-1009
Fassett, Doug	SWEC	GSSC to DOE-RL	(509) 376-3136
Fryer, Bill	SWEC	GSSC to DOE-RL	(509) 376-9830
April, John	USACE	Tech. Manager	(509) 522-6834
Foote, Kevin	USACE	Env. Eng.	(509) 522-6870
Greenwald, Wendell	USACE	Tech. Manager	(206) 376-1513
Healy, Kevin	USACE	DOE Support	(205) 955-5170
Stewart, John	USACE	PM	(509) 522-6331
Drost, Brian	USGS	EPA Support	(206) 593-6510
Lauterbach, Merle	WHC	Env. Eng.	(509) 376-5257

PAST PRACTICES UNIT MANAGERS MEETING


20 MARCH 1991

100-FR-1 OPERABLE UNIT

**U.S. ARMY CORPS OF ENGINEERS
WALLA WALLA DISTRICT**

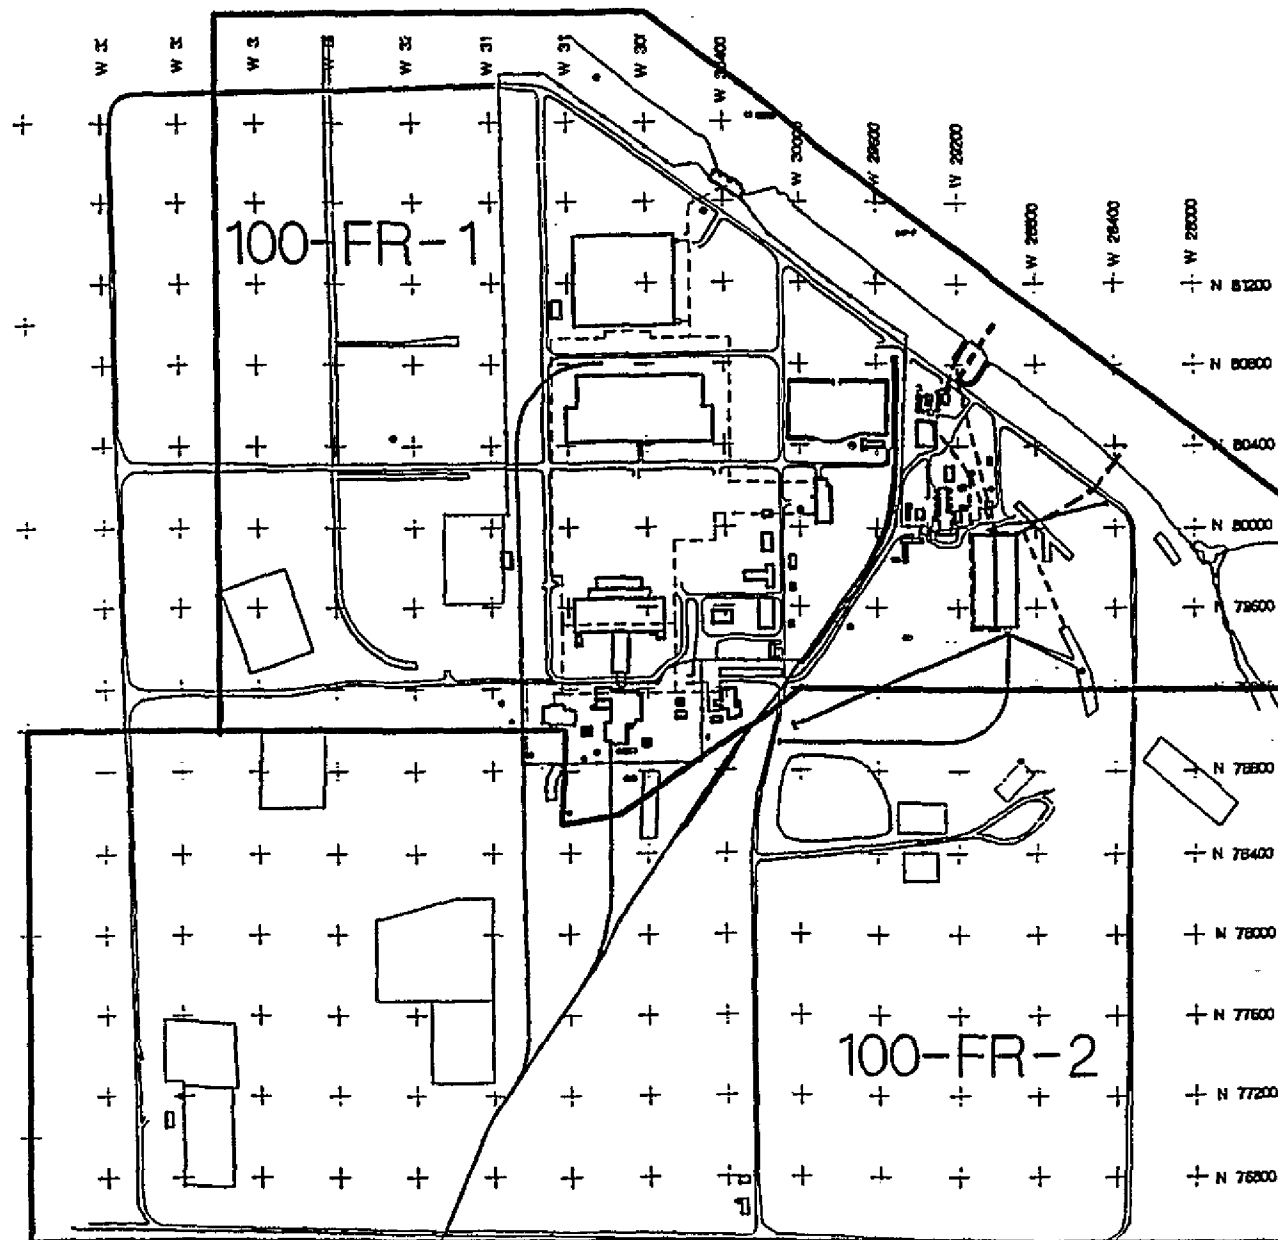

91112100073

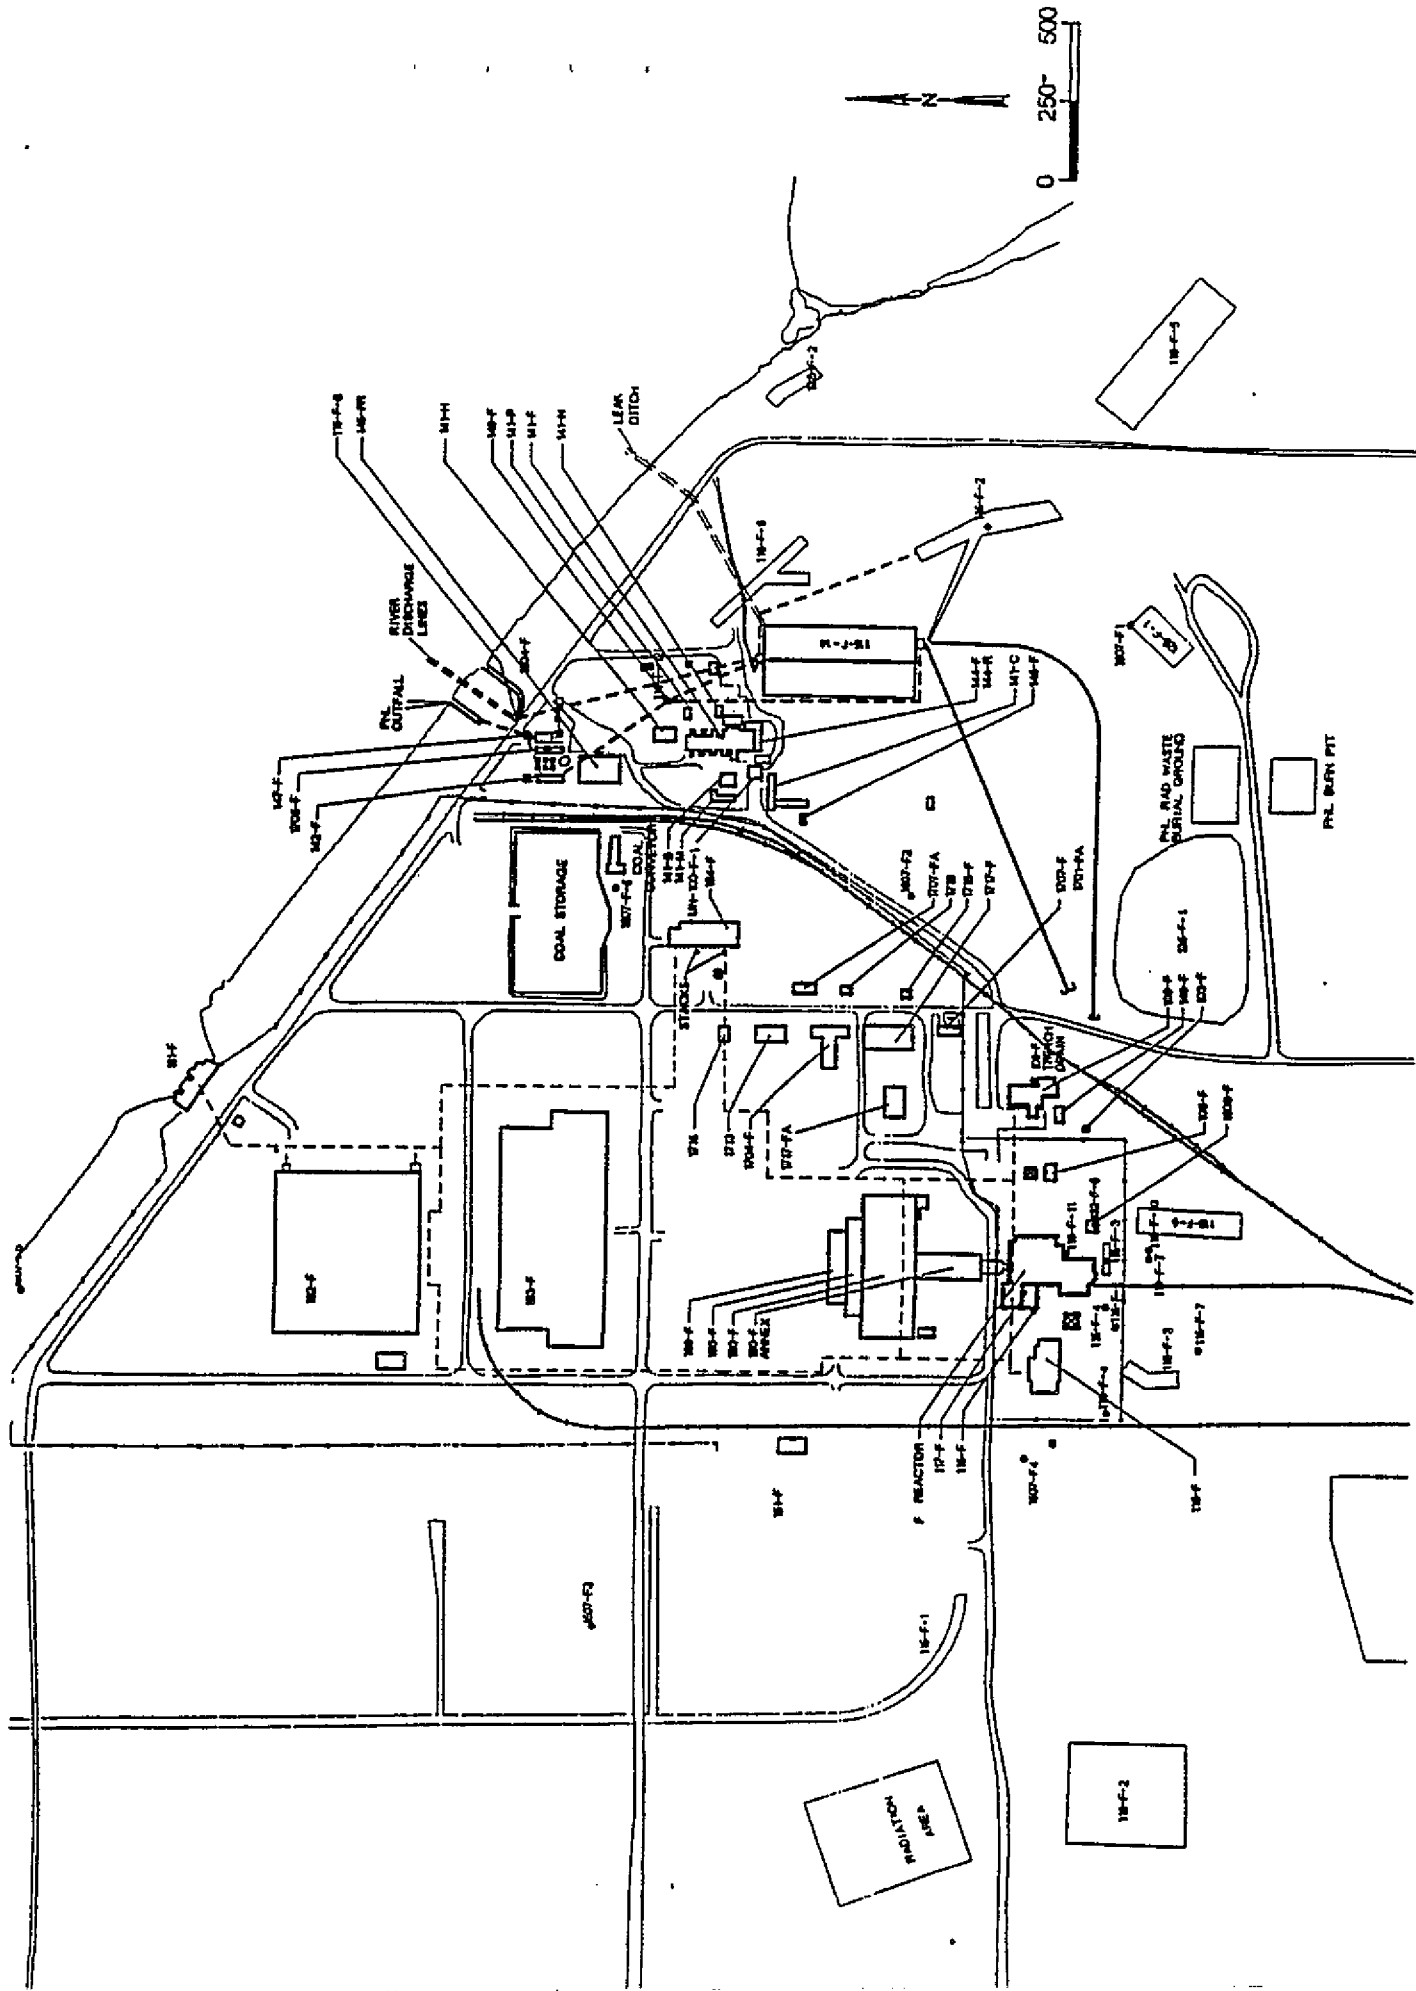

**PREPARATION OF A CERCLA
REMEDIAL INVESTIGATION / FEASIBILITY STUDY WORK PLAN
FOR THE 100-FR-1 OPERABLE UNIT**

**TASK ORDER No. DE-AT06-91RL12104
PROJECT No. 004-FR-1-01-00**

EXECUTED: 26 OCTOBER 1991

DRAFT "A" WORK PLAN TO DOE-RL: 15 APRIL 1991

DRAFT "B" WORK PLAN TO DOE-RL: 30 AUGUST 1991

NO ISSUES OR PROBLEMS

REMEDIAL INVESTIGATION/FEASIBILITY STUDY (RI/FS) WORK PLAN FOR THE 100-FR-1 OPERABLE UNIT

TABLE OF CONTENTS

1.0	INTRODUCTION
2.0	OPERABLE UNIT BACKGROUND SETTING
3.0	INITIAL EVALUATION
4.0	RATIONAL AND APPROACH
5.0	REMEDIAL INVESTIGATION/FEASIBILITY STUDY TASKS
5.1	PROJECT MANAGEMENT
5.2	COMMUNITY RELATIONS
5.3	OPERABLE UNIT CHARACTERIZATION
5.4	REMEDIAL ALTERNATIVES TASKS
5.5	FEASIBILITY STUDY-REMEDIAL ALTERNATIVES SCREENING
5.6	PHASE II REMEDIAL/TREATABILITY INVESTIGATIONS
5.7	FEASIBILITY STUDY-DETAILED ANALYSIS OF REMEDIAL ALTERNATIVES
6.0	PROJECT SCHEDULE
7.0	PROJECT MANAGEMENT
8.0	REFERENCES
9.0	GLOSSARY
ATTACHMENT 1:	SAMPLING ANALYSIS PLAN
ATTACHMENT 2:	HEALTH AND SAFETY PLAN
ATTACHMENT 3:	PROJECT MANAGEMENT PLAN
ATTACHMENT 4:	DATA MANAGEMENT PLAN
ATTACHMENT 5:	COMMUNITY RELATIONS PLAN

Distribution

Unit Managers Meeting: 100-FR-1
March 20, 1991

Dave Einan, EPA (B5-01)
Pamela Innis, EPA (B5-01)
Doug Sherwood, EPA (B5-01)
Dan Duncan, EPA, Region 10, RCRA
Chuck Cline, WDOE (two copies)
R.O. Patt, Oregon Water Resources Dept.
Ward Staubitz, USGS
Donna Lacombe, PRC
Doug Fassett, SWEC (A4-35)
Jim Goodenough, DOE-RL (A6-95)
Mary Harmon, DOE-HQ (EM-442)
Bob Stewart, DOE-RL (A6-95)
John Stewart, USACE
KaeRae Parnell, WHC (H4-18)
Jim Patterson, WHC (B2-15)
Linda Powers, WHC (B2-35)

ADMINISTRATIVE RECORDS: 100-FR-1, Care of Susan Wray, WHC (H4-²²~~51C~~)

Please inform Doug Fassett (SWEC) of deletions or additions to the distribution list.
