

START

15
0022670

Final

Meeting Minutes Transmittal/Approval
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
450 Hills, Richland, Washington

June 25, 1992


FROM/APPROVAL: Paul Pak Date 7-30-92
Paul Pak, 200 Aggregate Area Unit Manager, RL (A5-19)

APPROVAL: Lawrence E. Doolittle For Date 7-30-92
Doug Sherwood, 200 Aggregate Area Unit Manager, EPA (B5-01)

APPROVAL: Billie Mauss Date 7/30/92
Darci Teel, 200 Aggregate Area Unit Manager, WA Dept of Ecology

Meeting Minutes are attached. Minutes are comprised of the following:

- Attachment #1 - Meeting Summary
- Attachment #2 - Agenda
- Attachment #3 - Attendance
- Attachment #4 - Action Item Status List
- Attachment #5 - Status of 200 Aggregate Area Management Study Program
- Attachment #6 - Proposed Schedule Change for the 200 West Groundwater AAMSR
- Attachment #7 - 200 AAMS Geophysical Logging and Groundwater Sampling Field Activities Update



Prepared by: Suzanne Clarke Date: 7/30/92
Suzanne Clarke, Kay Kimmel, GSSC (A4-35)

Concurrence by: Curt Wittreich Date: 7/30/92
Curt Wittreich, WHC Coordinator (H4-55)

92120341302

Attachment #1
Meeting and Summary of Commitments and Agreements
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units

June 25, 1992

1. SIGNING OF THE MAY 200 AREA UNIT MANAGER'S MEETING MINUTES:

Meeting minutes were reviewed and approved.

2. ACTION ITEM UPDATE: See Attachment 4 for status (before June meeting)

No updates were made to existing Action Items.

3. NEW ACTION ITEMS (INITIATED June 25, 1992):

No new action items were initiated.

4. STATUS 200 AGGREGATE AREA MANAGEMENT STUDIES

- Curt Wittreich presented the status of 200 Aggregate Area Management Study Program, shown in Attachment #5.
- Proposed schedule change for the 200 West Groundwater AAMSR is under regulatory consideration. See Attachment #6.
- Steve Trent presented the update of the 200 AAMS Geophysical Logging and Groundwater Sampling Field Activities, shown in Attachment #7.

5. INFORMATION ITEMS/INFORMAL AGREEMENTS:

- Questions arose concerning comment disposition of the AAMSRs. WHC agreed to send a cc:mail message on 1) which sections to consider for review and 2) which sections have already been commented on and do not require review.
- 200 West spectral gamma-ray logging is behind schedule by sixteen wells. The regulators agreed they would prefer the report on schedule with less data.

9 2 1 2 6 5 4 1 3 3 3

Attachment #2
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

Agenda

- 200 AAMS Activities - Curt Wittreich
 - Status of AAMSRs
 - Geophysical Logging and Groundwater Sampling Field Activities Update

9 2 1 2 6 5 4 1 3 3 4

Attachment #4

Action Item Status List
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

Item No.	Action/Source of Action	Status
2AAMS.1	Identify and implement the actions that are required to install the calibration pits for the borehole logging equipment. Action: Allan Harris (9/19/91)	Open
2AAMS.5	DOE will initiate the paperwork for changing the content and/or boundaries of the 200-UP-2 OU. Action to Allan Harris (2/26/92).	Open
2AAMS.6	Allan Harris will meet with Mike Thompson to clarify what changes to the UP-1 and UP-2 units will be sought in a Level 2 Change Request. A new Change Request will be submitted after Allan meets with RL management and the TPA Project Manager Board.	Open

9 2 1 2 6 5 4 3 3 6

9 2 1 2 6 5 4 1 3 3 7

Attachment #5

200 AGGREGATE AREA MANAGEMENT STUDY PROGRAM

Curtis D. Wittreich
Technical Coordinator

Steven J. Trent
Field Activities Coordinator

June 25, 1992

Status 200 Aggregate Area Management Study Program

06/24/92

Area	Aggregate Area	AAMS Type	AAMS Report	Regulator Comments Due	M-27-00 Milestones
200 West	U Plant	Source	Redrafting Based on Regulator Comments	3/16/92	1/92
	Z Plant	Source	Regulator Review Comments Dispositioned	4/14/92	2/92
	S Plant	Source	Regulator Review Comments Dispositioned	5/15/92	3/92
	T Plant	Source	Regulator Review Comments Received	6/15/92	4/92
	200 West	Groundwater	Drafted-On Schedule		9/92
200 East	PUREX	Source	Draft A Under Regulatory Review	7/15/92	5/92
	B Plant	Source	Drafted-On Schedule		6/92
	Semi-Works	Source	Drafted-On Schedule		7/92
	200 East	Groundwater			9/92
200 North	200 North	Source	Drafted-On Schedule		8/92

9 2 1 2 5 3 4 1 3 3 9

Attachment #6

PROPOSED SCHEDULE CHANGE FOR THE 200 WEST GROUNDWATER AAMSR:

- **Move the Draft A submittal date up 1 month to August 31**
- **Schedule regulator review from September 1 - October 15**

9 2 1 2 5 5 4 1 3 9 0

Attachment #7

**200 AAMS
GEOPHYSICAL LOGGING AND
GROUNDWATER SAMPLING
FIELD ACTIVITIES UPDATE**

6/25/92
PAGE 1

#7/Page 1 of 6

GEOPHYSICS


● SPECTRAL GAMMA-RAY LOGGING COMPLETED TO DATE:

299-W22-75	216-S-21 CRIB	U PLANT	299-W11-18	216-T-35 CRIB	T PLANT
299-W23-4	216-U-12 CRIB	U PLANT	299-W11-70	216-T-26 CRIB	T PLANT
299-W19-11	216-U-1 CRIB	U PLANT	299-W14-4	216-T-28 CRIB	T PLANT
299-W19-9	216-U-2 CRIB	U PLANT	299-W11-11	216-T-18 CRIB	T PLANT
299-W18-10	216-Z-18 CRIB	Z PLANT	299-W15-4	216-T-19 CRIB	T PLANT
299-W15-83	216-Z-5 CRIB	Z PLANT	299-W15-210	216-T-21:24	T PLANT
299-W15-8	216-Z-9 CRIB	Z PLANT	299-W11-61	216-T-6 CRIB	T PLANT
299-W15-7	216-Z-7 CRIB	Z PLANT	299-W11-7	216-T-3 CRIB	T PLANT
299-W18-5	216-Z-7 CRIB	Z PLANT	299-W11-81	216-T-14:17	T PLANT
299-W22-21	216-S-13 CRIB	S PLANT			
299-W22-32	216-S-7 CRIB	S PLANT			
299-W22-74	216-S-20 CRIB	S PLANT			
299-W26-1	216-S-5 CRIB	S PLANT			
299-W26-51	216-S-6 CRIB	S PLANT			

****NO 200 AAMS BOREHOLE LOGGING COMPLETED SINCE LAST UMM****

6/25/92
PAGE 2

200 AGGREGATE AREA MANAGEMENT STUDY SPECTRAL GAMMA-RAY LOGGING STATUS

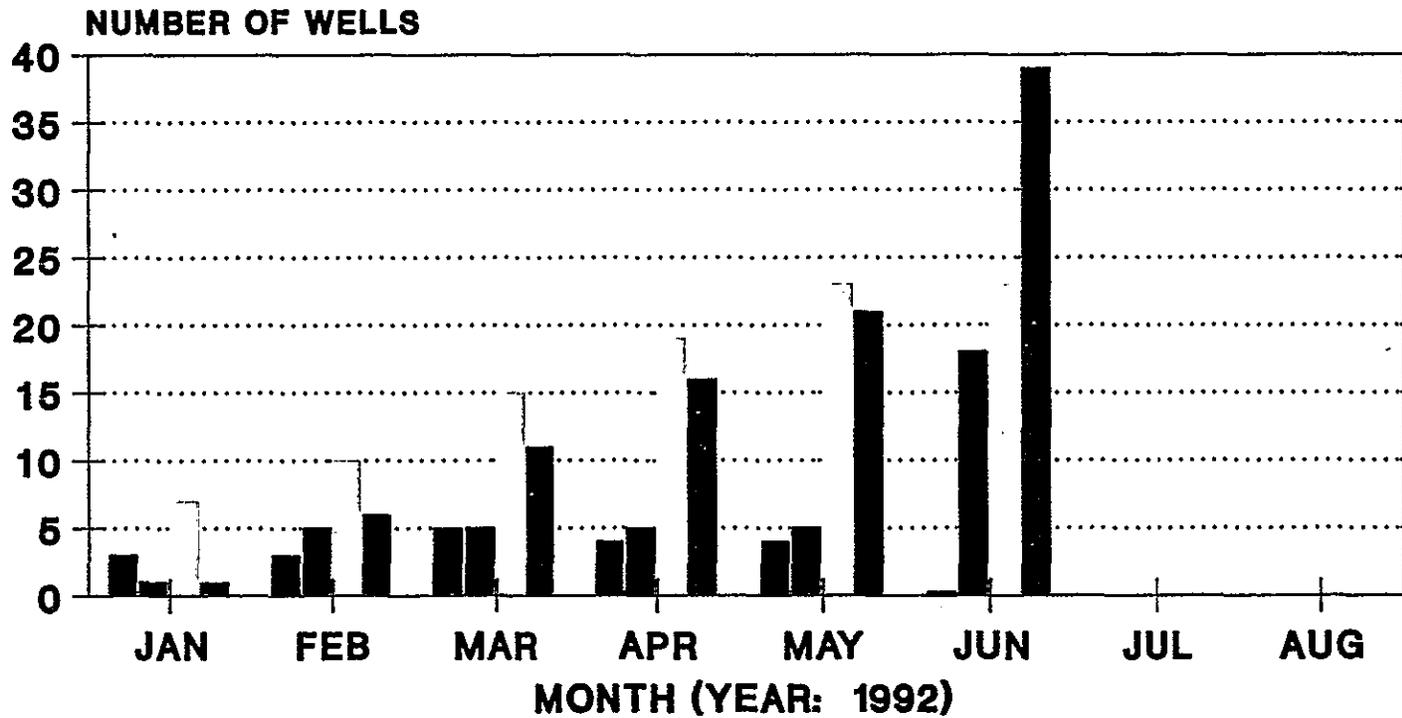

LOGGED DURING MONTH
 TTL. LOGGED TO DATE

SCHD. TO LOG
 TTL. SCHD. TO LOG

DATE: 6/25/92
NOTE: FOUR WELLS LOGGED DURING CY 1991

GEOPHYSICS (CONTINUED)

● SPECTRAL GAMMA-RAY LOGGING SCHEDULE DELAYED FOR TWO REASONS:

1) IMPLEMENTATION OF NEW RADIATION PROTECTION MANUAL

- ACCESS TO SURFACE CONTAMINATED ZONES UNCLEAR**
- POTENTIAL FOR REGULATION OF LOGGING TRUCK UNCLEAR**

- MANAGEMENT WORKING TO IDENTIFY CLARIFICATIONS ON ENTRY REQUIREMENTS AND IDENTIFYING SCENARIOS UNDER WHICH LOGGING TRUCK BECOMES A REGULATED VEHICLE

2) DELAY IN PROCUREMENT PROCESS FOR SUBCONTRACTOR SPECTRAL GAMMA-RAY LOGGING SERVICES

- PROCUREMENT PROBLEMS ENCOUNTERED WITH THE COMPETITIVE BID PROCESS**

- GEOPHYSICS TEAM WORKING WITH PROCUREMENT TO MODIFY BID AND CUT BID PROCESSING TIME

GEOPHYSICS (CONTINUED)

● IMPACTS:

- SLIP IN LOGGING SCHEDULE IDENTIFIED DURING THE JANUARY 1992 UNIT MANAGER MEETING**
- FIRST DRAFT OF 200 WEST SPECTRAL GAMMA-RAY LOGGING REPORT WILL NOT CONTAIN DATA FROM ALL WELLS IDENTIFIED IN THE 200 WEST BOREHOLE GEOPHYSICS SAP's**
- POTENTIAL DELAY IN RELEASE OF THE 200 EAST SPECTRAL GAMMA-RAY LOGGING REPORT**

RECOVERY SCHEDULE WILL BE PRESENTED AT THE JULY UNIT MANAGER MEETING

GROUNDWATER SAMPLING

● PHASE II GROUNDWATER SAMPLING CONTINUING

- 14 WELLS SAMPLED AS OF 6/25/92

● WELL MAINTENANCE ACTIVITIES COMPLETED

- 23 OLDER NON-RCRA STANDARD MONITORING WELLS REFURBISHED

● PHASE II SAMPLING AND ANALYSIS PLAN REVISED

- REVIEW AND FIELD CHECK OF ORIGINAL 80 WELLS INDICATES 10 WELLS ARE UNUSABLE
- 70 WELLS TO BE SAMPLED ONCE DURING FISCAL YEAR 1992
- REVISED PHASE II SAP TO BE DISTRIBUTED AT THIS UMM

Distribution

Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

- Julie K. Erickson Chief, DOE-RL, ERD/ERB (A5-19)
- Roger D. Freeberg Chief, Rstr. Br., DOE-RL, ERD/EPB (A5-19)
- Mike Thompson, DOE-RL, EAP/RPB (A5-15)
- Diane Clark, DOE-RL, TSD/SSB (A5-55)
- Mary Harmon, DOE-HQ (EM-442)
- Suzanne Clarke, SWEC, GSSC to DOE-RL (A4-35)

- Doug Sherwood 200 Aggregate Area Manager, EPA (B5-01)
- Ward Staubitz, USGS, Support to EPA
- Audree DeAngeles, PRC, Support to EPA

- Darci Teel 200 Aggregate Area Manager, WDOE, (Kennewick)
- Larry Goldstein WDOE, (Lacey)

- Lynn Albin Washington Dept. of Health

- Richard D. Wojtasek, WHC, Program. Manager (L4-92)
- Curt Wittreich, WHC, (H4-55)
- Tom Wintczak, WHC, (L4-92)
- Mel Adams, WHC, (H4-55)
- L.D. Arnold, WHC, (B2-35)
- Rich Carlson, WHC, (H4-55)
- M.J. Galgoul, WHC, (H4-55)

- Don Praast, GAO (A1-80)

ADMINISTRATIVE RECORD: 200 AAMS; Care of EDMC, WHC (H4-22)

This list has been updated. Please inform Suzanne Clarke (SWEC) of deletions or additions to the distribution list.

9 2 1 2 6 5 4 1 3 9 6
