

START

MEETING MINUTES

Subject: Expedited Response Action Weekly Interface

TO: Distribution

BUILDING: 2440 Stevens Center

FROM: W. L. Johnson

CHAIRMAN: W. L. Johnson *wlj*

Dept-Operation-Component	Area	Shift	Meeting Dates	Number Attending
Environmental Engineering	RCHN	Day	11/29/93	2

Distribution

State of Washington Department of Ecology

J. Donnelly
G. Freedman
L. Goldstein
D. Goswami
R. L. Hibbard
D. Holland
J. Phillips
C. Poindexter
P. Statts
D. D. Teel
N. Uziemblo
J. Yoke
T. Wooley

U.S. Army Corps of Engineers

W. D. Perro A5-19
M. D. Mahoney A5-19

U.S. Department of Energy

H. L. Chapman A5-19
J. K. Erickson A5-19
B. L. Foley A5-19
G. I. Goldberg* A5-19
E. D. Goller A5-19
R. G. McLeod A5-19
P. M. Pak A5-19
R. K. Stewart A5-19

U.S. Environmental Protection Agency

P. R. Beaver B5-01
D. R. Einan
D. A. Faulk
L. E. Gadbois
P. S. Innis
D. R. Sherwood

Westinghouse Hanford Company

M. R. Adams H6-01
L. D. Arnold B2-35
M. V. Berriochoa B3-30
A. S. Carlson B3-35
H. D. Downey H6-27
W. F. Heine B3-63
G. C. Henckel H6-04
W. L. Johnson* H6-04
J. K. Patterson H6-27
D. L. Sickle H6-27
T. M. Wintczak H6-27
EPIC H6-08
ERAG Route H6-04
WLJ File



*Attendees

The monthly interface meetings on the expedited response actions (ERAs) was held to status the ERAs for the U.S. Department of Energy, Richland Operations Office, the U.S. Environmental Protection Agency, and the State of Washington Department of Ecology. The meeting was conducted in accordance with the attached agenda.

Distribution
Page 2
November 29, 1993

It was agreed to go to a monthly format for the ERA Interface Meeting and schedule topical meetings to cover specific areas of concern or involvement. The next monthly ERA Interface Meeting is scheduled for Monday, December 27, 1993. The following topical meetings have also been scheduled:

MEETING SUBJECT	DATE	TIME	LOCATION
CCl ₄ GAC Overheating Presentation.	Monday 12/6/93	9:30 - 11:30	2440 STVCN, CR 1200
North Slope Pre-Public Meeting Review	Monday 12/13/93	9:30 - 10:30	2440 STVCN, CR 1600
General ERA Interface Monthly Meeting	Monday 12/27/93	9:30 - 11:00	2440 STVCN, CR 1600

Attachments:

1. Agenda
2. Action Item List
3. Decisions, Agreements & Commitments
4. Expedited Response Action Weekly Reports, period ending 11/26/93
5. Draft schedule for Riverland/Sodium Dichromate Pickling Acid Crib close outs.

9413092.0026

WEEKLY ERA INTERFACE AGENDA

SUBJECT: STATUS OF THE EXPEDITED RESPONSE ACTIONS

DATE: November 29, 1993

- GENERAL ISSUES
 - ERA Interface Action Item Review
- INDIVIDUAL PROJECT STATUS
 - Riverland, Sodium Dichromate, Pickling Acid Crib
 - Status of integrated schedule for the above projects
 - N-Springs
 - Response to comments, meeting set for 11/29/93
 - North Slope
 - Proposal status - pre-public meeting proposed 12/13/93
 - 200-W Carbon Tetrachloride
 - Restart at Z-1A was initiated on 11/12/93 - GAC meeting proposed for 12/6/93
 - 618-11
 - Transition to OU status
- OTHER ISSUES
- SUMMARY OF ACTION ITEMS
- SIGN-OFF ON ANY DECISIONS, AGREEMENTS, OR COMMITMENTS

9413092.0027

EXPEDITED RESPONSE ACTION INTERFACE MEETING

-ACTION ITEMS-
November 29, 1993

ORGANIZATION

ACTION ITEM

WHC

Provide copy of the CCl₄ summary analysis report (open). Meeting has been scheduled for 12/6/93.

RL/WHC

RL to provide a brief description on the plan to transition the CCl₄ ERA into an IRM. Included in this plan will be any discussion of alternate treatment technologies (i.e. condensers). (open)

WHC

Provide information on potential to reseed the Riverland site with endangered or threatened species (request of Yakima Indian Nation). (open)

WHC

WHC will prepare a briefing on the Operational Readiness Review requirements for Environmental Restoration field activities. (open)

9413092.1828

Weekly Report, Period Ending November 26, 1993
EXPEDITED RESPONSE ACTIONS
Technical and Management Contact - Wayne L. Johnson, 376-1721
Environmental Division

North Slope Expedited Response Action - The EE/CA has been revised to incorporate comments from DOE-HQ, RL, ACOE, and the regulators and is undergoing a final edit. Public review was initiated on November 8, 1993.

N-Springs Expedited Response Action - DOE-HQ, EPA, and Ecology's comments have been received and are being reviewed.

White Bluffs Pickling Acid Crib Expedited Response Action - A strategy is being prepared to address the September 7, 1993, letter concerning the requirements for issuing an Interim Record of Decision for the ERA site. An integrated schedule for reaching records of decisions for the Pickling Acid Crib, Sodium Dichromate site, and the Riverland site is in preparation.

618-11 Burial Ground Expedited Response Action - Regulator comments were received on September 28, 1993. Formal guidance has been provided by RL and the regulators to cease all work on this ERA, consistent with the recent TPA modifications. A closeout meeting with RL and the regulators was held on November 22, 1993.

Riverland Expedited Response Action - The final assessment report is under preparation.

Sodium Dichromate Expedited Response Action - The Sodium Dichromate ERA assessment report has been distributed.

200 West Area Carbon Tetrachloride Expedited Response Action - On November 12, 1993, vapor extraction operations resumed at the 216-Z-1A site. RL concurred on November 19, 1993, that the CCl_4 vapor extraction system activities do not require a Type 5 Nuclear Facility Operational Readiness Review and the line management procedure was adequate. WHC approval for restart was issued following the RL concurrence. The 216-Z-1A system final walkdown and prestart checks were completed on November 12, 1993, with individual borehole characterization initiated on November 12, 1993. Characterization was completed on November 18, 1993 with full system operation commencing on November 18, 1993. The safety assessment for 216-Z-9 is being revised to incorporate new data which should allow operations to proceed with concentrations of CCl_4 of less than 10,000 ppm. The planning documents will now be ready in mid-December. Five members of the operations team attended a five day training class in Albuquerque, New Mexico.

6780-7608-116
9413092-0929

DRAFT


Schedule Name : Integrated ERA Scheudle for FY 1994

Responsible :

As-of Date : 11/29/93

Schedule File : ERACOMBO

/ll Plans/Proposals will be reviewed concurrently. The US
Army Corp of Engineers is responsible for the Ordnance

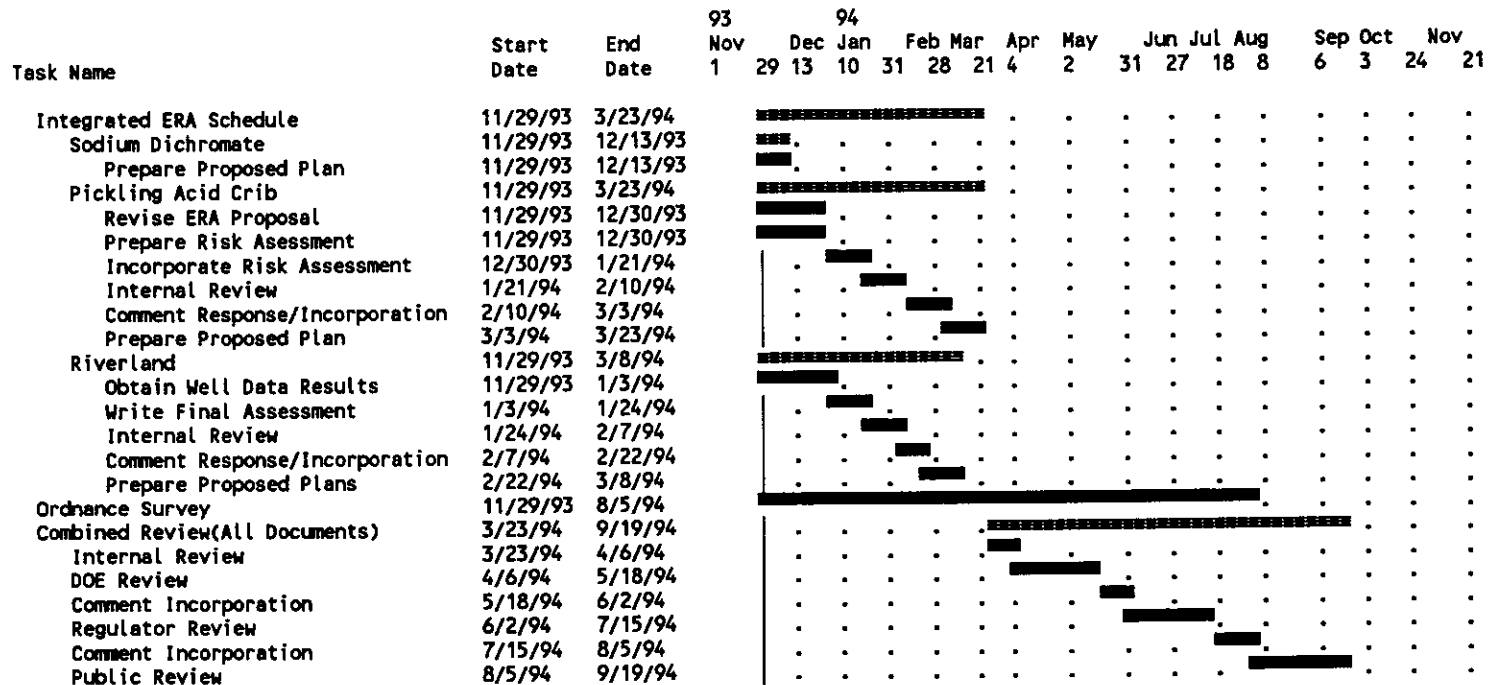

■ Detail Task ■■■■ Summary Task Baseline
 ■■■ (Progress) ■■■■ (Progress) >>> Conflict
 ■■■ (Slack) ■■■■ (Slack) ■■■ Resource delay

Progress shows Spaces on Actual ▲ Milestone

----- Scale: 4 days per character -----

TIME LINE Gantt Chart Report, Strip 1
