

START

9513335.1240

0040517 ⁷

Final

Meeting Minutes Transmittal/Approval
Unit Manager's Meeting: 200-BP-1 Operable Unit
3000 George Washington Way, Walkley Boardroom, Richland, Washington
September 28, 1994

FROM/APPROVAL: Bryan J Foley Date 2/16/95
Bryan Foley, 200-BP-1 Unit/Manager, RL (H4-83)

APPROVAL: Paul R. Beaver Date 2/16/95
Paul R. Beaver, 200-BP-1 Unit Manager, EPA (B5-01)

APPROVAL: Fenggang Ma Date 2/16/95
Fenggang Ma, 200-BP-1 Unit Manager, WA Department of Ecology

Meeting Minutes are attached. Minutes are comprised of the following:

- Attachment #1 - Meeting Summary/Summary of Commitments and Agreements
 - Attachment #2 - Attendance List
 - Attachment #3 - Agenda for the Meeting
 - Attachment #4 - Status of Action Items
 - Attachment #5 - Schedule
-

Prepared by: Kay Kimmel Date: 2/16/95
Jim Consort, Kay Kimmel, GSSC (B1-42)

Concurrence by: Joe Zoghbi Date: 2/16/95
Joe Zoghbi, BHI Project Manager - 200 Areas (H4-79)

H4-07



Attachment #1**Meeting Summary and Summary of Commitments and Agreements
Unit Manager's Meeting: 200-BP-1 Operable Unit
September 28, 1994****1. SIGNING OF THE PREVIOUS 200-BP-1 MEETING MINUTES:**

Minutes from the previous meeting were reviewed and approved with no changes.

2. ACTION ITEM UPDATE: (See Attachment 4 for status)

No open action items.

3. NEW ACTION ITEMS (INITIATED September 28, 1994):

2BP1.57 Obtain firm dates from the EPA for issuing the Proposed Plan and the Record of Decision on 200-BP-1 Operable Unit. Action: Donna Wanek.

4. INFORMATION ITEMS:

- Status of Activities for 200-BP-1

Mark Buckmaster provided the update on the 200-BP-1 OU (see Attachments #3 and #5). EPA indicated that the longevity and permeability of the asphaltic layer of the RCRA Modified Barrier remains an issue and will be regulated through the Focused Feasibility Study process.

- **Modified RCRA Barrier:** Mark Buckmaster provided the status of the Modified RCRA Barrier by indicating that the Proposed Plan is at the EPA. He noted that, earlier in the week, EPA had indicated that the Record of Decision would be issued eight months after the Proposed Plan. Donna Wanek heard from Paul Beaver that December 1, 1994 will be the issue date of the Proposed Plan along with other Proposed Plans. Mark Buckmaster says that this delay poses no large cost impact, just escalations, since no contracts had been given.

- Next Meetings - The next CERCLA Unit Manager Meetings are scheduled for October 20, 1994.

200 Aggregate Area Unit Manager's Meeting
Official Attendance Record
September 28, 1994

Please print clearly and use black ink

PRINTED NAME	ORGANIZATION	O.U. ROLE	TELEPHONE
M.A. Buckmaster	BHI	OU Coord	376-1792
Donna Waneke	- RL	OU mgr for RL	376-5778
GEORGE C. HENRIKSEN III	BHI	Asst. Dir. 200 Area Projects	
Kenneth R Porter	ITH	200 Area Task Lead	372-9022
DAVID A MYERS	ITH	Hydrology	372-9491
Tony Knapp	BHI	Hydrology	372-9189
Jim Consort	Dames & Moore/GSSC	AL Support	9463694
Diana Szeikla	BHI	BHI/TPA Support	375-9422
D. B. Eab	ITH	BP-5	372-1402
MICHAEL D. BAKER	ITH	BP-5	373-6862
JEFF JAMES	BHI	ENV. ENGR. SUPPORT	375-9690
Jeff Ross	PREMI	EPA Support	206/624-2692
William E. Lum II	- USGS	EPA Support	206 593 6510
Michael J Galgowl	ITH	200-UP-2 OU TASK LEAD	509 376 2038
Beth Ward	DOE-RL	OU mgr for RL	376-7142
Andrea Hopkins	ITH	Reg Support Compliance	372-9027
CURT WITTEICH	ITH	OU Mgr UP-1	376-1862
Frank Gustafson	ITH	200-VP-1 Treatability Test	376-1734
D. Goswami	Eldon	OU Mgr OUM	736-3015
Nancy Hernandez	Ecology	O.U.M	736-3014
Paul Pak	DOE-RL	UM	376-4498
Gary Freedman	Ecology	oum	736-3026
Bever Ford	BHI	TECH OVERSIGHT/ 200-UP-1 Support	372-9176
Sean A. Driggers	ITH	200-2P-2 OU Lead	372-3493
DAN PARKER	ITH	200-2P-1 OU Coord.	372-1031
KAY KIMMEL	GSSC ID&M	RL SUPPORT	946-3692

200-BP-1 UNIT MANAGERS MEETING AGENDA
SEPTEMBER 28, 1994
WPPS-WALKLEY BOARDROOM

Action Items:

- 2BP1.56 Provide RL the barrier design requirements associated with the RCRA modified barrier to assure RL that the RCRA modified barrier currently being designed for construction in 1995 is acceptable. Action: Paul Beaver (5/26/94)

closed 8/24/94

Prototype Barrier Status:

- o Utilities are being installed to support testing and monitoring activities.
- o PNL has begun installing testing and monitoring equipment.
- o The final Constructability Report will be completed by the end of September.

Modified RCRA Barrier


- o Definitive design
 - Design drawings and construction specification are currently being finalized. Submittal of final drawings and specifications will depend on ROD date.

Proposed Plan:

- o Preliminary schedule-Based on November 1, 1994 public comment period and 8 month EPA ROD preparation.

Attachment #4
Action Item Status List
Unit Manager's Meeting: 200-BP-1 Operable Unit
September 28, 1994

ITEM NO.	ACTION	STATUS
2BP1.56	Provide to RL the barrier design requirements associated with the RCRA Modified Barrier to assure RL that the RCRA Modified Barrier currently being designed for construction in 1995 is acceptable. Action: Paul Beaver.	Closed 08/24/94.
2BP1.57	Obtain firm dates from the EPA for issuing the Proposed Plan and the Record of Decision on 200-BP-1 Operable Unit. Action: Donna Wanek.	Open 09/28/94

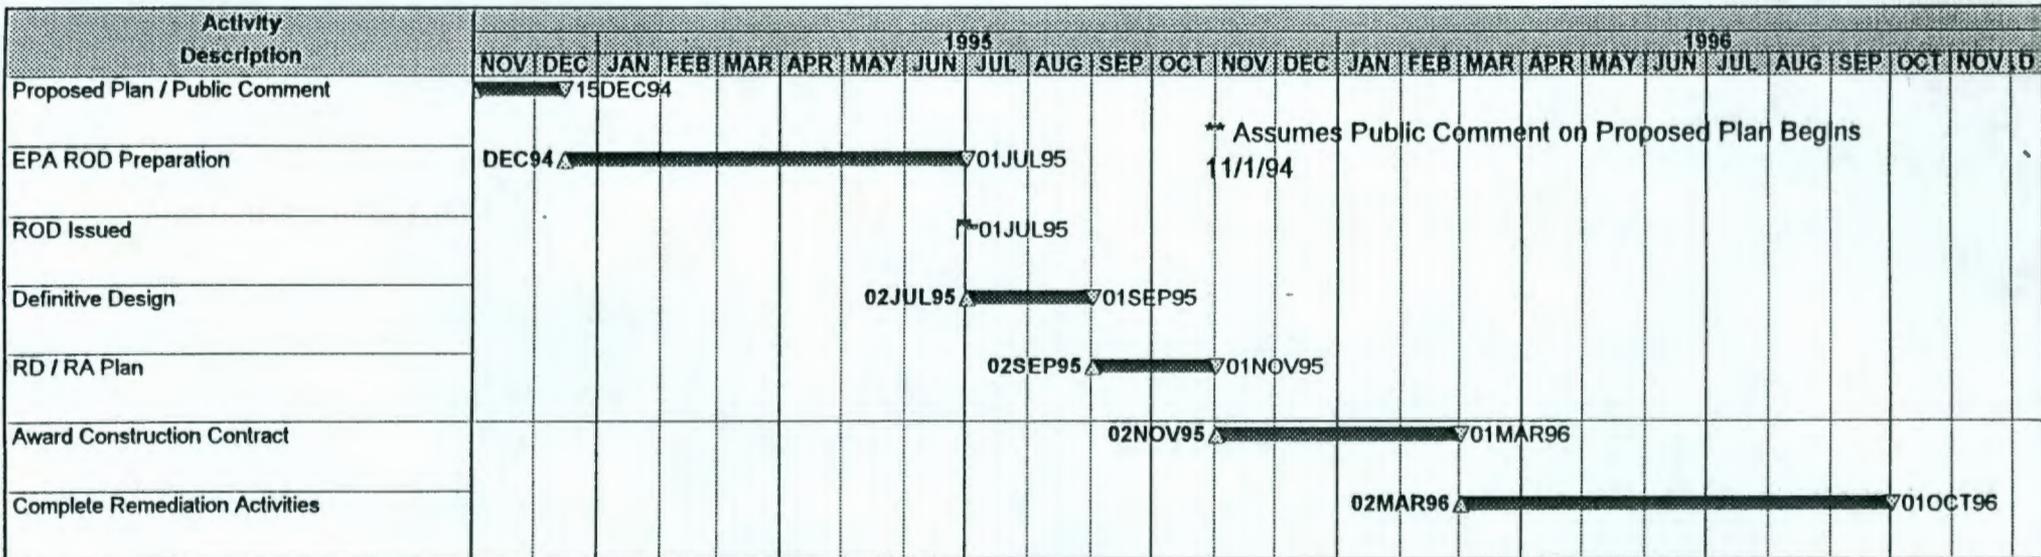

Attachment #5

Page 1 of 1

9513335.1245

Project Start 01NOV94
 Project Finish 01OCT96
 Date Date 01NOV94
 Plot Date 27SEP94



MARK

Distribution

Unit Manager's Meeting: 200-BP-1 Operable Unit
September 28, 1994

Donna Wanek DOE-RL, PRD (H4-83)
 Bryan Foley DOE-RL, PRD (H4-83)
 Mary Harmon DOE-HQ (EM-442)
 Richard Person DOE-HQ (EM-442)

Paul Beaver 200-BP-1 Operable Unit Manager, EPA (B5-01)
 Bill Lum, USGS Support to EPA
 Jim Pankanin, PRC Support to EPA

Fenggang Ma 200-BP-1 Operable Unit Manager, WDOE (Kennewick)
 Larry Goldstein WDOE (Lacey)

Lynn Albin Washington Dept. of Health
 Joe Zoghbi BHI (H4-79)
 Mark Buckmaster BHI (H6-03)
 Diana Sickle BHI (H4-79)
 200-BP-1 RI Project File (H6-08)
 Doug Dunster Golder Associates, Support to BHI
 Alvina Goforth BHI (H6-08)
 R. Scott Hajner BHI (H4-79)
 Andrea Hopkins BHI (H4-79)
 Tom Page (Please route to:) PNL (K1-31)
 Cheryl Thornhill PNL (K1-19) Steve Slate PNL (K1-19)
 Mark Hanson PNL (K1-51) Bill Stillwell PNL (K1-30)
 ~~Roy Gephart PNL (K1-22)~~ Ben Johnson PNL (K1-78)
 Ralph O. Patt Oregon Water Resources Department
 K. Kimmel GSSC (B1-42)

Original Sent To: ADMINISTRATIVE RECORD: 200-BP-1; Care of EDMC, WHC (H6-08)

This list was updated 09/26/94. Please inform Kay Kimmel (946-3692) GSSC-Dames & Moore (B1-42) of deletions or additions to the distribution list.
