

START

15
0022670

Final

Meeting Minutes Transmittal/Approval
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
450 Hills, Richland, Washington

June 25, 1992

FROM/APPROVAL: *Paul Pak* Date 7-30-92
Paul Pak, 200 Aggregate Area Unit Manager, RL (A5-19)

APPROVAL: *Lawrence E. Sherwood For* Date 7-30-92
Doug Sherwood, 200 Aggregate Area Unit Manager, EPA (B5-01)

APPROVAL: *Billie Mauss* Date 7/30/92
Darci Teel, 200 Aggregate Area Unit Manager, WA Dept of Ecology

Meeting Minutes are attached. Minutes are comprised of the following:

- Attachment #1 - Meeting Summary
- Attachment #2 - Agenda
- Attachment #3 - Attendance
- Attachment #4 - Action Item Status List
- Attachment #5 - Status of 200 Aggregate Area Management Study Program
- Attachment #6 - Proposed Schedule Change for the 200 West Groundwater AAMSR
- Attachment #7 - 200 AAMS Geophysical Logging and Groundwater Sampling Field Activities Update

9 2 1 2 6 5 4 1 3 8 2



Prepared by: *Suzanne Clarke* Date: 7/30/92
Suzanne Clarke, Kay Kimmel, GSSC (A4-85)

Concurrence by: *Curt Wittreich* Date: 7/30/92
Curt Wittreich, WHC Coordinator (H4-55)

Attachment #1
Meeting and Summary of Commitments and Agreements
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units

June 25, 1992

1. SIGNING OF THE MAY 200 AREA UNIT MANAGER'S MEETING MINUTES:

Meeting minutes were reviewed and approved.

2. ACTION ITEM UPDATE: See Attachment 4 for status (before June meeting)

No updates were made to existing Action Items.

3. NEW ACTION ITEMS (INITIATED June 25, 1992):

No new action items were initiated.

4. STATUS 200 AGGREGATE AREA MANAGEMENT STUDIES

- Curt Wittreich presented the status of 200 Aggregate Area Management Study Program, shown in Attachment #5.
- Proposed schedule change for the 200 West Groundwater AAMSR is under regulatory consideration. See Attachment #6.
- Steve Trent presented the update of the 200 AAMS Geophysical Logging and Groundwater Sampling Field Activities, shown in Attachment #7.

5. INFORMATION ITEMS/INFORMAL AGREEMENTS:

- Questions arose concerning comment disposition of the AAMSRs. WHC agreed to send a cc:mail message on 1) which sections to consider for review and 2) which sections have already been commented on and do not require review.
- 200 West spectral gamma-ray logging is behind schedule by sixteen wells. The regulators agreed they would prefer the report on schedule with less data.

9 2 1 2 5 1 4 1 3 3 3

Attachment #2
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

Agenda

- 200 AAMS Activities - Curt Wittreich
 - Status of AAMSRs
 - Geophysical Logging and Groundwater Sampling Field Activities Update

9 2 1 2 5 4 1 3 3 4

Attachment #3

200 Aggregate Area Unit Manager's Meeting
Official Attendance Record
June 25, 1992

Please print clearly and use black ink

PRINTED NAME	SIGNATURE	ORGANIZATION	O.U. ROLE	TELEPHONE
Suzanne Clarke	Suzanne Clarke	SWEC	GSSC to DOE/RL	312-0630
Paul Pak	Paul Pak	DOE-RL	DU	376-4798
DAN PARKER	Dan Parker	WHC	200 WGW	372-1031
CHUCK CLINE	Chuck Cline	ECOLOGY	Geol. Support	206 438-7556
D. Goswami	D. Goswami	Ecology	Unit Mgr.	509/546-4301
RICH MULLEN	Rich Mullen	PARAMETRIX	Ecology Support	206-455-2550
Jon Spreckle	Jon Spreckle	Brown & Caldwell	Ecology Support	(503) 244-7005
NANCY UZIEMBO	Nancy Uziembo	ECOLOGY	Unit Mgr.	509 546-2994
KAY KIMMEL	Kay Kimmel	SWEC	GSSC	509-372-0610
Paul Beaver	Paul Beaver	EPA	Unit Mgr.	376-8665
PAMELA INNIS	Pamela Innis	EPA	UNIT MANAGER	509/376-4419
Larry Gadbois	Larry Gadbois	EPA	Unit Manager	509 376-9884
STEVE + TREAT	Steve + Treat	WHC	Geosci Support	376-7226
HA PARKER	HA Parker	WHC	ESCORT	
H.D. Downey	H.D. Downey	WHC	ER Program office	509/376-5539
BISA CHETNIK TRICKEL	Bisa Chetnik Trickel	DOE-HQ/EH-442	observer Program Mgr.	301 903-8177
Ward Stambitz	Ward Stambitz	USGS	EPA Support	206 593 6510
Brian Drost	Brian Drost	USGS	EPA Support	206 593 6510
Billie Mauss	Billie Mauss	Ecology	CERCLA-Support	509-546-2993
Michael J Galgoul	Michael Galgoul	WHC	200 UPZ Tech lead	376-2038 509-435
Andree De Angeles	Andree De Angeles	PRC	EPA Support	206-624-2692

Attachment #4

Action Item Status List
Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

Item No.	Action/Source of Action	Status
2AAMS.1	Identify and implement the actions that are required to install the calibration pits for the borehole logging equipment. Action: Allan Harris (9/19/91)	Open
2AAMS.5	DOE will initiate the paperwork for changing the content and/or boundaries of the 200-UP-2 OU. Action to Allan Harris (2/26/92).	Open
2AAMS.6	Allan Harris will meet with Mike Thompson to clarify what changes to the UP-1 and UP-2 units will be sought in a Level 2 Change Request. A new Change Request will be submitted after Allan meets with RL management and the TPA Project Manager Board.	Open

9 2 1 2 6 3 4 1 3 1 6

9 2 1 2 5 3 4 1 3 3 7

Attachment #5

200 AGGREGATE AREA MANAGEMENT STUDY PROGRAM

Curtis D. Wittreich
Technical Coordinator

Steven J. Trent
Field Activities Coordinator

June 25, 1992

Status 200 Aggregate Area Management Study Program

06/24/92

Area	Aggregate Area	AAMS Type	AAMS Report	Regulator Comments Due	M-27-00 Milestones
200 West	U Plant	Source	Redrafting Based on Regulator Comments	3/16/92	1/92
	Z Plant	Source	Regulator Review Comments Dispositioned	4/14/92	2/92
	S Plant	Source	Regulator Review Comments Dispositioned	5/15/92	3/92
	T Plant	Source	Regulator Review Comments Received	6/15/92	4/92
	200 West	Groundwater	Drafted-On Schedule		9/92
200 East	PUREX	Source	Draft A Under Regulatory Review	7/15/92	5/92
	B Plant	Source	Drafted-On Schedule		6/92
	Semi-Works	Source	Drafted-On Schedule		7/92
	200 East	Groundwater			9/92
200 North	200 North	Source	Drafted-On Schedule		8/92

9 2 1 2 5 3 4 1 3 3 9

Attachment #6

PROPOSED SCHEDULE CHANGE FOR THE 200 WEST GROUNDWATER AAMSR:

- **Move the Draft A submittal date up 1 month to August 31**
- **Schedule regulator review from September 1 - October 15**

9 2 1 2 5 1 4 1 3 9 0

Attachment #7

**200 AAMS
GEOPHYSICAL LOGGING AND
GROUNDWATER SAMPLING
FIELD ACTIVITIES UPDATE**

6/25/92
PAGE 1

GEOPHYSICS


● SPECTRAL GAMMA-RAY LOGGING COMPLETED TO DATE:

299-W22-75	216-S-21 CRIB	U PLANT	299-W11-18	216-T-35 CRIB	T PLANT
299-W23-4	216-U-12 CRIB	U PLANT	299-W11-70	216-T-26 CRIB	T PLANT
299-W19-11	216-U-1 CRIB	U PLANT	299-W14-4	216-T-28 CRIB	T PLANT
299-W19-9	216-U-2 CRIB	U PLANT	299-W11-11	216-T-18 CRIB	T PLANT
299-W18-10	216-Z-18 CRIB	Z PLANT	299-W15-4	216-T-19 CRIB	T PLANT
299-W15-63	216-Z-5 CRIB	Z PLANT	299-W15-210	216-T-21:24	T PLANT
299-W15-8	216-Z-9 CRIB	Z PLANT	299-W11-61	216-T-6 CRIB	T PLANT
299-W15-7	216-Z-7 CRIB	Z PLANT	299-W11-7	216-T-3 CRIB	T PLANT
299-W18-5	216-Z-7 CRIB	Z PLANT	299-W11-81	216-T-14:17	T PLANT
299-W22-21	216-S-13 CRIB	S PLANT			
299-W22-32	216-S-7 CRIB	S PLANT			
299-W22-74	216-S-20 CRIB	S PLANT			
299-W26-1	216-S-5 CRIB	S PLANT			
299-W26-51	216-S-8 CRIB	S PLANT			

****NO 200 AAMS BOREHOLE LOGGING COMPLETED SINCE LAST UMM****

6/26/92
PAGE 2

200 AGGREGATE AREA MANAGEMENT STUDY SPECTRAL GAMMA-RAY LOGGING STATUS

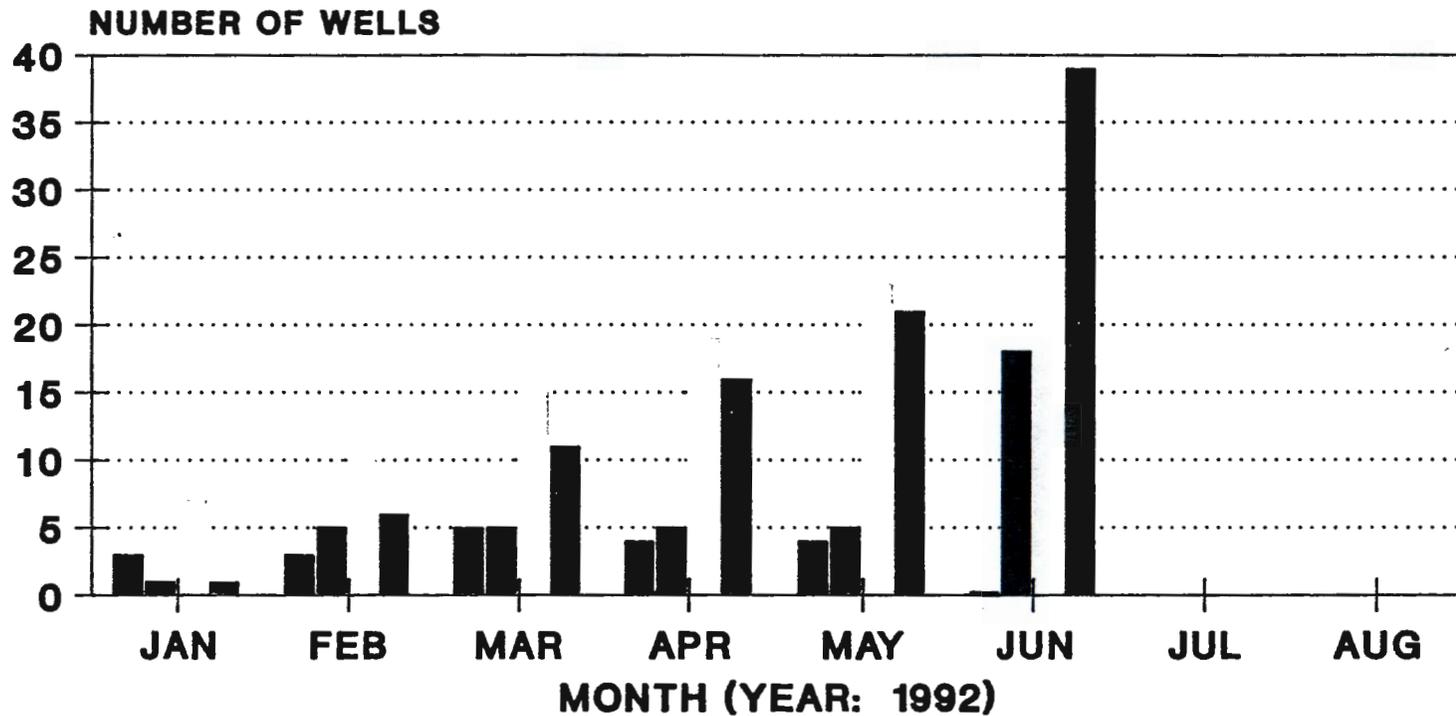

LOGGED DURING MONTH
 SCHD. TO LOG
 TTL. LOGGED TO DATE
 TTL. SCHD. TO LOG

DATE: 6/25/92
NOTE: FOUR WELLS LOGGED DURING CY 1991

GEOPHYSICS (CONTINUED)

● SPECTRAL GAMMA-RAY LOGGING SCHEDULE DELAYED FOR TWO REASONS:

1) IMPLEMENTATION OF NEW RADIATION PROTECTION MANUAL

- ACCESS TO SURFACE CONTAMINATED ZONES UNCLEAR**
- POTENTIAL FOR REGULATION OF LOGGING TRUCK UNCLEAR**

- MANAGEMENT WORKING TO IDENTIFY CLARIFICATIONS ON ENTRY REQUIREMENTS AND IDENTIFYING SCENARIOS UNDER WHICH LOGGING TRUCK BECOMES A REGULATED VEHICLE

2) DELAY IN PROCUREMENT PROCESS FOR SUBCONTRACTOR SPECTRAL GAMMA-RAY LOGGING SERVICES

- PROCUREMENT PROBLEMS ENCOUNTERED WITH THE COMPETITIVE BID PROCESS**

- GEOPHYSICS TEAM WORKING WITH PROCUREMENT TO MODIFY BID AND CUT BID PROCESSING TIME

GEOPHYSICS (CONTINUED)

● IMPACTS:

- SLIP IN LOGGING SCHEDULE IDENTIFIED DURING THE JANUARY 1992 UNIT MANAGER MEETING**
- FIRST DRAFT OF 200 WEST SPECTRAL GAMMA-RAY LOGGING REPORT WILL NOT CONTAIN DATA FROM ALL WELLS IDENTIFIED IN THE 200 WEST BOREHOLE GEOPHYSICS SAP's**
- POTENTIAL DELAY IN RELEASE OF THE 200 EAST SPECTRAL GAMMA-RAY LOGGING REPORT**

RECOVERY SCHEDULE WILL BE PRESENTED AT THE JULY UNIT MANAGER MEETING

GROUNDWATER SAMPLING

● PHASE II GROUNDWATER SAMPLING CONTINUING

- 14 WELLS SAMPLED AS OF 6/25/92

● WELL MAINTENANCE ACTIVITIES COMPLETED

- 23 OLDER NON-RCRA STANDARD MONITORING WELLS REFURBISHED

● PHASE II SAMPLING AND ANALYSIS PLAN REVISED

- REVIEW AND FIELD CHECK OF ORIGINAL 80 WELLS INDICATES 10 WELLS ARE UNUSABLE
- 70 WELLS TO BE SAMPLED ONCE DURING FISCAL YEAR 1992
- REVISED PHASE II SAP TO BE DISTRIBUTED AT THIS UMM

6/25/92
PAGE 5

Distribution

Unit Manager's Meeting: 200 Aggregate Area/200 Area Operable Units
June 25, 1992

- Julie K. Erickson Chief, DOE-RL, ERD/ERB (A5-19)
- Roger D. Freeberg Chief, Rstr. Br., DOE-RL, ERD/EPB (A5-19)
- Mike Thompson, DOE-RL, EAP/RPB (A5-15)
- Diane Clark, DOE-RL, TSD/SSB (A5-55)
- Mary Harmon, DOE-HQ (EM-442)
- Suzanne Clarke, SWEC, GSSC to DOE-RL (A4-35)

- Doug Sherwood 200 Aggregate Area Manager, EPA (B5-01)
- Ward Staubitz, USGS, Support to EPA
- Audree DeAngeles, PRC, Support to EPA

- Darci Teel 200 Aggregate Area Manager, WDOE, (Kennewick)
- Larry Goldstein WDOE, (Lacey)

- Lynn Albin Washington Dept. of Health

- Richard D. Wojtasek, WHC, Program. Manager (L4-92)
- Curt Wittreich, WHC, (H4-55)
- Tom Wintczak, WHC, (L4-92)
- Mel Adams, WHC, (H4-55)
- L.D. Arnold, WHC, (B2-35)
- Rich Carlson, WHC, (H4-55)
- M.J. Galgoul, WHC, (H4-55)

- Don Praast, GAO (A1-80)

ADMINISTRATIVE RECORD: 200 AAMS; Care of EDMC, WHC (H4-22)

This list has been updated. Please inform Suzanne Clarke (SWEC) of deletions or additions to the distribution list.

9 2 1 2 9 3 4 1 3 9 6
